


Superintendent's Report April, 2016



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District

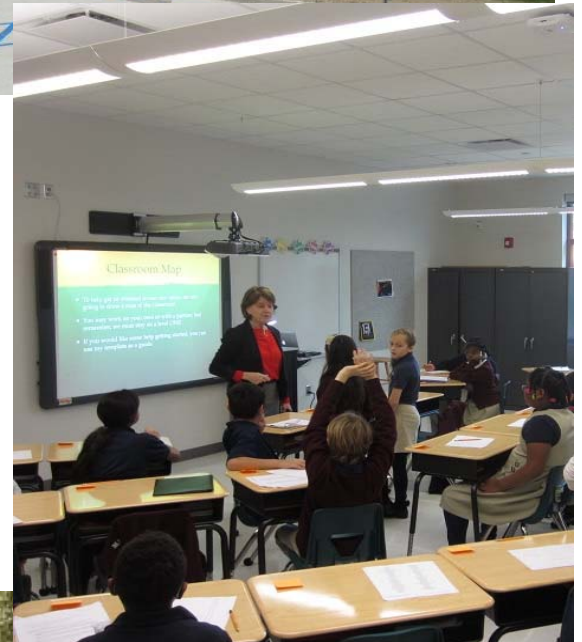

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	3
COMMUNITY MEETINGS	4
BID OPENINGS	5
DBE OVERVIEW MONTHLY SUMMARY	6
NEW & MAJOR RENOVATION	11
Ray Abrams Elementary School ^(RSD)	11
Avery Alexander Elementary School ^(RSD)	11
George Washington Carver School ^(RSD)	11
Benjamin Franklin Elementary School Renovation ^(OPSB)	12
Paul B. Habans School ^(RSD)	12
JoEllen Smith Medical Center Demolition ^(OPSB)	12
New Karr High School, CMAR ^(OPSB)	13
John McDonogh High School Renovation CMAR ^(RSD)	13
Eleanor L. McMain School Gymnasium ^(OPSB)	13
Ernest "Dutch" Morial Elementary School ^(RSD)	14
Sherwood Forest School ^(RSD)	14
Harriet R. Tubman Elementary School Renovation ^(RSD)	14
Booker T. Washington School CMAR ^(RSD)	15
Sophie B. Wright School ^(RSD)	15

REFURBISHMENTS	16
Benjamin Banneker Elementary Kitchen School Refurbishment ^(RSD)	16
Agnes L. Bauduit Elementary School Refurbishment ^(RSD)	16
Walter L. Cohen High School Kitchen Refurbishment ^(RSD)	16
A. D. Crossman School Kitchen Refurbishment ^(RSD)	17
Frederick A. Douglass High School Science Lab ^(RSD)	17
William J. Fischer Elementary Refurbishment ^(RSD)	17
Fortier (Lusher) High School Refurbishment ^(OPSB)	18
Gaudet Elementary School Refurbishment ^(RSD)	18
Edgar P. Harney Elementary School Refurbishment ^(RSD)	18
Andrew Jackson School Refurbishment ^(RSD)	19
J. W. Johnson Elementary School Refurbishment ^(RSD)	19
Lafayette Elementary School Refurbishment ^(RSD)	19
Laurel Elementary School Refurbishment ^(RSD)	20
Live Oak Elementary School Refurbishment ^(RSD)	20
Lusher Elementary School Refurbishment ^(OPSB)	20
Thurgood Marshall Elementary School Refurbishment ^(RSD)	21
McDonogh #28 School Refurbishment ^(RSD)	21
McDonogh #32 School Refurbishment ^(RSD)	21
Rosenwald Elementary School Refurbishment ^(RSD)	22
Village de l'Est Elementary School Refurbishment ^(RSD)	22
Albert Wicker School Kitchen Refurbishment ^(RSD)	22
OTHER PROJECTS	23
Eleanor L. McMain School Roof Replacement ^(OPSB)	23
Eleanor L. McMain School Maintenance Upgrades ^(OPSB)	23
Building Automation System Integration At Recovery School District Central And Remote Offices ^(RSD)	23
MOTHBALL OR SAFE & SECURE OF SELECTED SCHOOLS	24
Demolition of Modulars at Abramson and Carver ^(RSD)	24
Demolition of Modulars at Livingston ^(RSD)	24
COMPLETED PROJECTS	25

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$556 million in open contracts for the capital program after issuing \$4.2 million in new contracts, change orders and amendments in April. In addition, the total change orders to date, \$6.2 million, account for one percent (1.28%) of the total open construction contracts. RSD anticipates issuing approximately \$17 million in construction contracts/change orders, and \$536 thousand in professional service contracts/amendments in May.



The OPSB has \$231 million in open contracts for the capital program after issuing \$3.4 million in new contracts, change orders and amendments in April. In addition, the total change orders to date, \$7.2 million, account for approximately four percent (3.67%) of the total open construction contracts. OPSB anticipates issuing approximately no construction contracts/change orders and \$282 thousand in professional service contracts and amendments in May.

Community Meetings



Future Community Meetings

May 11, 2016

Harriet Tubman Charter School Community / Contractor Meeting
2832 General Meyer Avenue New Orleans, LA 70114

Bid Openings

Bids that were opened in April, 2016

April 13, 2016

- Lafayette School Refurbishment

April 27, 2016

- Sophie B. Wright School Cornice Replacement

The following projects are scheduled to bid in the next 60 days

May 18, 2016

- Laurel School Refurbishment

Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District



New & Renovations:

DBE Contractors secured subcontracts on 22 projects as of April 30, 2016. The DBE subcontracts value is \$77,607,713 of the \$362,046,187 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 44 projects as of April 30, 2016. The DBE subcontracts value is \$17,345,475 of the \$53,851,020 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of April 30, 2016. The DBE subcontracts value is \$34,701,554 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$ 525,034,764

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of April 30, 2016. The DBE subcontracts value is \$54,086,557 of the \$199,371,360 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of April 30, 2016. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$200,274,359

* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

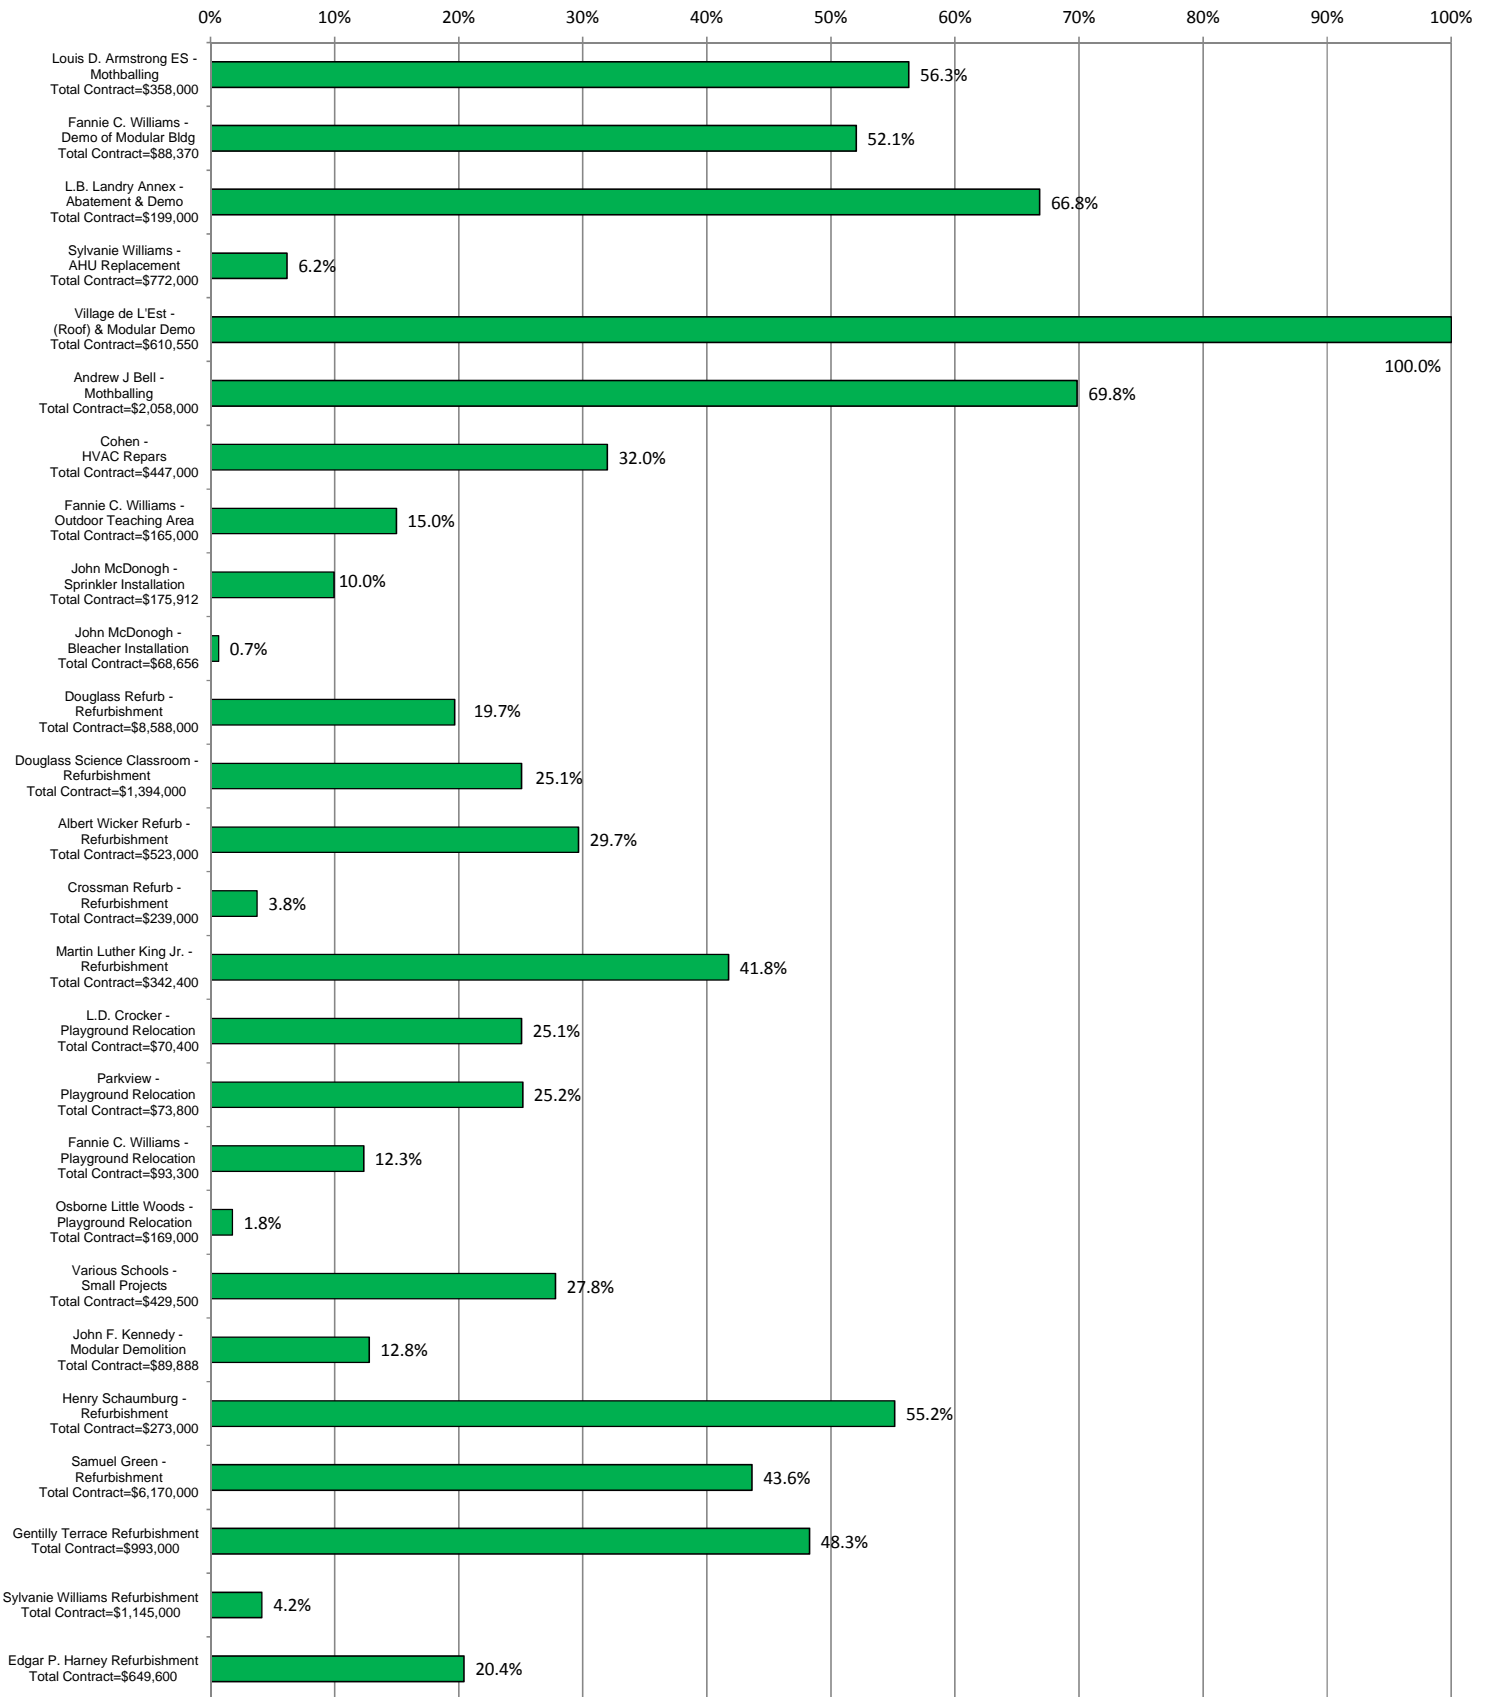


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Status Date: 30 April 2016


Current RSD Program DBE Participation

(Continued)

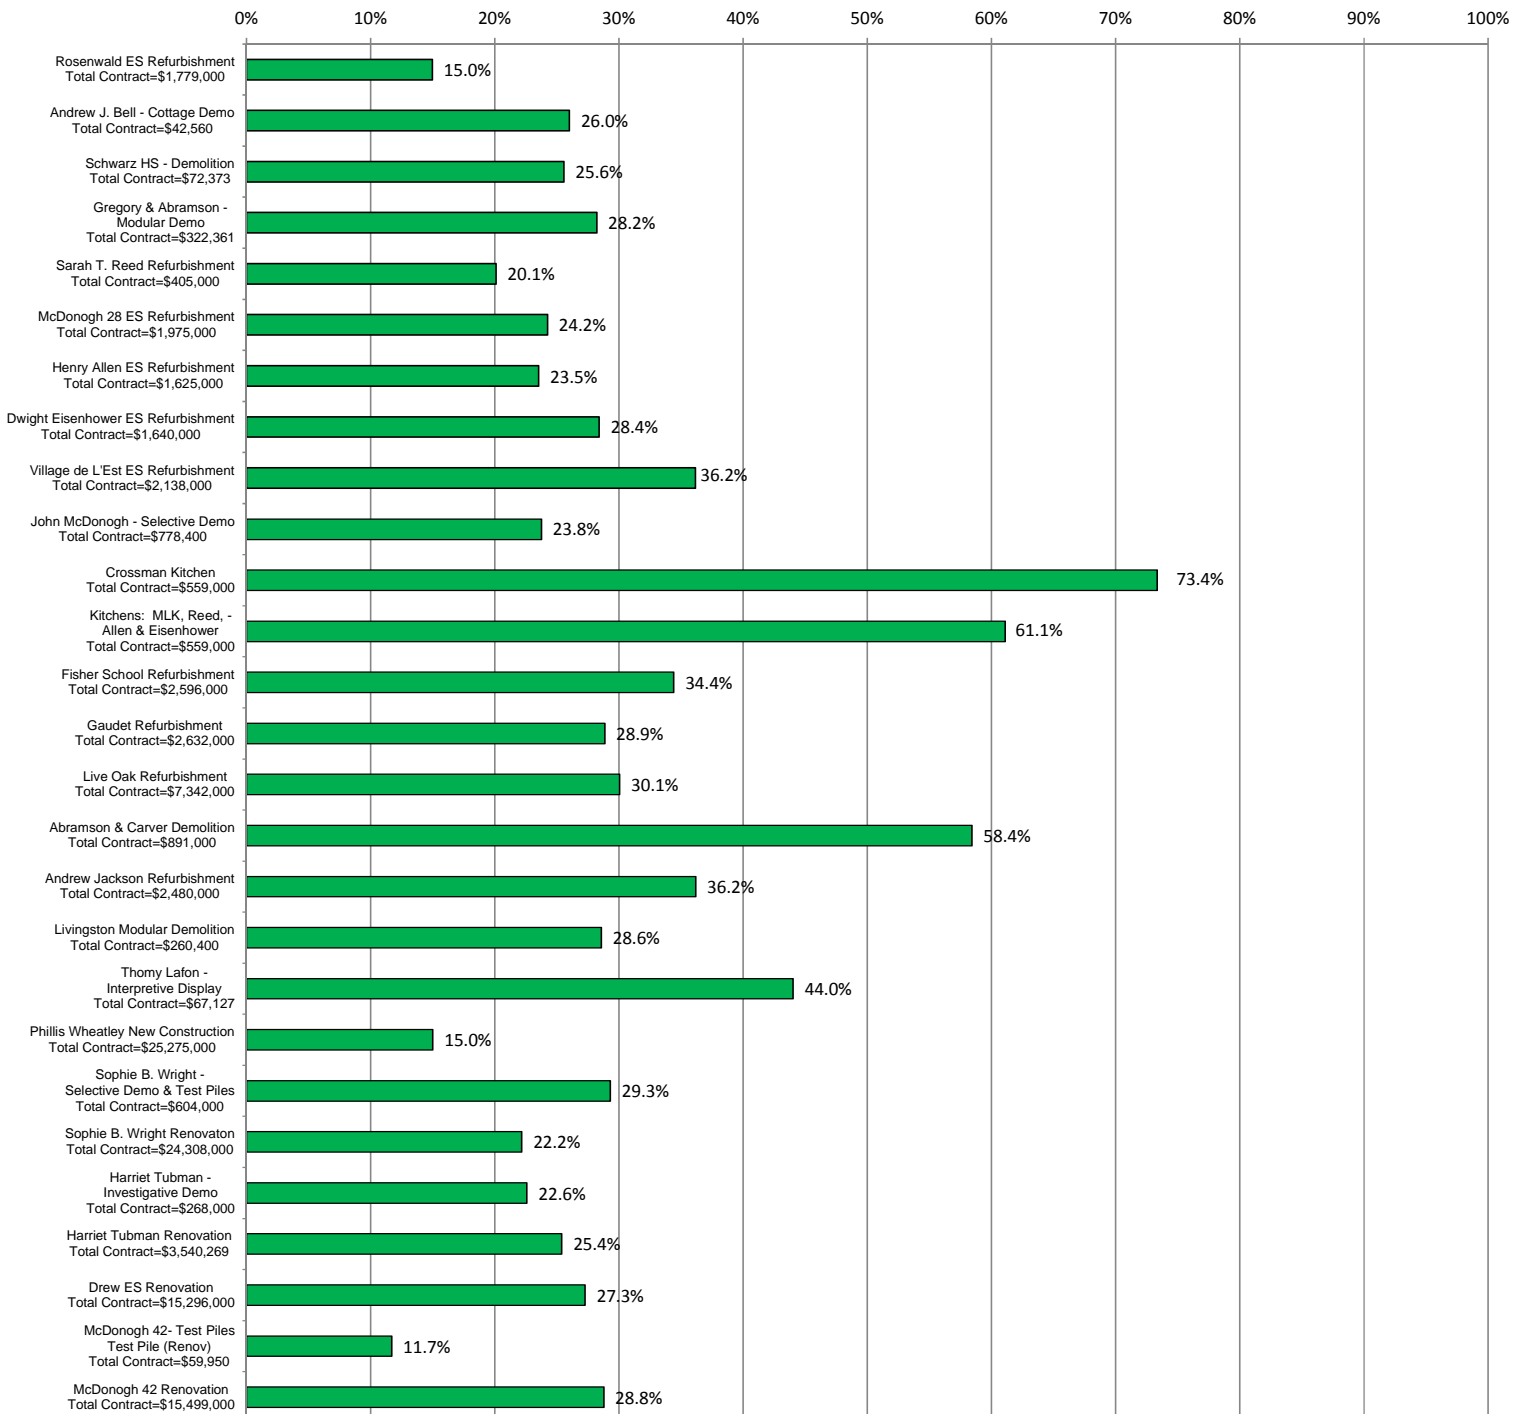


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current RSD Program DBE Participation (Continued)

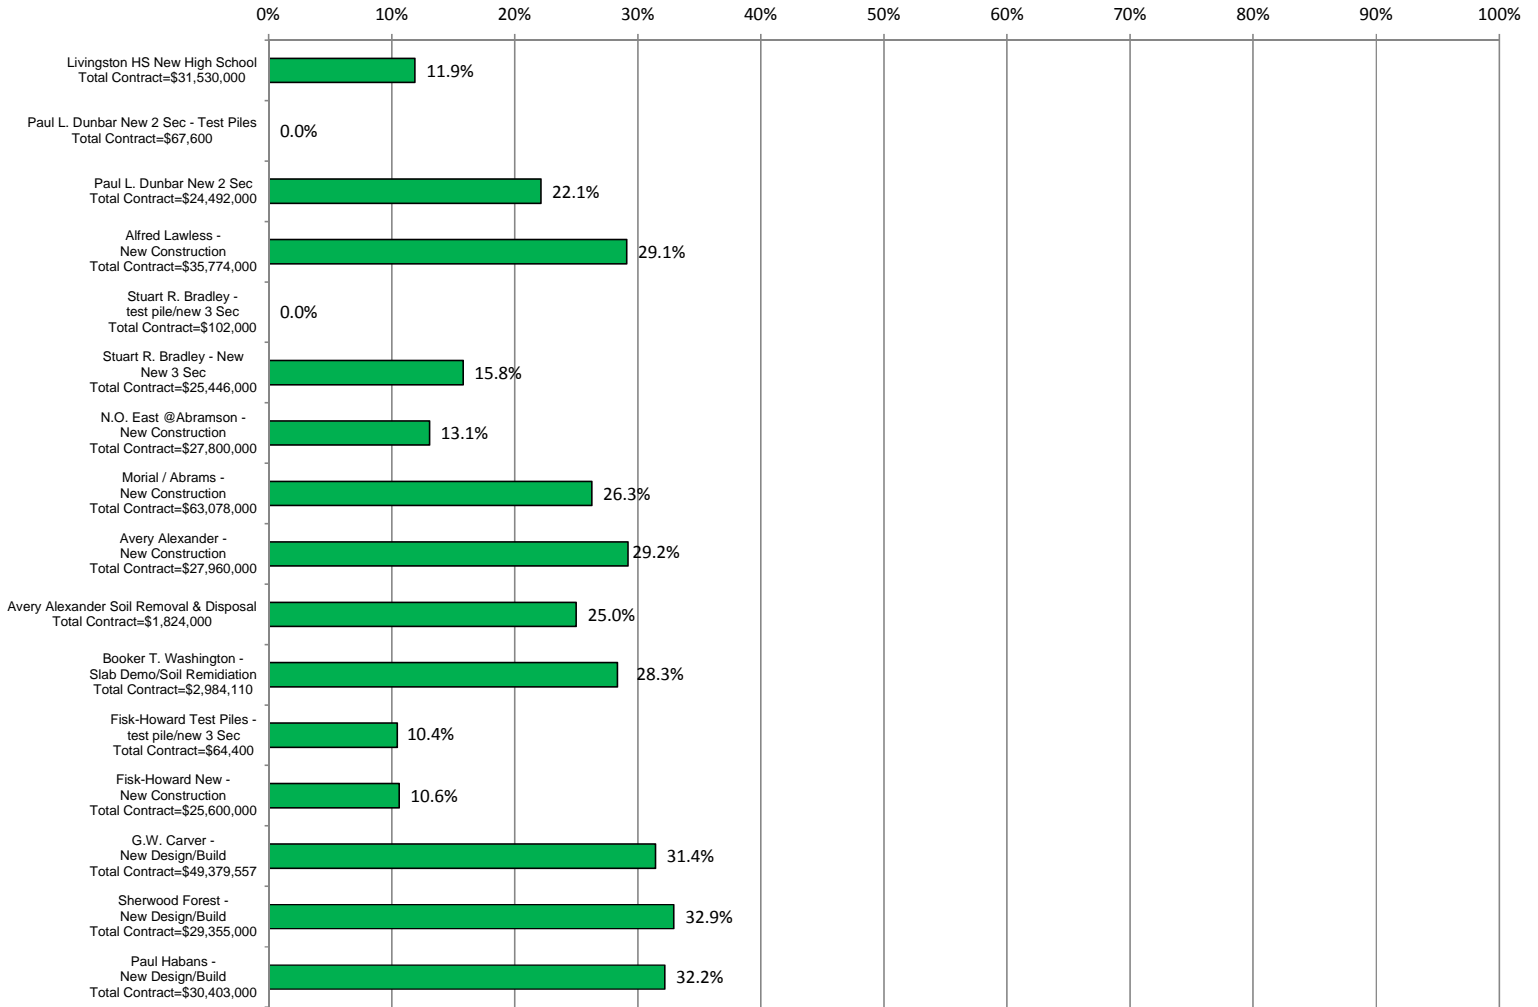

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

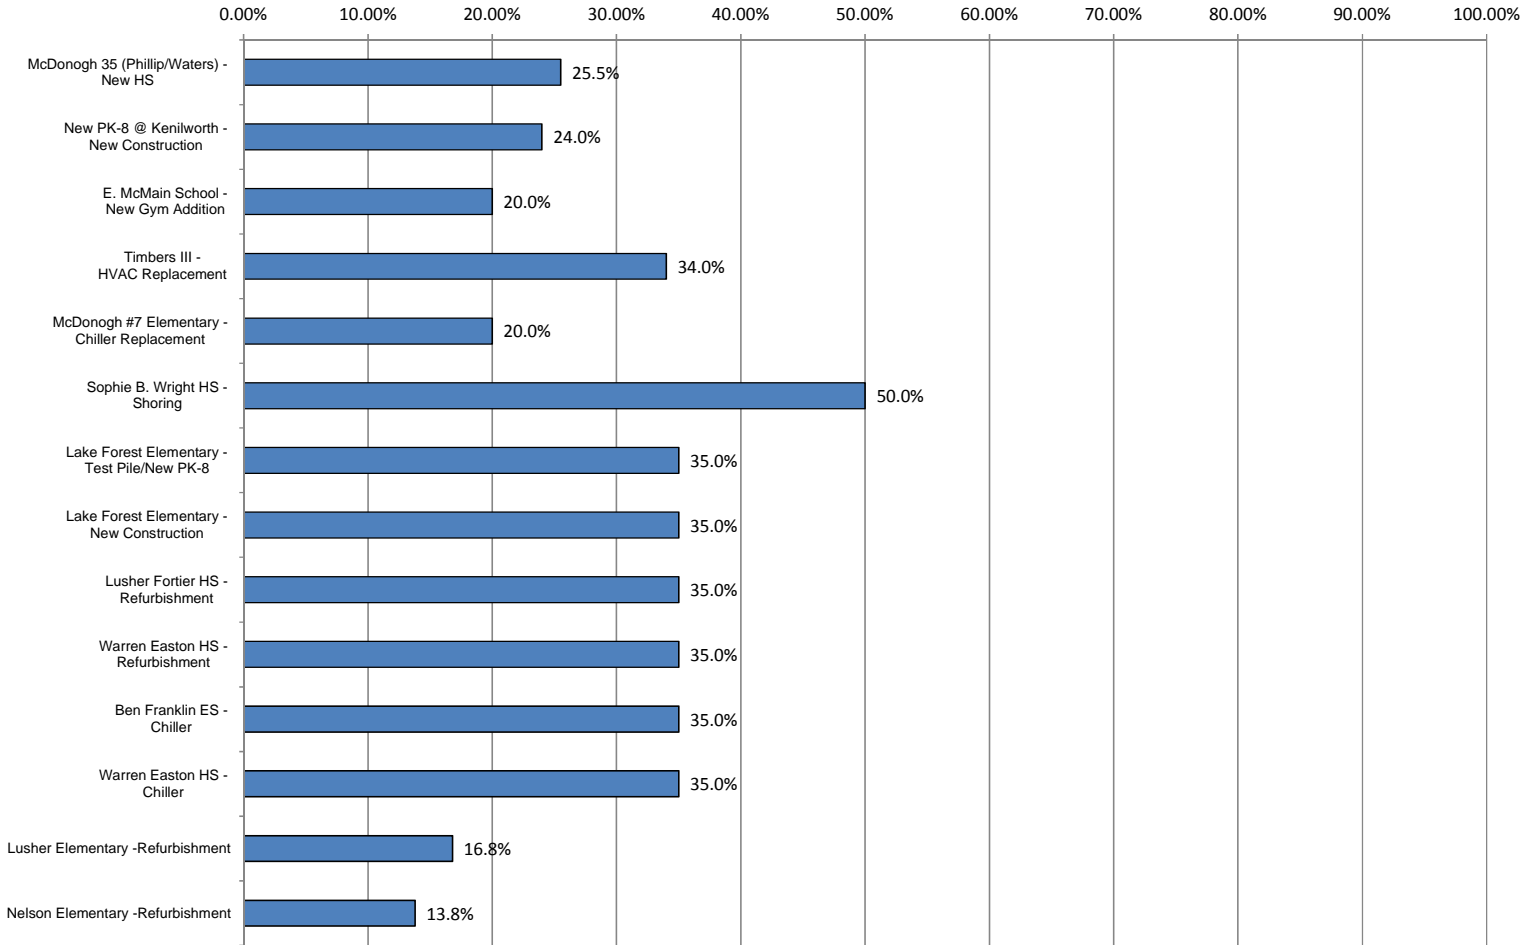

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School ^(RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Metal stud wall installation continues
- Exterior face brick installation is ongoing
- Installation of pipe and ductwork insulation continues
- Site prep and paving is ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



Avery Alexander Elementary School ^(RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- Exterior wall sheathing installation is starting
- Steel stud wall framing has started
- Overhead mechanical rough in continues
- Exterior CMU has started
- Soil removal is ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



George Washington Carver School ^(RSD)

3059 Higgins Blvd., New Orleans, LA 70126 District E Ward 9

Scope of work: New High School, Design Build

Funding Source – FEMA

Contractor – Broadmoor LLC

Construction Phase

- Farnsworth retesting is complete
- State Fire Marshal April 21st
- Swales are being adjusted to improve drainage

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- Owner has placed project on hold



Paul B. Habans School ^(RSD)

3501 Siene Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

Construction Phase

- Installation of ceilings is nearly complete
- Flooring installation is ongoing
- Millwork installation continues
- Final site grading continues
- Test and balance is scheduled for May 2016

Contractual Substantial Completion – June 2016

Forecasted Substantial Completion – June 2016



JoEllen Smith Medical Center Demolition ^(OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – Core Construction

Demolition Phase

- Demolition team to provide safety, abatement, and demolition plans
- Demolition Notice to Proceed May 9th

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – November 2016



New Karr High School CMAR (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – TBD

Contractor - TBD

Procurement Phase

- Owner has placed project on hold

Contractual Substantial Completion – November 2018

Forecasted Substantial Completion – November 2018



John McDonogh High School Renovation CMAR (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Design Phase

- Design Development Documents were received April 26th
- Project Team is working on community presentation

Contractual Substantial Completion – June 2018

Forecasted Substantial Completion – June 2018



Eleanor L. McMain School Gymnasium (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source – FEMA

Architect – Jahncke & Burns Architects

Contractor – Gibbs Construction

Construction Phase

- Architect is working on the punch list
- Installation of gymnasium flooring is complete
- Final Commissioning is ongoing

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – August 2016



Ernest "Dutch" Morial Elementary School ^(RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Metal stud installation is ongoing
- Installation of roofing has started
- Mechanical equipment installation is ongoing
- Face brick installation continues

Contractual Substantial Completion – January 2017

Forecasted Substantial Completion – January 2017



Sherwood Forest School ^(RSD)

4801 Maid Marion Drive, New Orleans, LA 70128 District E Ward 9

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

Construction Phase

- Interior finishes are nearly complete
- Media center furniture installation has started
- Site lighting is being installed
- Testing and Balance is ongoing

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – June 2016



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

Procurement Phase

- Contractor is mobilizing
- Notice to Proceed May 9th

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Project team is soliciting for test piles
- Project team continues VE exercise
- South Prieur street pricing is being reviewed

Contractual Substantial Completion – April 2018

Forecasted Substantial Completion – April 2018



Sophie B. Wright High School Renovation ^(RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Renovation of existing school and gymnasium addition

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – Core Construction

Construction Phase

- Contractor has started a punch list on 2nd and 3rd floors
- Interior finishes are nearly complete
- Auditorium seating to arrive in May
- Gymnasium flooring installation is ongoing
- Exterior site work continues

Contractual Substantial Completion – June 2016

Forecasted Substantial Completion – June 2016



REFURBISHMENTS

Benjamin Banneker Elementary School Kitchen Refurbishment ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are due in June

Procurement Phase

- Anticipated 1st Advertisement – July 2016
- Anticipated Bid Opening – August 2016



Agnes L. Bauduit Elementary School Refurbishment ^(RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor – One Construction

Procurement Phase

- Contracts we sent to LDOE
- Pre-construction conference is scheduled for May 13th



Walter L. Cohen High School Kitchen Refurbishment ^(RSD)

3520 Dryades, New Orleans Street, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Owner has placed this project on hold

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



A. D. Crossman School Kitchen Refurbishment (RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - CDW Services

Construction Phase

- Dumpster pad will be delayed due to unforeseen underground obstructions

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



Frederick A. Douglass High School Science Lab (RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovations to science lab

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – One Construction

Construction Phase

- Vent hood shroud to be installed by the beginning of May
- Add work to install sump pump will extend contract

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – May 2016



William J. Fischer Elementary School Refurbishment (RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Perez

Construction Phase

- General Contractor is mobilizing

Contractual Substantial Completion – February 2017

Forecasted Substantial Completion – February 2017



Fortier (Lusher) High School Refurbishment ^(OPSB)

5624 Freret Street, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation and repairs to the roof, masonry, plaster, windows, exterior doors, canopies, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Core Construction

Construction Phase

- Project is 99% complete
- Contractor is working on punch list
- Project is substantially complete

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



Gaudet Elementary School Refurbishment ^(RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - One Construction

Construction Phase

- Demolition of mechanical room has started
- Exterior site demolition is ongoing
- Pool demolition is complete

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – November 2016



Edgar P. Harney Elementary School Refurbishment ^(RSD)

2503 Willow Street, New Orleans, LA 70113 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Hamp's Construction, LLC

Construction Phase

- Kitchen flooring work to be finished early May
- Contractor installing side walls at cooler

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – May 2016



Andrew Jackson School Refurbishment ^(RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Construction Phase

- Notice to Proceed is anticipated for May 2nd
- Community meeting is anticipated May 16th

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



J. W. Johnson Elementary School Refurbishment ^(RSD)

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Owner has placed this project on hold

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



Lafayette Elementary School Refurbishment ^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- Owner is reviewing the bids



Laurel Elementary School Refurbishment ^(RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are due end March 3rd

Procurement Phase

- 1st Advertisement - April 6th
- 2nd Advertisement - April 13th
- 3rd Advertisement - April 20th
- Pre-Bid Conference - April 21st
- Bid Opening - May 18th



Live Oak Elementary School Refurbishment ^(RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- Window refurbishment is underway
- Exterior demolition has started
- Ceiling grid installation on third floor has started
- Dumpster pad has been poured

Contractual Substantial Completion – July 2017

Forecasted Substantial Completion – July 2017



Lusher Elementary School Refurbishment ^(OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source – FEMA

Architect – Meyer Engineers, LTD.

Contractor - Dynamic

Construction Phase

- Chiller replacement is ongoing
- Concrete masonry installation is finishing
- Elevator shaft work is ongoing

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – August 2016



Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- FEMA is reviewing the construction documents
- Bid Documents are anticipate in June

Procurement Phase

- Anticipated 1st Advertisement – September 2016
- Anticipated Bid Opening – November 2016



McDonogh #28 School Refurbishment ^(RSD)

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – SCNZ Architects, LLC

Contractor - Tuna Construction

Construction Phase

- Project is substantially complete
- Punch list work has started

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – April 2016



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- Bid documents are being reviewed by PM

Procurement Phase

- Anticipated 1st Advertisement – June 2016
- Anticipated Bid Opening – August 2016



Rosenwald Elementary School Refurbishment ^(RSD)

6501 Berkley Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - One Construction

Construction Phase

- Project is substantially complete
- Punch list work has started

Contractual Substantial Completion – February 2016

Forecasted Substantial Completion – April 2016



Village de l'Est Elementary School Refurbishment ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CBDG

Architect – Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

Construction Phase

- HVAC controls is 95% complete
- Test and Balance is ongoing
- General Contractor is working on punch list
- Substantial Completion is anticipates in May

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – May 2016



Albert Wicker School Kitchen Refurbishment ^(RSD)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Owner has placed this project on hold

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



OTHER PROJECTS

Eleanor L. McMain School Roof Replacement (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Roof replacement

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – Rycars Construction

Construction Phase

- Contractor is starting on roof punch list
- Stucco repair work is complete
- Anticipate Substantial Completion May 2016

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – May 2016



Eleanor L. McMain School Maintenance Upgrades (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work.

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group


Contractor – Tuna Construction

Construction Phase

- Flooring repairs are ongoing
- Restroom work continues
- Kitchen work will start at the end of school

Contractual Substantial Completion – June 2016

Forecasted Substantial Completion – July 2016

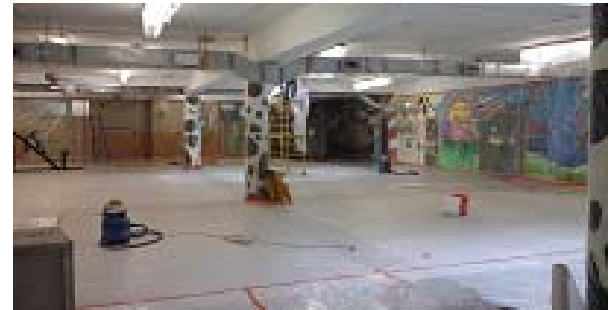

Building Automation System Integration At Recovery School

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview ES

Funding Source – FEMA

Architect – Moses Engineers

Contractor – Synergy Building Solutions, Inc.

Construction Phase

- Moses is reviewing training docs and O&M manuals

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – June 2016



MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

Demolition of Modular Buildings at Abramson and Carver ^(RSD)

5552 Read Boulevard and 3059 Higgins Boulevard, New Orleans, LA

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters, Inc.

Construction Phase

- Abramson - All limestone has been removed
- Abramson - All trailer have been removed from site
- Carver - Removal of exterior canopy and stairs has started
- Carver - Trailers are been prepped to be moved

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – September 2016



Demolition of Modular Buildings at Livingston ^(RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – Concrete Busters of Louisiana

Construction Phase

- Removal of exterior canopy and stairs has started
- Received quotes for environmental work

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – September 2016



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
6	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
7	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
8	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
9	Alfred Lawless Senior ^(RSD)	12/18/2015
10	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
11	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
12	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
13	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
14	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
15	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
16	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
17	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
18	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
19	Augustine Elementary School Roof ^(RSD)	04/13/2012
20	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
21	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
22	Bell JH Shoring ^(RSD)	06/28/2011
23	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
24	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
25	Bienville Elementary School Demolition ^(RSD)	05/04/2009
26	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
27	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
28	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
29	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
30	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
31	Charles J. Colton Elementary School ^(RSD)	05/23/2013
32	Charles R. Drew Elementary School ^(RSD)	04/17/2015
33	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
34	Cohen High School Health Clinic ^(RSD)	12/24/2008
35	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
36	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
37	Douglass High School Under Floor Utilities ^(RSD)	
38	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
39	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
40	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
41	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
42	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
43	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011

44	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
45	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
46	Edna Karr High School - Assessment ^(OPSB)	
47	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
48	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
49	New Edward Hynes School ^(OPSB)	02/06/2012
50	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
51	Edward Livingston High School ^(RSD)	01/05/2015
52	Eleanor L. McMMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
53	Eleanor L. McMMain School Clinic ^(OPSB)	07/24/2013
54	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
55	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
56	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
57	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
58	Francis W. Gregory Demolition ^(RSD)	12/21/2011
59	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
60	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
61	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
62	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
63	George Mondy Elementary School Mothball ^(RSD)	
64	George Washington Carver High School Demolition ^(RSD)	08/24/2011
65	Greater St. Stephens School ^(OPSB)	03/18/2013
66	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
67	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
68	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
69	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
70	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
71	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
72	Holy Cross Modular Relocation ^(RSD)	12/14/2010
73	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
74	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
75	James Derham Demolition ^(RSD)	02/23/2012
76	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
77	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
78	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
79	John Dibert Elementary School Roof ^(RSD)	08/20/2010
80	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
81	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
82	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
83	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
84	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
85	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
86	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
87	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
88	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
89	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011

90	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
91	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
92	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
93	Lake Area Landry Demolition ^(RSD)	05/01/2008
94	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
95	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
96	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
97	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
98	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
99	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
100	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
101	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
102	Live Oak Elementary School Roof ^(RSD)	08/04/2011
103	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
104	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
105	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
106	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
107	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
108	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
109	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
110	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
111	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
112	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
113	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
114	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
115	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
116	McDonogh #7 High School Repairs ^(OPSB)	
117	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
118	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
119	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
120	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
121	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
122	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
123	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
124	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
125	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
126	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
127	Modular Campuses Close Outs ^(RSD)	
128	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
129	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010
130	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
131	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
132	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
133	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
134	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009

135	New Carter G. Woodson School ^(RSD)	09/14/2012
136	New Fannie C. Williams School ^(RSD)	08/24/2012
137	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
138	New L.B. Landry High School ^(RSD)	06/30/2010
139	New Lake Area High School ^(RSD)	12/28/2009
140	New Lawrence D. Crocker School ^(RSD)	04/29/2013
141	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
142	New Parkview School ^(RSD)	10/12/2012
143	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
144	New William Frantz Elementary School ^(RSD)	
145	New Orleans High School Signature Center Study ^(RSD)	
146	Oretha C. Haley Demo ^(RSD)	05/07/2012
147	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
148	Parkview Elementary School Demolition ^(RSD)	08/06/2009
149	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
150	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
151	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
152	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
153	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
154	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
155	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
156	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
157	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
158	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
159	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
160	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
161	Schaumburg Chillers ^(RSD)	11/14/2008
162	Schwarz Alternative Repairs ^(RSD)	07/14/2009
163	Schwarz Alternative Modularity Demolition ^(RSD)	04/02/2015
164	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
165	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
166	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
167	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
168	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
169	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
170	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
171	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
172	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
173	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
174	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
175	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
176	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
177	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
178	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
179	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
180	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011

181	Timbers HVAC ^(OPSB)	09/11/2013
182	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
183	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
184	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
185	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
186	Valena C. Jones Elementary School ^(RSD)	01/10/2013
187	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
188	Warren Easton High School Renovation ^(OPSB)	12/15/2015
189	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
190	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
191	New William J. Guste Elementary School ^(RSD)	10/06/2008
192	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
193	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
194	William Frantz Elementary School Roof ^(RSD)	08/12/2010
