## Superintendent's Report January, 2015



**Mr. Stanley C. Smith**Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard

Recovery School District



Prepared By



### **Table of Contents**

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	4
COMMUNITY MEETINGS	5
BID OPENINGS	6
DBE OVERVIEW MONTHLY SUMMARY	7
NEW & MAJOR RENOVATION	11
Ray Abrams Elementary School (RSD)	11
Avery Alexander Elementary School (RSD)	11
James Audubon School (OPSB)	11
Stuart R. Bradley School (RSD)	12
George Washington Carver School (RSD)	12
Charles R. Drew Elementary School (RSD)	12
Paul L. Dunbar School (RSD)	13
Paul B. Habans School (RSD)	13
New PK-8 School at North Kenilworth Park at Curran Site (OPSB)	13
Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)	14
Alfred Lawless School (RSD)	14
Edward Livingston High School (RSD)	14
John McDonogh High School Selective Demolition (RSD)	15
John McDonogh High School Renovation (RSD)	15
McDonogh #35 School (Phillip/Waters Site) (OPSB)	15
McDonogh #42 Elementary School (RSD)	16
Eleanor L. McMain School Gymnasium (OPSB)	16
Ernest "Dutch" Morial Elementary School (RSD)	16
Small New Orleans East High School at Abramson (RSD)	17
Sherwood Forest School (RSD)	17
Harriet R. Tubman Elementary School Selective Demolition (RSD)	17
Harriet R. Tubman Elementary School Renovation (RSD)	18
Booker T. Washington School Environmental Remediation (RSD)	18
Booker T. Washington School (RSD)	18
Sophie B. Wright School (RSD)	19

1

REFURBISHMENTS	20
Henry Allen Elementary School Refurbishment (RSD)	20
Henry Allen Elementary School Kitchen Refurbishment (RSD)	20
Benjamin Banneker Elementary Kitchen School Refurbishment (RSD)	20
Bethune and Tureaud Elementary School Refurbishment (OPSB)	21
Agnes L. Bauduit Elementary School Refurbishment (RSD)	21
Walter L. Cohen High School Kitchen Refurbishment (RSD)	21
A. D. Crossman School Kitchen Refurbishment (RSD)	22
Frederick A. Douglass High School Science Lab (RSD)	22
Warren Easton School Refurbishment (OPSB)	22
Dwight D. Eisenhower Elementary School Refurbishment (RSD)	23
Dwight D. Eisenhower Elementary School Kitchen Refurbishment (RSD)	23
Benjamin Franklin Elementary School Renovation (OPSB)	23
William J. Fischer Elementary Refurbishment (RSD)	24
Fortier (Lusher) High School Refurbishment (OPSB)	24
Gaudet Elementary School Refurbishment (RSD)	24
Gentilly Terrace School Refurbishment (RSD)	25
Gentilly Terrace School Kitchen Refurbishment (RSD)	25
Samuel J. Green Elementary School Refurbishment (RSD)	25
Edgar P. Harney Elementary School Refurbishment (RSD)	26
Andrew Jackson School Refurbishment (RSD)	26
Andrew Jackson School Kitchen Refurbishment (RSD)	26
J. W. Johnson Elementary School Refurbishment (RSD)	27
Dr. Martin L. King Elementary School Kitchen Refurbishment (RSD)	27
Lafayette Elementary School Refurbishment (RSD)	27
Laurel Elementary School Refurbishment (RSD)	28
Live Oak Elementary School Refurbishment (RSD)	28
Lusher Elementary School Refurbishment (OPSB)	28
Thurgood Marshall Elementary School Refurbishment (RSD)	29
McDonogh #28 School Refurbishment (RSD)	29
McDonogh #28 School Kitchen Refurbishment (RSD)	29
McDonogh #32 School Refurbishment (RSD)	30
Nelson Elementary School Refurbishment (OPSB)	30
Sarah T. Reed School Refurbishment (RSD)	30
Sarah T. Reed School Kitchen Refurbishment (RSD)	31
Rosenwald Elementary School Refurbishment (RSD)	31
Henry C. Schaumburg Elementary School Refurbishment (RSD)	31
Village de l'Est Elementary School Refurbishment (RSD)	32
Albert Wicker School Kitchen Refurbishment (RSD)	32
Sylvanie F. Williams School Refurbishment (RSD)	32

2

OTHER PROJECTS	33
Eleanor L. McMain School Roof Replacement (OPSB)	33
Eleanor L. McMain School Maintenance Upgrades (OPSB)	33
Timbers III - Building Controls (OPSB)	33
Timbers III - IT Room Relocation (OPSB)	34
Building Automation System Integration At Recovery School District Central And Remote Offices (RSD)	34
MOTHBALL OR SAFE & SECURE OF SELECTED SCHOOLS	35
Andrew J. Bell Junior High School Shoring and Mothball (RSD)	35
Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School <sup>(RSD)</sup>	35
Demolition of Modular Buildings Gregory and Abramson (RSD)	35
JoEllen Smith Medical Center Demolition (OPSB)	36
Demolition of Modulars at Livingston (RSD)	36
Demolition of Modulars at Schwarz (RSD)	36
COMPLETED PROJECTS	37

3

### **Overview**

#### FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$529 million in open contracts for the capital program after issuing no new contracts and \$1.4 million in change orders and amendments in January. In addition, the total change orders to date, \$6.2 million, account for approximately one percent (1.23%) of the total open construction contracts. RSD anticipates issuing approximately \$2.1 million in construction contracts/change orders, and \$90 thousand in professional service contracts/amendments in February.



The OPSB has \$210 million in open contracts for the capital program after issuing no new contracts and \$76 thousand in change orders and amendments in January. In addition, the total change orders to date, \$3 million, account for approximately two percent (1.55%) of the total open construction contracts. OPSB anticipates issuing approximately \$103 thousand in construction contracts/change orders and \$374 thousand in professional service contracts/amendments in February.

## **Community Meetings**



Future Community Meetings
No Scheduled Community Meetings

5

### **Bid Openings**

### Bids that were opened in January, 2015

### **January 7, 2015**

• Dwight D. Eisenhower School Refurbishment

### **January 28, 2015**

McDonogh #28 School Refurbishment

### **January 29, 2015**

Henry Allen School Refurbishment

### The following projects are scheduled to bid in the next 60 days:

### **February 3, 2015**

• Ray Abrams & Ernest "Dutch" Morial Elementary Schools

### **February 4, 2015**

- Village de l'Est School Refurbishment
- Nelson Elementary School Refurbishment

### **February 10, 2015**

Andrew Jackson School Refurbishment

#### **February 11, 2015**

- Soil Remediation at Booker T. Washington High School
  - Avery Alexander Elementary School
  - Lusher Elementary School Refurbishment

#### **February 18, 2015**

• Rosenwald Elementary School Refurbishment

### **February 25, 2015**

• Selective Demolition at John McDonogh High School

#### March 4, 2015

Kitchen Improvements at Crossman & Gentilly Terrace

#### March 11, 2015

• Kitchen Improvements at Allen, Dr. Martin Luther King & Eisenhower

# Disadvantaged Business Enterprises (DBE) Monthly Summary





#### New & Renovations:

DBE Contractors secured subcontracts on 16 projects as of January 31, 2015. The DBE subcontracts value is \$44,983,289 of the \$252,253,077 total of awarded contracts.

#### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 23 projects as of January 31, 2015. The DBE subcontracts value is \$7,096,426 of the \$23,972,776 total of awarded contracts.

### **Design-Build New:**

DBE Contractors secured subcontracts on 3 projects as of January 31, 2015. The DBE subcontracts value is \$35,025,777 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$ 385,363,410

#### **Orleans Parish School Board**

#### New & Renovations:

DBE Contractors secured subcontracts on 8 projects as of January 31, 2015. The DBE subcontracts value is \$52,546,433 of the \$193,549,360 total of awarded contracts.

#### Stabilization/Demolition/Mothballing:


7

DBE Contractors secured subcontracts on 2 projects as of January 31, 2015. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$194,452,359

<sup>\*</sup> DBE provisions were included in projects bid after June 30, 2012

### **Current RSD Program DBE Participation**

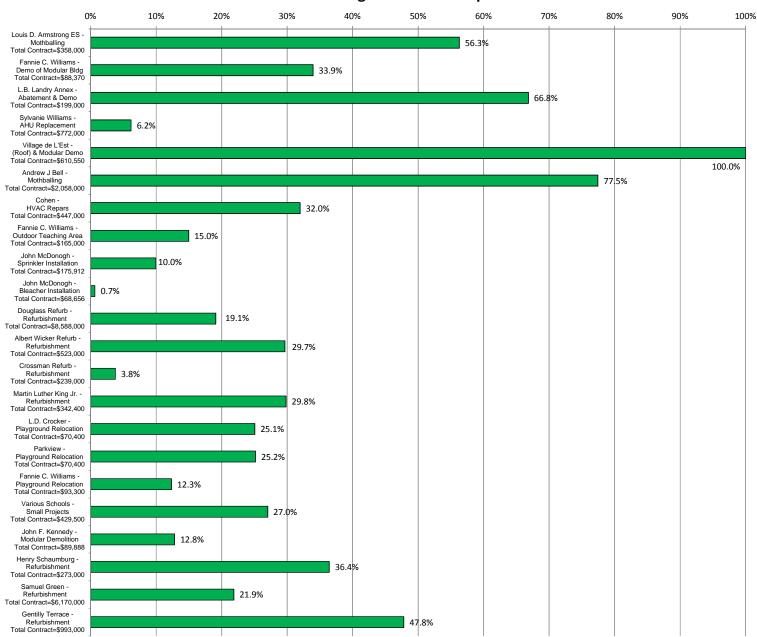


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount


8

### **Current RSD Program DBE Participation**

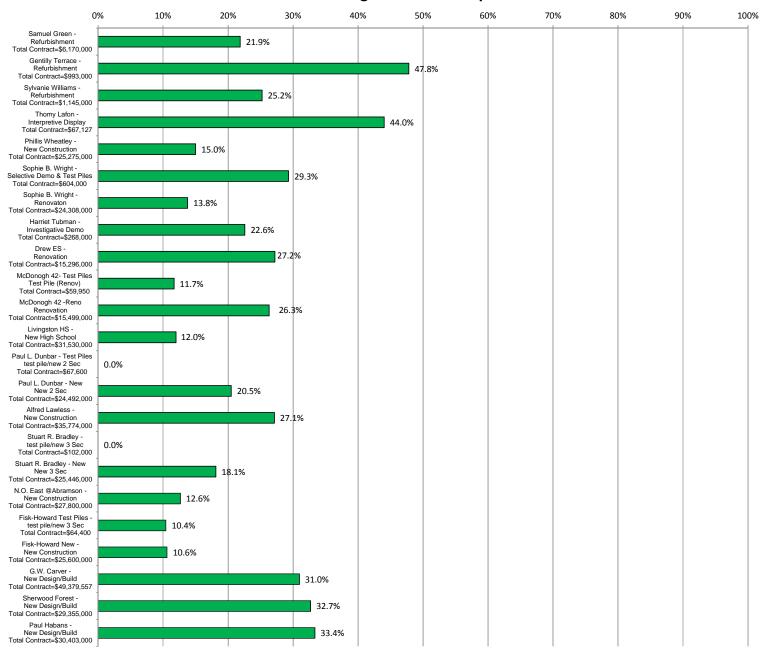

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. RSD DBE Participation Target = 25% of Total Contract Amount

### **Current OPSB Program DBE Participation**

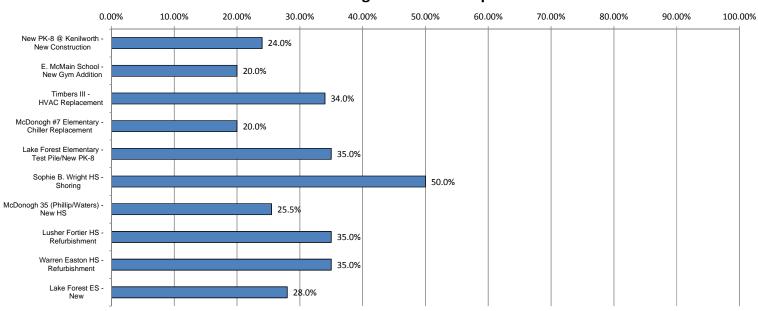

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

OPSB DBE Participation Target = 35% of Total Contract Amount

### **New & Major Renovation - Project Status**

(Forecasted dates only include the next project phase)

### Ray Abrams Elementary School (RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect - Waggonner & Ball Architects, APC

Contractor – TBD Procurement Phase

• Morial and Abrams will be packaged together as (1) project for the procurement process.

• 1st Advertisement – December 17th

• 2nd Advertisement – December 24th

• 3rd Advertisement – December 31st

• Pre-Bid Conference – January 6th

• Bid Opening – February 3rd



### Avery Alexander Elementary School (RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – TBD Procurement Phase

• 1st Advertisement – January 7th

• 2nd Advertisement – January 14th

• 3rd Advertisement – January 21st

• Pre-Bid Conference – January 23rd

• Bid Opening – February 11th



### James Audubon School (OPSB)

428 Broadway Avenue, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation of existing elementary school and new addition

Funding Source – FEMA

Architect - Blitch/Knevel Architects

Contractor – FHP Tectonics Corporation

**Construction Phase** 

• Phase two of the corrective plan is 75% complete

Installation of refurbished windows are complete

Installation of historic millwork and doors are complete

· Permanent power to be on February 26th

· Floor and ceiling tile installation has started in the existing building

Contractual Substantial Completion – September 2013

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – June 2015



## Stuart R. Bradley School (RSD)

2401 Humanity Street, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect – Sizeler Thompson Brown Architects

Contractor - Landis Construction Co.

#### **Construction Phase**

- · Window installation is ongoing
- Installation of brick and concrete masonry units is ongoing
- Installation of interior metal studs is 95% complete
- Installation of gypsum board continues
- · Roof installation is ongoing
- · Ceiling grid installation has started

Contractual Substantial Completion – April 2015 Forecasted Substantial Completion – May 2015 School Ready for Occupancy – June 2015



### George Washington Carver School (RSD)

3059 Higgins Blvd., New Orleans, LA 70126 District E Ward 9

Scope of work: New High School, Design Build

Funding Source – FEMA Contractor – Broadmoor LLC

#### **Construction Phase**

- Pouring of slabs on grade continues
- Under slab utility work continues
- · Concrete masonry unit installation has started at the convocation center
- $\bullet$  Steel erection is ongoing in areas A,D, and E

Contractual Substantial Completion – March 2016 Forecasted Substantial Completion – March 2016



### Charles R. Drew Elementary School (RSD)

3819 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Blitch / Knevel Architects, Inc.

Contractor – Core Construction

### **Construction Phase**

- Interior painting is ongoing
- Window refurbishment is nearing completion
- Tiling of restrooms continues
- Installation of ceiling grid is 90% complete
- Installation of flooring has started

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion - March 2015

School Ready for Occupancy – June 2015



### Paul L. Dunbar School (RSD)

9330 Forshey Street, New Orleans, LA 70125 District A Ward 17

Scope of work: New Pre-K - 8 School

Funding Source – FEMA

Architect – Chenevert Architects LLC Contractor – McDonnel Group, LLC

#### **Construction Phase**

- Subsurface drainage work continues
- Flooring and ceiling grid installation has started
- · Cast stone installation is ongoing
- Window installation is ongoing
- · Roof installation is ongoing

Contractual Substantial Completion – April 2015 Forecasted Substantial Completion – May 2015 School Ready for Occupancy – June 2015



### Paul B. Habans School (RSD)

3501 Siene Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: New School, Design Build

Funding Source – FEMA Architect – Grace Hebert Contractor – Core Construction

#### Construction Phase

- Pile driving is 90% complete
- Forming of piles caps has started
- Underground drainage is scheduled to start beginning of February
- Steel erection is anticipated mid April

Contractual Substantial Completion – May 2016 Forecasted Substantial Completion – May 2016



### New PK-8 School at North Kenilworth Park at Curran Site (OPSB)

8500 Curran Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New Pre-K - 8 School

Funding Source – FEMA

Architect - Mathes Brierre Architects

Contractor – Woodrow Wilson Construction Company, Inc.

#### **Construction Phase**

- · MEP work is ongoing
- · Ceramic wall tile installation is ongoing
- Gypsum board and metal stud installation is 60% complete
- Site work including sidewalks is 50% complete
- Installation of windows is nearly complete

Contractual Substantial Completion – September 2014

Forecasted Substantial Completion - June 2015

School Ready for Occupancy – July 2015



## Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)

11110 Lake Forest Boulevard 70128 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Imre Hegedus & Associates Architects

Contractor - The McDonnel Group

#### **Construction Phase**

- MEP rough-in continues
- Exterior concrete masonry is complete at classroom Building
- Masonry brick work continues
- Site work is 35% complete
- · Permanent power is anticipate mid March

Contractual Substantial Completion – July 2015 Forecasted Substantial Completion – July 2015

School Ready for Occupancy – August 2015



### Alfred Lawless School (RSD)

5300 Law Street, New Orleans, LA 70117 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

### Construction Phase

- · Installation of site utilities is ongoing
- Roof installation is 90% complete
- · Installation of stairs is ongoing
- · Exterior brick work has ongoing
- · Electric and HVAC main distribution has started

Contractual Substantial Completion – November 2015

Forecasted Substantial Completion – November 2015

School Ready for Occupancy – January 2016



## Edward Livingston High School (RSD)

7301 Dwyer Road, New Orleans, LA 70126 District E Ward 9

14

Scope of work: New High School

Funding Source - FEMA

Architect - RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

#### Close Out Phase

- Commissioning is complete
- · Substantial Completion January 5th
- · Work on the punch list is 50% complete

Contractual Substantial Completion – February 2015

Forecasted Substantial Completion - December 2014

School Ready for Occupancy – June 2015



### John McDonogh High School Selective Demolition (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect - VergesRome Architects, APAC

Contractor - TBD Procurement Phase

- 1st Advertisement January 7th
- 2nd Advertisement January 14th
- 3rd Advertisement January 21st
- Pre-Bid Conference January 22nd
- Bid Opening February 25th



## John McDonogh High School Renovation (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements Funding Source – FEMA

Architect - VergesRome Architects, APAC

Contractor - TBD Design Phase - SD

- Schematic Design Documents were received January 18th
- RFQ for CM at risk is being developed



## McDonogh #35 School (Phillip/Waters Site) (OPSB)

1200 Senate Street, New Orleans, LA 70122 District D Ward 7

Scope of work: New High School Funding Source – FEMA

Architect – Sizeler, Thompson, Brown Architects

Contractor - Citadel Builders, LLC

**Construction Phase** 

- Installation of CMU walls is complete
- Installation of MEP continues
- Brick masonry and window installation continues
- · Drywall installation continues in north and south classroom buildings
- Metal panel installation continues
- Permanent power anticipated early February

Contractual Substantial Completion - May 2015

Forecasted Substantial Completion – May 2015

School Ready for Occupancy – June 2015



### McDonogh #42 Elementary School (RSD)

1651 North Tonti Street, New Orleans, LA 70119 District A Ward 7

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source - FEMA, QSCB, NMTC, Insurance Proceeds

Architect – Eskew+Dumez+Ripple Contractor – Core Construction

#### **Construction Phase**

- · Window sash installation is 90% complete
- Ceiling tile installation continues
- Installation of VCT and terrazzo repair has started
- · Installation of millwork continues
- Sidewalks are being formed and poured

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – May 2015

School Ready for Occupancy – August 2015



## Eleanor L. McMain School Gymnasium (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source - FEMA

Architect - Jahncke & Burns Architects

Contractor – Ellis Construction

#### **Construction Phase**

- Interior & exterior masonry installation continues
- Roof decking installation is complete
- Chiller platform and steel stair installation is nearly finished
- MEP distribution lines work continues

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015



### Ernest "Dutch" Morial Elementary School (RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source - FEMA

Architect - Waggonner & Ball Architects, APC

Contractor – TBD Procurement Phase

- Morial and Abrams will be packaged together as (1) project for the procurement process.
- 1st Advertisement December 17th
- 2nd Advertisement December 24th
- 3rd Advertisement December 31st
- · Pre-Bid Conference January 6th
- · Bid Opening February 3rd



### Small New Orleans East High School at Abramson (RSD)

5552 Read Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New High School

Funding Source - FEMA

Architect - RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

#### **Construction Phase**

- Masonry installation continues
- · Installation of site utilities is ongoing
- MEP distribution lines are being installed
- Door and window installation is underway
- · Waterproofing and roof installation is nearly complete

Contractual Substantial Completion – August 2015 Forecasted Substantial Completion – August 2015 School Ready for Occupancy – November 2015



### Sherwood Forest School (RSD)

4801 Maid Marion Drive, New Orleans, LA 70128 District E Ward 9

Scope of work: New School, Design Build

Funding Source – FEMA Architect – Grace Hebert Contractor – Core Construction

#### Construction Phase

- Forming and pouring of pile caps has started
- Grade beam pours to begin mid February
- Steel erection is anticipated mid April

Contractual Substantial Completion – May 2016 Forecasted Substantial Completion – May 2016



### Harriet R. Tubman Elementary School Selective Demolition

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV Contractor - Insulation Technologies

Construction Phase

Substantial Completion - December 19th
 Contractual Substantial Completion - January 2015
 Forecasted Substantial Completion - January 2015



## Harriet R. Tubman Elementary School Renovation (RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - TBD Design Phase - DD

- · Design Development submittal was received January 22nd
- 50% Construction Documents due March 19th

#### **Procurement Phase**

- Anticipated 1st Advertisement July 2015
- Anticipated Bid Opening August 2015



## Booker T. Washington School Environmental Remediation (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The remediation of the site

Funding Source - FEMA

Architect – Hewitt-Washington & Associates

Contractor – TBD <u>Procurement Phase</u>

- 1st Advertisement January 7th
- 2nd Advertisement January 14th
- 3rd Advertisement January 21st
- Pre-Bid Conference January 22nd
- Bid Opening February 11th



### Booker T. Washington School (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source - FEMA

Architect – Hewitt-Washington & Associates

Contractor - TBD

Design Phase - CD

- Procurement will be delayed until Environmental concerns have been addressed
- · CM at-Risk RFQ is being prepared



## Sophie B. Wright High School Renovation $^{(RSD)}$

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Renovation of existing school and gymnasium addition Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – Core Construction

#### Construction Phase

- Interior demolition is 90% complete
- · Removal and refurbishment of windows is ongoing
- Pile driving for the new gymnasium will be complete mid February
- Steel to be delivered mid of February

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



### **REFURBISHMENTS**

## Henry Allen Elementary School Refurbishment (RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

**Procurement Phase** 

· Bids are being reviewed



## Henry Allen Elementary School Kitchen Refurbishment (RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source - FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### **Procurement Phase**

- 1st Advertisement February 4th
- 2nd Advertisement February 11th
- 3rd Advertisement February 18th
- Pre-Bid Conference February 19th
- · Bid Opening March 11th



## Benjamin Banneker Elementary School Kitchen Refurbishment (RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD Design Phase - CD

- 100% Construction Documents are due February 13th
- · Procurement schedule has been adjusted pending FEMA funding approval

### **Procurement Phase**

- Anticipated 1st Advertisement January 2016
- Anticipated Bid Opening March 2016



## Agnes L. Bauduit Elementary School Refurbishment (RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG

Architect - Duplantis Design Group, PC

Contractor - TBD Design Phase - CD

- · Bid Documents are due June 2015
- Procurement schedule has been adjusted pending FEMA funding approval

#### **Procurement Phase**

- Anticipated 1st Advertisement June 2015
- Anticipated Bid Opening July 2015



## Bethune and Tureaud Elementary School Refurbishment (OPSB)

4040 Eagle Street & 2021 Pauger Street, New Orleans, LA District A Ward 3 & District D Ward 7

Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - Chenevert Architects LLC

Contractor - TBD

Design Phase - SD

- Program Completion Documents are due January 30th
- Design Development Documents are due March 6th

#### Procurement Phase

- Anticipated 1st Advertisement June 2015
- Anticipated Bid Opening August 2015

### Walter L. Cohen High School Kitchen Refurbishment (RSD)

3520 Dryades, New Orleans Street, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD Design Phase - CD

- 100% Construction Documents are due March 2nd
- Procurement schedule has been adjusted pending FEMA funding approval

21

#### **Procurement Phase**

- Anticipated 1st Advertisement January 2016
- Anticipated Bid Opening March 2016



### A. D. Crossman School Kitchen Refurbishment (RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – SCNZ Architects

Contractor - TBD Procurement Phase

- 1st Advertisement January 28th
- · 2nd Advertisement February 4th
- 3rd Advertisement February 11th
- Pre-Bid Conference February 12th
- · Bid Opening March 4th



### Frederick A. Douglass High School Science Lab (RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovations to science lab

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor - TBD

### **Procurement Phase**

- 1st Advertisement January 28th
- 2nd Advertisement February 4th
- 3rd Advertisement February 11th
- Pre-Bid Conference February 12th
- · Bid Opening April 1st

## Warren Easton School (OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Refurbishment of existing high school, including but not limited to

structure, doors, masonry walls and roof

Funding Source – FEMA

Architect - Chenevert Architects LLC

Contractor - Tuna Construction

#### Construction Phase

- Work is ongoing in the classrooms
- · Restroom renovations continues
- · Ceiling work has started
- Radiator repairs are 95% complete

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



## Dwight D. Eisenhower Elementary School Refurbishment (RSD)

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Harry Baker Smith Architects II, PLLC

Contractor - CDW Construction

**Procurement Phase** 

· Contracts are being reviewed



### Dwight D. Eisenhower Elementary School Kitchen Refurbishment (R

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc.

Contractor - TBD

#### **Procurement Phase**

- 1st Advertisement February 4th
- 2nd Advertisement February 11th
- 3rd Advertisement February 18th
- Pre-Bid Conference February 19th
- Bid Opening March 11th



## Benjamin Franklin Elementary School Renovation (OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

#### Design Phase - CD

- · Schematic Design Documents are due February 18th
- 50% Construction Documents are due April 17th

#### **Procurement Phase**

- Anticipated 1st Advertisement May 2015
- Anticipated Bid Opening June 2015



## William J. Fischer Elementary School Refurbishment (RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA, CDBG

Architect - SCNZ Architects

Contractor - TBD Design Phase - CD

- 100% Construction Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

#### **Procurement Phase**

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



### Fortier (Lusher) High School Refurbishment

5624 Freret Street, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation and repairs to the roof, masonry, plaster, windows, exterior doors, canopies, mechanical systems, and electrical systems.

Funding Source - FEMA Architect - SCNZ Architects

Contractor - Core Construction

#### Construction Phase

- · Installation of mechanical ductwork is ongoing
- · Window mock-up will be complete mid March
- Plaster repair is 90% complete
- · Installation of new doors and hardware has started

Contractual Substantial Completion - March 2016

Forecasted Substantial Completion – March 2016



## Gaudet Elementary School Refurbishment (RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA Architect - SCNZ Architects

Contractor - TBD Design Phase - CD

- 100% Construction Documents were received January 29th
- · Procurement schedule has been adjusted pending FEMA funding approval

#### **Procurement Phase**

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



### Gentilly Terrace School Refurbishment (RSD)

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Byron J. Stewart & Associates, APC Architects & Planners

Contractor - One Construction

**Construction Phase** 

- Floor demolition is 80% complete
- · Kitchen renovations are ongoing
- · Roofing repair is ongoing

Contractual Substantial Completion – May 2015 Forecasted Substantial Completion – May 2015



## Gentilly Terrace School Kitchen Refurbishment (RSD)

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – SCNZ Architects

Contractor - TBD Procurement Phase

- 1st Advertisement January 28th
- 2nd Advertisement February 4th
- 3rd Advertisement February 11th
- Pre-Bid Conference February 12th
- Bid Opening March 4th



## Samuel J. Green Elementary School Refurbishment (RSD)

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC Contractor - Hernandez Consulting, LLC

#### **Construction Phase**

- Installation of gypsum board at restrooms continues
- · Rough in of fire suppression is ongoing
- · Electrical and plumbing renovations is ongoing
- · Stripping and staining of wood floors has started
- · Exterior brick repairs has begun

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015



## Edgar P. Harney Elementary School Refurbishment (RSD)

2503 Willow Street, New Orleans, LA 70113 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect – VergesRome Architects, APAC Contractor - Hamp's Construction, LLC

**Procurement Phase** 

- · Contracts are being reviewed
- · Anticipated Notice to Proceed February 18th



### Andrew Jackson School Refurbishment (RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

#### **Procurement Phase**

- 1st Advertisement December 24th
- 2nd Advertisement December 31st
- 3rd Advertisement January 7th
- Pre-Bid Conference January 8th
- · Bid Opening February 10th



### Andrew Jackson School Kitchen Refurbishment (RSI

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD Design Phase - CD

- 100% Construction Documents are due March 2nd
- · Procurement schedule has been adjusted pending FEMA funding approval

### **Procurement Phase**

- Anticipated 1st Advertisement January 2016
- Anticipated Bid Opening March 2016



### J. W. Johnson Elementary School Refurbishment (RSD)

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD Design Phase - CD

- 100% Construction Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

#### **Procurement Phase**

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



## Dr. Martin L. King Elementary School Kitchen Refurbishment (RSD)

1617 Caffin Avenue, New Orleans, LA 70117 District E Ward 9

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect - N-Y Associates, Inc.

Contractor - TBD Procurement Phase

- 1st Advertisement February 4th
- 2nd Advertisement February 11th
- 3rd Advertisement February 18th
- Pre-Bid Conference February 19th
- Bid Opening March 11th



### Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
  - · Anticipated 1st Advertisement March 2014
  - Anticipated Bid Opening April 2015



### Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect - Mahlum Scairono Martinez JV

Contractor - TBD Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
  - Anticipated 1st Advertisement June 2015
  - Anticipated Bid Opening July 2015



### Live Oak Elementary School Refurbishment (RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
  - Anticipated 1st Advertisement April 2015
  - Anticipated Bid Opening May 2015



## Lusher Elementary School Refurbishment (OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows,

exterior doors, and restroom accessibility

Funding Source – FEMA

Architect - Meyer Engineers, LTD.

Contractor - TBD

#### **Procurement Phase**

- 1st Advertisement December 17th
- 2nd Advertisement December 24th
- 3rd Advertisement December 31st
- Pre-Bid Conference January 5th
- Bid Opening February 11th



## Thurgood Marshall Elementary School Refurbishment (RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - TBD Design Phase - SD

• Schematic Design Documents are due February 13th

#### **Procurement Phase**

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



### McDonogh #28 School Refurbishment (RSD)

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects, LLC

Contractor - Tuna Construction

**Procurement Phase** 

Bids are being reviewed



## McDonogh #28 School Kitchen Refurbishment (RSD)

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD Design Phase - CD

- 100% Construction Documents are due February 13th
- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
  - Anticipated 1st Advertisement January 2016
  - Anticipated Bid Opening March 2016



### McDonogh #32 School Refurbishment (RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase - CD

- · Bid Documents are due August 18th
- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
  - Anticipated 1st Advertisement September 2015
  - Anticipated Bid Opening October 2015



### Nelson Elementary School Refurbishment (OPSB)

3121 St. Bernard Avenue, New Orleans, LA 70119 District D Ward 7

Scope of work: Renovation and repairs to the roof, masonry, windows, exterior doors, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect - Harry Baker Smith Architects

Contractor - TBD

#### **Procurement Phase**

- 1st Advertisement December 31st
- 2nd Advertisement January 7th
- 3rd Advertisement January 14th
- Pre-Bid Conference January 15th
- Bid Opening February 4th



### Sarah T. Reed School Refurbishment (RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - Byron J. Stewart & Associates, APC Architects & Planners

Contractor - Tuna Construction

#### **Procurement Phase**

- Contracts are being reviewed and signed
- Anticipated Notice to Proceed March 2nd



### Sarah T. Reed School Kitchen Refurbishment (RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc.

Contractor - TBD Procurement Phase

1st Advertisement – February 4th

• 2nd Advertisement – February 11th

• 3rd Advertisement – February 18th

• Pre-Bid Conference – February 19th

· Bid Opening - March 11th



## Rosenwald Elementary School Refurbishment (RSD)

6501 Berkley Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase - CD

• 100% Construction Documents were received December 12th

#### **Procurement Phase**

- 1st Advertisement January 13th
- · 2nd Advertisement January 20th
- 3rd Advertisement January 27th
- Pre-Bid Conference January 29th
- · Bid Opening February 18th



## Henry C. Schaumburg Elementary School (RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - N-Y Associates, Inc

Contractor - Hernandez Consulting, LLC

#### Construction Phase

- Kitchen floor drain installation is complete
- · Electrical work is complete
- Installation of grease trap has started
- Sidewalk and dumpster pad work is ongoing

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



## Village de l'Est Elementary School Refurbishment (RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CBDG

Architect - Duplantis Design Group, PC

Contractor - TBD Procurement Phase

- 1st Advertisement December 31st
- 2nd Advertisement January 7th
- 3rd Advertisement January 14th
- Pre-Bid Conference January 15th
- Bid Opening February 4th



### Albert Wicker School Kitchen Refurbishment (RSD)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – SCNZ Architects Contractor - TBD

Contractor - TBD Design Phase - CD

- 100% Construction Documents are due February 13th
- Procurement schedule has been adjusted pending FEMA funding approval

### **Procurement Phase**

- Anticipated 1st Advertisement January 2016
- Anticipated Bid Opening March 2016



## Sylvanie F. Williams School Refurbishment (RSD)

3127 Martin Luther King Jr. Boulevard, New Orleans, LA 70125 District B Ward 2 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - N-Y Associates, Inc.

Contractor - Hamps

#### **Construction Phase**

- Abatement of window caulk for the 3rd floor will happen over Mardi Gras
- Plumbing work is ongoing
- Stucco repairs continues

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015



#### **OTHER PROJECTS**

## Eleanor L. McMain School Roof Replacement (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Roof replacement

Funding Source - General Fund & Harrah's

Architect - Duplantis Design Group

Contractor – TBD Design Phase - SD

- Schematic Design Documents were received January 9th
- Design Development Documents are due February 2nd
- 50% Construction Documents are due March 9th

#### Procurement Phase

- Anticipated 1st Advertisement May 2015
- Anticipated Bid Opening June 2015

### Eleanor L. McMain School Maintenance Upgrades (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work. Funding Source – General Fund & Harrah's Architect – Duplantis Design Group

 $Contractor-\mathsf{TBD}$ 

### Design Phase - SD

- · Schematic Design Documents were received January 9th
- Design Development Documents are due February 2nd
- 50% Construction Documents are due March 9th

#### **Procurement Phase**

- Anticipated 1st Advertisement May 2015
- Anticipated Bid Opening June 2015

## Timbers III - Building Controls (OPSB)

3520 General DeGaulle Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: Design and installation of new building controls

Funding Source - OPSB General Fund


Architect – N-Y Associates, Inc.

Contractor - TBD Design Phase - PC

· Owner has placed project on hold

#### Procurement Phase

- Anticipated 1st Advertisement TBD
- Anticipated Bid Opening TBD

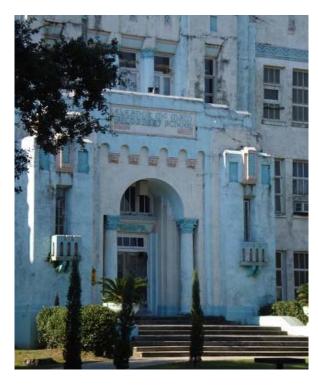



### Timbers III - IT Room Relocation (OPSB)

3520 General DeGaulle Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: Relocation of the Information Technology Room


Funding Source – OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - Huda, LLC Construction Phase

- Anticipated Substantial Completion Mid February
- · Contractor is waiting on equipment

Contractual Substantial Completion – February 2015 Forecasted Substantial Completion – February 2015



### **Building Automation System Integration At Recovery School**

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview ES

Funding Source - FEMA

Architect – Moses Engineers

Contractor – Synergy Building Solutions, Inc.

#### **Construction Phase**

- The five Quick Start Schools are complete, the Energy Dash Board is being implemented
- Sylvanie Williams Elementary School, Sarah T. Reed Elementary School, Fannie C. Williams Elementary School, Bienville Elementary School, Charles L. Colton Elementary School, William Frantz Elementary School, Parkview Elementary School, Osborne Elementary School, Carter G.
   Woodson Elementary School, Walter Cohen High School, Dolores T Aaron Elementary School, A. D. Crossman Elementary School, and Albert Wicker Elementary School are complete
- New integration work is ongoing at Benjamin Banneker Elementary School

34

• Integration has started at Lawrence D. Crocker Elementary School

Contractual Substantial Completion – January 2015

Forecasted Substantial Completion - January 2015



# MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

### Andrew J. Bell Junior High School Mothball (RSD)

1010 N. Galvez St., New Orleans, LA 70119 District D Ward 6

Scope of work: Design Services to assist in determining the condition of the facilities both interior and exterior, make recommendations to stabilize the facilities and provide drawings required to provide a water barrier, ventilation, and rudimentary fire detection and to secure openings and entryways. Construction Services to stabilize the facility according to the designer's drawings and specifications.

Funding Source – FEMA Architect – VergesRome Architects, APAC Contractor – CDW Services, LLC Mothballing of Closed Schools - Safe & Secure

 Mothballing of the Gymnasium, Administration Building, Annex, Building "C", Building "D", Chapel, & E.A.Christy Building

#### **Construction Phase**

 Structural roof repairs on the Christy building will extend the project timeline Contractual Substantial Completion – March 2015
 Forecasted Substantial Completion – April 2015



### Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School (RSD)

1010 N. Galvez St. & 2327 St. Philip Street, New Orleans, LA 70119 District D Ward 6

Scope of work: Demolition of existing caretakers cottages

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor – Concrete Busters

#### **Procurement Phase**

- Contracts are being reviewed and signed
- Anticipated Notice to Proceed February 19th



## Demolition of Modular Buildings at Gregory and Abramson (RSD)

1700 Pratt Drive & 5552 Read Boulevard, New Orleans, LA District D Ward 7 & District E Ward 9

Scope of work: Demolition of existing modular buildings

Funding Source - FEMA

Architect – Holly & Smith Architects

Contractor – Ashley Savarino Unlimited Construction

#### **Procurement Phase**

- Contracts are being reviewed and signed
- · Anticipated Notice to Proceed January 23rd



## JoEllen Smith Medical Center Demolition (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center

Funding Source – FEMA

Architect - VergesRome Architects, APAC

Contractor – TBD Design Phase - CD

· School Board is reviewing the increase in the AFC

#### **Procurement Phase**

- Anticipated 1st Advertisement TBD
- Anticipated Bid Opening TBD



## Demolition of Modular Buildings at Livingston (RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect - GAEA Consultants, LLC

Contractor – TBD

### <u>Procurement Phase</u>

- 1st Advertisement May 27th
- 2nd Advertisement June 3rd
- 3rd Advertisement June 10th
- Pre-Bid Conference June 11th
- Bid Opening July 1st



## Demolition of Modular Buildings at Schwarz (RSD)

709 Park Boulevard, New Orleans, LA District E Ward 9

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect - GAEA Consultants, LLC

Contractor – Concrete Busters

#### **Procurement Phase**

- · Contracts are being Reviewed
- Anticipated Notice to Proceed February 18th



### **Comprehensive List - Completed Projects**

- 1 Abrams | Morial | Abramson | Coghill Demolition (RSD)
- 2 A. D. Cross Elementary School Energy Conservation (RSD)
- 3 A. D. Crossman Elementary School and Benjamin Banneker Elementary School (RSD)
- 4 A. D. Crossman Elementary School Refurbishment (RSD)
- 5 A. P. Tureaud Elementary School Roof Repairs (RSD)
- 6 Agnes Bauduit Elementary School Boiler (RSD)
- 7 Albert Wicker Elementary School Refurbishment (RSD)
- 8 Albert Wicker Elementary School Roof Repairs (RSD)
- 9 Alfred Lawless Senior High Security Fencing (RSD)
- 10 Alice M. Harte Elementary School (OPSB)
- 11 Alice M. Harte Elementary School Demolition (OPSB)
- 12 Andrew J. Bell Junior High School Roof Replacement (RSD)
- 13 Andrew Jackson Elementary School Roof Repairs (RSD)
- 14 Andrew Jackson Elementary School Solar Panels (RSD)
- 15 Andrew H. Wilson Elementary School Cottage (RSD)
- 16 Arthur Ashe Elementary School Kitchen Renovation (OPSB)
- 17 Augustine Elementary School Roof (RSD)
- 18 Avery-Alexander Elementary School Demolition (RSD)
- 19 Barbara C. Jordan Elementary School Demolition (RSD)
- 20 Bell JH Shoring (RSD)
- 21 Benjamin Banneker Elementary School Energy Conservation (RSD)
- 22 Benjamin Franklin Senior High School (OPSB)
- 23 Bienville Elementary School Demolition (RSD)
- 24 Booker T. Washington High School Partial Demolition (RSD)
- 25 Carter G. Woodson Middle School Demolition (RSD)
- 26 Central Services Warehouse Demolition (OPSB)
- 27 Charles J. Colton Elementary Selective Demolition (RSD)
- 28 Charles J. Colton Elementary School (RSD)
- 29 Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)
- 30 Cohen High School Health Clinic (RSD)
- 31 Douglass High School Under Floor Utilities (RSD)
- 32 Dr. Martin Luther King School Roof Repairs (RSD)
- 33 Dr. Martin Luther King Jr. School Renovation (RSD)
- 34 Dwight D. Eisenhower Elementary School Roof Repairs (RSD)
- 35 East Bank Swing Space for Audubon Charter School (OPSB)
- 36 Edgar P. Harney Elementary School Roof Repairs (RSD)
- 37 Edna Karr High School Gymnasium Repair (OPSB)
- 38 Edna Karr High School Assessment (OPSB)
- 39 Edward Livingston Middle School Demolition (RSD)
- 40 Edward Henry Phillips Junior High School Demolition (OPSB)
- 41 New Edward Hynes School (OPSB)
- 42 Edwards | Hardin | Lockett | Lawless Demolition (RSD)

- 43 Eleanor L. McMain School Replacement of Existing Chillers (OPSB)
- 44 Eleanor L. McMain School Clinic (OPSB)
- 45 Ernest N. Morial Elementary Security Fencing (RSD)
- 46 Fannie C. Williams Elementary School Demolition (RSD)
- 47 Fisk-Howard Elementary School Demolition (RSD)
- 48 Florence J. Chester Elementary School Demolition (RSD)
- 49 Francis W. Gregory Demolition (RSD)
- 50 Frederick A. Douglass High Refurbishment (RSD)
- 51 Frederick A. Douglass High Switchgear (RSD)
- 52 Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)
- 53 George Mondy Elementary School Mothball (RSD)
- 54 George Washington Carver High School Demolition (RSD)
- 55 Greater St. Stephens School (OPSB)
- 56 Henry Allen Elementary School Roof (RSD)
- 57 Henry C. Schaumburg Window/Door, Air Condition, Water Fountain/Sink Installation (RSD)
- 58 Holy Cross Modular Relocation (RSD)
- 59 Israel M. Augustine Middle School Roof Replacement (RSD)
- 60 Israel M. Augustine Middle School Mothball (RSD)
- 61 James Derham Demolition (RSD)
- 62 James W. Johnson Elementary School Roof (RSD)
- 63 New Jean Batiste de Bienville School (RSD)
- 64 Jean Gordon Elementary School Demolition (RSD)
- **John Dibert Elementary School Roof** (RSD)
- 66 John W. Hoffman Elementary School Demolition (RSD)
- 67 John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)
- 68 John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)
- 69 John F. Kennedy Modular Demolition (RSD)
- 70 John F. Kennedy High School Demolition (RSD)
- 71 John McDonogh Senior High School Bleachers and Sprinklers (RSD)
- 72 John McDonogh Senior High School Roof (RSD)
- 73 John A. Shaw Elementary School Mothball (RSD)
- 74 Joseph S. Clark Senior High School Roof Repairs (RSD)
- 75 Joseph A. Craig Elementary Canopies (RSD)
- 76 Joseph A. Craig Elementary Elevator Installation (RSD)
- 77 Joseph A. Hardin Elementary Security Fencing (RSD)
- 78 Lafayette Elementary School Roof and Masonry (RSD)
- 79 Lake Area | Landry Demolition (RSD)
- 80 Langston Hughes Elementary School (Phase I) (RSD)
- 81 Langston Hughes Elementary School New Gymnasium (Phase II) (RSD)
- 82 Langston Hughes Elementary School Dumpster Pad (RSD)
- 83 Lawrence D. Crocker Elementary School Demolition (RSD)
- 84 L.B. Landry Annex Demolition (RSD)
- 85 Little Woods Elementary School Demolition (RSD)
- 86 Little Woods School (Dolores T. Aaron Elementary School) (RSD)
- 87 Live Oak Elementary School Roof (RSD)

- 88 Live Oak Elementary School Exterior Door Replacement (RSD)
- 89 Lorraine Hansberry Elementary School Mothball (RSD)
- 90 Louis D. Armstrong Elementary School (RSD)
- 91 Mahalia Jackson Elementary School (OPSB)
- 92 Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)
- 93 Mahalia Jackson Elementary School Office Renovation (OPSB)
- 94 Martin Behrman Elementary School Roof (RSD)
- 95 Martin Luther King Jr. Elementary Canopy System (RSD)
- 96 Martin Luther King Jr. School Modular Building, Deck, Canopy (RSD)
- 97 Mary Church Terrell Elementary School Demolition (RSD)
- 98 Mary M. Bethune Elementary 1st Floor Replacement (OPSB)
- 99 Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)
- 100 McDonogh #7 High School Repairs (OPSB)
- 101 McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)
- 102 McDonogh #28 Elementary School Roof (RSD)
- 103 McDonogh #32 Roof Replacement (RSD)
- 104 McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium (OPSB)
- 105 McDonogh #42 Elementary School Roof (RSD)
- 106 McDonogh #42 Elementary School HVAC Replacement (RSD)
- 107 Mildred C. Osborne Elementary School Demolition (RSD)
- 108 Mildred C. Osborne Elementary School (RSD)
- 109 Modular Campuses Close Outs (RSD)
- 110 Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)
- 111 Modular Structures at Langston Hughes Elementary School (RSD)
- 112 Morris F.X. Jeff Elementary School Demolition (RSD)
- 113 Morris F.X. Jeff Elementary School Mothball (RSD)
- 114 Murray G. Henderson Elementary School Roof (RSD)
- 115 New Andrew H. Wilson Elementary School (RSD)
- 116 New Carter G. Woodson School (RSD)
- 117 New Fannie C. Williams School (RSD)
- 118 New Joseph A. Craig Elementary School (RSD)
- 119 New L.B. Landry High School (RSD)
- 120 New Lake Area High School (RSD)
- 121 New Lawrence D. Crocker School (RSD)
- 122 New Parkview School (RSD)
- 123 New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD)
- 124 New William Frantz Elementary School (RSD)
- 125 New Orleans High School Signature Center Study (RSD)
- 126 Oretha C. Haley Demo (RSD)
- 127 Oretha C. Haley Elementary School Mothball (RSD)
- 128 Parkview Elementary School Demolition (RSD)
- 129 Paul L. Dunbar Elementary School Demolition (RSD)
- 130 Paul B. Habans Elementary School Roof Repairs (RSD)
- 131 Phillis Wheatley Elementary School Demolition (RSD)

- 132 Phillis Wheatley Elementary School (RSD)
- 133 Robert M. Lusher Elementary Roof Removal & Replacement (OPSB)
- 134 Sarah T. Reed High School Bleachers (RSD)
- 135 Sarah T. Reed High School Auditorium Wall (RSD)
- 136 Seabrook Computer Training Center Demolition (OPSB)
- 137 Schaumburg Chillers (RSD)
- 138 Schwarz Alternative Repairs (RSD)
- 139 Schwarz Alternative Modulars Demolition (RSD)
- 140 Sherwood Forest Elementary School Demolition (RSD)
- 141 Sophie B. Wright School Selective Demolition (RSD)
- 142 Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)
- 143 Stuart R. Bradley Elementary School Demolition (RSD)
- 144 Sylvanie Williams Elementary School AHU Replacement (RSD)
- 145 Sylvanie Williams Elementary School Play Yard (RSD)
- 146 Sylvanie Williams Elementary School Roof Repairs (RSD)
- 147 Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)
- 148 Temporary Campus for McDonogh #11 Expropriation (OPSB)
- 149 Thomas A. Edison Elementary School Demolition (RSD)
- 150 Thomy Lafon Elementary School Demolition (RSD)
- 151 Thomy Lafon School Interpretative Display (RSD)
- 152 Timbers Park Office Building #1 & #2 Demolition (OPSB)
- 153 Timbers HVAC (OPSB)
- 154 Village de L'est Elementary School Subsidence (RSD)
- 155 Village de L'est Elementary School Roof and Modular Demolition (RSD)
- 156 Vorice J. Waters Elementary School Demolition (RSD)
- 157 Valena C. Jones Elementary School (RSD)
- 158 Walter L. Cohen High School HVAC (RSD)
- 159 Warren Easton High School Window Replacement (OPSB)
- 160 West Bank Swing Space for Alice Harte Elementary School (OPSB)
- 161 New William J. Guste Elementary School (RSD)
- 162 William J. Guste Elementary School Science Lab (RSD)
- 163 William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)

40

- 164 William Frantz Elementary School (RSD)
- 165 William Frantz Elementary School Roof (RSD)
