Superintendent's Report June, 2015



Dr. Henderson Lewis Jr.Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District



Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	4
COMMUNITY MEETINGS	5
BID OPENINGS	6
DBE OVERVIEW MONTHLY SUMMARY	7
NEW & MAJOR RENOVATION	13
Ray Abrams Elementary School (RSD)	13
Avery Alexander Elementary School (RSD)	13
James Audubon School (OPSB)	13
Stuart R. Bradley School (RSD)	14
George Washington Carver School (RSD)	14
Paul L. Dunbar School (RSD)	14
Benjamin Franklin Elementary School Renovation (OPSB)	15
Paul B. Habans School (RSD)	15
New Karr High School, CMAR (OPSB)	15
New PK-8 School at North Kenilworth Park at Curran Site (OPSB)	16
Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)	16
Alfred Lawless School (RSD)	16
John McDonogh High School Selective Demolition (RSD)	17
John McDonogh High School Renovation (RSD)	17
McDonogh #35 School (Phillip/Waters Site) (OPSB)	17
McDonogh #42 Elementary School (RSD)	18
Eleanor L. McMain School Gymnasium (OPSB)	18
Ernest "Dutch" Morial Elementary School (RSD)	18
Small New Orleans East High School at Abramson (RSD)	19
Sherwood Forest School (RSD)	19
Harriet R. Tubman Elementary School Renovation (RSD)	19
Booker T. Washington School Environmental Remediation (RSD)	20
Booker T. Washington School (RSD)	20
Sophie B. Wright School (RSD)	20

REFURBISHMENTS	21
Henry Allen Elementary School Refurbishment (RSD)	21
Henry Allen Elementary School Kitchen Refurbishment (RSD)	21
Benjamin Banneker Elementary Kitchen School Refurbishment (RSD)	21
Agnes L. Bauduit Elementary School Refurbishment (RSD)	22
Bethune and Tureaud Elementary School Refurbishment (OPSB)	22
Walter L. Cohen High School Kitchen Refurbishment (RSD)	22
A. D. Crossman School Kitchen Refurbishment (RSD)	23
Frederick A. Douglass High School Science Lab (RSD)	23
Warren Easton School Refurbishment (OPSB)	23
Dwight D. Eisenhower Elementary School Refurbishment (RSD)	24
Dwight D. Eisenhower Elementary School Kitchen Refurbishment (RSD)	24
William J. Fischer Elementary Refurbishment (RSD)	24
Fortier (Lusher) High School Refurbishment (OPSB)	25
Gaudet Elementary School Refurbishment (RSD)	25
Gentilly Terrace School Refurbishment (RSD)	25
Samuel J. Green Elementary School Refurbishment (RSD)	26
Edgar P. Harney Elementary School Refurbishment (RSD)	26
Andrew Jackson School Refurbishment (RSD)	26
J. W. Johnson Elementary School Refurbishment (RSD)	27
Dr. Martin L. King Elementary School Kitchen Refurbishment (RSD)	27
Lafayette Elementary School Refurbishment (RSD)	27
Laurel Elementary School Refurbishment (RSD)	28
Live Oak Elementary School Refurbishment (RSD)	28
Lusher Elementary School Refurbishment (OPSB)	28
Thurgood Marshall Elementary School Refurbishment (RSD)	29
McDonogh #28 School Refurbishment (RSD)	29
McDonogh #32 School Refurbishment (RSD)	29
Nelson Elementary School Refurbishment (OPSB)	30
Sarah T. Reed School Refurbishment (RSD)	30
Sarah T. Reed School Kitchen Refurbishment (RSD)	30
Rosenwald Elementary School Refurbishment (RSD)	31
Henry C. Schaumburg Elementary School Refurbishment (RSD)	31
Village de l'Est Elementary School Refurbishment (RSD)	31
Albert Wicker School Kitchen Refurbishment (RSD)	32
Sylvanie F. Williams School Refurbishment (RSD)	32

OTHER PROJECTS	33
Eleanor L. McMain School Roof Replacement (OPSB)	33
Eleanor L. McMain School Maintenance Upgrades (OPSB)	33
Timbers III - Building Controls (OPSB)	33
Building Automation System Integration At Recovery School District Central And Remote Offices (RSD)	34
MOTHBALL OR SAFE & SECURE OF SELECTED SCHOOLS	35
Demolition of Modular Buildings Gregory and Abramson (RSD)	35
Demolition of Modulars at Livingston (RSD)	35
COMPLETED PROJECTS	36

3

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$591 million in open contracts for the capital program after issuing \$642 thousand in new contracts and \$1.6 million in change orders and amendments in July. In addition, the total change orders to date, \$6 million, account for approximately one percent (1.15%) of the total open construction contracts. RSD anticipates issuing approximately \$4 million in construction contracts/change orders, and \$1 million in professional service contracts/amendments in July.



The OPSB has \$217 million in open contracts for the capital program after issuing no new contracts and \$285 thousand in change orders and amendments in June. In addition, the total change orders to date, \$3.6 million, account for approximately two percent (1.93%) of the total open construction contracts. OPSB anticipates issuing approximately no construction contracts/change orders and \$1.6 million in professional service contracts/amendments in July.

Community Meetings



Future Community Meetings

August 18, 2015

Ribbon Cutting for Charles R. Drew Elementary School 3819 St. Claude Avenue New Orleans, LA 70117

August 19, 2015

Ribbon Cutting for McDonogh 42 Elementary School 1651 North Tonti Street New Orleans, LA 70119

August 25, 2015

Ribbon Cutting for Stuart R. Bradley Elementary School 2401 Humanity Street New Orleans, LA 70122

August 26, 2015

Ribbon Cutting for New 2 Section Elementary School @ Paul L Dunbar School 9330 Forshey Street New Orleans, LA 70118

August 27, 2015

Ribbon Cutting for Edward R. Livingston School 7301 Dwyer Road New Orleans, LA 70126

5

Bid Openings

Bids that were opened in June, 2015

June 10, 2015

• McMain High School New Roof

The following projects are scheduled to bid in the next 60 days:

July 8, 2015

• McMain High School Maintenance Upgrades

July 29, 2015

• Laurel School Refurbishment

6

Disadvantaged Business Enterprises (DBE) Monthly Summary





New & Renovations:

DBE Contractors secured subcontracts on 20 projects as of June 30, 2015. The DBE subcontracts value is \$70,890,524 of the \$346,275,187 total of awarded contracts.

<u>Stabilization/Demolition/Mothballing:</u>

DBE Contractors secured subcontracts on 37 projects as of June 30, 2015. The DBE subcontracts value is \$10,657,934 of the \$37,522,070 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of June 30, 2015. The DBE subcontracts value is \$34,691,592 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$492,934,814

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 12 projects as of June 30, 2015. The DBE subcontracts value is \$54,086,557 of the \$199,371,360 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of June 30, 2015. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$200,274,359

^{*} DBE provisions were included in projects bid after June 30, 2012


Current RSD Program DBE Participation

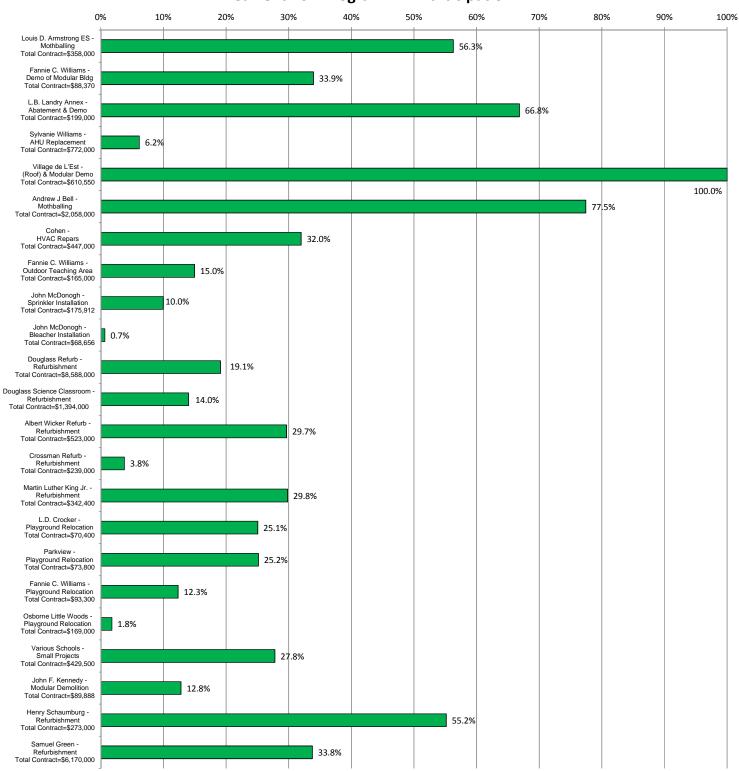

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Current RSD Program DBE Participation

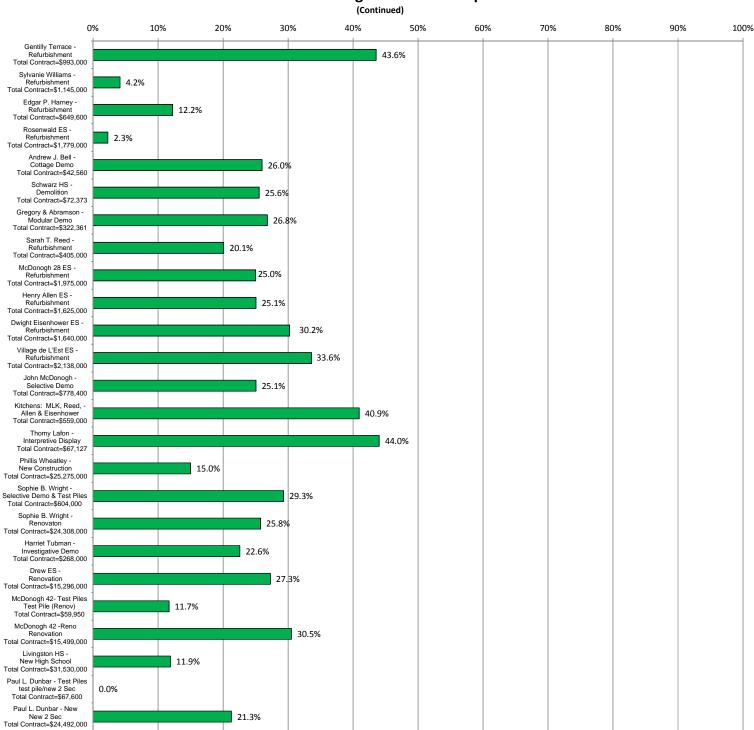


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Current RSD Program DBE Participation


(Continued)

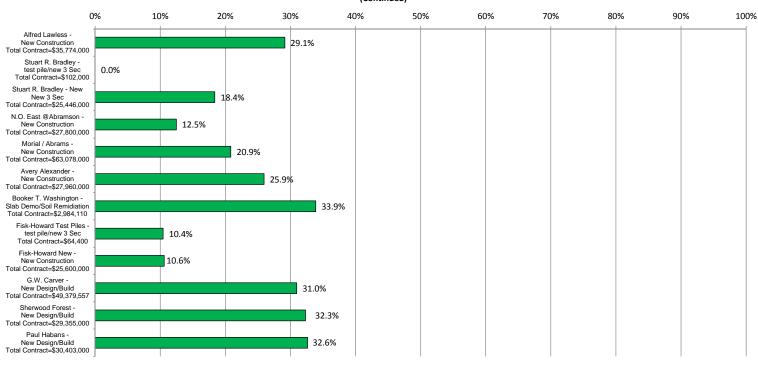

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

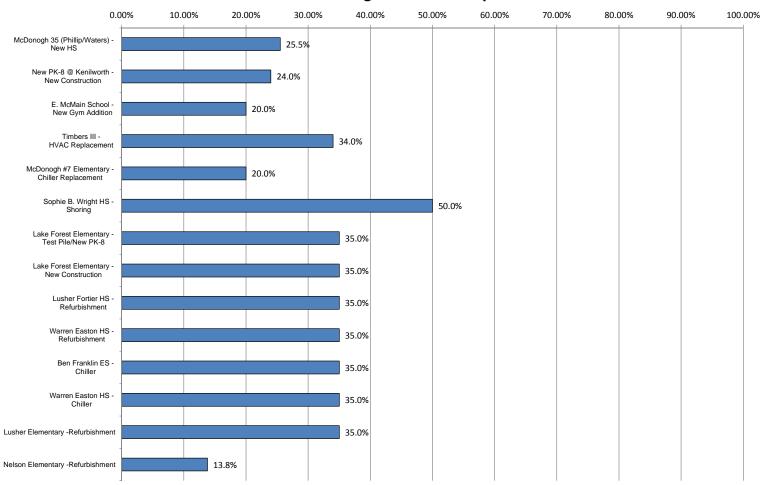

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation - Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School (RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect - Waggonner & Ball Architects, APC

Contractor – McDonnel Group, LLC

Construction Phase

- · Re-steel fabrication has started
- Pile driving continues
- · Installation of formwork for pile caps has started

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – May 2017



Avery Alexander Elementary School (RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect – Sizeler Thompson Brown Architects

Contractor - Core Construction

Construction Phase

- Soil remediation continues
- A survey of the existing piles is being preformed
- · Installation of auger cast piles is scheduled to start beginning of August

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – May 2017



James Audubon School (OPSB)

428 Broadway Avenue, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation of existing elementary school and new addition

Funding Source - FEMA

Architect – Blitch/Knevel Architects

Contractor – FHP Tectonics Corporation

Construction Phase

- · Kitchen equipment being installed
- Terrazzo layout continues on 1st floor of addition
- · Contractor working on the punch list for the existing building

Contractual Substantial Completion – September 2013 Forecasted Substantial Completion – August 2015

School Ready for Occupancy – August 2015



Stuart R. Bradley School (RSD)

2401 Humanity Street, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source - FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Landis Construction Co.

Close-out Phase

- Substantial Completion June 26th
- Punch list work is ongoing

Contractual Substantial Completion – June 2015 Forecasted Substantial Completion – June 2015 School Ready for Occupancy – August 2015



George Washington Carver School (RSD)

3059 Higgins Blvd., New Orleans, LA 70126 District E Ward 9

Scope of work: New High School, Design Build

Funding Source – FEMA Contractor – Broadmoor LLC

Construction Phase

- Insulation and gypsum board installation is ongoing
- MEP and sprinkler rough-ins at both buildings
- Stud framing at Convocation center
- · Storefront and curtain wall installation is ongoing
- Roofing installation continues on both buildings

Contractual Substantial Completion – March 2016 Forecasted Substantial Completion – March 2016



Paul L. Dunbar School (RSD)

9330 Forshey Street, New Orleans, LA 70125 District A Ward 17

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect – Chenevert Architects LLC Contractor – McDonnel Group, LLC

Close-out Phase

- Substantial Completion June 1st
- · Punch list work is ongoing

Contractual Substantial Completion – June 2015 Forecasted Substantial Completion – June 2015 School Ready for Occupancy – August 2015



Benjamin Franklin Elementary School Renovation (OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA Architect – N-Y Associates, Inc.

Contractor - TBD Design Phase - CD

- A&E to submit phasing plan
- The Owner is evaluating the refurbishment or replacement of the windows

Procurement Phase

- Anticipated 1st Advertisement TBD
- Anticipated Bid Opening TBD



Paul B. Habans School (RSD)

3501 Siene Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: New School, Design Build

Funding Source – FEMA
Architect – Grace Hebert
Contractor – Core Construction

Construction Phase

- · Courtyard slab to be poured mid of July
- · Structural steel installation is ongoing at classroom building
- Grease trap installation is complete
- Roof decking is ongoing at gymnasium

Contractual Substantial Completion – May 2016 Forecasted Substantial Completion – May 2016



New Karr High School CMAR (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center and construction of new high

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor – TBD Design Phase - CD

- SOQ was transmitted Jun 2nd
- · Scoring meetings beginning of July
- Interviews are scheduled for end of July



New PK-8 School at North Kenilworth Park at Curran Site (OPSB)

8500 Curran Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect - Mathes Brierre Architects

Contractor – Woodrow Wilson Construction Company, Inc.

Construction Phase

- · HVAC startup anticipated early July
- VCT flooring installation continues
- · Electrical wiring is ongoing
- Installation of glazing continues

Contractual Substantial Completion – September 2014 Forecasted Substantial Completion – July 2015 School Ready for Occupancy – July 2015



Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)

11110 Lake Forest Boulevard 70128 District E Ward 9

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect – Imre Hegedus & Associates Architects

Contractor - The McDonnel Group

Construction Phase

- · Installation of MEP branch line is ongoing
- Installation of interior finishes is ongoing
- · Window installation continues
- Installation of masonry brick is 80% complete
- Site work is 50% complete, pouring of parking area is ongoing

Contractual Substantial Completion – July 2015 Forecasted Substantial Completion – September 2015 School Ready for Occupancy – October 2015



Alfred Lawless School (RSD)

5300 Law Street, New Orleans, LA 70117 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor - Core Construction

Construction Phase

- · Interior painting continues
- Exterior metal wall panels 98% complete
- Flooring installation is ongoing
- Science classroom casework complete
- HVAC start up beginning of June
- Site work continues

Contractual Substantial Completion – November 2015 Forecasted Substantial Completion – November 2015 School Ready for Occupancy – January 2016



John McDonogh High School Selective Demolition (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect – VergesRome Architects, APAC Contractor - Zimmer-Eschette Services Construction Phase

- Interior demolition is 25% complete
- · Selective demolition of walls is ongoing

Contractual Substantial Completion – October 2015 Forecasted Substantial Completion – October 2015



John McDonogh High School Renovation (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

Contracts are being reviewed by both parties



McDonogh #35 School (Phillip/Waters Site) (OPSB)

1200 Senate Street, New Orleans, LA 70122 District D Ward 7

Scope of work: New High School Funding Source – FEMA

Architect - Sizeler, Thompson, Brown Architects

Contractor - Citadel Builders, LLC

Construction Phase

- · MEP is ready for start up
- Brick masonry and window installation is 95% complete
- · Contractor is finishing interior work and starting self punch list
- Site work is ongoing

Contractual Substantial Completion – May 2015 Forecasted Substantial Completion – August 2015 School Ready for Occupancy – August 2015



McDonogh #42 Elementary School (RSD)

1651 North Tonti Street, New Orleans, LA 70119 District A Ward 7

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source - FEMA, QSCB, NMTC, Insurance Proceeds

Architect – Eskew+Dumez+Ripple Contractor – Core Construction

Construction Phase

Punch List work is 95% complete
 Contractual Substantial Completion – June 2015
 Forecasted Substantial Completion – May 2015
 School Ready for Occupancy – June 2015



Eleanor L. McMain School Gymnasium (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source - FEMA

Architect – Jahncke & Burns Architects

Contractor - Gibbs Construction

Construction Phase

- · Installation of roofing is ongoing
- · Concrete flat work continues
- Interior finishes has started

Contractual Substantial Completion – April 2015 Forecasted Substantial Completion – January 2016



Ernest "Dutch" Morial Elementary School (RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect - Waggonner & Ball Architects, APC

Contractor – McDonnel Group, LLC

Construction Phase

- · Ground Breaking June 18th
- Pile driving is 30% complete
- · Erection of from for pile caps has started

Contractual Substantial Completion – January 2017 Forecasted Substantial Completion – January 2017



Small New Orleans East High School at Abramson (RSD)

5552 Read Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New High School

Funding Source - FEMA

Architect – RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

Construction Phase

- Exterior metal wall panels 65% complete
- Interior painting is ongoing
- · Floor installation continues
- Data wire installation is ongoing

Contractual Substantial Completion - June 2015 Forecasted Substantial Completion – September 2015

School Ready for Occupancy – October 2015



Sherwood Forest School (RSD)

4801 Maid Marion Drive, New Orleans, LA 70128 District E Ward 9

Scope of work: New School, Design Build

Funding Source - FEMA Architect - Grace Hebert Contractor - Core Construction

Construction Phase

- · Classroom wing structural steel installation has begun
- MEP rough is ongoing in kitchen and cafeteria
- CMU installation at gymnasium is ongoing
- Decking is being installed on the gymnasium

Contractual Substantial Completion - May 2016

Forecasted Substantial Completion - May 2016



Harriet R. Tubman Elementary School Renovation

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect - Mahlum Scairono Martinez JV

Documents until July

Contractor - TBD

Design Phase - CD • Plan modifications will extend the completion of 100% Construction

Procurement Phase

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



Booker T. Washington School Environmental Remediation (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The remediation of the site

Funding Source - FEMA

Architect – Hewitt-Washington & Associates

Contractor – SEMS, Inc Procurement Phase

- · Contractor is mobilized
- Excavation to start July 13th

Contractual Substantial Completion – December 2015 Forecasted Substantial Completion – December 2015



Booker T. Washington School (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source - FEMA

Architect - Hewitt-Washington & Associates

Contractor - TBD

Design Phase - SD

Successful Proposal will be announced July 2015



Sophie B. Wright High School Renovation (RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Renovation of existing school and gymnasium addition

Funding Source – FEMA

Architect - Waggonner & Ball Architects, APC

Contractor - Core Construction

Construction Phase

- MEP rough-in ongoing
- Steel for auditorium to be complete by August
- Window refurbishment continues
- · Floor repairs are ongoing

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



REFURBISHMENTS

Henry Allen Elementary School Refurbishment (RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - Tuna Construction

Construction Phase

- Window refurbishment is 50% complete
- Mechanical work is 20% complete
- Tuck pointing has started on the exterior brick
- Installation of back flow preventer is ongoing

Contractual Substantial Completion – February 2016 Forecasted Substantial Completion – February 2016



Henry Allen Elementary School Kitchen Refurbishment (RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA
Architect – N-Y Associates, Inc.
Contractor - CDW Services

Construction Phase

 Project will be delayed due to permitting issues Contractual Substantial Completion – November 2016 Forecasted Substantial Completion – November 2016



Benjamin Banneker Elementary School Kitchen Refurbishment (RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – SCNZ Architects Contractor - TBD

Design Phase - CD

• Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase

- Anticipated 1st Advertisement January 2016
- Anticipated Bid Opening March 2016



Agnes L. Bauduit Elementary School Refurbishment (RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect - Duplantis Design Group, PC

Contractor - TBD Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
 - Anticipated 1st Advertisement August 2015
 - Anticipated Bid Opening September 2015



Bethune and Tureaud Elementary School Refurbishment (OPSB)

4040 Eagle Street & 2021 Pauger Street, New Orleans, LA District A Ward 3 & District D Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Chenevert Architects LLC

Contractor - TBD

Design Phase - CD

• 100% Construction Documents are complete

Procurement Phase

- Anticipated 1st Advertisement August 2015
- Anticipated Bid Opening September 2015



Walter L. Cohen High School Kitchen Refurbishment (RSD)

3520 Dryades, New Orleans Street, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD Design Phase - CD

 Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase

- Anticipated 1st Advertisement January 2016
- Anticipated Bid Opening March 2016



A. D. Crossman School Kitchen Refurbishment (RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source - FEMA Architect – SCNZ Architects

Contractor - TBD **Procurement Phase**

• 1st Advertisement - July 29th

• 2nd Advertisement - August 5th

• 3rd Advertisement - August 12th

• Pre-Bid Conference - August 13th

· Bid Opening - September 3rd



Frederick A. Douglass High School Science Lab (RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovations to science lab

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor – One Construction

Construction Phase

· Demolition work is ongoing

· Plaster repairs has started

Contractual Substantial Completion – November 2015 Forecasted Substantial Completion – November 2015

Warren Easton School (OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Refurbishment of existing high school, including but not limited to

structure, doors, masonry walls and roof

Funding Source – FEMA

Architect - Chenevert Architects LLC

Contractor - Tuna Construction

Construction Phase

- Rooms 322 and 229A are complete
- · Restroom renovations continues
- Exterior tuck pointing continues
- Sprinkler work at the Gymnasium will continue during summer break

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



Dwight D. Eisenhower Elementary School Refurbishment (RSD)

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Harry Baker Smith Architects II, PLLC

Contractor - CDW Construction

Construction Phase

- HVAC work ins underway
- · Canopy work is complete
- · Interior work on Annex B has started
- Installation of interior lighting to start beginning of July

Contractual Substantial Completion – January 2016 Forecasted Substantial Completion – January 2016



Dwight D. Eisenhower Elementary School Kitchen Refurbishment

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA
Architect – N-Y Associates, Inc.
Contractor - CDW Services

Construction Phase

 Project will be delayed due to permitting issues Contractual Substantial Completion – November 2016 Forecasted Substantial Completion – November 2016



William J. Fischer Elementary School Refurbishment (RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD Design Phase - CD

- 100% Construction Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



Fortier (Lusher) High School Refurbishment (OPSB)

5624 Freret Street, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation and repairs to the roof, masonry, plaster, windows, exterior doors, canopies, mechanical systems, and electrical systems.

Funding Source – FEMA Architect – SCNZ Architects Contractor - Core Construction Construction Phase

- · Contractor is working on punch list from phase one
- MEP work for phase two has started
- Painting of walls and doors continues
- Installation of new door and hardware continues
- Repairs to exterior brick work is ongoing

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



Gaudet Elementary School Refurbishment (RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- \bullet Procurement schedule has been adjusted pending FEMA funding approval $\underline{\text{Procurement Phase}}$
 - Anticipated 1st Advertisement September 2015
 - Anticipated Bid Opening October 2015



Gentilly Terrace School Refurbishment (RSD)

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners Contractor - One Construction

Construction Phase

- · Contractor is working on punch list items from original contract
- · Additional kitchen work has started
- · Work at the dumpster pad has started

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015



Samuel J. Green Elementary School Refurbishment (RSD)

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC Contractor - Hernandez Consulting, LLC Construction Phase

- · Fire Alarm work is ongoing
- · Window replacement continues
- Electrical and plumbing renovations continues
- Exterior brick repairs is 50% complete
- Roof repairs are 50% complete

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015



Edgar P. Harney Elementary School Refurbishment (RSD)

2503 Willow Street, New Orleans, LA 70113 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - VergesRome Architects, APAC

Contractor - Hamp's Construction, LLC

Construction Phase

- Repair to exterior brick work has started
- Work at new dumpster pad is ongoing
- · Electrical work continues

Contractual Substantial Completion – September 2015

Forecasted Substantial Completion – September 2015



Andrew Jackson School Refurbishment (RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source - FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- 1st Advertisement August 19th
- · 2nd Advertisement August 26th
- 3rd Advertisement September 2nd
- Pre-Bid Conference September 3rd
- Bid Opening September 23rd



J. W. Johnson Elementary School Refurbishment (RSD)

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
 - Anticipated 1st Advertisement September 2015
 - Anticipated Bid Opening October 2015



Dr. Martin L. King Elementary School Kitchen Refurbishment (RSD)

1617 Caffin Avenue, New Orleans, LA 70117 District E Ward 9

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Construction Phase

Project will be delayed due to permitting issues

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – November 2016



Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16 Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
 - Anticipated 1st Advertisement August 2015
 - Anticipated Bid Opening September 2015



Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect - Mahlum Scairono Martinez JV

Contractor - TBD Procurement Phase

- 1st Advertisement June 24th
- 2nd Advertisement July 1st
- 3rd Advertisement July 8th
- Pre-Bid Conference July 9th
- · Bid Opening July 29th



Live Oak Elementary School Refurbishment (RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval <u>Procurement Phase</u>
 - Anticipated 1st Advertisement August 2015
 - Anticipated Bid Opening September 2015



Lusher Elementary School Refurbishment (OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows,

exterior doors, and restroom accessibility

Funding Source – FEMA

Architect - Meyer Engineers, LTD.

Contractor - Dynamic

Construction Phase

- · Window installation has started
- · Interior demolition has started

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – November 2016



Thurgood Marshall Elementary School Refurbishment (RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - TBD Design Phase - CD

• 100% Construction Documents are due late July

Procurement Phase

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



McDonogh #28 School Refurbishment (RSD)

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source - FEMA

Architect - SCNZ Architects, LLC

Contractor - Tuna Construction

Construction Phase

- · Kitchen scope change order is being reviewed
- · Window removal and abatement is almost complete
- · Roof work is 75% complete
- · Exterior plaster work is ongoing

Contractual Substantial Completion – March 2016 Forecasted Substantial Completion – March 2016



McDonogh #32 School Refurbishment (RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase - CD

- · Bid Documents are due August 18th
- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
 - Anticipated 1st Advertisement September 2015
 - Anticipated Bid Opening October 2015



Nelson Elementary School Refurbishment (OPSB)

3121 St. Bernard Avenue, New Orleans, LA 70119 District D Ward 7

Scope of work: Renovation and repairs to the roof, masonry, windows, exterior doors, mechanical systems, and electrical systems.

Funding Source - FEMA

Architect – Harry Baker Smith Architects Contractor - Blanchard Mechanical Contractor

Construction Phase

- · Notice to Proceed June 3rd
- Contractor has mobilized and started work
- Assessments of AHU's has been completed



Sarah T. Reed School Refurbishment (RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - Byron J. Stewart & Associates, APC Architects & Planners

Contractor - Tuna Construction

Construction Phase

- · Roof repairs is ongoing
- · Window installation is 50% complete
- Electrical work is 90% complete
- Exterior drainage work is complete

Contractual Substantial Completion – December 2015

Forecasted Substantial Completion – December 2015



Sarah T. Reed School Kitchen Refurbishment (RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services

Construction Phase

Project will be delayed due to permitting issues
 Contractual Substantial Completion – November 2016
 Forecasted Substantial Completion – November 2016



Rosenwald Elementary School Refurbishment (RSD)

6501 Berkley Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Byron J. Stewart & Associates, APC Architects & Planners

Contractor - One Construction

Construction Phase

- HVAC repairs are 20% complete
- Work on dumpster pad and grease trap continues
- Electrical work is 40% complete
- · Roof repairs have started

Contractual Substantial Completion – January 2016

Forecasted Substantial Completion – January 2016



Henry C. Schaumburg Elementary School (RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - N-Y Associates, Inc

Contractor - Hernandez Consulting, LLC

Close-Out

· Substantial Completion June 25th

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



Village de l'Est Elementary School Refurbishment (RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA, CBDG

Architect - Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

Construction Phase

- Work continues on dumpster pad and grease trap
- Replacement of Ceiling tile and grid in hallways is 80% complete
- · Painting of classrooms is ongoing
- Mechanical and plumbing work has started

Contractual Substantial Completion - April 2016

Forecasted Substantial Completion - April 2016



Albert Wicker School Kitchen Refurbishment (RSD)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – SCNZ Architects

Contractor - TBD Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval <u>Procurement Phase</u>
 - Anticipated 1st Advertisement January 2016
 - Anticipated Bid Opening March 2016



Sylvanie F. Williams School Refurbishment (RSD)

3127 Martin Luther King Jr. Boulevard, New Orleans, LA 70125 District B Ward 2 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Hamps

Construction Phase

- · Door and window repairs is ongoing
- Work on parking resurfacing has started
- Stucco work is 75% complete
- Dumpster and grease trap work is almost complete

Contractual Substantial Completion – August 2015 Forecasted Substantial Completion – August 2015



OTHER PROJECTS

Eleanor L. McMain School Roof Replacement (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Roof replacement
Funding Source – General Fund & Harrah's
Architect – Duplantis Design Group
Contractor – TBD
Procurement Phase


Owner is review bids

Eleanor L. McMain School Maintenance Upgrades (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work. Funding Source – General Fund & Harrah's Architect – Duplantis Design Group Contractor – TBD

- Procurement Phase
 - · 1st Advertisement June 3rd
 - 2nd Advertisement June 10th
 - 3rd Advertisement June 17th
 - Pre-Bid Conference June 18th
 - · Bid Opening July 8th



Timbers III - Building Controls (OPSB)

3520 General DeGaulle Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: Design and installation of new building controls

Funding Source – OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - PC

· Owner has placed project on hold

Procurement Phase

- Anticipated 1st Advertisement TBD
- Anticipated Bid Opening TBD



Building Automation System Integration At Recovery School

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview ES

Funding Source – FEMA Architect – Moses Engineers Contractor – Synergy Building Solutions, Inc. Construction Phase

- The five Quick Start Schools are complete, the Energy Dash Board is being implemented
- Sylvanie Williams Elementary School, Sarah T. Reed Elementary School, Fannie C. Williams Elementary School, Bienville Elementary School, Charles L. Colton Elementary School, William Frantz Elementary School, Parkview Elementary School, Osborne Elementary School, Carter G.
 Woodson Elementary School, Walter Cohen High School, Dolores T Aaron Elementary School, A. D. Crossman Elementary School, and Albert Wicker Elementary School are complete
- · Punch list work is ongoing at Benjamin Banneker Elementary School
- Integrations 95% complete at Lawrence D. Crocker Elementary School

Contractual Substantial Completion – May 2015 Forecasted Substantial Completion – May 2015



MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

Demolition of Modular Buildings at Gregory and Abramson (RSD)

1700 Pratt Drive & 5552 Read Boulevard, New Orleans, LA District D Ward 7 & District E Ward 9

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Holly & Smith Architects

Contractor – Ashley Savarino Unlimited Construction

Close-Out

Substantial Completion June 23rd
 Contractual Substantial Completion – June 2015
 Forecasted Substantial Completion – June 2015



Demolition of Modular Buildings at Livingston (RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect - GAEA Consultants, LLC

Contractor - TBD

Procurement Phase

- Anticipated 1st Advertisement November 2015
- Anticipated Bid Opening December 2015



Comprehensive List - Completed Projects

- 1 Abrams | Morial | Abramson | Coghill Demolition (RSD)
- 2 A. D. Cross Elementary School Energy Conservation (RSD)
- 3 A. D. Crossman Elementary School and Benjamin Banneker Elementary School (RSD)
- 4 A. D. Crossman Elementary School Refurbishment (RSD)
- A. P. Tureaud Elementary School Roof Repairs (RSD)
- 6 Agnes Bauduit Elementary School Boiler (RSD)
- 7 Albert Wicker Elementary School Refurbishment (RSD)
- 8 Albert Wicker Elementary School Roof Repairs (RSD)
- 9 Alfred Lawless Senior High Security Fencing (RSD)
- 10 Alice M. Harte Elementary School (OPSB)
- 11 Alice M. Harte Elementary School Demolition (OPSB)
- 12 Andrew J. Bell Junior High School Roof Replacement (RSD)
- 13 Andrew J. Bell Junior High School Mothball (RSD)
- 14 Andrew Jackson Elementary School Roof Repairs (RSD)
- 15 Andrew Jackson Elementary School Solar Panels (RSD)
- 16 Andrew H. Wilson Elementary School Cottage (RSD)
- 17 Arthur Ashe Elementary School Kitchen Renovation (OPSB)
- 18 Augustine Elementary School Roof (RSD)
- 19 Avery-Alexander Elementary School Demolition (RSD)
- 20 Barbara C. Jordan Elementary School Demolition (RSD)
- 21 Bell JH Shoring (RSD)
- 22 Benjamin Banneker Elementary School Energy Conservation (RSD)
- 23 Benjamin Franklin Senior High School (OPSB)
- 24 Bienville Elementary School Demolition (RSD)
- 25 Booker T. Washington High School Partial Demolition (RSD)
- 26 Carter G. Woodson Middle School Demolition (RSD)
- 27 Central Services Warehouse Demolition (OPSB)
- 28 Charles J. Colton Elementary Selective Demolition (RSD)
- 29 Charles J. Colton Elementary School (RSD)
- 30 Charles R. Drew Elementary School (RSD)
- 31 Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)
- 32 Cohen High School Health Clinic (RSD)
- 33 Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School (RSD)
- 34 Douglass High School Under Floor Utilities (RSD)
- 35 Dr. Martin Luther King School Roof Repairs (RSD)
- 36 Dr. Martin Luther King Jr. School Renovation (RSD)
- 37 Dwight D. Eisenhower Elementary School Roof Repairs (RSD)
- 38 East Bank Swing Space for Audubon Charter School (OPSB)
- Edgar P. Harney Elementary School Roof Repairs (RSD)
- 40 Edna Karr High School Gymnasium Repair (OPSB)
- 41 Edna Karr High School Assessment (OPSB)
- 42 Edward Livingston Middle School Demolition (RSD)

- 43 Edward Henry Phillips Junior High School Demolition (OPSB)
- New Edward Hynes School (OPSB)
- 45 Edwards | Hardin | Lockett | Lawless Demolition (RSD)
- 46 Edward Livingston High School (RSD)
- 47 Eleanor L. McMain School Replacement of Existing Chillers (OPSB)
- 48 Eleanor L. McMain School Clinic (OPSB)
- 49 Ernest N. Morial Elementary Security Fencing (RSD)
- 50 Fannie C. Williams Elementary School Demolition (RSD)
- 51 Fisk-Howard Elementary School Demolition (RSD)
- 52 Florence J. Chester Elementary School Demolition (RSD)
- 53 Francis W. Gregory Demolition (RSD)
- 54 Frederick A. Douglass High Refurbishment (RSD)
- 55 Frederick A. Douglass High Switchgear (RSD)
- 56 Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)
- 57 George Mondy Elementary School Mothball (RSD)
- 58 George Washington Carver High School Demolition (RSD)
- 59 Greater St. Stephens School (OPSB)
- 60 Harriet R. Tubman Elementary School Selective Demolition (RSD)
- 61 Henry Allen Elementary School Roof (RSD)
- 62 Henry C. Schaumburg Window/Door, Air Condition, Water Fountain/Sink Installation (RSD)
- 63 Holy Cross Modular Relocation (RSD)
- 64 Israel M. Augustine Middle School Roof Replacement (RSD)
- 65 Israel M. Augustine Middle School Mothball (RSD)
- 66 James Derham Demolition (RSD)
- 67 James W. Johnson Elementary School Roof (RSD)
- New Jean Batiste de Bienville School (RSD)
- 69 Jean Gordon Elementary School Demolition (RSD)
- 70 John Dibert Elementary School Roof (RSD)
- 71 John W. Hoffman Elementary School Demolition (RSD)
- 72 John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)
- 73 John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)
- 74 John F. Kennedy Modular Demolition (RSD)
- 75 John F. Kennedy High School Demolition (RSD)
- 76 John McDonogh Senior High School Bleachers and Sprinklers (RSD)
- 77 John McDonogh Senior High School Roof (RSD)
- 78 John A. Shaw Elementary School Mothball (RSD)
- 79 Joseph S. Clark Senior High School Roof Repairs (RSD)
- 80 Joseph A. Craig Elementary Canopies (RSD)
- 81 Joseph A. Craig Elementary Elevator Installation (RSD)
- 82 Joseph A. Hardin Elementary Security Fencing (RSD)
- 83 Lafayette Elementary School Roof and Masonry (RSD)
- 84 Lake Area | Landry Demolition (RSD)
- 85 Langston Hughes Elementary School (Phase I) (RSD)
- 86 Langston Hughes Elementary School New Gymnasium (Phase II) (RSD)
- 87 Langston Hughes Elementary School Dumpster Pad (RSD)

- 88 Lawrence D. Crocker Elementary School Demolition (RSD)
- 89 L.B. Landry Annex Demolition (RSD)
- 90 Little Woods Elementary School Demolition (RSD)
- 91 Little Woods School (Dolores T. Aaron Elementary School) (RSD)
- 92 Live Oak Elementary School Roof (RSD)
- 93 Live Oak Elementary School Exterior Door Replacement (RSD)
- 94 Lorraine Hansberry Elementary School Mothball (RSD)
- 95 Louis D. Armstrong Elementary School (RSD)
- 96 Mahalia Jackson Elementary School (OPSB)
- 97 Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)
- 98 Mahalia Jackson Elementary School Office Renovation (OPSB)
- 99 Martin Behrman Elementary School Roof (RSD)
- 100 Martin Luther King Jr. Elementary Canopy System (RSD)
- 101 Martin Luther King Jr. School Modular Building, Deck, Canopy (RSD)
- 102 Mary Church Terrell Elementary School Demolition (RSD)
- 103 Mary M. Bethune Elementary 1st Floor Replacement (OPSB)
- 104 Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)
- 105 McDonogh #7 High School Repairs (OPSB)
- 106 McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)
- 107 McDonogh #28 Elementary School Roof (RSD)
- 108 McDonogh #32 Roof Replacement (RSD)
- 109 McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium (OPSB)
- 110 McDonogh #42 Elementary School Roof (RSD)
- 111 McDonogh #42 Elementary School HVAC Replacement (RSD)
- 112 Mildred C. Osborne Elementary School Demolition (RSD)
- 113 Mildred C. Osborne Elementary School (RSD)
- 114 Modular Campuses Close Outs (RSD)
- 115 Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)
- 116 Modular Structures at Langston Hughes Elementary School (RSD)
- 117 Morris F.X. Jeff Elementary School Demolition (RSD)
- 118 Morris F.X. Jeff Elementary School Mothball (RSD)
- 119 Murray G. Henderson Elementary School Roof (RSD)
- 120 New Andrew H. Wilson Elementary School (RSD)
- 121 New Carter G. Woodson School (RSD)
- 122 New Fannie C. Williams School (RSD)
- 123 New Joseph A. Craig Elementary School (RSD)
- 124 New L.B. Landry High School (RSD)
- 125 New Lake Area High School (RSD)
- 126 New Lawrence D. Crocker School (RSD)
- 127 New Parkview School (RSD)
- 128 New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD)
- 129 New William Frantz Elementary School (RSD)
- 130 New Orleans High School Signature Center Study (RSD)
- 131 Oretha C. Haley Demo (RSD)

- 132 Oretha C. Haley Elementary School Mothball (RSD)
- 133 Parkview Elementary School Demolition (RSD)
- 134 Paul L. Dunbar Elementary School Demolition (RSD)
- 135 Paul B. Habans Elementary School Roof Repairs (RSD)
- 136 Phillis Wheatley Elementary School Demolition (RSD)
- 137 Phillis Wheatley Elementary School (RSD)
- 138 Robert M. Lusher Elementary Roof Removal & Replacement (OPSB)
- 139 Sarah T. Reed High School Bleachers (RSD)
- 140 Sarah T. Reed High School Auditorium Wall (RSD)
- 141 Seabrook Computer Training Center Demolition (OPSB)
- 142 Schaumburg Chillers (RSD)
- 143 Schwarz Alternative Repairs (RSD)
- 144 Schwarz Alternative Modulars Demolition (RSD)
- 145 Schwarz Modular Building Demolition (RSD)
- 146 Sherwood Forest Elementary School Demolition (RSD)
- 147 Sophie B. Wright School Selective Demolition (RSD)
- 148 Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)
- 149 Stuart R. Bradley Elementary School Demolition (RSD)
- 150 Sylvanie Williams Elementary School AHU Replacement (RSD)
- 151 Sylvanie Williams Elementary School Play Yard (RSD)
- 152 Sylvanie Williams Elementary School Roof Repairs (RSD)
- 153 Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)
- 154 Temporary Campus for McDonogh #11 Expropriation (OPSB)
- 155 Thomas A. Edison Elementary School Demolition (RSD)
- 156 Thomy Lafon Elementary School Demolition (RSD)
- 157 Thomy Lafon School Interpretative Display (RSD)
- 158 Timbers Park Office Building #1 & #2 Demolition (OPSB)
- 159 Timbers HVAC (OPSB)
- 160 Timbers III IT Room Relocation (OPSB)
- 161 Village de L'est Elementary School Subsidence (RSD)
- 162 Village de L'est Elementary School Roof and Modular Demolition (RSD)
- 163 Vorice J. Waters Elementary School Demolition (RSD)
- 164 Valena C. Jones Elementary School (RSD)
- 165 Walter L. Cohen High School HVAC (RSD)
- 166 Warren Easton High School Window Replacement (OPSB)
- 167 West Bank Swing Space for Alice Harte Elementary School (OPSB)
- 168 New William J. Guste Elementary School (RSD)
- 169 William J. Guste Elementary School Science Lab (RSD)
- 170 William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)
- 171 William Frantz Elementary School (RSD)
- 172 William Frantz Elementary School Roof (RSD)
