


Superintendent's Report March, 2016



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District

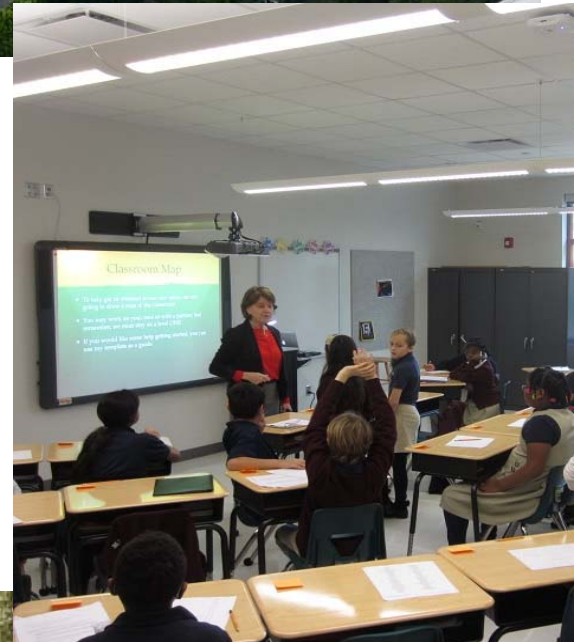

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	3
COMMUNITY MEETINGS	4
BID OPENINGS	5
DBE OVERVIEW MONTHLY SUMMARY	6
NEW & MAJOR RENOVATION	11
Ray Abrams Elementary School ^(RSD)	11
Avery Alexander Elementary School ^(RSD)	11
George Washington Carver School ^(RSD)	11
Benjamin Franklin Elementary School Renovation ^(OPSB)	12
Paul B. Habans School ^(RSD)	12
New Karr High School, CMAR ^(OPSB)	12
John McDonogh High School Renovation CMAR ^(RSD)	13
Eleanor L. McMain School Gymnasium ^(OPSB)	13
Ernest "Dutch" Morial Elementary School ^(RSD)	13
Sherwood Forest School ^(RSD)	14
Harriet R. Tubman Elementary School Renovation ^(RSD)	14
Booker T. Washington School CMAR ^(RSD)	14
Sophie B. Wright School ^(RSD)	15

REFURBISHMENTS	16
Henry Allen Elementary School Refurbishment ^(RSD)	16
Benjamin Banneker Elementary Kitchen School Refurbishment ^(RSD)	16
Agnes L. Bauduit Elementary School Refurbishment ^(RSD)	16
Walter L. Cohen High School Kitchen Refurbishment ^(RSD)	17
A. D. Crossman School Kitchen Refurbishment ^(RSD)	17
Frederick A. Douglass High School Science Lab ^(RSD)	17
William J. Fischer Elementary Refurbishment ^(RSD)	18
Fortier (Lusher) High School Refurbishment ^(OPSB)	18
Gaudet Elementary School Refurbishment ^(RSD)	18
Edgar P. Harney Elementary School Refurbishment ^(RSD)	19
Andrew Jackson School Refurbishment ^(RSD)	19
J. W. Johnson Elementary School Refurbishment ^(RSD)	19
Lafayette Elementary School Refurbishment ^(RSD)	20
Laurel Elementary School Refurbishment ^(RSD)	20
Live Oak Elementary School Refurbishment ^(RSD)	20
Lusher Elementary School Refurbishment ^(OPSB)	21
Thurgood Marshall Elementary School Refurbishment ^(RSD)	21
McDonogh #28 School Refurbishment ^(RSD)	21
McDonogh #32 School Refurbishment ^(RSD)	22
Nelson Elementary School Refurbishment ^(OPSB)	22
Rosenwald Elementary School Refurbishment ^(RSD)	22
Village de l'Est Elementary School Refurbishment ^(RSD)	23
Albert Wicker School Kitchen Refurbishment ^(RSD)	23
OTHER PROJECTS	
Eleanor L. McMain School Roof Replacement ^(OPSB)	24
Eleanor L. McMain School Maintenance Upgrades ^(OPSB)	24
Building Automation System Integration At Recovery School District Central And Remote Offices ^(RSD)	24
MOTHBALL OR SAFE & SECURE OF SELECTED SCHOOLS	25
Demolition of Modulares at Abramson and Carver ^(RSD)	25
Demolition of Modulares at Livingston ^(RSD)	25
COMPLETED PROJECTS	26

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$553 million in open contracts for the capital program after issuing \$4 million in new contracts, change orders and amendments in March. In addition, the total change orders to date, \$5.7 million, account for one percent (1.2%) of the total open construction contracts. RSD anticipates issuing approximately \$20 million in construction contracts/change orders, and no professional service contracts/amendments in April.



The OPSB has \$228 million in open contracts for the capital program after issuing \$615 thousand in new contracts, change orders and amendments in March. In addition, the total change orders to date, \$7.2 million, account for approximately four percent (3.74%) of the total open construction contracts. OPSB anticipates issuing approximately \$472 thousand in construction contracts/change orders and \$282 thousand in professional service contracts and amendments in April.

Community Meetings



Future Community Meetings

Bid Openings

Bids that were opened in February, 2016

March 16, 2016

- Agnes L. Bauduit School Refurbishment

The following projects are scheduled to bid in the next 60 days

April 13, 2016

- Lafayette School Refurbishment

April 27, 2016

- Sophie B. Wright School Cornice Replacement

May 18, 2016

- Laurel School Refurbishment

June 1, 2016

- Benjamin Franklin Elementary School Renovation

Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District



New & Renovations:

DBE Contractors secured subcontracts on 21 projects as of March 31, 2016. The DBE subcontracts value is \$73,887,431 of the \$348,099,187 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 44 projects as of March 31, 2016. The DBE subcontracts value is \$17,313,447 of the \$53,851,020 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of March 31, 2016. The DBE subcontracts value is \$34,701,554 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$ 511,087,764

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of March 31, 2016. The DBE subcontracts value is \$54,086,557 of the \$199,371,360 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of March 31, 2016. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$200,274,359

* DBE provisions were included in projects bid after June 30, 2012


Current RSD Program DBE Participation

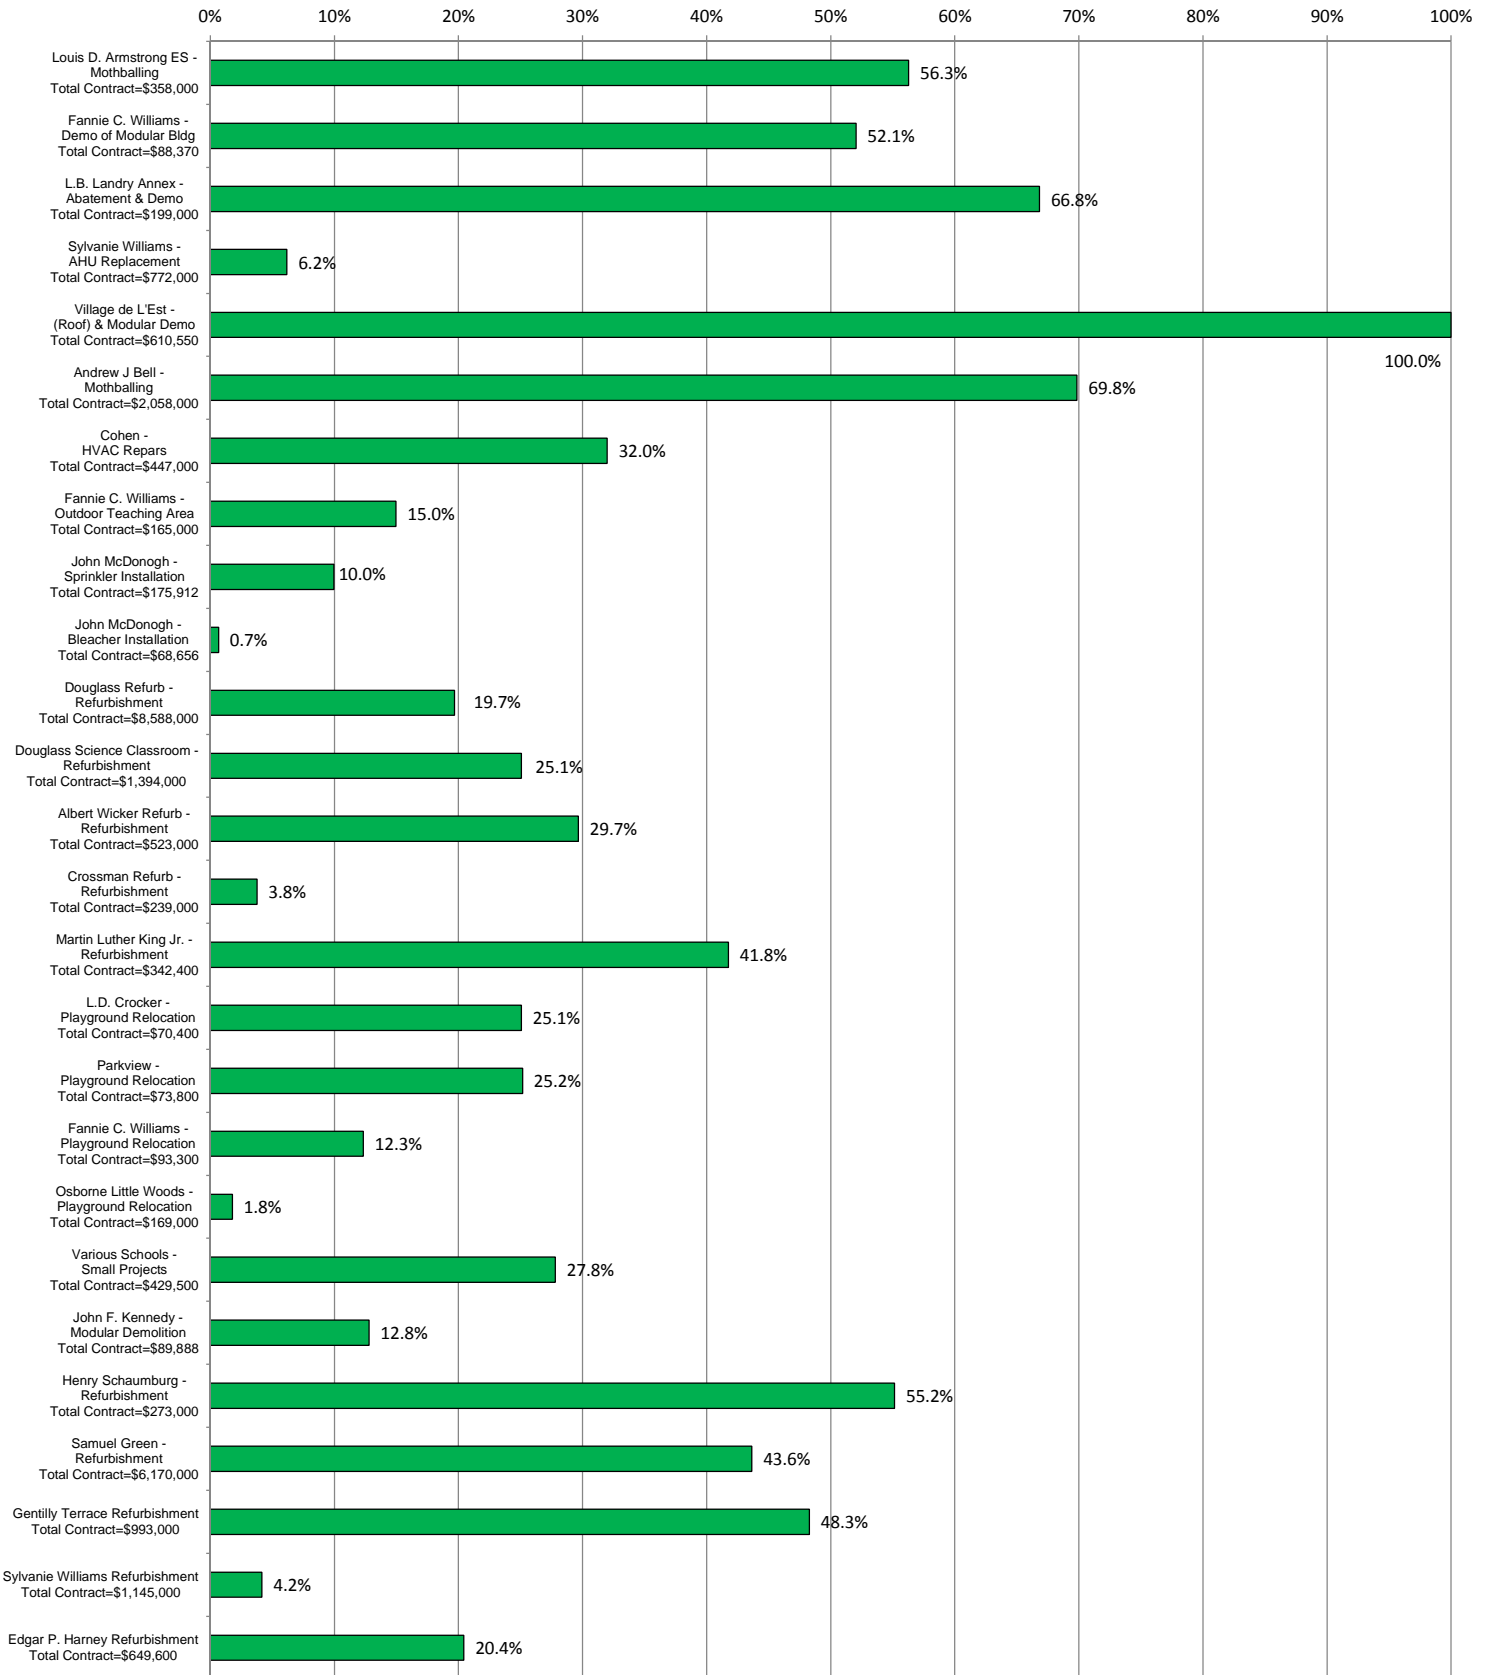

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

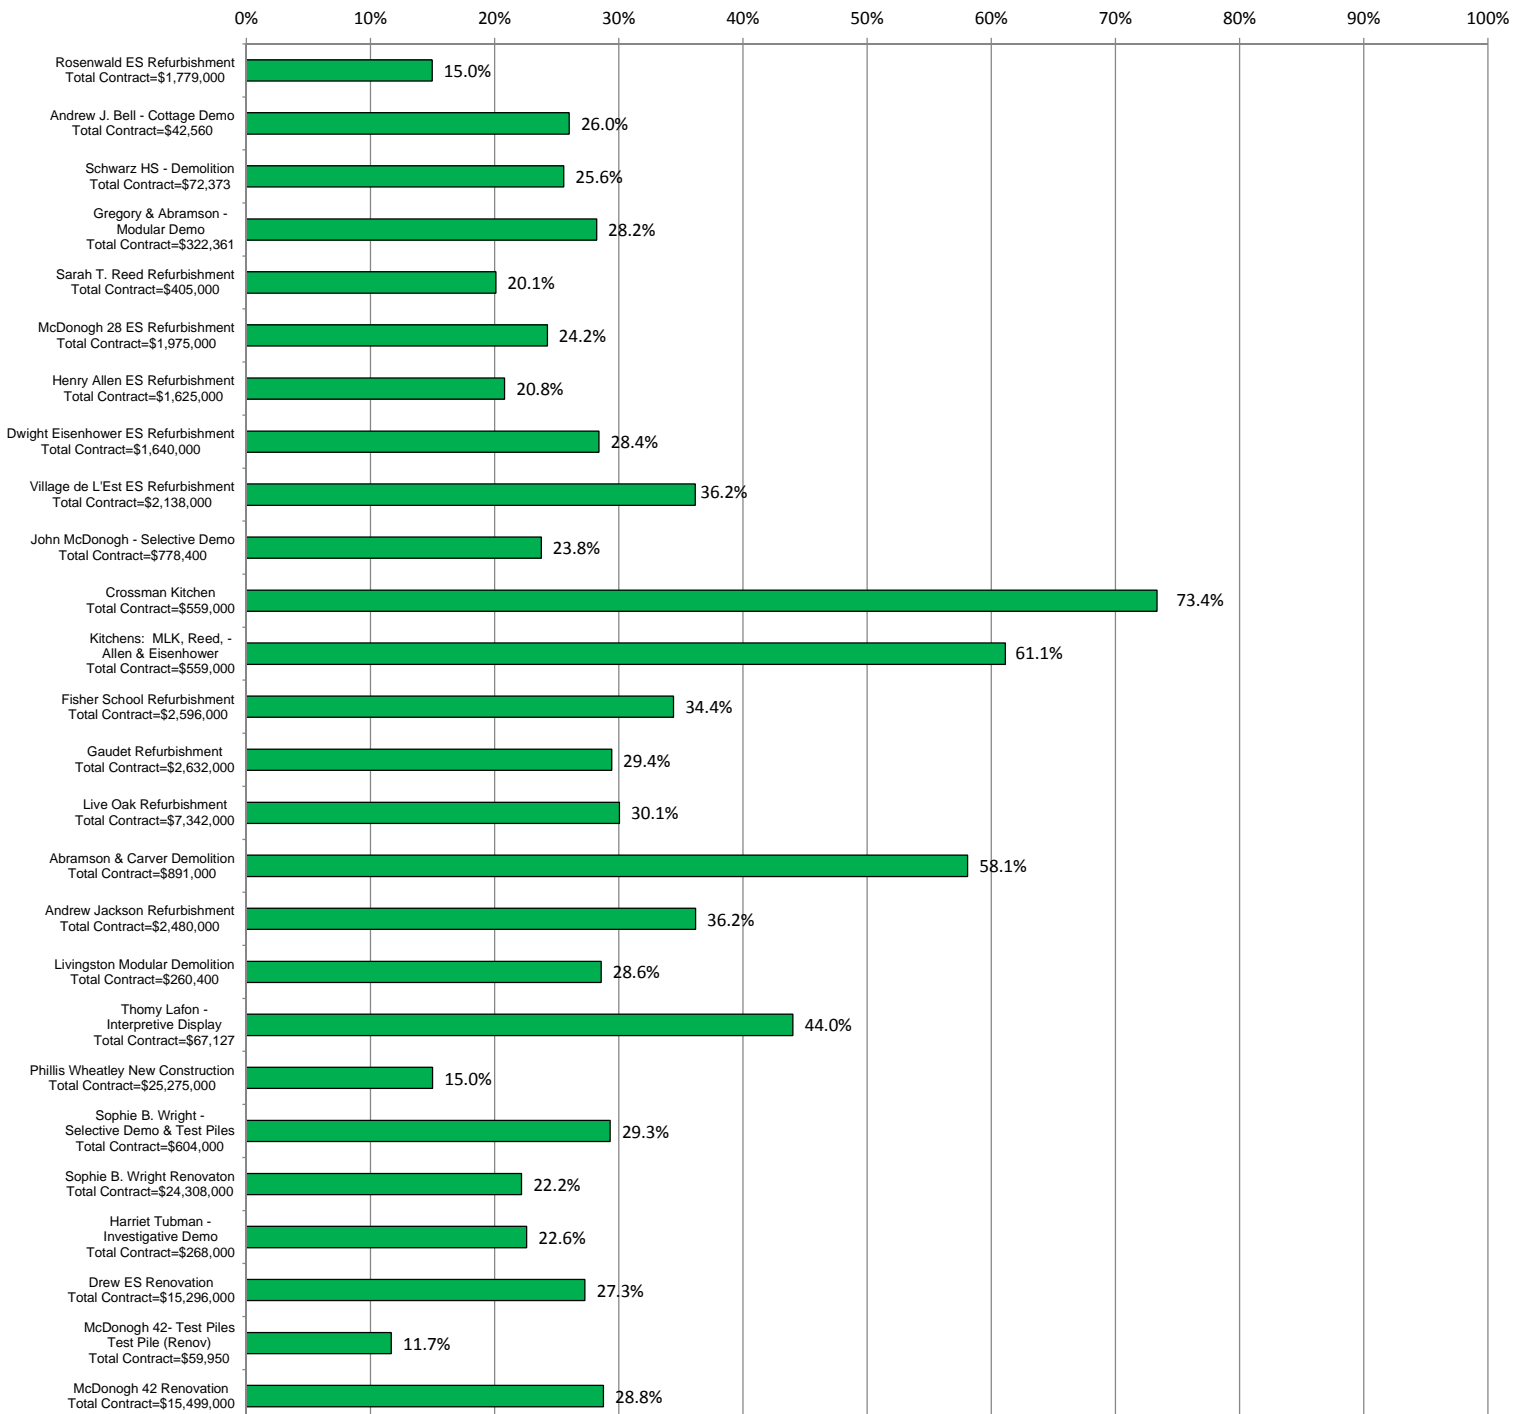


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current RSD Program DBE Participation (Continued)

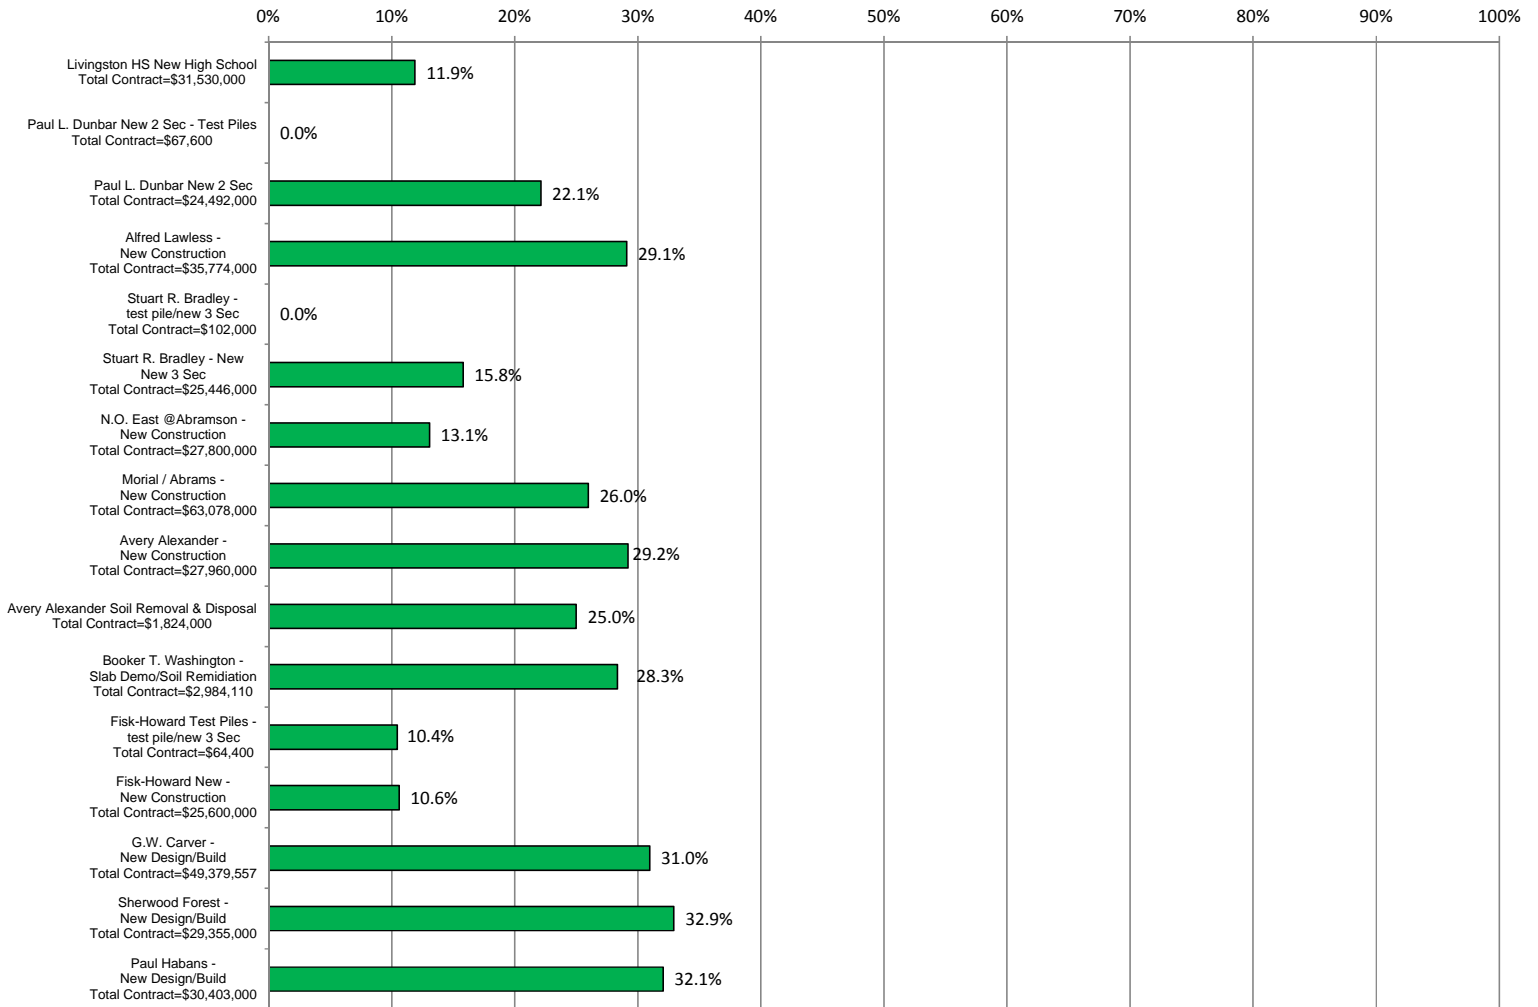

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

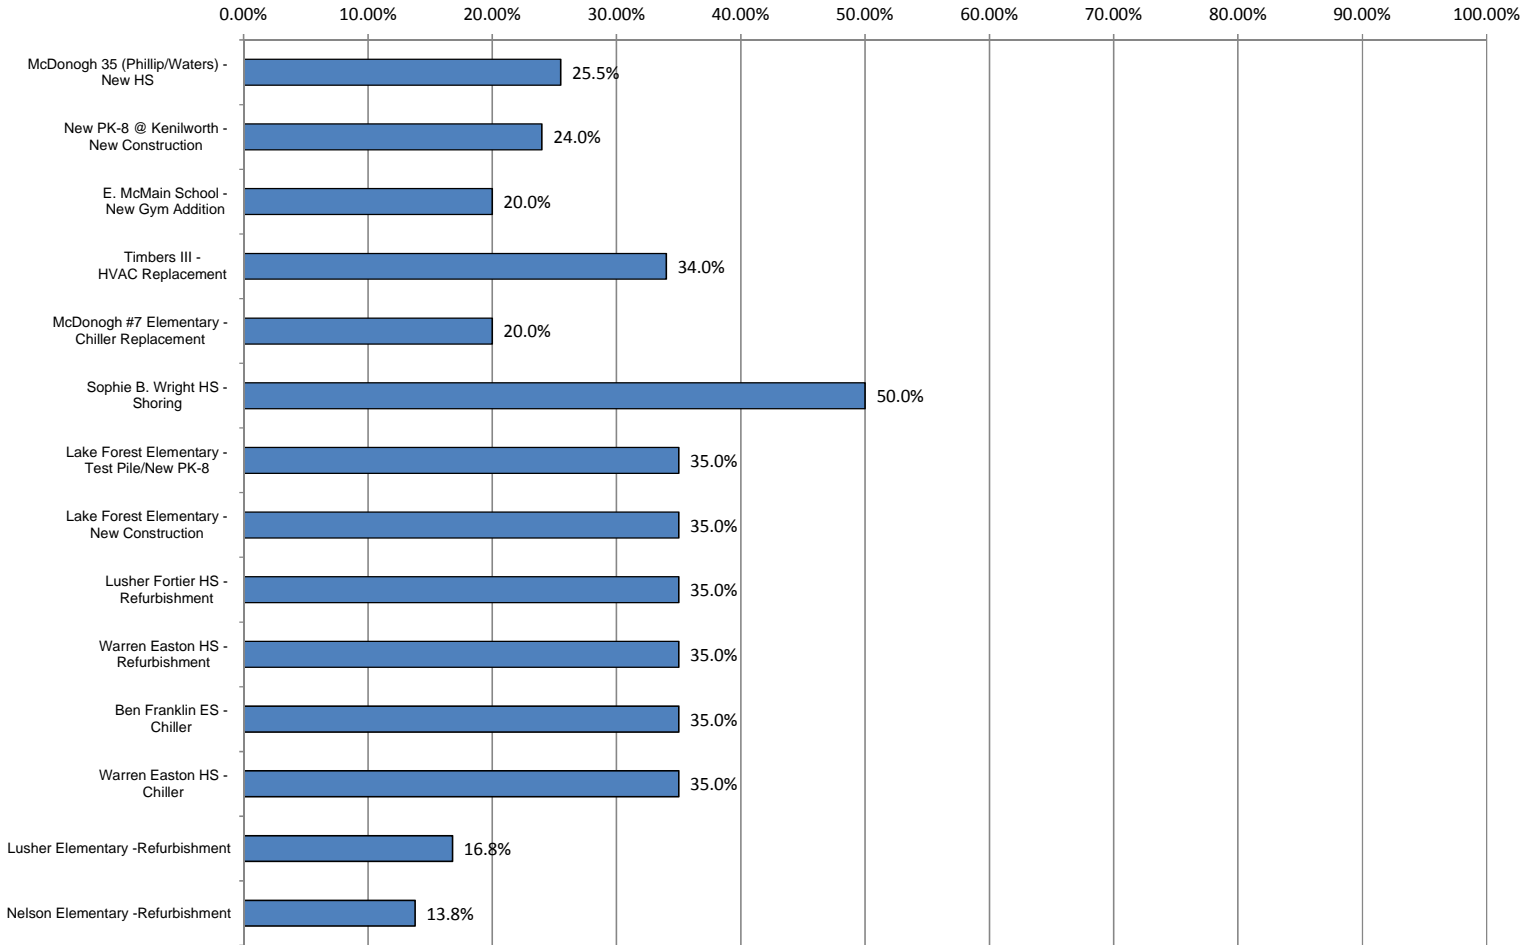

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School ^(RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Steel joist installation is ongoing
- Exterior face brick installation has started
- Installation of ductwork insulation continues
- Exterior waterproofing his ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



Avery Alexander Elementary School ^(RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- Storm drainage installation is ongoing on North side of building
- Roof decking to be finished in April
- Steel erection is 95% complete
- Exterior CMU installation has started
- Soil removal will start mid April

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



George Washington Carver School ^(RSD)

3059 Higgins Blvd., New Orleans, LA 70126 District E Ward 9

Scope of work: New High School, Design Build

Funding Source – FEMA

Contractor – Broadmoor LLC

Construction Phase

- Farnsworth to begin retesting in May
- State Fire Marshal review anticipate April 2016
- Punch list is 90% complete

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- 1st Advertisement - April 27th
- 2nd Advertisement - May 4th
- 3rd Advertisement - May 11th
- Pre-Bid Conference - May 12th
- Bid Opening - June 1st



Paul B. Habans School ^(RSD)

3501 Siene Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

Construction Phase

- Installation of ceilings in conditioned areas continues
- Flooring installation is ongoing
- Millwork installation continues
- Kitchen equipment installation is complete
- Bleacher installation to start mid April

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



New Karr High School CMAR ^(OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center and construction of new high

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – Core Construction

Construction Phase

- Design Development Drawing are due March 22nd
- Demolition Notice to Proceed February 15th

Contractual Substantial Completion – November 2018

Forecasted Substantial Completion – November 2018



John McDonogh High School Renovation CMAR ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Design Phase

- Design Development Documents are due April 26th
- Project Team is assessing existing building conditions

Contractual Substantial Completion – June 2018

Forecasted Substantial Completion – June 2018



Eleanor L. McMain School Gymnasium ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source – FEMA

Architect – Jahncke & Burns Architects

Contractor – Gibbs Construction

Construction Phase

- Architect has started the punch list
- Project is 97% complete
- Installation of gymnasium flooring 90% complete
- Final Commissioning has started

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – August 2016



Ernest "Dutch" Morial Elementary School ^(RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Metal stud installation is ongoing
- Erection of steel joist continues
- Duct work installation is ongoing
- Face brick installation has started

Contractual Substantial Completion – January 2017

Forecasted Substantial Completion – January 2017



Sherwood Forest School ^(RSD)

4801 Maid Marion Drive, New Orleans, LA 70128 District E Ward 9

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

Construction Phase

- Flooring installation is ongoing
- Ceiling installation is nearly complete
- Millwork installation is complete
- Testing and Balance has started

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

Procurement Phase

- Preconstruction conference is April 21st
- Notice to Proceed May 2nd

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Project team is revising foundation package
- Project team continues VE exercise
- Prieur street pricing is being reviewed

Contractual Substantial Completion – April 2018

Forecasted Substantial Completion – April 2018



Sophie B. Wright High School Renovation ^(RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Renovation of existing school and gymnasium addition

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – Core Construction

Construction Phase

- Door hardware installation is ongoing
- Interior finishes are ongoing
- Millwork installation has started
- Lighting installation is ongoing on 1st and 2nd floor
- Site work continues

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



REFURBISHMENTS

Henry Allen Elementary School Refurbishment ^(RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Tuna Construction

Construction Phase

- Substantial Completion March 8th
- Masonry cleaning is 85% complete

Contractual Substantial Completion – February 2016

Forecasted Substantial Completion – March 2016



Benjamin Banneker Elementary School Kitchen Refurbishment ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval
- 100% Construction Documents are anticipated beginning of April

Procurement Phase

- Anticipated 1st Advertisement – April 2016
- Anticipated Bid Opening – May 2016



Agnes L. Bauduit Elementary School Refurbishment ^(RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor - TBD

Procurement Phase

- Bid Opening - March 16th
- Owner is reviewing the bids



Walter L. Cohen High School Kitchen Refurbishment ^(RSD)

3520 Dryades, New Orleans Street, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Owner has placed this project on hold

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



A. D. Crossman School Kitchen Refurbishment ^(RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - CDW Services

Construction Phase

- Dumpster pad work has started

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



Frederick A. Douglass High School Science Lab ^(RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovations to science lab

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – One Construction

Construction Phase

- Lab fume hood install is ongoing
- Add work to install sump pump will extend contract

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – May 2016



William J. Fischer Elementary School Refurbishment ^(RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Perez

Procurement Phase

- Anticipate Notice to Proceed May 25th

Contractual Substantial Completion – February 2017

Forecasted Substantial Completion – February 2017



Fortier (Lusher) High School Refurbishment ^(OPSB)

5624 Freret Street, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation and repairs to the roof, masonry, plaster, windows, exterior doors, canopies, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Core Construction

Construction Phase

- Project is 90% complete
- Modular buildings move is complete
- Phase four work continues, to be complete in March

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



Gaudet Elementary School Refurbishment ^(RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects


Contractor - One Construction

Construction Phase

- Selective demolition has started
- Contractor is working on submittals

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – November 2016

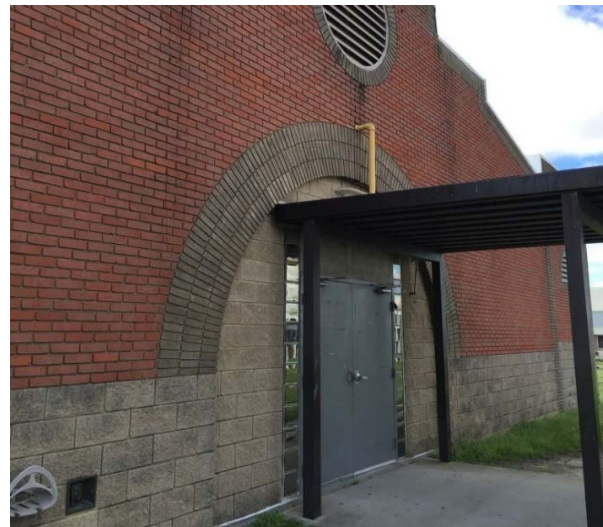

Edgar P. Harney Elementary School Refurbishment ^(RSD)

2503 Willow Street, New Orleans, LA 70113 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Hamp's Construction, LLC

Construction Phase

- Kitchen flooring work is ongoing
- Cooler freezer work is complete

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – April 2016



Andrew Jackson School Refurbishment ^(RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Procurement Phase

- Notice to Proceed is anticipates for May 2nd

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



J. W. Johnson Elementary School Refurbishment ^(RSD)

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Owner has placed this project on hold

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



Lafayette Elementary School Refurbishment ^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- 1st Advertisement - March 9th
- 2nd Advertisement - March 16th
- 3rd Advertisement - March 23th
- Pre-Bid Conference - March 24th
- Bid Opening - April 13th



Laurel Elementary School Refurbishment ^(RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are due end March 3rd

Procurement Phase

- 1st Advertisement - April 6th
- 2nd Advertisement - April 13th
- 3rd Advertisement - April 20th
- Pre-Bid Conference - April 21st
- Bid Opening - May 18th



Live Oak Elementary School Refurbishment ^(RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Procurement Phase

- Abatement has started on third floor

Contractual Substantial Completion – July 2017

Forecasted Substantial Completion – July 2017



Lusher Elementary School Refurbishment ^(OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source – FEMA

Architect – Meyer Engineers, LTD.

Contractor - Dynamic

Construction Phase

- Chiller replacement is ongoing
- Structural erection is ongoing
- Elevator shaft work is ongoing

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – August 2016



Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- A&E is adding HVAC scope to job
- Bid Documents are anticipate in June

Procurement Phase

- Anticipated 1st Advertisement – June 2016
- Anticipated Bid Opening – July 2016



McDonogh #28 School Refurbishment ^(RSD)

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – SCNZ Architects, LLC

Contractor - Tuna Construction

Construction Phase

- Project is 95% complete
- Punch list work has started

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – May 2016



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- A&E to finish bid documents end of March

Procurement Phase

- Anticipated 1st Advertisement – May 2016
- Anticipated Bid Opening – June 2016



Nelson Elementary School Refurbishment ^(OPSB)

3121 St. Bernard Avenue, New Orleans, LA 70119 District D Ward 7

Scope of work: Renovation and repairs to the roof, masonry, windows, exterior doors, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – Harry Baker Smith Architects

Contractor - Blanchard Mechanical Contractor

Construction Phase

- Punch list is complete
- Project is substantially complete

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



Rosenwald Elementary School Refurbishment ^(RSD)

6501 Berkley Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - One Construction

Construction Phase

- Install of new HVAC controls is 85% complete
- State Fire Marshal review is complete
- Reroofing of the band room is 95% complete

Contractual Substantial Completion – February 2016

Forecasted Substantial Completion – March 2016



Village de l'Est Elementary School Refurbishment ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CBDG

Architect – Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

Construction Phase

- HVAC controls is 95% complete
- Test and Balance is ongoing

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – April 2016



Albert Wicker School Kitchen Refurbishment ^(RSD)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Owner has placed this project on hold

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



OTHER PROJECTS

Eleanor L. McMain School Roof Replacement ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Roof replacement

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – Rycars Construction

Construction Phase

- Installation of resin flashing is ongoing
- Stucco repair work continues
- Anticipate Substantial Completion end of April

Contractual Substantial Completion – June 2016

Forecasted Substantial Completion – June 2016



Eleanor L. McMain School Maintenance Upgrades ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work.

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – Tuna Construction

Procurement Phase

- Door repairs ongoing
- Kitchen work is complete
- Restroom work continues
- HVAC replacement is ongoing

Contractual Substantial Completion – June 2016

Forecasted Substantial Completion – June 2016



Building Automation System Integration At Recovery School

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview ES

Funding Source – FEMA

Architect – Moses Engineers

Contractor – Synergy Building Solutions, Inc.

Construction Phase

- Moses is reviewing training docs and O&M manuals

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – June 2016



MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

Demolition of Modular Buildings at Abramson and Carver ^(RSD)

5552 Read Boulevard and 3059 Higgins Boulevard, New Orleans, LA

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters, Inc.

Construction Phase

- Notice to Proceed March 15th
- Trailers being removed from Abramson site

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – September 2016



Demolition of Modular Buildings at Livingston ^(RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – Concrete Busters of Louisiana

Construction Phase

- Pre-Construction meeting was held March 15th
- Notice to Proceed March 21st

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – September 2016



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
6	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
7	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
8	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
9	Alfred Lawless Senior ^(RSD)	12/18/2015
10	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
11	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
12	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
13	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
14	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
15	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
16	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
17	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
18	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
19	Augustine Elementary School Roof ^(RSD)	04/13/2012
20	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
21	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
22	Bell JH Shoring ^(RSD)	06/28/2011
23	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
24	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
25	Bienville Elementary School Demolition ^(RSD)	05/04/2009
26	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
27	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
28	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
29	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
30	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
31	Charles J. Colton Elementary School ^(RSD)	05/23/2013
32	Charles R. Drew Elementary School ^(RSD)	04/17/2015
33	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
34	Cohen High School Health Clinic ^(RSD)	12/24/2008
35	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
36	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
37	Douglass High School Under Floor Utilities ^(RSD)	
38	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
39	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
40	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
41	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
42	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
43	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011

44	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
45	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
46	Edna Karr High School - Assessment ^(OPSB)	
47	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
48	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
49	New Edward Hynes School ^(OPSB)	02/06/2012
50	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
51	Edward Livingston High School ^(RSD)	01/05/2015
52	Eleanor L. McMMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
53	Eleanor L. McMMain School Clinic ^(OPSB)	07/24/2013
54	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
55	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
56	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
57	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
58	Francis W. Gregory Demolition ^(RSD)	12/21/2011
59	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
60	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
61	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
62	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
63	George Mondy Elementary School Mothball ^(RSD)	
64	George Washington Carver High School Demolition ^(RSD)	08/24/2011
65	Greater St. Stephens School ^(OPSB)	03/18/2013
66	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
67	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
68	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
69	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
70	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
71	Holy Cross Modular Relocation ^(RSD)	12/14/2010
72	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
73	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
74	James Derham Demolition ^(RSD)	02/23/2012
75	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
76	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
77	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
78	John Dibert Elementary School Roof ^(RSD)	08/20/2010
79	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
80	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
81	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
82	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
83	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
84	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
85	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
86	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
87	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
88	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
89	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012

90	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
91	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
92	Lake Area Landry Demolition ^(RSD)	05/01/2008
93	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
94	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
95	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
96	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
97	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
98	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
99	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
100	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
101	Live Oak Elementary School Roof ^(RSD)	08/04/2011
102	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
103	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
104	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
105	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
106	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
107	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
108	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
109	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
110	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
111	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
112	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
113	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
114	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
115	McDonogh #7 High School Repairs ^(OPSB)	
116	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
117	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
118	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
119	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
120	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
121	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
122	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
123	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
124	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
125	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
126	Modular Campuses Close Outs ^(RSD)	
127	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
128	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010
129	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
130	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
131	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
132	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
133	New Carter G. Woodson School ^(RSD)	09/14/2012
134	New Fannie C. Williams School ^(RSD)	08/24/2012

135	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
136	New L.B. Landry High School ^(RSD)	06/30/2010
137	New Lake Area High School ^(RSD)	12/28/2009
138	New Lawrence D. Crocker School ^(RSD)	04/29/2013
139	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
140	New Parkview School ^(RSD)	10/12/2012
141	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
142	New William Frantz Elementary School ^(RSD)	
143	New Orleans High School Signature Center Study ^(RSD)	
144	Oretha C. Haley Demo ^(RSD)	05/07/2012
145	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
146	Parkview Elementary School Demolition ^(RSD)	08/06/2009
147	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
148	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
149	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
150	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
151	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
152	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
153	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
154	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
155	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
156	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
157	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
158	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
159	Schaumburg Chillers ^(RSD)	11/14/2008
160	Schwarz Alternative Repairs ^(RSD)	07/14/2009
161	Schwarz Alternative Modularity Demolition ^(RSD)	04/02/2015
162	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
163	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
164	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
165	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
166	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
167	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
168	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
169	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
170	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
171	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
172	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
173	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
174	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
175	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
176	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
177	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
178	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
179	Timbers HVAC ^(OPSB)	09/11/2013
180	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015

181	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
182	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
183	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
184	Valena C. Jones Elementary School ^(RSD)	01/10/2013
185	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
186	Warren Easton High School Renovation ^(OPSB)	12/15/2015
187	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
188	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
189	New William J. Guste Elementary School ^(RSD)	10/06/2008
190	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
191	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
192	William Frantz Elementary School Roof ^(RSD)	08/12/2010
