Superintendent's Report May, 2015



Dr. Henderson Lewis Jr.Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District



Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

| TABLE OF CONTENTS | 1 |
|--|----|
| FINANCIAL OVERVIEW | 4 |
| COMMUNITY MEETINGS | 5 |
| BID OPENINGS | 6 |
| DBE OVERVIEW MONTHLY SUMMARY | 7 |
| NEW & MAJOR RENOVATION | 13 |
| Ray Abrams Elementary School (RSD) | 13 |
| Avery Alexander Elementary School (RSD) | 13 |
| James Audubon School (OPSB) | 13 |
| Stuart R. Bradley School (RSD) | 14 |
| George Washington Carver School (RSD) | 14 |
| Paul L. Dunbar School (RSD) | 14 |
| Benjamin Franklin Elementary School Renovation (OPSB) | 15 |
| Paul B. Habans School (RSD) | 15 |
| New Karr High School, CMAR (OPSB) | 15 |
| New PK-8 School at North Kenilworth Park at Curran Site (OPSB) | 16 |
| Lake Forest PK-8 at the Greater St. Stephens Site (OPSB) | 16 |
| Alfred Lawless School (RSD) | 16 |
| John McDonogh High School Selective Demolition (RSD) | 17 |
| John McDonogh High School Renovation (RSD) | 17 |
| McDonogh #35 School (Phillip/Waters Site) (OPSB) | 17 |
| McDonogh #42 Elementary School (RSD) | 18 |
| Eleanor L. McMain School Gymnasium (OPSB) | 18 |
| Ernest "Dutch" Morial Elementary School (RSD) | 18 |
| Small New Orleans East High School at Abramson (RSD) | 19 |
| Sherwood Forest School (RSD) | 19 |
| Harriet R. Tubman Elementary School Renovation (RSD) | 19 |
| Booker T. Washington School Environmental Remediation (RSD) | 20 |
| Booker T. Washington School (RSD) | 20 |
| Sophie B. Wright School (RSD) | 20 |

| REFURBISHMENTS | 21 |
|--|----|
| Henry Allen Elementary School Refurbishment (RSD) | 21 |
| Henry Allen Elementary School Kitchen Refurbishment (RSD) | 21 |
| Benjamin Banneker Elementary Kitchen School Refurbishment (RSD) | 21 |
| Agnes L. Bauduit Elementary School Refurbishment (RSD) | 22 |
| Bethune and Tureaud Elementary School Refurbishment (OPSB) | 22 |
| Walter L. Cohen High School Kitchen Refurbishment (RSD) | 22 |
| A. D. Crossman School Kitchen Refurbishment (RSD) | 23 |
| Frederick A. Douglass High School Science Lab (RSD) | 23 |
| Warren Easton School Refurbishment (OPSB) | 23 |
| Dwight D. Eisenhower Elementary School Refurbishment (RSD) | 24 |
| Dwight D. Eisenhower Elementary School Kitchen Refurbishment (RSD) | 24 |
| William J. Fischer Elementary Refurbishment (RSD) | 24 |
| Fortier (Lusher) High School Refurbishment (OPSB) | 25 |
| Gaudet Elementary School Refurbishment (RSD) | 25 |
| Gentilly Terrace School Refurbishment (RSD) | 25 |
| Samuel J. Green Elementary School Refurbishment (RSD) | 26 |
| Edgar P. Harney Elementary School Refurbishment (RSD) | 26 |
| Andrew Jackson School Refurbishment (RSD) | 26 |
| J. W. Johnson Elementary School Refurbishment (RSD) | 27 |
| Dr. Martin L. King Elementary School Kitchen Refurbishment (RSD) | 27 |
| Lafayette Elementary School Refurbishment (RSD) | 27 |
| Laurel Elementary School Refurbishment (RSD) | 28 |
| Live Oak Elementary School Refurbishment (RSD) | 28 |
| Lusher Elementary School Refurbishment (OPSB) | 28 |
| Thurgood Marshall Elementary School Refurbishment (RSD) | 29 |
| McDonogh #28 School Refurbishment (RSD) | 29 |
| McDonogh #32 School Refurbishment (RSD) | 29 |
| Nelson Elementary School Refurbishment (OPSB) | 30 |
| Sarah T. Reed School Refurbishment (RSD) | 30 |
| Sarah T. Reed School Kitchen Refurbishment (RSD) | 30 |
| Rosenwald Elementary School Refurbishment (RSD) | 31 |
| Henry C. Schaumburg Elementary School Refurbishment (RSD) | 31 |
| Village de l'Est Elementary School Refurbishment (RSD) | 31 |
| Albert Wicker School Kitchen Refurbishment (RSD) | 32 |
| Sylvanie F. Williams School Refurbishment (RSD) | 32 |

2

| OTHER PROJECTS | 33 |
|---|----|
| Eleanor L. McMain School Roof Replacement (OPSB) | 33 |
| Eleanor L. McMain School Maintenance Upgrades (OPSB) | 33 |
| Timbers III - Building Controls (OPSB) | 33 |
| Building Automation System Integration At Recovery School District Central And Remote Offices (RSD) | 34 |
| MOTHBALL OR SAFE & SECURE OF SELECTED SCHOOLS | 35 |
| Demolition of Modular Buildings Gregory and Abramson (RSD) | 35 |
| Demolition of Modulars at Livingston (RSD) | 35 |
| COMPLETED PROJECTS | 36 |

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$585 million in open contracts for the capital program after issuing \$2.5 million in new contracts and \$120 thousand in change orders and amendments in May. In addition, the total change orders to date, \$5.8 million, account for approximately one percent (1.06%) of the total open construction contracts. RSD anticipates issuing approximately \$4 million in construction contracts/change orders, and \$1 million in professional service contracts/amendments in June.



The OPSB has \$216 million in open contracts for the capital program after issuing \$4.3 million in new contracts and \$394 thousand in change orders and amendments in May. In addition, the total change orders to date, \$3.5 million, account for approximately two percent (1.90%) of the total open construction contracts. OPSB anticipates issuing approximately no construction contracts/change orders and \$752 thousand in professional service contracts/amendments in June.

Community Meetings



Future Community Meetings

June 15, 2015

Ground Breaking for Ray Abrams Elementary School 6519 Virgilian Street New Orleans, LA 70126

June 18, 2015

Ground Breaking for Ernest "Dutch" Morial Elementary School 7701 Grant Street New Orleans, LA 70126

August 18, 2015

Ribbon Cutting for Charles R. Drew Elementary School 3819 St. Claude Avenue New Orleans, LA 70117

August 19, 2015

Ribbon Cutting for McDonogh 42 Elementary School 1651 North Tonti Street New Orleans, LA 70119

August 25, 2015

Ribbon Cutting for Stuart R. Bradley Elementary School 2401 Humanity Street New Orleans, LA 70122

August 26, 2015

Ribbon Cutting for New 2 Section Elementary School @ Paul L Dunbar School 9330 Forshey Street New Orleans, LA 70118

August 27, 2015

Ribbon Cutting for Edward R. Livingston School 7301 Dwyer Road New Orleans, LA 70126

5

Bid Openings

No Bids were opened in May, 2015

The following projects are scheduled to bid in the next 60 days:

June 10, 2015

• McMain High School New Roof

July 8, 2015

• McMain High School Maintenance Upgrades

July 29, 2015

• Laurel School Refurbishment

6

Disadvantaged Business Enterprises (DBE) Monthly Summary





New & Renovations:

DBE Contractors secured subcontracts on 19 projects as of May 31, 2015. The DBE subcontracts value is \$69,304,090 of the \$343,291,077 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 35 projects as of May 31, 2015. The DBE subcontracts value is \$10,346,378 of the \$36,184,670 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of May 31, 2015. The DBE subcontracts value is \$34,691,592 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$488,613,304

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 12 projects as of May 31, 2015. The DBE subcontracts value is \$54,086,557 of the \$199,371,360 total of awarded contracts.

Stabilization/Demolition/Mothballing:


7

DBE Contractors secured subcontracts on 2 projects as of May 31, 2015. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$200,274,359

^{*} DBE provisions were included in projects bid after June 30, 2012


Current RSD Program DBE Participation

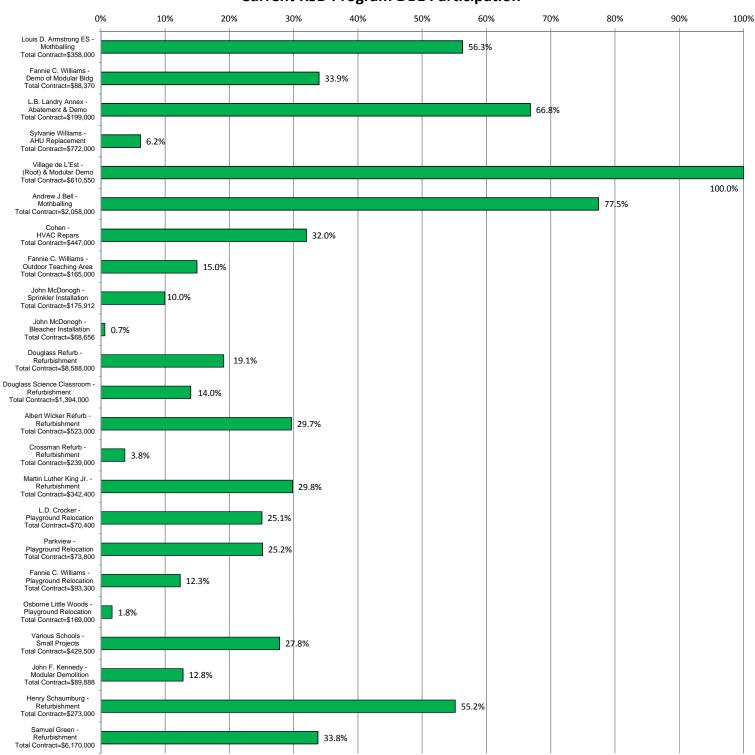

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Current RSD Program DBE Participation

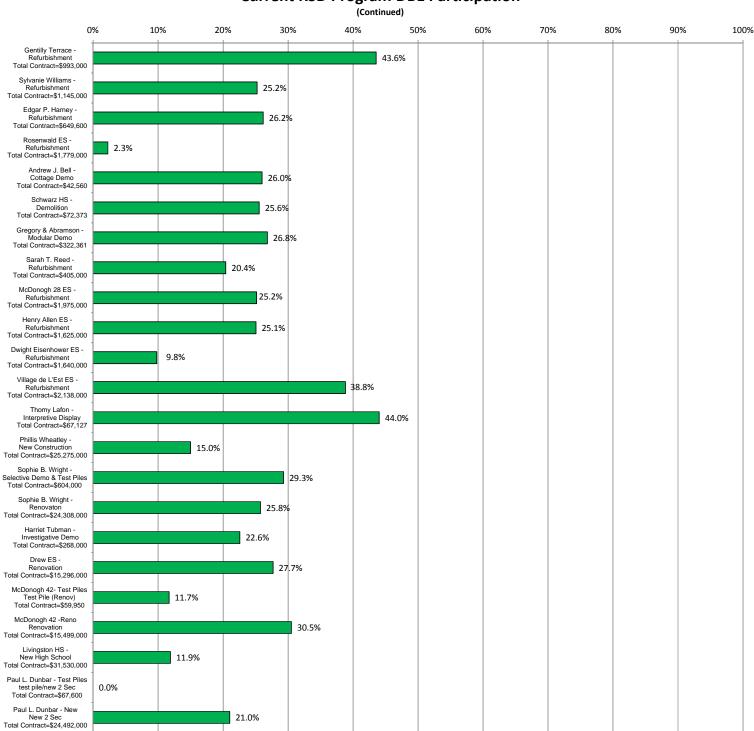


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Current RSD Program DBE Participation


(Continued)

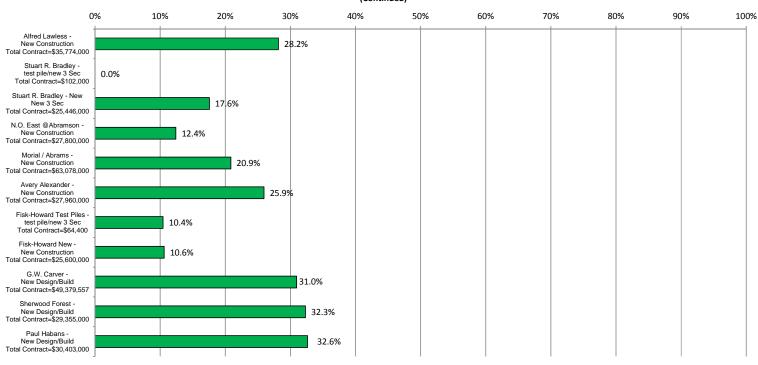

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

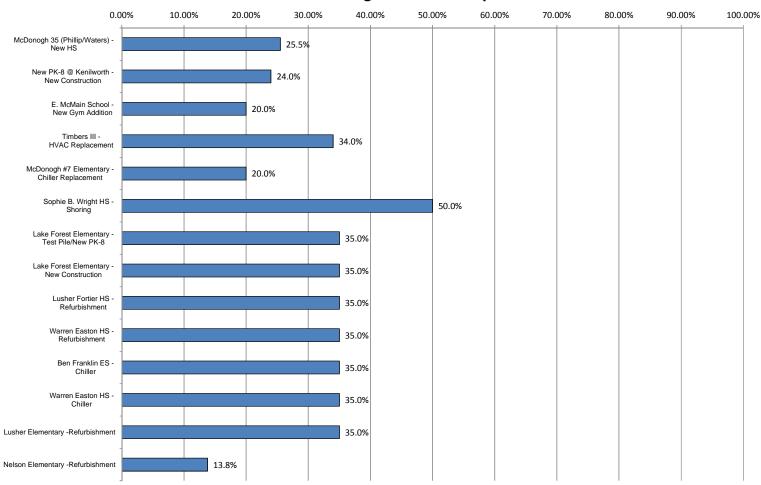

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation - Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School (RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect - Waggonner & Ball Architects, APC

Contractor – McDonnel Group, LLC

Construction Phase

- · Notice to Proceed May 5th
- · Site clearing is complete
- Pile Driving has begun
- · Ground Breaking June 15th

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – May 2017



Avery Alexander Elementary School (RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect – Sizeler Thompson Brown Architects

Contractor - Core Construction

Construction Phase

- Notice to Proceed May 15th
- Soil excavation has started, additional excavation will be required

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – May 2017



James Audubon School (OPSB)

428 Broadway Avenue, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation of existing elementary school and new addition

Funding Source – FEMA

Architect - Blitch/Knevel Architects

Contractor – FHP Tectonics Corporation

Construction Phase

- · Reinstall of exterior curtain wall continues
- · Exterior cleaning and painting is ongoing
- Terrazzo installation is ongoing in the addition

Contractual Substantial Completion – September 2013

Forecasted Substantial Completion – July 2015

School Ready for Occupancy – July 2015



Stuart R. Bradley School (RSD)

2401 Humanity Street, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source - FEMA

Architect – Sizeler Thompson Brown Architects

Contractor - Landis Construction Co.

Construction Phase

- Anticipated Substantial Completion June
- Landscaping is ongoing
- Rough cleaning is underway
- Punch list work continues

Contractual Substantial Completion – June 2015 Forecasted Substantial Completion – June 2015 School Ready for Occupancy – August 2015



George Washington Carver School (RSD)

3059 Higgins Blvd., New Orleans, LA 70126 District E Ward 9

Scope of work: New High School, Design Build

Funding Source – FEMA Contractor – Broadmoor LLC

Construction Phase

- Insulation and gypsum board installation is ongoing
- · MEP above ceilings is ongoing
- · Installation of glazing at windows is ongoing
- Precast panels installation continues at Convocation Center
- · Roofing installation continues on classroom building

Contractual Substantial Completion – March 2016 Forecasted Substantial Completion – March 2016



Paul L. Dunbar School (RSD)

9330 Forshey Street, New Orleans, LA 70125 District A Ward 17

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect – Chenevert Architects LLC Contractor – McDonnel Group, LLC

Construction Phase

- Substantial Completion June 1st
- Punch list work has started

Contractual Substantial Completion – June 2015 Forecasted Substantial Completion – June 2015 School Ready for Occupancy – August 2015



Status Date: 31 May 2015

Benjamin Franklin Elementary School Renovation (OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA Architect – N-Y Associates, Inc.

Contractor - TBD Design Phase - CD

- 100% Construction Documents are finished
- The Owner is evaluating the refurbishment or replacement of the windows

Procurement Phase

- Anticipated 1st Advertisement TBD
- Anticipated Bid Opening TBD



Paul B. Habans School (RSD)

3501 Siene Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: New School, Design Build

Funding Source – FEMA Architect – Grace Hebert Contractor – Core Construction Construction Phase

- Transformer and dumpster pad are poured
- Underground MEP work is ongoing
- · Kitchen slab has been poured
- Gymnasium steel erection continues

Contractual Substantial Completion – May 2016 Forecasted Substantial Completion – May 2016



New Karr High School CMAR (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center and construction of new high

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor – TBD <u>Design Phase - CD</u>

- SOQ is being reviewed by committee
- Anticipated Announcement August 2015



New PK-8 School at North Kenilworth Park at Curran Site (OPSB)

8500 Curran Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect - Mathes Brierre Architects

Contractor – Woodrow Wilson Construction Company, Inc.

Construction Phase

- HVAC startup anticipated early June
- VCT flooring installation continues
- · Installation of ceiling grid is ongoing
- Installation of glazing continues

Contractual Substantial Completion – September 2014 Forecasted Substantial Completion – July 2015 School Ready for Occupancy – July 2015



Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)

11110 Lake Forest Boulevard 70128 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source - FEMA

Architect – Imre Hegedus & Associates Architects

Contractor – The McDonnel Group

Construction Phase

- · Installation of MEP branch line is ongoing
- · Installation of gypsum board is ongoing
- Window installation continues
- Installation of masonry brick is 75% complete
- Site work is 30% complete, pouring of parking has started

Contractual Substantial Completion – July 2015 Forecasted Substantial Completion – September 2015 School Ready for Occupancy – October 2015



Alfred Lawless School (RSD)

5300 Law Street, New Orleans, LA 70117 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor - Core Construction

Construction Phase

- · Interior painting continues
- Exterior metal wall panels 95% complete
- Flooring installation is ongoing
- Elevator installation continues
- HVAC start up beginning of June
- Site work is ongoing

Contractual Substantial Completion – November 2015 Forecasted Substantial Completion – November 2015 School Ready for Occupancy – January 2016



Status Date: 31 May 2015

John McDonogh High School Selective Demolition (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect – VergesRome Architects, APAC Contractor - Zimmer-Eschette Services

Construction Phase

- Notice to Proceed May 11th
- · Selective demolition of walls is ongoing

Contractual Substantial Completion – October 2015

Forecasted Substantial Completion – October 2015



John McDonogh High School Renovation (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor - TBD Design Phase - SD

- · Short list was announced May 1st
- · Interviews were May 4th
- Successful Proposal will be announced June 2015



McDonogh #35 School (Phillip/Waters Site) (OPSB)

1200 Senate Street, New Orleans, LA 70122 District D Ward 7

Scope of work: New High School Funding Source – FEMA Architect – Sizeler, Thompson, Brown Architects

Architect – Sizeler, Monipson, Drown Architects

Contractor - Citadel Builders, LLC

Construction Phase

- Installation of MEP nearly complete
- Brick masonry and window installation is 95% complete
- · Drywall installation is finished
- Metal panel installation is 95% complete

Contractual Substantial Completion - May 2015

Forecasted Substantial Completion – July 2015

School Ready for Occupancy – July 2015



Status Date: 31 May 2015

McDonogh #42 Elementary School (RSD)

1651 North Tonti Street, New Orleans, LA 70119 District A Ward 7

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA, QSCB, NMTC, Insurance Proceeds

Architect – Eskew+Dumez+Ripple Contractor – Core Construction

Construction Phase

- · Punch List work is ongoing
- Substantial Completion May 28th

Contractual Substantial Completion – June 2015 Forecasted Substantial Completion – May 2015 School Ready for Occupancy – June 2015



Eleanor L. McMain School Gymnasium (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source – FEMA

Architect – Jahncke & Burns Architects

Contractor – Gibbs Construction

Construction Phase

Installation of roofing is ongoing
 Contractual Substantial Completion – April 2015
 Forecasted Substantial Completion – January 2016

Ernest "Dutch" Morial Elementary School (RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect - Waggonner & Ball Architects, APC

Contractor – McDonnel Group, LLC

Construction Phase

- · Notice to Proceed May 5th
- · Site clearing is complete
- · Pile driving has started
- · Ground Breaking June 18th

Contractual Substantial Completion – January 2017 Forecasted Substantial Completion – January 2017



Small New Orleans East High School at Abramson (RSD)

5552 Read Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New High School

Funding Source - FEMA

Architect – RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

Construction Phase

- Exterior metal wall panels 60% complete
- · Final site work has begun
- · Door hardware installation is ongoing
- Installation of interior finishes continues

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – September 2015

School Ready for Occupancy – October 2015



Sherwood Forest School (RSD)

4801 Maid Marion Drive, New Orleans, LA 70128 District E Ward 9

Scope of work: New School, Design Build

Funding Source – FEMA Architect - Grace Hebert Contractor - Core Construction

Construction Phase

- · Classroom slab has been poured
- · MEP rough in has started
- · CMU installation has begun
- Structural steel erection on the gymnasium has started

Contractual Substantial Completion – May 2016 Forecasted Substantial Completion - May 2016



Harriet R. Tubman Elementary School Renovation

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

• Plan modifications will extend the completion of 100% Construction Documents until July

Procurement Phase

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



Booker T. Washington School Environmental Remediation (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The remediation of the site

Funding Source - FEMA

Architect – Hewitt-Washington & Associates

Contractor – SEMS, Inc Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed July 2015



Booker T. Washington School (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source - FEMA

Architect – Hewitt-Washington & Associates

Contractor - TBD

Design Phase - SD

Successful Proposal will be announced June 2015



Sophie B. Wright High School Renovation (RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Renovation of existing school and gymnasium addition

Funding Source - FEMA

Architect - Waggonner & Ball Architects, APC

Contractor – Core Construction

Construction Phase

- MEP rough-in ongoing
- Steel for auditorium is on site
- Window refurbishment continues
- · Floor repairs are ongoing

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



REFURBISHMENTS

Henry Allen Elementary School Refurbishment (RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - Tuna Construction

Construction Phase

- Window refurbishment has started
- Submittals are being processed

Contractual Substantial Completion – February 2016 Forecasted Substantial Completion – February 2016



Henry Allen Elementary School Kitchen Refurbishment (RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services Construction Phase

- Pre-Construction Meeting was held May 28th
- · Notice to Proceed June 1st

Contractual Substantial Completion – November 2016 Forecasted Substantial Completion – November 2016



Benjamin Banneker Elementary School Kitchen Refurbishment (RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – SCNZ Architects Contractor - TBD

Contractor - TBD Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
 - Anticipated 1st Advertisement January 2016
 - Anticipated Bid Opening March 2016



Agnes L. Bauduit Elementary School Refurbishment (RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect - Duplantis Design Group, PC

Contractor - TBD Design Phase - CD

- Bid Documents are due June 2015
- $\boldsymbol{\cdot}$ Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement July 2015
- Anticipated Bid Opening August 2015



Bethune and Tureaud Elementary School Refurbishment (OPSB)

4040 Eagle Street & 2021 Pauger Street, New Orleans, LA District A Ward 3 & District D Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - Chenevert Architects LLC

Contractor - TBD

Design Phase - CD

• 100% Construction Documents were received May 26th

Procurement Phase

- Anticipated 1st Advertisement July 2015
- Anticipated Bid Opening August 2015



Walter L. Cohen High School Kitchen Refurbishment (RSD)

3520 Dryades, New Orleans Street, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source - FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

Procurement schedule has been adjusted pending FEMA funding approval
 Procurement Phase

Procurement Phase

- Anticipated 1st Advertisement January 2016
- Anticipated Bid Opening March 2016



A. D. Crossman School Kitchen Refurbishment (RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – SCNZ Architects

Contractor - TBD Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
 - Anticipated 1st Advertisement July 2015
 - Anticipated Bid Opening August 15th



Frederick A. Douglass High School Science Lab (RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovations to science lab

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor – One Construction

Construction Phase

Notice to Proceed - May 26th

Contractual Substantial Completion – November 2015 Forecasted Substantial Completion – November 2015

Warren Easton School (OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Refurbishment of existing high school, including but not limited to structure, doors, masonry walls and roof

Funding Source – FEMA

Architect - Chenevert Architects LLC

Contractor - Tuna Construction

Construction Phase

- Rooms 322 and 229A are near complete
- · Restroom renovations continues
- Exterior tuck pointing continues
- Sprinkler work at the Gymnasium will continue during summer break

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



Dwight D. Eisenhower Elementary School Refurbishment (RSD)

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Harry Baker Smith Architects II, PLLC

Contractor - CDW Construction

Construction Phase

- Demolition of roof equipment has started
- · Canopy repairs have started

Contractual Substantial Completion – January 2016 Forecasted Substantial Completion – January 2016



Dwight D. Eisenhower Elementary School Kitchen Refurbishment

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services

Construction Phase

- Pre-Construction Meeting was held May 28th
- · Notice to Proceed June 1st

Contractual Substantial Completion – November 2016 Forecasted Substantial Completion – November 2016



William J. Fischer Elementary School Refurbishment (RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA, CDBG

Architect - SCNZ Architects

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



Fortier (Lusher) High School Refurbishment (OPSB)

5624 Freret Street, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation and repairs to the roof, masonry, plaster, windows, exterior doors, canopies, mechanical systems, and electrical systems.

Funding Source – FEMA Architect – SCNZ Architects Contractor - Core Construction Construction Phase

- Phase one is 90% complete
- Phase #2 has started
- Painting of walls and doors continues
- Installation of new door and hardware continues
- Repairs to exterior brick work is ongoing

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



Gaudet Elementary School Refurbishment (RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 100% Construction Documents were received April 1st
 - \bullet Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



Gentilly Terrace School Refurbishment (RSD)

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source - FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - One Construction

Construction Phase

- · Substantial Completion May 26th
- Contractor is working on punch list items
- The contract will be extended due to added kitchen scope

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



Samuel J. Green Elementary School Refurbishment (RSD)

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect – VergesRome Architects, APAC Contractor - Hernandez Consulting, LLC

Construction Phase

- Installation of gypsum board at restrooms continues
- Window replacement is ongoing
- Electrical and plumbing renovations continues
- · Exterior brick repairs is ongoing
- Roof repairs continues

Contractual Substantial Completion – August 2015 Forecasted Substantial Completion – August 2015



Edgar P. Harney Elementary School Refurbishment (RSD)

2503 Willow Street, New Orleans, LA 70113 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor - Hamp's Construction, LLC

Construction Phase

- Demolition of dumpster area is complete
- Forming of new dumpster pad has started
- · Electrical work to start in June

Contractual Substantial Completion - May 2015

Forecasted Substantial Completion – September 2015



Andrew Jackson School Refurbishment (RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source - FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- Kitchen scope was added to the refurbishment project
- Anticipated 1st Advertisement August 2015
- Anticipated Bid Opening September 2015



Status Date: 31 May 2015

J. W. Johnson Elementary School Refurbishment (RSD)

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
 - Anticipated 1st Advertisement September 2015
 - Anticipated Bid Opening October 2015



Dr. Martin L. King Elementary School Kitchen Refurbishment (RSD)

1617 Caffin Avenue, New Orleans, LA 70117 District E Ward 9

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Construction Phase

- Pre-Construction Meeting was held May 28th
- · Notice to Proceed June 1st

Contractual Substantial Completion – November 2016 Forecasted Substantial Completion – November 2016



Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval <u>Procurement Phase</u>
 - Anticipated 1st Advertisement June 2015
 - Anticipated Bid Opening August 2015



Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect - Mahlum Scairono Martinez JV

Contractor - TBD Procurement Phase

- 1st Advertisement June 24th
- 2nd Advertisement July 1st
- 3rd Advertisement July 8th
- Pre-Bid Conference July 9th
- · Bid Opening July 29th



Live Oak Elementary School Refurbishment (RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase
 - Anticipated 1st Advertisement July 2015
 - Anticipated Bid Opening August 2015



Lusher Elementary School Refurbishment (OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows,

exterior doors, and restroom accessibility

Funding Source – FEMA

Architect - Meyer Engineers, LTD.

Contractor - Dynamic

Construction Phase

- · Notice to Proceed May 14th
- · Interior demolition has started

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – November 2016



Thurgood Marshall Elementary School Refurbishment (RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - TBD Design Phase - CD

• 100% Construction Documents are due June 9th

Procurement Phase

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



McDonogh #28 School Refurbishment (RSD)

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source - FEMA

Architect - SCNZ Architects, LLC

Contractor - Tuna Construction

Construction Phase

- Kitchen scope to be added to the refurbishment project
- · Window removal and abatement has started
- Demolition of roofing continues

Contractual Substantial Completion - March 2016

Forecasted Substantial Completion – March 2016



McDonogh #32 School Refurbishment (RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect - Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase - CD

- Bid Documents are due August 18th
- · Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement September 2015
- Anticipated Bid Opening October 2015



Nelson Elementary School Refurbishment (OPSB)

3121 St. Bernard Avenue, New Orleans, LA 70119 District D Ward 7

Scope of work: Renovation and repairs to the roof, masonry, windows, exterior doors, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – Harry Baker Smith Architects Contractor - Blanchard Mechanical Contractor

Construction Phase

Anticipated Notice to Proceed - June 1st



Sarah T. Reed School Refurbishment (RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Byron J. Stewart & Associates, APC Architects & Planners

Contractor - Tuna Construction

Construction Phase

- Window installation is 35% complete
- · Chilled water and heat pumps are installed
- Sidewalk and drainage are complete

Contractual Substantial Completion – December 2015

Forecasted Substantial Completion – December 2015



Sarah T. Reed School Kitchen Refurbishment (RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services Construction Phase

Pre-Construction Meeting was held May 28th

Notice to Proceed - June 1st

Contractual Substantial Completion – November 2016 Forecasted Substantial Completion – November 2016



Rosenwald Elementary School Refurbishment (RSD)

6501 Berkley Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Byron J. Stewart & Associates, APC Architects & Planners

Contractor - One Construction

Construction Phase · Contractor has mobilized Demolition has started Contractual Substantial Completion – January 2016 Forecasted Substantial Completion – January 2016

31

Henry C. Schaumburg Elementary School (RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA Architect - N-Y Associates, Inc

Contractor - Hernandez Consulting, LLC

Construction Phase

- Tuck pointing of brick continues
- · Roof repairs are ongoing

Contractual Substantial Completion – July 2015 Forecasted Substantial Completion – July 2015



Village de l'Est Elementary School Refurbishment (RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA, CBDG

Architect - Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

Construction Phase

- · Demolition of dumpster pad has started
- · Removal of ceiling tile is ongoing
- · Painting of classrooms has started
- · Cleaning of exterior has started

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – April 2016



Albert Wicker School Kitchen Refurbishment (RSD)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – SCNZ Architects

Contractor - TBD Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval <u>Procurement Phase</u>
 - Anticipated 1st Advertisement January 2016
 - Anticipated Bid Opening March 2016



Sylvanie F. Williams School Refurbishment (RSD)

3127 Martin Luther King Jr. Boulevard, New Orleans, LA 70125 District B Ward 2 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Hamps Construction Phase

- · Roof work is Complete
- Stucco work is 50% complete
- Dumpster enclosure is 80% complete

Contractual Substantial Completion – August 2015 Forecasted Substantial Completion – August 2015



OTHER PROJECTS

Eleanor L. McMain School Roof Replacement (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Roof replacement

Funding Source – General Fund & Harrah's

Architect - Duplantis Design Group

Contractor – TBD

Procurement Phase

- 1st Advertisement May 6th
- 2nd Advertisement May 13th
- 3rd Advertisement May 20th
- · Pre-Bid Conference May 21st
- · Bid Opening June 10th




5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work. Funding Source – General Fund & Harrah's Architect – Duplantis Design Group

Contractor - TBD

Procurement Phase

- 1st Advertisement June 3rd
- · 2nd Advertisement June 10th
- 3rd Advertisement June 17th
- · Pre-Bid Conference June 18th
- Bid Opening July 8th

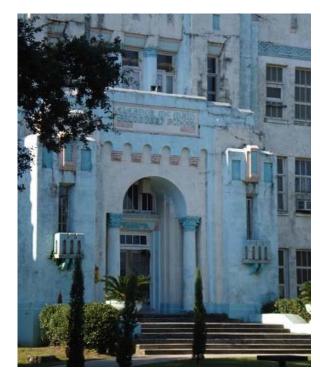

Timbers III - Building Controls (OPSB)

3520 General DeGaulle Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: Design and installation of new building controls

Funding Source - OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - TBD Design Phase - PC

Owner has placed project on hold

Procurement Phase

- Anticipated 1st Advertisement TBD
- Anticipated Bid Opening TBD



Status Date: 31 May 2015

Building Automation System Integration At Recovery School

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview ES

Funding Source – FEMA Architect – Moses Engineers Contractor – Synergy Building Solutions, Inc. Construction Phase

- The five Quick Start Schools are complete, the Energy Dash Board is being implemented
- Sylvanie Williams Elementary School, Sarah T. Reed Elementary School, Fannie C. Williams Elementary School, Bienville Elementary School, Charles L. Colton Elementary School, William Frantz Elementary School, Parkview Elementary School, Osborne Elementary School, Carter G.
 Woodson Elementary School, Walter Cohen High School, Dolores T Aaron Elementary School, A. D. Crossman Elementary School, and Albert Wicker Elementary School are complete
- New integration work is ongoing at Benjamin Banneker Elementary School
- Integrations 90% complete at Lawrence D. Crocker Elementary School

Contractual Substantial Completion – May 2015 Forecasted Substantial Completion – May 2015



MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

Demolition of Modular Buildings at Gregory and Abramson (RSD)

1700 Pratt Drive & 5552 Read Boulevard, New Orleans, LA District D Ward 7 & District E Ward 9

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Holly & Smith Architects

Contractor – Ashley Savarino Unlimited Construction

Construction Phase

· Gregory - Site work ins ongoing

Abramson - Final grading and Hydro seeding is 98% complete

Contractual Substantial Completion – June 2015 Forecasted Substantial Completion – June 2015



Demolition of Modular Buildings at Livingston (RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect - GAEA Consultants, LLC

Contractor - TBD

Procurement Phase

- Anticipated 1st Advertisement November 2015
- Anticipated Bid Opening December 2015



Comprehensive List - Completed Projects

- 1 Abrams | Morial | Abramson | Coghill Demolition (RSD)
- 2 A. D. Cross Elementary School Energy Conservation (RSD)
- 3 A. D. Crossman Elementary School and Benjamin Banneker Elementary School (RSD)
- 4 A. D. Crossman Elementary School Refurbishment (RSD)
- 5 A. P. Tureaud Elementary School Roof Repairs (RSD)
- 6 Agnes Bauduit Elementary School Boiler (RSD)
- 7 Albert Wicker Elementary School Refurbishment (RSD)
- 8 Albert Wicker Elementary School Roof Repairs (RSD)
- Alfred Lawless Senior High Security Fencing (RSD)
- 10 Alice M. Harte Elementary School (OPSB)
- 11 Alice M. Harte Elementary School Demolition (OPSB)
- 12 Andrew J. Bell Junior High School Roof Replacement (RSD)
- 13 Andrew J. Bell Junior High School Mothball (RSD)
- 14 Andrew Jackson Elementary School Roof Repairs (RSD)
- 15 Andrew Jackson Elementary School Solar Panels (RSD)
- 16 Andrew H. Wilson Elementary School Cottage (RSD)
- 17 Arthur Ashe Elementary School Kitchen Renovation (OPSB)
- 18 Augustine Elementary School Roof (RSD)
- 19 Avery-Alexander Elementary School Demolition (RSD)
- 20 Barbara C. Jordan Elementary School Demolition (RSD)
- 21 Bell JH Shoring (RSD)
- 22 Benjamin Banneker Elementary School Energy Conservation (RSD)
- 23 Benjamin Franklin Senior High School (OPSB)
- 24 Bienville Elementary School Demolition (RSD)
- 25 Booker T. Washington High School Partial Demolition (RSD)
- 26 Carter G. Woodson Middle School Demolition (RSD)
- 27 Central Services Warehouse Demolition (OPSB)
- 28 Charles J. Colton Elementary Selective Demolition (RSD)
- 29 Charles J. Colton Elementary School (RSD)
- 30 Charles R. Drew Elementary School (RSD)
- 31 Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)
- 32 Cohen High School Health Clinic (RSD)
- 33 Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School (RSD)
- 34 Douglass High School Under Floor Utilities (RSD)
- 35 Dr. Martin Luther King School Roof Repairs (RSD)
- 36 Dr. Martin Luther King Jr. School Renovation (RSD)
- 37 Dwight D. Eisenhower Elementary School Roof Repairs (RSD)
- 38 East Bank Swing Space for Audubon Charter School (OPSB)
- 39 Edgar P. Harney Elementary School Roof Repairs (RSD)
- 40 Edna Karr High School Gymnasium Repair (OPSB)
- 41 Edna Karr High School Assessment (OPSB)
- 42 Edward Livingston Middle School Demolition (RSD)

- 43 Edward Henry Phillips Junior High School Demolition (OPSB)
- 44 New Edward Hynes School (OPSB)
- 45 Edwards | Hardin | Lockett | Lawless Demolition (RSD)
- 46 Edward Livingston High School (RSD)
- 47 Eleanor L. McMain School Replacement of Existing Chillers (OPSB)
- 48 Eleanor L. McMain School Clinic (OPSB)
- 49 Ernest N. Morial Elementary Security Fencing (RSD)
- 50 Fannie C. Williams Elementary School Demolition (RSD)
- 51 Fisk-Howard Elementary School Demolition (RSD)
- 52 Florence J. Chester Elementary School Demolition (RSD)
- 53 Francis W. Gregory Demolition (RSD)
- 54 Frederick A. Douglass High Refurbishment (RSD)
- 55 Frederick A. Douglass High Switchgear (RSD)
- 56 Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)
- 57 George Mondy Elementary School Mothball (RSD)
- 58 George Washington Carver High School Demolition (RSD)
- 59 Greater St. Stephens School (OPSB)
- 60 Harriet R. Tubman Elementary School Selective Demolition (RSD)
- 61 Henry Allen Elementary School Roof (RSD)
- 62 Henry C. Schaumburg Window/Door, Air Condition, Water Fountain/Sink Installation (RSD)
- 63 Holy Cross Modular Relocation (RSD)
- 64 Israel M. Augustine Middle School Roof Replacement (RSD)
- 65 Israel M. Augustine Middle School Mothball (RSD)
- 66 James Derham Demolition (RSD)
- 67 James W. Johnson Elementary School Roof (RSD)
- 68 New Jean Batiste de Bienville School (RSD)
- 69 Jean Gordon Elementary School Demolition (RSD)
- 70 John Dibert Elementary School Roof (RSD)
- 71 John W. Hoffman Elementary School Demolition (RSD)
- 72 John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)
- 73 John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)
- 74 John F. Kennedy Modular Demolition (RSD)
- 75 John F. Kennedy High School Demolition (RSD)
- 76 John McDonogh Senior High School Bleachers and Sprinklers (RSD)
- 77 John McDonogh Senior High School Roof (RSD)
- 78 John A. Shaw Elementary School Mothball (RSD)
- 79 Joseph S. Clark Senior High School Roof Repairs (RSD)
- 80 Joseph A. Craig Elementary Canopies (RSD)
- 81 Joseph A. Craig Elementary Elevator Installation (RSD)
- 82 Joseph A. Hardin Elementary Security Fencing (RSD)
- 83 Lafayette Elementary School Roof and Masonry (RSD)
- 84 Lake Area | Landry Demolition (RSD)
- 85 Langston Hughes Elementary School (Phase I) (RSD)
- 86 Langston Hughes Elementary School New Gymnasium (Phase II) (RSD)
- 87 Langston Hughes Elementary School Dumpster Pad (RSD)

- 88 Lawrence D. Crocker Elementary School Demolition (RSD)
- 89 L.B. Landry Annex Demolition (RSD)
- 90 Little Woods Elementary School Demolition (RSD)
- 91 Little Woods School (Dolores T. Aaron Elementary School) (RSD)
- 92 Live Oak Elementary School Roof (RSD)
- 93 Live Oak Elementary School Exterior Door Replacement (RSD)
- 94 Lorraine Hansberry Elementary School Mothball (RSD)
- 95 Louis D. Armstrong Elementary School (RSD)
- 96 Mahalia Jackson Elementary School (OPSB)
- 97 Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)
- 98 Mahalia Jackson Elementary School Office Renovation (OPSB)
- 99 Martin Behrman Elementary School Roof (RSD)
- 100 Martin Luther King Jr. Elementary Canopy System (RSD)
- 101 Martin Luther King Jr. School Modular Building, Deck, Canopy (RSD)
- 102 Mary Church Terrell Elementary School Demolition (RSD)
- 103 Mary M. Bethune Elementary 1st Floor Replacement (OPSB)
- 104 Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)
- 105 McDonogh #7 High School Repairs (OPSB)
- 106 McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)
- 107 McDonogh #28 Elementary School Roof (RSD)
- 108 McDonogh #32 Roof Replacement (RSD)
- 109 McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium (OPSB)
- 110 McDonogh #42 Elementary School Roof (RSD)
- 111 McDonogh #42 Elementary School HVAC Replacement (RSD)
- 112 Mildred C. Osborne Elementary School Demolition (RSD)
- 113 Mildred C. Osborne Elementary School (RSD)
- 114 Modular Campuses Close Outs (RSD)
- 115 Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)
- 116 Modular Structures at Langston Hughes Elementary School (RSD)
- 117 Morris F.X. Jeff Elementary School Demolition (RSD)
- 118 Morris F.X. Jeff Elementary School Mothball (RSD)
- 119 Murray G. Henderson Elementary School Roof (RSD)
- 120 New Andrew H. Wilson Elementary School (RSD)
- 121 New Carter G. Woodson School (RSD)
- 122 New Fannie C. Williams School (RSD)
- 123 New Joseph A. Craig Elementary School (RSD)
- 124 New L.B. Landry High School (RSD)
- 125 New Lake Area High School (RSD)
- 126 New Lawrence D. Crocker School (RSD)
- 127 New Parkview School (RSD)
- 128 New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD)
- 129 New William Frantz Elementary School (RSD)
- 130 New Orleans High School Signature Center Study (RSD)
- 131 Oretha C. Haley Demo (RSD)

- 132 Oretha C. Haley Elementary School Mothball (RSD)
- 133 Parkview Elementary School Demolition (RSD)
- 134 Paul L. Dunbar Elementary School Demolition (RSD)
- 135 Paul B. Habans Elementary School Roof Repairs (RSD)
- 136 Phillis Wheatley Elementary School Demolition (RSD)
- 137 Phillis Wheatley Elementary School (RSD)
- 138 Robert M. Lusher Elementary Roof Removal & Replacement (OPSB)
- 139 Sarah T. Reed High School Bleachers (RSD)
- 140 Sarah T. Reed High School Auditorium Wall (RSD)
- 141 Seabrook Computer Training Center Demolition (OPSB)
- 142 Schaumburg Chillers (RSD)
- 143 Schwarz Alternative Repairs (RSD)
- 144 Schwarz Alternative Modulars Demolition (RSD)
- 145 Schwarz Modular Building Demolition (RSD)
- 146 Sherwood Forest Elementary School Demolition (RSD)
- 147 Sophie B. Wright School Selective Demolition (RSD)
- 148 Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)
- 149 Stuart R. Bradley Elementary School Demolition (RSD)
- 150 Sylvanie Williams Elementary School AHU Replacement (RSD)
- 151 Sylvanie Williams Elementary School Play Yard (RSD)
- 152 Sylvanie Williams Elementary School Roof Repairs (RSD)
- 153 Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)
- 154 Temporary Campus for McDonogh #11 Expropriation (OPSB)
- 155 Thomas A. Edison Elementary School Demolition (RSD)
- 156 Thomy Lafon Elementary School Demolition (RSD)
- 157 Thomy Lafon School Interpretative Display (RSD)
- 158 Timbers Park Office Building #1 & #2 Demolition (OPSB)
- 159 Timbers HVAC (OPSB)
- 160 Timbers III IT Room Relocation (OPSB)
- 161 Village de L'est Elementary School Subsidence (RSD)
- 162 Village de L'est Elementary School Roof and Modular Demolition (RSD)
- 163 Vorice J. Waters Elementary School Demolition (RSD)
- 164 Valena C. Jones Elementary School (RSD)
- 165 Walter L. Cohen High School HVAC (RSD)
- 166 Warren Easton High School Window Replacement (OPSB)
- 167 West Bank Swing Space for Alice Harte Elementary School (OPSB)
- 168 New William J. Guste Elementary School (RSD)
- 169 William J. Guste Elementary School Science Lab (RSD)
- 170 William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)
- William Frantz Elementary School (RSD)
- 172 William Frantz Elementary School Roof (RSD)
