Superintendent's Report May, 2016



Dr. Henderson Lewis Jr. Orleans Parish School Board



Mr. John White Louisiana Department of Education Mr. Patrick Dobard Recovery School District





Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	3
COMMUNITY MEETINGS	4
BID OPENINGS	5
DBE OVERVIEW MONTHLY SUMMARY	6
NEW & MAJOR RENOVATION	11
Ray Abrams Elementary School (RSD)	11
Avery Alexander Elementary School (RSD)	11
Benjamin Franklin Elementary School Renovation (OPSB)	11
Paul B. Habans School ^(RSD)	12
JoEllen Smith Medical Center Demolition ^(OPSB)	12
New Karr High School, CMAR ^(OPSB)	12
John McDonogh High School Renovation CMAR ^(RSD)	13
Eleanor L. McMain School Gymnasium (OPSB)	13
Ernest "Dutch" Morial Elementary School ^(RSD)	13
Sherwood Forest School (RSD)	14
Harriet R. Tubman Elementary School Renovation (RSD)	14
Booker T. Washington School CMAR (RSD)	14
Sophie B. Wright School (RSD)	15

REFURBISHMENTS	16
Benjamin Banneker Elementary Kitchen School Refurbishment (RSD)	16
Agnes L. Bauduit Elementary School Refurbishment (RSD)	16
Walter L. Cohen High School Kitchen Refurbishment (RSD)	16
A. D. Crossman School Kitchen Refurbishment (RSD)	17
Frederick A. Douglass High School Science Lab ^(RSD)	17
William J. Fischer Elementary Refurbishment (RSD)	17
Gaudet Elementary School Refurbishment (RSD)	18
Edgar P. Harney Elementary School Refurbishment (RSD)	18
Andrew Jackson School Refurbishment (RSD)	18
J. W. Johnson Elementary School Refurbishment (RSD)	19
Lafayette Elementary School Refurbishment (RSD)	19
Laurel Elementary School Refurbishment (RSD)	19
Live Oak Elementary School Refurbishment (RSD)	20
Lusher Elementary School Refurbishment (OPSB)	20
Thurgood Marshall Elementary School Refurbishment (RSD)	20
McDonogh #32 School Refurbishment ^(RSD)	21
Village de l'Est Elementary School Refurbishment (RSD)	21
Albert Wicker School Kitchen Refurbishment (RSD)	21

OTHER PROJECTS	22
Eleanor L. McMain School Maintenance Upgrades (OPSB)	22
Building Automation System Integration At Recovery School District	22
Central And Remote Offices (RSD)	ZZ

MOTHBALL OR SAFE & SECURE OF SELECTED23SCHOOLS23Demolition of Modulars at Abramson and Carver ^(RSD)23Demolition of Modulars at Livingston ^(RSD)23

COMPLETED PROJECTS

24

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$551 million in open contracts for the capital program after issuing \$14.2 million in new contracts, change orders and amendments in May. In addition, the total change orders to date, \$5.7 million, account for one percent (1.11%) of the total open construction contracts. RSD anticipates issuing approximately \$5.9 million in construction contracts/change orders, and \$119 thousand in professional service contracts/amendments in June.



The OPSB has \$232 million in open contracts for the capital program after issuing \$5 thousand in new contracts, change orders and amendments in May. In addition, the total change orders to date, \$7.3 million, account for approximately four percent (3.70%) of the total open construction contracts. OPSB anticipates issuing approximately \$472 thousand construction contracts/change orders and \$282 thousand in professional service contracts and amendments in June.

Community Meetings



Future Community Meetings

<u>May 11, 2016</u>

Harriet Tubman Charter School Community / Contractor Meeting 2832 General Meyer Avenue New Orleans, LA 70114

Bid Openings

Bids that were opened in May, 2016

May 18, 2016

• Laurel School Refurbishment

The following projects are scheduled to bid in the next 60 days

August 3, 2016

Green School Refurbishment Phase II



Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of May 31, 2016. The DBE subcontracts value is \$80,797,772 of the \$362,548,187 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 46 projects as of May 31, 2016. The DBE subcontracts value is \$19,753,671 of the \$62,249,020 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of May 31, 2016. The DBE subcontracts value is \$34,981,230 of the \$109,137,557 total of awarded contracts.

Total Amount of Contracts: \$533,934,764

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of May 31, 2016. The DBE subcontracts value is \$54,086,557 of the \$199,371,360 total of awarded contracts.

Stabilization/Demolition/Mothballing:


DBE Contractors secured subcontracts on 2 projects as of May 31, 2016. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.


Total Amount of Contracts: \$200,274,359

* DBE provisions were included in projects bid after June 30, 2012



Current RSD Program DBE Participation

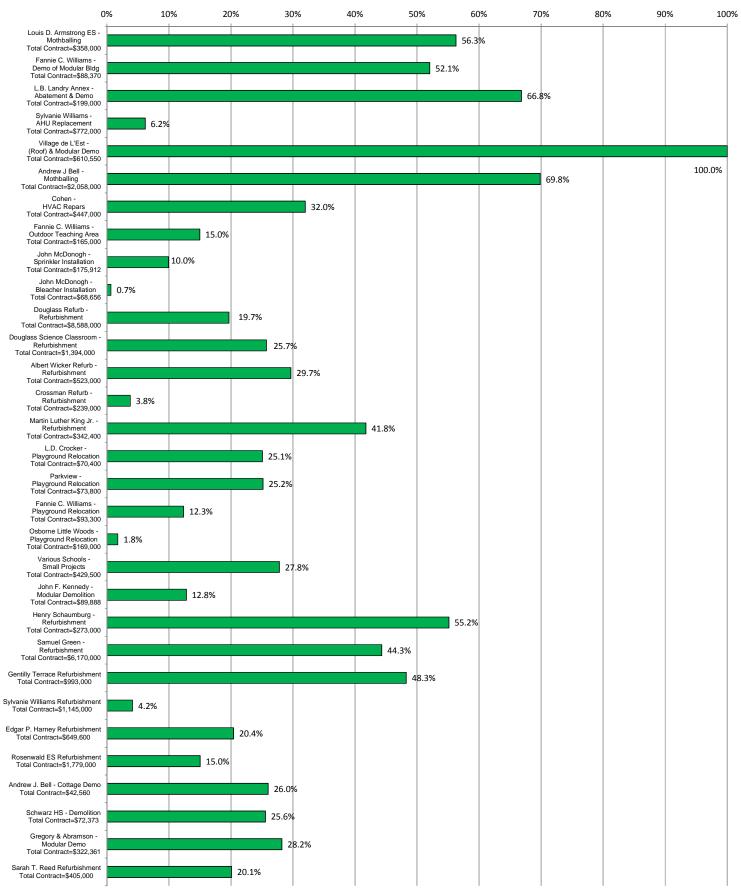


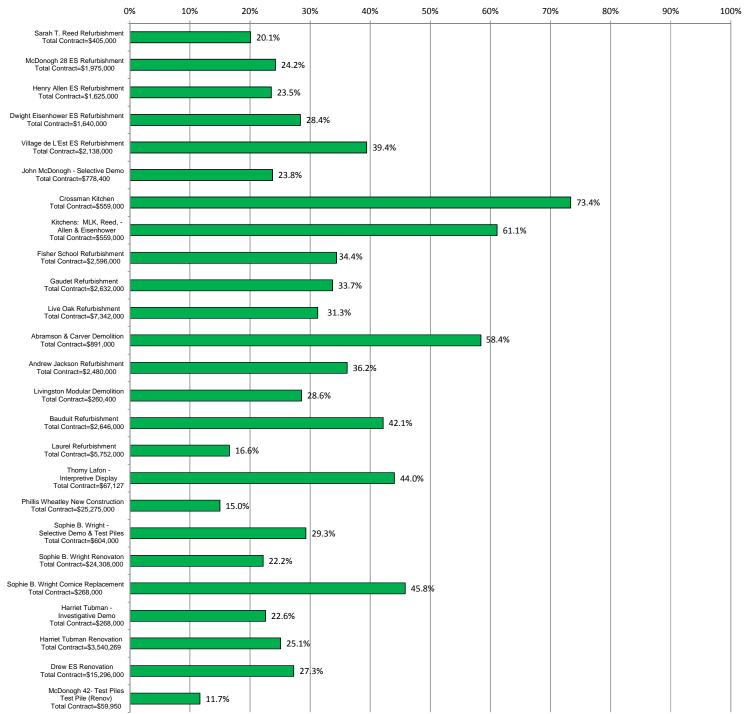

Current RSD Program DBE Participation


(Continued)

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. RSD DBE Participation Target = 25% of Total Contract Amount

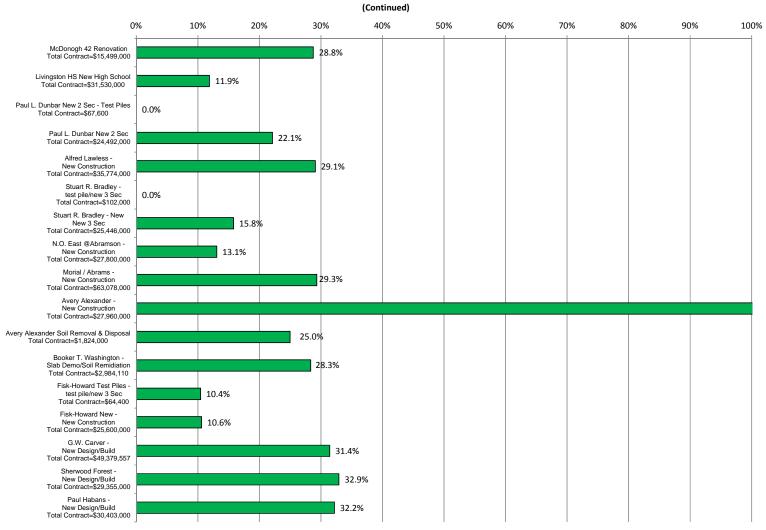

Current RSD Program DBE Participation

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. RSD DBE Participation Target = 25% of Total Contract Amount

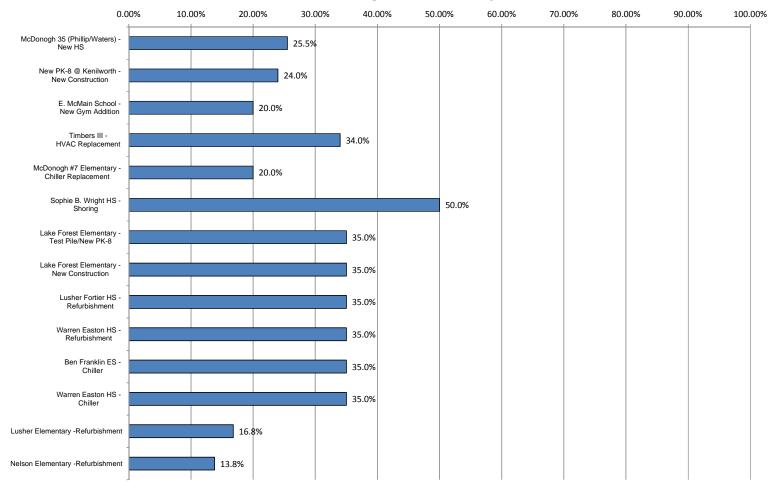

Current OPSB Program DBE Participation

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation - Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School (RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9 Scope of work: New Pre-K – 8 School Funding Source – FEMA Architect – Waggonner & Ball Architects, APC Contractor – McDonnel Group, LLC <u>Construction Phase</u>

- Window installation is proceeding
- Exterior face brick installation is nearly complete
- HVAC duct work installation continues
- Site prep and paving continues

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – May 2017



Avery Alexander Elementary School (RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School Funding Source – FEMA

Architect - Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- · Exterior wall sheathing installation continues
- Steel stud wall framing and exterior sheathing is ongoing
- Overhead mechanical rough in continues
- Exterior CMU continues

 Installation of storm drainage has started Contractual Substantial Completion – May 2017
 Forecasted Substantial Completion – May 2017



Benjamin Franklin Elementary School Renovation (OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14 Scope of work: Renovation of existing elementary school Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - TBD <u>Procurement Phase</u>

Owner has placed project on hold



Paul B. Habans School (RSD)

3501 Siene Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: New School, Design Build Funding Source – FEMA Architect – Grace Hebert Contractor – Core Construction <u>Construction Phase</u>

- State Fire Marshal inspection is anticipated late June
- Commissioning is progressing
- Final site grading is being completed
- FF& E has been delivered
- Punch list is progressing

Contractual Substantial Completion – June 2016 Forecasted Substantial Completion – June 2016



JoEllen Smith Medical Center Demolition (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15 Scope of work: Demolition of existing medical center Funding Source – FEMA Architect – VergesRome Architects, APAC Contractor – Core Construction Demolition Phase

Contractor is mobilized and on site
Contractual Substantial Completion – November 2016
Forecasted Substantial Completion – November 2016



New Karr High School CMAR (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school Funding Source – FEMA Architect – TBD Contractor - TBD <u>Procurement Phase</u> • Owner has placed project on hold Contractual Substantial Completion – November 2018 Forecasted Substantial Completion – November 2018



John McDonogh High School Renovation CMAR ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6 Scope of work: Renovation of existing school to meet code requirements Funding Source – FEMA Architect – VergesRome Architects, APAC Contractor - Core Construction Design Phase

50% Construction Documents are due June 24th

 Project Team is working on community presentation Contractual Substantial Completion – June 2018 Forecasted Substantial Completion – June 2018



Eleanor L. McMain School Gymnasium (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14 Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source – FEMA Architect – Jahncke & Burns Architects Contractor – Gibbs Construction Construction Phase

Contractor is working on the punch list

Final Commissioning is ongoing

Substantial Completion is anticipated in June

Contractual Substantial Completion – June 2016 Forecasted Substantial Completion – June 2016



Ernest "Dutch" Morial Elementary School (RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9 Scope of work: New Pre-K – 8 School Funding Source – FEMA Architect – Waggonner & Ball Architects, APC Contractor – McDonnel Group, LLC <u>Construction Phase</u> • HVAC duct work is ongoing

- Installation of roofing continues
- Interior sheathing continues

• Face brick installation is nearing completion Contractual Substantial Completion – January 2017 Forecasted Substantial Completion – January 2017



Sherwood Forest School (RSD)

4801 Maid Marion Drive, New Orleans, LA 70128 District E Ward 9

Scope of work: New School, Design Build Funding Source – FEMA Architect – Grace Hebert Contractor – Core Construction <u>Construction Phase</u>

- Substantial completion is anticipate in June
- · Fencing installation has started
- Commissioning has started
- Testing and Balance is ongoing

Contractual Substantial Completion – May 2016 Forecasted Substantial Completion – June 2016



Harriet R. Tubman Elementary School Renovation (RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15 Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA Architect – Mahlum Scairono Martinez JV Contractor - Construction Masters Inc Procurement Phase

Selective demolition is finishing

Environmental Abatement is ongoing

Contractual Substantial Completion – May 2018 Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates Contractor – Core Construction Construction Phase

- onstruction Phase
 - · Project team has made a recommendation for test piles package
 - Project team continues VE exercise
 - A revised corrective plan of action for South Prieur street has been submitted

Contractual Substantial Completion – April 2018 Forecasted Substantial Completion – April 2018



Sophie B. Wright High School Renovation (RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13 Scope of work: Renovation of existing school and gymnasium addition Funding Source – FEMA Architect – Waggonner & Ball Architects, APC Contractor – Core Construction <u>Construction Phase</u>

- Final cleaning has started on 2nd and 3rd floors
- Waterproofing has started on north side of building
- Finish work continues on first floor
- ${\boldsymbol{\cdot}}$ State Fire Marshal review is anticipated at the end of June
- Exterior site work continues

Contractual Substantial Completion – June 2016 Forecasted Substantial Completion – June 2016



REFURBISHMENTS

Benjamin Banneker Elementary School Kitchen Refurbishment (RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16 Scope of work: Refurbishment of existing elementary school kitchen Funding Source – FEMA Architect – SCNZ Architects Contractor - TBD Design Phase - CD • 100% Construction Documents are due June 23rd

Procurement Phase

- Anticipated 1st Advertisement July 2016
- Anticipated Bid Opening August 2016



Agnes L. Bauduit Elementary School Refurbishment (RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect – Duplantis Design Group, PC Contractor – One Construction

Construction Phase

- Notice to Proceed is anticipated June 20th
- Revisions to the dumpster and mechanical yard have been submitted to the city

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – May 2017



Walter L. Cohen High School Kitchen Refurbishment (RSD)

3520 Dryades, New Orleans Street, LA 70115 District B Ward 12 Scope of work: Refurbishment of existing elementary school kitchen Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - TBD <u>Design Phase - CD</u> • Owner has placed this project on hold <u>Procurement Phase</u>

- Anticipated 1st Advertisement TBD
- Anticipated Bid Opening TBD



A. D. Crossman School Kitchen Refurbishment (RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3 Scope of work: Refurbishment of existing elementary school kitchen Funding Source – FEMA Architect – SCNZ Architects Contractor - CDW Services <u>Construction Phase</u>

 Dumpster pad was redesigned, Contractor will start dumpster pad once rain subsides

Contractual Substantial Completion – July 2016 Forecasted Substantial Completion – July 2016

Frederick A. Douglass High School Science Lab (RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9 Scope of work: Renovations to science lab Funding Source – FEMA Architect – VergesRome Architects, APAC Contractor – One Construction <u>Construction Phase</u>

- State Fire Marshal has given temporary occupancy
- Installation of sump pump to start beginning of June

 Auditorium roof eyebrow installation is pending Contractual Substantial Completion – March 2016 Forecasted Substantial Completion – July 2016





William J. Fischer Elementary School Refurbishment (RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect – SCNZ Architects

Contractor - Perez

Construction Phase

- · Environmental abatement has started
- Exterior plaster repairs are 50% complete
- Work is being preformed on existing HVAC

 New conduit for lighting is being run on the second floor Contractual Substantial Completion – February 2017

Forecasted Substantial Completion – February 2017



Gaudet Elementary School Refurbishment (RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – SCNZ Architects Contractor - One Construction <u>Construction Phase</u>

- Plumbing rough-in has started
- Pre-roofing meeting is scheduled for June 13th
- Exterior site work has started

Contractual Substantial Completion – November 2016 Forecasted Substantial Completion – November 2016



Edgar P. Harney Elementary School Refurbishment (RSD)

2503 Willow Street, New Orleans, LA 70113 District B Ward 11 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – VergesRome Architects, APAC

Architect – VergesRome Architects, APAC Contractor - Hamp's Construction, LLC Construction Phase

Project is substantially complete

• Added fencing scope to be approved soon Contractual Substantial Completion – June 2016 Forecasted Substantial Completion – June 2016



Andrew Jackson School Refurbishment (RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services <u>Construction Phase</u>

Environmental abatement contractor has mobilized

 General contactor submitting shop drawings Contractual Substantial Completion – June 2017 Forecasted Substantial Completion – June 2017



J. W. Johnson Elementary School Refurbishment ^(RSD)

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect – SCNZ Architects Contractor - TBD Design Phase - CD • Owner has placed this project on hold Procurement Phase

- Anticipated 1st Advertisement TBD
- Anticipated Bid Opening TBD



Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - TBD <u>Procurement Phase</u> • LDOE is reviewing contracts



Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect – Mahlum Scairono Martinez JV Contractor - TBD Procurement Phase

- Bid Opening May 18th
- Bids are being reviewed



Live Oak Elementary School Refurbishment (RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – VergesRome Architects, APAC Contractor - Core Construction Construction Phase

- Window refurbishment continues
- Stairwells have been abated
- · New sub-floor in restrooms has been installed
- Classroom doors and transoms are being dipped for restoration
- Contractual Substantial Completion July 2017 Forecasted Substantial Completion – July 2017



Lusher Elementary School Refurbishment (OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14 Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility Funding Source – FEMA Architect – Meyer Engineers, LTD. Contractor - Dynamic <u>Construction Phase</u> • Interior finishes are being installed

• Elevator shaft work is ongoing

Contractual Substantial Completion – June 2016 Forecasted Substantial Completion – August 2016

Thurgood Marshall Elementary School Refurbishment (RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – Mahlum Scairono Martinez JV Contractor - TBD Design Phase - CD

• FEMA is reviewing the construction documents

Increased scope of work to include elevator, security, and basketball court
 <u>Procurement Phase</u>

- Anticipated 1st Advertisement September 2016
- Anticipated Bid Opening November 2016



McDonogh #32 School Refurbishment (RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect – Byron J. Stewart & Associates, APC Architects & Planners Contractor - TBD Design Phase – CD

A&E revising Bid Documents

Procurement Phase

- Anticipated 1st Advertisement July 2016
- Anticipated Bid Opening September 2016



Village de l'Est Elementary School Refurbishment (RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CBDG Architect – Duplantis Design Group, PC Contractor - Dynamic Constructors LLC <u>Construction Phase</u>

- HVAC controls is 98% complete
- Test and Balance is ongoing
- General Contractor is working on punch list

• Substantial Completion is anticipates in June Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – June 2016



Albert Wicker School Kitchen Refurbishment (RSD)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4 Scope of work: Refurbishment of existing elementary school kitchen Funding Source – FEMA Architect – SCNZ Architects Contractor - TBD <u>Design Phase - CD</u> • Owner has placed this project on hold Procurement Phase

Anticipated 1st Advertisement – TBD

Anticipated Bid Opening – TBD



OTHER PROJECTS

Eleanor L. McMain School Maintenance Upgrades (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14 Scope of work: Various maintenance work. Funding Source – General Fund & Harrah's Architect – Duplantis Design Group Contractor – Tuna Construction <u>Construction Phase</u>

- Flooring repairs are ongoing
- Restroom work nearing completion
- · Kitchen work has started

Contractual Substantial Completion – June 2016 Forecasted Substantial Completion – July 2016



Building Automation System Integration At Recovery School

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview ES

Funding Source – FEMA Architect – Moses Engineers Contractor – Synergy Building Solutions, Inc. <u>Construction Phase</u>

 Moses is reviewing training docs and O&M manuals Contractual Substantial Completion – May 2015 Forecasted Substantial Completion – June 2016



MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

Demolition of Modular Buildings at Abramson and Carver ^(RSD)

5552 Read Boulevard and 3059 Higgins Boulevard, New Orleans, LA Scope of work: Demolition of existing modular buildings Funding Source – FEMA Architect – Mahlum Scairono Martinez JV Contractor - Construction Masters, Inc. <u>Construction Phase</u>

- Abramson Site Restoration nearing completion
- Abramson piles to be removed from under electrical pads
- Carver Trailer demobilization underway
- All environmental testing is complete

Contractual Substantial Completion – September 2016 Forecasted Substantial Completion – September 2016



Demolition of Modular Buildings at Livingston (RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – Concrete Busters of Louisiana

Construction Phase

- Removal of exterior canopy and stairs is complete
- Environmental work is complete
- Trailers to be removed from site

Contractual Substantial Completion – September 2016 Forecasted Substantial Completion – September 2016



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition (RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	11/17/2000
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
6	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
7	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
, 8	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
9	Alfred Lawless Senior ^(RSD)	12/18/2015
10	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
11	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
12	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
13	Andrew J. Bell Junior High School Roof Replacement (RSD)	02/08/2014
14	Andrew J. Bell Junior High School Mothball (RSD)	06/28/2011
15	Andrew Jackson Elementary School Roof Repairs (RSD)	07/27/2012
16	Andrew Jackson Elementary School Solar Panels (RSD)	01/14/2013
17	Andrew H. Wilson Elementary School Cottage (RSD)	10/11/2010
18	Arthur Ashe Elementary School Kitchen Renovation (OPSB)	
19	Augustine Elementary School Roof ^(RSD)	04/13/2012
20	Avery-Alexander Elementary School Demolition (RSD)	06/15/2012
21	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
22	Bell JH Shoring ^(RSD)	06/28/2011
23	Benjamin Banneker Elementary School Energy Conservation (RSD)	
24	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
25	Bienville Elementary School Demolition (RSD)	05/04/2009
26	Booker T. Washington High School Environmental Remediation (RSD)	12/13/2015
27	Booker T. Washington High School Partial Demolition (RSD)	04/07/2013
28	Carter G. Woodson Middle School Demolition (RSD)	02/09/2010
29	Central Services Warehouse Demolition (OPSB)	01/05/2012
30	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
31	Charles J. Colton Elementary School (RSD)	05/23/2013
32	Charles R. Drew Elementary School ^(RSD)	04/17/2015
33	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
34	Cohen High School Health Clinic ^(RSD)	12/24/2008
35	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
36	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
37	Douglass High School Under Floor Utilities ^(RSD)	0 / / 0 / 0 0 / 0
38	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
39	Dr. Martin Luther King Jr. School Renovation (RSD)	12/15/2014
40 41	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
41 42	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
42 43	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015 12/30/2011
43	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011

11	Edger D. Herney Elementary School Deef Densire ^(RSD)	06/13/2012
44 45	Edgar P. Harney Elementary School Roof Repairs (RSD)	12/23/2013
45 46	Edna Karr High School - Gymnasium Repair ^(OPSB) Edna Karr High School - Assessment ^(OPSB)	12/23/2013
40 47	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
48	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
40 49	New Edward Hynes School ^(OPSB)	02/06/2012
47 50	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
51	Edward Livingston High School ^(RSD)	01/05/2008
52	Eleanor L. McMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
52	Eleanor L. McMain School Clinic ^(OPSB)	07/24/2013
53 54		07/24/2013
54 55	Eleanor L. McMain School Roof Replacement ^(OPSB)	05/10/2011
	Ernest N. Morial Elementary Security Fencing (RSD)	03/10/2009
56 57	Fannie C. Williams Elementary School Demolition ^(RSD)	10/04/2011
57 50	Fisk-Howard Elementary School Demolition ^(RSD)	06/05/2011
58 50	Florence J. Chester Elementary School Demolition ^(RSD)	
59	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
60	Francis W. Gregory Demolition ^(RSD)	12/21/2011
61	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
62	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
63	Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)	
64	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
65	George Mondy Elementary School Mothball ^(RSD)	
66	George Washington Carver School ^(RSD)	03/07/2016
67	George Washington Carver High School Demolition ^(RSD)	08/24/2011
68	Greater St. Stephens School ^(OPSB)	03/18/2013
69	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
70	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
71	Henry Allen Elementary School Kitchen Refurbishment (RSD)	02/18/2016
72	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
73	Henry C. Schaumburg School Refurbishment (RSD)	06/26/2015
74	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation (RSI	^{D)} 12/16/2011
75	Holy Cross Modular Relocation ^(RSD)	12/14/2010
76	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
77	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
78	James Derham Demolition ^(RSD)	02/23/2012
79	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
80	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
81	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
82	John Dibert Elementary School Roof ^(RSD)	08/20/2010
83	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
84	John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)	11/05/2010
85	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
86	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
87	John F. Kennedy High School Demolition (RSD)	01/12/2012
88	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
89	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
		D /

00	Is has A. Characteria Calification (RSD)	10/10/2012
90 01	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
91 02	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012 06/06/2011
92 93	Joseph A. Craig Elementary Canopies ^(RSD)	01/20/2011
93 94	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
	Joseph A. Hardin Elementary Security Fencing ^(RSD)	
95 04	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
96 07	Lake Area Landry Demolition ^(RSD)	05/01/2008
97 00	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015 08/11/2009
98 00	Langston Hughes Elementary School (Phase I) ^(RSD)	
99 100	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010 10/12/2012
100	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	04/02/2012
101	Lawrence D. Crocker Elementary School Demolition ^(RSD)	
	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
103	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
104	Little Woods School (Dolores T. Aaron Elementary School) (RSD)	08/01/2013
	Live Oak Elementary School Roof ^(RSD)	08/04/2011
	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
107	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
109	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
111	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
113	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
	Martin Luther King Jr. School Modular Building, Deck, Canopy (RSD)	07/31/2012
115	Martin Luther King Jr. School Kitchen Refurbishment (RSD)	02/18/2016
	Mary Church Terrell Elementary School Demolition (RSD)	04/17/2013
	Mary M. Bethune Elementary 1st Floor Replacement (OPSB)	01/24/2011
	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
119	McDonogh #7 High School Repairs ^(OPSB)	
120	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
121	McDonogh #28 School Refurbishment (RSD)	
122		11/19/2011
123	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
124	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior	01/17/2014
	Ramp & Handicap Seating in the Auditorium ^(OPSB)	
	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
127	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
128	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
129	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
130	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
131	Modular Campuses Close Outs ^(RSD)	
	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
	Modular Structures at Langston Hughes Elementary School (RSD)	04/05/2010
134	Morris F.X. Jeff Elementary School Demolition (RSD)	

100	(RSD)	01/15/0010
	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
137	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
138	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
	New Carter G. Woodson School ^(RSD)	09/14/2012
	New Fannie C. Williams School ^(RSD)	08/24/2012
141	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
142		06/30/2010
143	· · · · · · · · · · · · · · · · · · ·	12/28/2009
144		04/29/2013
145	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
146	New Parkview School ^(RSD)	10/12/2012
147		
148	New William Frantz Elementary School ^(RSD)	
149	New Orleans High School Signature Center Study ^(RSD)	
150	Oretha C. Haley Demo ^(RSD)	05/07/2012
151	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
152	Parkview Elementary School Demolition (RSD)	08/06/2009
	Paul L. Dunbar Elementary School Demolition (RSD)	06/16/2010
	Paul L. Dunbar Elementary School (RSD)	06/02/2015
	Paul B. Habans Elementary School Roof Repairs (RSD)	07/27/2012
	Phillis Wheatley Elementary School Demolition (RSD)	09/26/2011
157	(RCD)	07/10/2014
158	Rosenwald Elementary School Refurbishment (RSD)	
159		07/14/2011
160	Samuel J. Green Elementary School Refurbishment (RSD)	02/15/2016
	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
163	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
164	(020)	12/01/2015
165	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
166	(828)	11/14/2008
167	Schwarz Alternative Repairs ^(RSD)	07/14/2009
168	Schwarz Alternative Modulars Demolition ^(RSD)	04/02/2015
169		04/02/2015
170	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
171	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
172	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
173	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
174	(DCD)	01/27/2010
175	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
176	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
177	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
178	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
179	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
180	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
100		

181	Temporary Campus for McDonogh #11 Expropriation (OPSB)	
182	Thomas A. Edison Elementary School Demolition (RSD)	03/25/2010
183	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
184	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
185	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
186	Timbers HVAC ^(OPSB)	09/11/2013
187	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
188	Village de L'est Elementary School Subsidence (RSD)	06/18/2012
189	Village de L'est Elementary School Roof and Modular Demolition (RSD)	06/16/2013
190	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
191	Valena C. Jones Elementary School ^(RSD)	01/10/2013
192	Walter L. Cohen High School HVAC (RSD)	04/04/2014
193	Warren Easton High School Renovation (OPSB)	12/15/2015
194	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
195	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
196	New William J. Guste Elementary School ^(RSD)	10/06/2008
197	William J. Guste Elementary School Science Lab (RSD)	08/04/2009
198	William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)	04/15/2010
199	William Frantz Elementary School Roof ^(RSD)	08/12/2010
