

# Superintendent's Report June, 2014



**Mr. Stanley C. Smith**  
Orleans Parish School Board



**Mr. John White**  
Louisiana Department of Education  
**Mr. Patrick Dobard**  
Recovery School District



Prepared By





# Table of Contents

Right-Click on the school name to proceed to that page

<b>TABLE OF CONTENTS</b>	1
<b>FINANCIAL OVERVIEW</b>	4
<b>COMMUNITY MEETINGS</b>	5
<b>BID OPENINGS</b>	6
<b>DBE OVERVIEW MONTHLY SUMMARY</b>	7
<b>NEW &amp; MAJOR RENOVATION</b>	11
Ray Abrams Elementary School <sup>(RSD)</sup>	11
Avery Alexander Elementary School <sup>(RSD)</sup>	11
James Audubon School <sup>(OPSB)</sup>	12
Stuart R. Bradley School <sup>(RSD)</sup>	12
George Washington Carver School <sup>(RSD)</sup>	12
Charles R. Drew Elementary School <sup>(RSD)</sup>	13
Paul L. Dunbar School <sup>(RSD)</sup>	13
Fisk-Howard School <sup>(RSD)</sup>	13
Paul B. Habans School <sup>(RSD)</sup>	14
Alice Harte School <sup>(OPSB)</sup>	14
New Karr High School at the JoEllen Smith Site <sup>(OPSB)</sup>	14
New PK-8 School at North Kenilworth Park at Curran Site <sup>(OPSB)</sup>	15
Lake Forest PK-8 at the Greater St. Stephens Site <sup>(OPSB)</sup>	15
Alfred Lawless School <sup>(RSD)</sup>	15
Edward Livingston High School <sup>(RSD)</sup>	16
John McDonogh High School Selective Demolition <sup>(RSD)</sup>	16
John McDonogh High School Renovation <sup>(RSD)</sup>	16
McDonogh #35 School (Phillip/Waters Site) <sup>(OPSB)</sup>	17
McDonogh #42 Elementary School <sup>(RSD)</sup>	17
Eleanor L. McMain School Gymnasium <sup>(OPSB)</sup>	17
Ernest "Dutch" Morial Elementary School <sup>(RSD)</sup>	18
Small New Orleans East High School at Abramson <sup>(RSD)</sup>	18
Sherwood Forest School <sup>(RSD)</sup>	18
Harriet R. Tubman Elementary School Selective Demolition <sup>(RSD)</sup>	19
Harriet R. Tubman Elementary School Renovation <sup>(RSD)</sup>	19
Booker T. Washington School Environmental Remediation <sup>(RSD)</sup>	19
Booker T. Washington School <sup>(RSD)</sup>	20
Phillis Wheatley Elementary School <sup>(RSD)</sup>	20

Sophie B. Wright School <sup>(RSD)</sup> 20

**REFURBISHMENTS** 21

Henry Allen Elementary School Refurbishment <sup>(RSD)</sup> 21

Henry Allen Elementary School Kitchen Refurbishment <sup>(RSD)</sup> 21

Benjamin Banneker Elementary Kitchen School Refurbishment <sup>(RSD)</sup> 21

Agnes L. Bauduit Elementary School Refurbishment <sup>(RSD)</sup> 22

Walter L. Cohen High School Kitchen Refurbishment <sup>(RSD)</sup> 22

A. D. Crossman School Kitchen Refurbishment <sup>(RSD)</sup> 22

Frederick A. Douglass High School <sup>(RSD)</sup> 23

Warren Easton School Refurbishment <sup>(OPSB)</sup> 23

Dwight D. Eisenhower Elementary School Refurbishment <sup>(RSD)</sup> 23

Dwight D. Eisenhower Elementary School Kitchen Refurbishment <sup>(RSD)</sup> 24

William J. Fischer Elementary Refurbishment <sup>(RSD)</sup> 24

Fortier (Lusher) High School Refurbishment <sup>(OPSB)</sup> 24

Gaudet Elementary School Refurbishment <sup>(RSD)</sup> 25

Gentilly Terrace School Refurbishment <sup>(RSD)</sup> 25

Gentilly Terrace School Kitchen Refurbishment <sup>(RSD)</sup> 25

Samuel J. Green Elementary School Refurbishment <sup>(RSD)</sup> 26

Edgar P. Harney Elementary School Refurbishment <sup>(RSD)</sup> 26

Andrew Jackson School Refurbishment <sup>(RSD)</sup> 26

Andrew Jackson School Kitchen Refurbishment <sup>(RSD)</sup> 27

J. W. Johnson Elementary School Refurbishment <sup>(RSD)</sup> 27

Dr. Martin L. King Elementary School Refurbishment <sup>(RSD)</sup> 27

Dr. Martin L. King Elementary School Kitchen Refurbishment <sup>(RSD)</sup> 28

Lafayette Elementary School Refurbishment <sup>(RSD)</sup> 28

Laurel Elementary School Refurbishment <sup>(RSD)</sup> 28

Live Oak Elementary School Refurbishment <sup>(RSD)</sup> 29

Lusher Elementary School Refurbishment <sup>(OPSB)</sup> 29

Thurgood Marshall Elementary School Refurbishment <sup>(RSD)</sup> 29

McDonogh #28 School Refurbishment <sup>(RSD)</sup> 30

McDonogh #28 School Kitchen Refurbishment <sup>(RSD)</sup> 30

McDonogh #32 School Refurbishment <sup>(RSD)</sup> 30

Nelson Elementary School Refurbishment <sup>(OPSB)</sup> 31

Sarah T. Reed School Refurbishment <sup>(RSD)</sup> 31

Sarah T. Reed School Kitchen Refurbishment <sup>(RSD)</sup> 31

Rosenwald Elementary School Refurbishment <sup>(RSD)</sup> 32

Henry C. Schaumburg Elementary School Refurbishment <sup>(RSD)</sup> 32

Village de l'Est Elementary School Refurbishment <sup>(RSD)</sup> 32

Albert Wicker School Kitchen Refurbishment <sup>(RSD)</sup> 33

Sylvanie F. Williams School Refurbishment <sup>(RSD)</sup> 33

<b>OTHER PROJECTS</b>	34
Timbers III - Building Controls <sup>(OPSB)</sup>	34
Timbers III - IT Room Relocation <sup>(OPSB)</sup>	34
Building Automation System Integration At Recovery School District Central And Remote Offices <sup>(RSD)</sup>	35
 <b>MOTHBALL OR SAFE &amp; SECURE OF SELECTED SCHOOLS</b>	36
Andrew J. Bell Junior High School Shoring and Mothball <sup>(RSD)</sup>	36
Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School <sup>(RSD)</sup>	36
John F. Kennedy Modular Demolition <sup>(RSD)</sup>	37
George Mondy Elementary School Mothball <sup>(RSD)</sup>	37
 <b>COMPLETED PROJECTS</b>	38

# Overview

## FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$570 million in open contracts for the capital program after issuing \$109 million in new contracts and \$1.5 million in change orders and amendments in June. In addition, the total change orders to date, \$5.6 million, account for approximately one percent (1.12%) of the total open construction contracts. RSD anticipates issuing approximately \$1.1 million in construction contracts/change orders, and no professional service contracts/amendments in July.



The OPSB has \$213 million in open contracts for the capital program after issuing \$0 thousand in new contracts and \$142 thousand in change orders and amendments in June. In addition, the total change orders to date, \$3 million, account for approximately two percent (1.61%) of the total open construction contracts. OPSB anticipates issuing no construction contracts/change orders and \$626 thousand in professional service contracts/amendments in July.

## Community Meetings



**There were no community meetings for the month of June**

# Bid Openings

## Bids that were opened in June 2014:

### June 11, 2014

Warren Easton High School Refurbishment

### June 12, 2014

Various School Small Projects at RSD Schools

### June 18, 2014

Lusher (Fortier) High School Refurbishment

## The following projects are scheduled to bid in the next 60 days:

### July 16, 2014

Henry C. Schaumburg Elementary School Refurbishment

### July 16, 2014

Gentilly Terrace School Renovation

### July 17, 2014

Sophie B. Wright High School Renovation

### July 17, 2014

Samuel J. Green Elementary School Refurbishment

### August 13, 2014

Harriet R. Tubman Elementary School Selective Demolition

### August 13, 2014

Relocation of Playground Equipment at Osborne and Little Woods (Dolores T. Aaron Elementary School)

### September 3, 2014

Sylvanie Williams School Refurbishment



## Disadvantaged Business Enterprises (DBE) Monthly Summary



### Recovery School District

#### New & Renovations:

DBE Contractors secured subcontracts on 15 projects as of May 31, 2014. The DBE subcontracts value is \$38,499,709 of the \$227,677,077 total of awarded contracts.

#### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 15 projects as of May 31, 2014. The DBE subcontracts value is \$4,892,130 of the \$14,731,232 total of awarded contracts.

Total Amount of Contracts: \$ 242,408,309

### Orleans Parish School Board



#### New & Renovations:

DBE Contractors secured subcontracts on 6 projects as of May 31, 2014. The DBE subcontracts value is \$46,610,783 of the \$176,590,360 total of awarded contracts.


#### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of May 31, 2014. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$177,493,359


\* DBE provisions were included in projects bid after June 30, 2012

## Current RSD Program DBE Participation

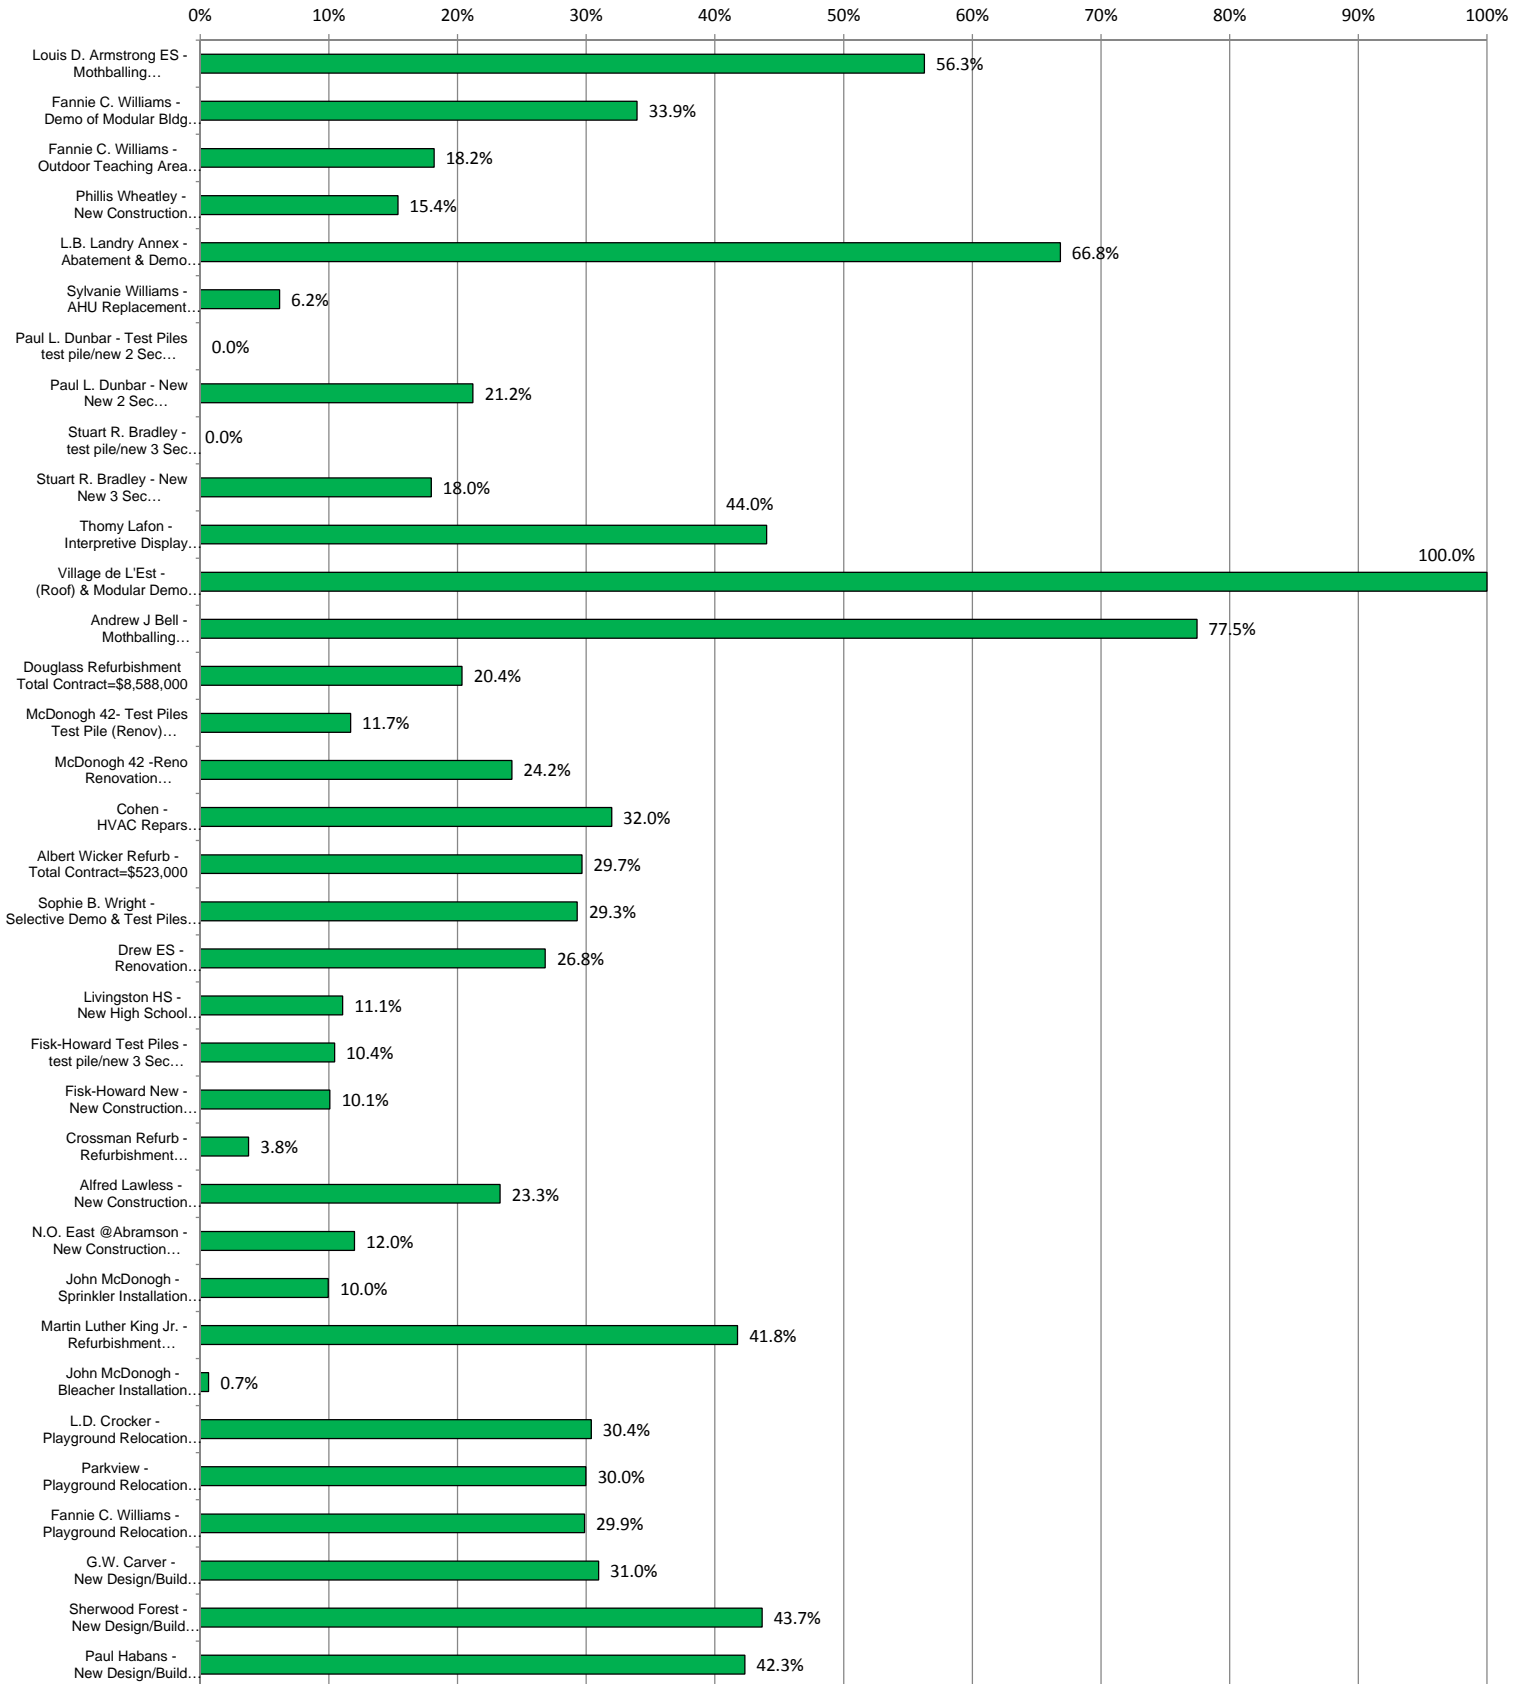

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

### Current OPSB Program DBE Participation

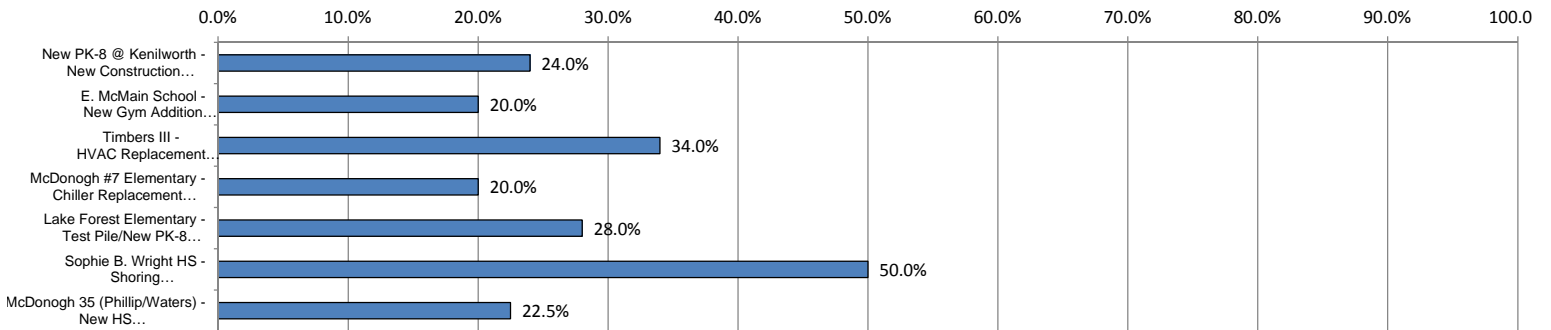

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
 OPSB DBE Participation Target = 35% of Total Contract Amount



## New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

### Ray Abrams Elementary School <sup>(RSD)</sup>

6519 Virgilian Street, New Orleans, LA 70126

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – TBD

#### Design Phase - DD

- Design Development Documents were received June 4th
- 50% Construction Documents are due June 21st
- LDEQ " No Further Action" letter concerning the environmental issues was received June 25th
- Morial and Abrams will be packaged together as (1) project for the procurement process.

#### Procurement Phase

- Anticipated 1st Advertisement – September 2014
- Anticipated Bid Opening – November 2014



### Avery Alexander Elementary School <sup>(RSD)</sup>

5800 St. Roch Avenue, New Orleans, LA 70122

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – TBD

#### Design Phase - CD

- 100% Construction Documents are complete
- Procurement will be pushed by LDEQ approval of environmental issues
- Environmental Report was submitted to LDEQ end of June

#### Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



## James Audubon School <sup>(OPSB)</sup>

428 Broadway Avenue, New Orleans, LA 70118

Scope of work: Renovation of existing elementary school and new addition

Funding Source – FEMA

Architect – Blitch/Knevel Architects

Contractor – FHP Tectonics Corporation

### Construction Phase

- Structural steel has been determined to be mis-aligned
- Contractor is developing a corrective plan for the mis-aligned steel
- Refurbished windows are being installed on the 2nd and 3rd floors

Contractual Substantial Completion – September 2013

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – June 2015



## Stuart R. Bradley School <sup>(RSD)</sup>

2401 Humanity Street, New Orleans, LA 70122

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Landis Construction Co.

### Construction Phase

- Structural steel erection is ongoing
- Kitchen area to be poured early July
- Pouring of 3rd floor deck to be finished early July

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015

School Ready for Occupancy – June 2015



## George Washington Carver School <sup>(RSD)</sup>

3019 & 3059 Higgins Blvd., New Orleans, LA 70126

Scope of work: New High School, Design Build

Funding Source – FEMA

Contractor – Broadmoor LLC

### Procurement Phase

- Anticipated Notice to Proceed - July 2nd
- Anticipated Kick-off meeting July 7th
- Forecasted Substantial Completion - March 2016





## Charles R. Drew Elementary School <sup>(RSD)</sup>

3819 St. Claude Avenue, New Orleans, LA 70117

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Blitch / Knevel Architects, Inc.

Contractor – Core Construction

### Construction Phase

- Metal stud installation is ongoing
- Rooftop mechanical equipment has been installed
- MEP rough-in is ongoing
- Window refurbishment is ongoing

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015

School Ready for Occupancy – June 2015



## Paul L. Dunbar School <sup>(RSD)</sup>

9330 Forshey Street, New Orleans, LA 70125

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor – McDonnel Group, LLC

### Construction Phase

- Foundation work is 90% complete
- Subsurface drainage work is ongoing
- Structural steel erection has started at the gymnasium
- Installation of CMU and metal studs is ongoing

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015

School Ready for Occupancy – June 2015



## Fisk-Howard School <sup>(RSD)</sup>

211 South Lopez Street, New Orleans, LA 70119

Scope of work: New Pre-K – 8 School

Funding Source - FEMA

Architect - VergesRome Architects+Fanning Howey

Contractor – FHP Tectonics Corporation

### Construction Phase

- Installation of interior finishes is ongoing
- Building has permanent power
- Installation of HVAC ductwork is ongoing
- Ramps and stairs have been poured

Contractual Substantial Completion – October 2014

Forecasted Substantial Completion – October 2014

School Ready for Occupancy – January 2015



## Paul B. Habans School <sup>(RSD)</sup>

3501 Siene Drive, New Orleans, LA 70114

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

### Procurement Phase

- Notice to Proceed - June 30th
- Kick-off meeting July 1st
- Forecasted Substantial Completion - May 2016



## Alice Harte School <sup>(OPSB)</sup>

5300 Berkley Drive, New Orleans, La 70131

Scope of work: New Pre-K – 8 School

Funding Source – CDBG & FEMA

Architect – WDG Architects Engineers

Contractor – Woodrow Wilson Construction Company, Inc.

### Construction Phase

- Site work is ongoing
- Installation of metal soffit and gutters are 90% complete
- Installation of Terrazzo Flooring is 85% complete
- Installation of sprinkler system is 98% complete
- Installation of interior finishes: painting and VCT is 90% complete

Contractual Substantial Completion – January 2014

Forecasted Substantial Completion – October 2104

School Ready for Occupancy – November 2014



## New Karr High School at the JoEllen Smith Site <sup>(OPSB)</sup>

4400 General Meyer Avenue, New Orleans, LA 70131

Scope of work: New High School, Design Build

Funding Source – FEMA

Architect – Trapolin Peer Architects, LLC

Contractor – TBD

### Procurement Phase

- Determination of contract award is under review by the Owner





## **New PK-8 School at North Kenilworth Park at Curran Site <sup>(OPSB)</sup>**

8500 Curran Boulevard, New Orleans, LA 70127

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Mathes Brierre Architects

Contractor – Woodrow Wilson Construction Company, Inc.

### Construction Phase

- MEP work is ongoing
- Installation of interior metal studs continues
- Exterior masonry and metal panel installation is ongoing
- Site work is ongoing

Contractual Substantial Completion – September 2014

Forecasted Substantial Completion – 1st Quarter of 2015

School Ready for Occupancy – January 2015



## **Lake Forest PK-8 at the Greater St. Stephens Site <sup>(OPSB)</sup>**

11110 Lake Forest Boulevard 70128

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Imre Hegedus & Associates Architects

Contractor – The McDonnell Group

### Construction Phase

- Pouring of pile caps is complete
- Pouring of grade beams and pile caps is ongoing
- Slab on grade pours are scheduled for mid June
- Structural steel to arrive on site late July

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015

School Ready for Occupancy – August 2015



## **Alfred Lawless School <sup>(RSD)</sup>**

5300 Law Street, New Orleans, LA 70117

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

### Construction Phase

- Pouring of slabs on grade is ongoing
- Forming and pouring of columns and raised slabs is ongoing
- Installation of site utilities has started
- Steel erection has started

Contractual Substantial Completion – November 2015

Forecasted Substantial Completion – November 2015

School Ready for Occupancy – February 2016



## Edward Livingston High School <sup>(RSD)</sup>

7301 Dwyer Road, New Orleans, LA 70126

Scope of work: New High School

Funding Source – FEMA

Architect – RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

### Construction Phase

- Interior finishes has started on administration and media core area
- Exterior brick work and metal panel work is ongoing
- Window installation is ongoing
- Installation of roofing systems is ongoing

Contractual Substantial Completion – February 2015

Forecasted Substantial Completion – February 2015

School Ready for Occupancy – June 2015



## John McDonogh High School Selective Demolition <sup>(RSD)</sup>

2426 Esplanade Avenue, New Orleans, LA 70119

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents were received June 23rd
- Assessment of remediation issue is ongoing

### Procurement Phase

- Anticipated 1st Advertisement – September 2014
- Anticipated Bid Opening – October 2014



## John McDonogh High School Renovation <sup>(RSD)</sup>

2426 Esplanade Avenue, New Orleans, LA 70119

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

### Design Phase - PC

- Design will start when program issues are resolved

### Procurement Phase

- Anticipated 1st Advertisement – 2nd Quarter 2015
- Anticipated Bid Opening – 2nd Quarter 2015



## McDonogh #35 School (Phillip/Waters Site) <sup>(OPSB)</sup>

1200 Senate Street, New Orleans, LA 70122

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler, Thompson, Brown Architects

Contractor – Citadel Builders, LLC

### Construction Phase

- Installation of CMU walls is ongoing
- Exterior metal studs and sheathing on the gymnasium is complete
- Classroom building roof deck to be poured mid July
- Installation of MEP is ongoing

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – May 2015

School Ready for Occupancy – June 2015



## McDonogh #42 Elementary School <sup>(RSD)</sup>

1651 North Tonti Street, New Orleans, LA 70119

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA, QSCB, NMTC, Insurance Proceeds

Architect – Eskew+Dumez+Ripple

Contractor – Core Construction

### Construction Phase

- HVAC installation is ongoing
- Installation of metal studs is complete
- Steel erection is ongoing for the cafeteria addition

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – August 2015



## Eleanor L. McMain School Gymnasium <sup>(OPSB)</sup>

5721 S. Claiborne Avenue, New Orleans, LA 70125

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source – FEMA

Architect – Jahncke & Burns Architects

Contractor – Ellis Construction

### Construction Phase

- Pouring of 2nd floor slab early July
- Underground utility rough-in work is ongoing
- Installation of exterior paving is ongoing

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015





## Ernest "Dutch" Morial Elementary School <sup>(RSD)</sup>

7701 Grant Street, New Orleans, LA 70126

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – TBD

### Design Phase - CD

- Bid Documents are complete
- Morial and Abrams will be packaged together as (1) project for the procurement process.

### Procurement Phase

- Anticipated 1st Advertisement – September 2014
- Anticipated Bid Opening – November 2014



## Small New Orleans East High School at Abramson <sup>(RSD)</sup>

5552 Read Boulevard, New Orleans, LA 70127

Scope of work: New High School

Funding Source – FEMA

Architect – RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

### Construction Phase

- Installation of formwork for slab on grade has started for the administration, media, and classroom area
- Gymnasium slab on grade pour is complete
- Structural steel erection has started
- Installation of site utilities is ongoing

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015

School Ready for Occupancy – November 2015



## Sherwood Forest School <sup>(RSD)</sup>

4801 Maid Marion Drive, New Orleans, LA 70128

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

### Procurement Phase

- Notice to Proceed - June 30th
- Kick-off meeting July 1st
- Forecasted Substantial Completion - May 2016



## Harriet R. Tubman Elementary School Selective Demolition <sup>(RSD)</sup>

2013 General Meyer Avenue, New Orleans, LA 70114

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents are complete

### Procurement Phase

- 1st Advertisement – July 9th
- 2nd Advertisement – July 16th
- 3rd Advertisement – July 23rd
- Pre-Bid Conference – July 24th
- Bid Opening – August 13th



## Harriet R. Tubman Elementary School Renovation <sup>(RSD)</sup>

2013 General Meyer Avenue, New Orleans, LA 70114

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

### Design Phase - CD

- Construction Documents will be delayed due to added scope
- 50% Construction Documents will be delayed until, August 8th

### Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



## Booker T. Washington School Environmental Remediation <sup>(RSD)</sup>

1201 South Roman Street, New Orleans, LA 70125

Scope of work: The remediation of the site

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – TBD

### Design Phase - CD

- Bid Documents were received
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



## **Booker T. Washington School <sup>(RSD)</sup>**

1201 South Roman Street, New Orleans, LA 70125

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – TBD

### Design Phase - CD

- Procurement will be delayed until Environmental concerns have been addressed

### Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



## **Phillis Wheatley Elementary School <sup>(RSD)</sup>**

2300 Dumaine Street, New Orleans, LA 70119

Scope of work: New Pre-K – 8 School

Funding Source – FEMA, QSCB, NMTC, Insurance Proceeds

Architect – Holly & Smith Architects

Contractor – Gibbs Construction

### Construction Phase

- Installation of interior finishes is ongoing
- Bleacher installation is complete
- State Fire Marshal walk - July 10th
- Anticipated Substantial Completion - July 10th

Contractual Substantial Completion – July 2014

Forecasted Substantial Completion – July 2014

School Ready for Occupancy – August 2014



## **Sophie B. Wright High School Renovation <sup>(RSD)</sup>**

1426 Napoleon Avenue, New Orleans, LA 70115

Scope of work: Renovation of existing school and gymnasium addition

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – TBD

### Procurement Phase

- 1st Advertisement – May 14th
- 2nd Advertisement – May 21st
- 3rd Advertisement – May 28th
- Pre-Bid Conference – May 29th
- Bid Opening – July 17th





## REFURBISHMENTS

### Henry Allen Elementary School Refurbishment <sup>(RSD)</sup>

5626 Loyola Avenue, New Orleans, LA 70115

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Bid Documents are complete
- Procurement will be delayed so that installation of windows will commence during summer break

Procurement Phase

- Anticipated 1st Advertisement – August 2014
- Anticipated Bid Opening – September 2014



### Henry Allen Elementary School Kitchen Refurbishment <sup>(RSD)</sup>

421 Burdette Street, New Orleans, LA 70118

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - SD

- Kitchen work scope is being adjusted per the owners comments
- Schematic Design Documents are due July 17th

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



### Benjamin Banneker Elementary School Kitchen Refurbishment <sup>(RSD)</sup>

5626 Loyola Avenue, New Orleans, LA 70115

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - SD

- Kitchen work scope is being adjusted per the owners comments
- Schematic Design Documents are due July 17th

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



## **Agnes L. Bauduit Elementary School Refurbishment <sup>(RSD)</sup>**

3649 Laurel Street, New Orleans, LA 70115

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor - TBD

### Design Phase - CD

- Bid Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – September 2014
- Anticipated Bid Opening – October 2014



## **Walter L. Cohen High School Kitchen Refurbishment <sup>(RSD)</sup>**

3520 Dryades, New Orleans Street, LA 70115

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - SD

- Kitchen work scope is being adjusted per the owners comments
- Schematic Design Documents are due July 17th

### Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



## **A. D. Crossman School Kitchen Refurbishment <sup>(RSD)</sup>**

4407 South Carrollton Avenue, New Orleans, LA 70119

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - SD

- Kitchen work scope is being adjusted per the owners comments
- Schematic Design Documents are due July 17th

### Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015





## Frederick A. Douglass High School <sup>(RSD)</sup>

3820 St. Claude Avenue, New Orleans, LA 70117

Scope of work: Phased refurbishment of the existing high school

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – FHP Tectonics Corporation

### Construction Phase

- Phase 1 was complete for the start of the school year
- Phase 2 work is complete except for windows
- Removal of the windows and painting of the exterior is ongoing

Contractual Substantial Completion – September 2014

Forecasted Substantial Completion – September 2014



## Warren Easton School <sup>(OPSB)</sup>

3019 Canal Street, New Orleans, LA 70119

Scope of work: Refurbishment of existing high school, including but not limited to structure, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - Tuna Construction

### Procurement Phase

- Bid Opening – June 11th
- Owner is reviewing bid recommendation
- Anticipated Notice to Proceed - August 5th



## Dwight D. Eisenhower Elementary School Refurbishment <sup>(RSD)</sup>

3700 Tall Pines Drive, New Orleans, LA 70131

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Harry Baker Smith Architects II, PLLC

Contractor - TBD

### Design Phase - CD

- Bid Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval
- Procurement will be delayed so that installation of HVAC will commence during summer break
- Anticipated 1st Advertisement – August 2014
- Anticipated Bid Opening – October 2014



## Dwight D. Eisenhower Elementary School Kitchen Refurbishment <sup>(RSD)</sup>

3700 Tall Pines Drive, New Orleans, LA 70131

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - SD

- Kitchen work scope is being adjusted per the owners comments
- Schematic Design Documents are due July 17th

### Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



## William J. Fischer Elementary School Refurbishment <sup>(RSD)</sup>

1801 L.B. Landry Avenue, New Orleans, LA 70114

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - CD

- Schematic Design Documents were received June 26th
- 50% Construction Documents are due August 6th

### Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – December 2014



## Fortier (Lusher) High School Refurbishment <sup>(OPSB)</sup>

5624 Freret Street, New Orleans, LA 70115

Scope of work: Renovation and repairs to the roof, masonry, plaster, windows, exterior doors, canopies, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

### Procurement Phase

- Bid Opening – June 18th
- Owner is reviewing bid recommendation



## Gaudet Elementary School Refurbishment <sup>(RSD)</sup>

12000 Haynes Boulevard, New Orleans, LA 70128

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - SD

- Schematic Design will be delayed due to scope redefinition
- Schematic Design Documents are due August 11th

### Procurement Phase

- Anticipated 1st Advertisement – December 2014
- Anticipated Bid Opening – January 2015



## Gentilly Terrace School Refurbishment <sup>(RSD)</sup>

4720 Painters Street, New Orleans, LA 70122

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

### Design Phase - CD

- Bid Documents are complete

### Procurement Phase

- 1st Advertisement – June 11th
- 2nd Advertisement – June 18th
- 3rd Advertisement – June 25th
- Pre-Bid Conference – June 26th
- Bid Opening – July 16th



## Gentilly Terrace School Kitchen Refurbishment <sup>(RSD)</sup>

4720 Painters Street, New Orleans, LA 70122

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - SD

- Kitchen work scope is being adjusted per the owners comments
- Schematic Design Documents are due July 17th

### Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015





## Samuel J. Green Elementary School Refurbishment <sup>(RSD)</sup>

2319 Valence Street, New Orleans, LA 70115

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

### Design Phase - CD

- Bid Documents are complete

### Procurement Phase

- 1st Advertisement – June 11th
- 2nd Advertisement – June 18th
- 3rd Advertisement – June 25th
- Bid Opening – July 17th



## Edgar P. Harney Elementary School Refurbishment <sup>(RSD)</sup>

2503 Willow Street, New Orleans, LA 70113

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Hamilton Anderson Associates

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents were received June 20th
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – July 2014
- Anticipated Bid Opening – September 2014



## Andrew Jackson School Refurbishment <sup>(RSD)</sup>

1400 Camp Street, New Orleans, LA 70130

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - CD

- Bid Documents are complete
- Procurement will be delayed so that installation of windows will commence during summer break

### Procurement Phase

- Anticipated 1st Advertisement – August 2014
- Anticipated Bid Opening – September 2014



## Andrew Jackson School Kitchen Refurbishment <sup>(RSD)</sup>

1400 Camp Street, New Orleans, LA 70130

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - SD

- Kitchen work scope is being adjusted per the owners comments
- Schematic Design Documents are due July 17th

### Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



## J. W. Johnson Elementary School Refurbishment <sup>(RSD)</sup>

1800 Monroe Street, New Orleans, LA 70118

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - CD

- Schematic Design Documents were received June 23rd
- 50% Construction Documents are due August 11th

### Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – December 2014



## Dr. Martin L. King Elementary School Refurbishment <sup>(RSD)</sup>

1617 Caffin Avenue, New Orleans, LA 70117

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Hamp's Construction, LLC

### Construction

- Pressure washing of the exterior has been completed
- All repairs to gutters and downspouts has been completed

Contractual Substantial Completion – November 2014

Forecasted Substantial Completion – November 2014



## **Dr. Martin L. King Elementary School Kitchen Refurbishment (RSD)**

1617 Caffin Avenue, New Orleans, LA 70117

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - SD

- Kitchen work scope is being adjusted per the owners comments
- Schematic Design Documents are due July 17th

### Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



## **Lafayette Elementary School Refurbishment (RSD)**

2727 South Carrollton Avenue, New Orleans, LA 70118

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - CD

- 50% Construction Documents were received June 5th
- Owner has requested that the project be placed on hold while the scope of work is reviewed

### Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – December 2014



## **Laurel Elementary School Refurbishment (RSD)**

820 Jackson Avenue, New Orleans, LA 70130

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents were received
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – August 2014
- Anticipated Bid Opening – September 2014





## Live Oak Elementary School Refurbishment<sup>(RSD)</sup>

3128 Constance Street, New Orleans, LA 70115

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents were received June 9th
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



## Lusher Elementary School Refurbishment<sup>(OPSB)</sup>

7315 Willow Street, New Orleans, LA 70118

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source – FEMA

Architect – Meyer Engineers, LTD.


Contractor - TBD

### Design Phase - CD

- 100% Construction Documents will be delayed until August 29th due to adjustments with the phasing plan and alternates

### Procurement Phase

- Anticipated 1st Advertisement – September 2014
- Anticipated Bid Opening – November 2014

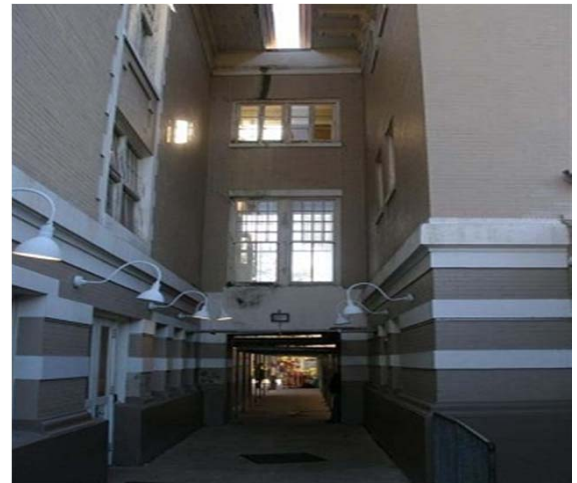

## Thurgood Marshall Elementary School Refurbishment<sup>(RSD)</sup>

4621 Canal Street, New Orleans, LA 70119

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Hamilton Anderson Associates

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents are due September 5th

### Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



## **McDonogh #28 School Refurbishment** <sup>(RSD)</sup>

2733 Esplanade Avenue, New Orleans, LA 70119

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects, LLC

Contractor - TBD

Design Phase – CD

- Bid Documents are complete
- Procurement will be delayed so that installation of windows will commence during summer break

Procurement Phase

- Anticipated 1st Advertisement – September 2014
- Anticipated Bid Opening – October 2014



## **McDonogh #28 School Kitchen Refurbishment** <sup>(RSD)</sup>

2733 Esplanade Avenue, New Orleans, LA 70119

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - SD

- Kitchen work scope is being adjusted per the owners comments
- Schematic Design Documents are due July 17th

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



## **McDonogh #32 School Refurbishment** <sup>(RSD)</sup>

800 DeArmas Street, New Orleans, LA 70114

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- 50% Construction Documents are due July 7th
- 100% Construction Documents are due August 23rd

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014





## **Nelson Elementary School Refurbishment** <sup>(OPSB)</sup>

3121 St. Bernard Avenue, New Orleans, LA 70119

Scope of work: Renovation and repairs to the roof, masonry, windows, exterior doors, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – Harry Baker Smith Architects

Contractor - TBD

Design Phase - CD

- Bid Documents are due end of September

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



## **Sarah T. Reed School Refurbishment** <sup>(RSD)</sup>

5316 Michoud Boulevard, New Orleans, LA 70129

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase - CD

- Bid Documents are being revised by the Architect

Procurement Phase

- Anticipated 1st Advertisement – August 2014
- Anticipated Bid Opening – September 2014



## **Sarah T. Reed School Kitchen Refurbishment** <sup>(RSD)</sup>

5316 Michoud Boulevard, New Orleans, LA 70129

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - SD

- Kitchen work scope is being adjusted per the owners comments
- Schematic Design Documents are due July 17th

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



## Rosenwald Elementary School Refurbishment <sup>(RSD)</sup>

6501 Berkley Drive, New Orleans, LA 70131

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

### Design Phase – SD

- Program Completion Documents were received June 11th
- Schematic Design Documents are due July 6th

### Procurement Phase

- Anticipated 1st Advertisement – December 2014
- Anticipated Bid Opening – January 2015



## Henry C. Schaumburg Elementary School <sup>(RSD)</sup>

9501 Grant Street, New Orleans, LA 70127

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc

Contractor - TBD

### Design Phase - CD

- Bid Documents are complete

### Procurement Phase

- 1st Advertisement – June 11th
- 2nd Advertisement – June 18th
- 3rd Advertisement – June 25th
- Pre-Bid Conference – June 26th
- Bid Opening – July 16th



## Village de l'Est Elementary School Refurbishment <sup>(RSD)</sup>

5100 Cannes Street, New Orleans, LA 70129

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CBDG

Architect – Duplantis Design Group, PC

Contractor - TBD

### Design Phase - CD

- 50% Construction Documents were received June 10th
- 100% Construction Documents are due July 27th

### Procurement Phase

- Anticipated 1st Advertisement – September 2014
- Anticipated Bid Opening – October 2014



## **Albert Wicker School Kitchen Refurbishment** <sup>(RSD)</sup>

2011 Bienville Street, New Orleans, LA 70112

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - SD

- Kitchen work scope is being adjusted per the owners comments
- Schematic Design Documents are due July 17th

### Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



## **Sylvanie F. Williams School Refurbishment** <sup>(RSD)</sup>

3127 Martin Luther King Jr. Boulevard, New Orleans, LA 70125

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - CD

- Bid Documents are complete

### Procurement Phase

- 1st Advertisement – July 30th
- 2nd Advertisement – August 6th
- 3rd Advertisement – August 13th
- Pre-Bid Conference – August 14th
- Bid Opening – September 3rd



## OTHER PROJECTS

### **Timbers III - Building Controls** <sup>(OPSB)</sup>

3520 General DeGaulle Drive, New Orleans, LA 70114

Scope of work: Design and installation of new building controls

Funding Source – OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - TBD

#### Design Phase - PC

- Program Completion Documents are due July 8th

#### Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – December 2014



### **Timbers III - IT Room Relocation** <sup>(OPSB)</sup>

3520 General DeGaulle Drive, New Orleans, LA 70114

Scope of work: Relocation of the Information Technology Room

Funding Source – OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - TBD

#### Design Phase - CD

- 100% Construction Documents are due July 7th

#### Procurement Phase

- Anticipated 1st Advertisement – July 2014
- Anticipated Bid Opening – August 2014





## Building Automation System Integration At Recovery School District Central And Remote Offices <sup>(RSD)</sup>

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview

Funding Source – FEMA

Architect – Moses Engineers

Contractor – Synergy Building Solutions, Inc.

### Construction Phase

- The five Quick Start Schools are complete, the Energy Dash Board is being implemented
- Sylvanie Williams Elementary School, Sarah T. Reed Elementary School, Fannie C. Williams Elementary School, Bienville Elementary School, Charles L. Colton Elementary School, William Frantz Elementary School, Parkview Elementary School, Osborne Elementary School, and Carter G. Woodson Elementary School are complete
- New integration work is ongoing on Dolores T Aaron Elementary School, A. D. Crossman Elementary School, Benjamin Banneker Elementary School, Walter Cohen High School, and Albert Wicker Elementary School
- Lawrence D. Crocker Elementary School is anticipated to start integration to the BAS early September 2014

Contractual Substantial Completion – November 2014

Forecasted Substantial Completion – November 2014



## MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

### **Andrew J. Bell Junior High School Mothball** <sup>(RSD)</sup>

1010 N. Galvez St., New Orleans, LA 70119

Scope of work: Design Services to assist in determining the condition of the facilities both interior and exterior, make recommendations to stabilize the facilities and provide drawings required to provide a water barrier, ventilation, and rudimentary fire detection and to secure openings and entryways. Construction Services to stabilize the facility according to the designer's drawings and specifications.

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – CDW Services, LLC

#### Mothballing of Closed Schools - Safe & Secure

- Mothballing of the Gymnasium, Administration Building, Annex, Building "C", Building "D", Chapel, & E.A.Christy Building

#### Construction Phase

- 95% of the window panels on the main building are installed
- Removal of debris from the Christy building is ongoing
- Roof system on the administration building is 85% complete
- Wood shoring in the main building is 85% complete
- Tuck-pointing of the main façade has been completed

Contractual Substantial Completion – May 2014

Forecasted Substantial Completion – July 2014



### **Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School** <sup>(RSD)</sup>

1010 N. Galvez St. & 2327 St. Philip Street, New Orleans, LA 70119

Scope of work: Demolition of existing caretakers cottages

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

#### Design Phase - CD

- 50% Construction Documents were received June 25th
- 100% Construction Documents are due July 28th

#### Procurement Phase

- Anticipated 1st Advertisement – September 2014
- Anticipated Bid Opening – October 2014



## **John F. Kennedy Modular Demolition (RSD)**

5700 Wisner Boulevard, New Orleans, LA 70124

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Harry Baker Smith Architects

Contractor – Hamps Construction

### Procurement Phase

- Signed contracts were returned the end of June



## **George Mondy Elementary School Mothball (RSD)**

2327 St. Philip Street, New Orleans, LA 70119

Scope of work: Design Services to assist in determining the condition of the facilities both interior and exterior, make recommendations to stabilize the facilities and provide drawings required to provide a water barrier, ventilation, and rudimentary fire detection and to secure openings and entryways. Construction Services to stabilize the facility according to the designer's drawings and specifications.

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

### Design Phase - CD

- 50% Construction Documents were received June 16th
- 100% Construction Documents are due July 15th

### Procurement Phase

- Anticipated 1st Advertisement – December 2014
- Anticipated Bid Opening – January 2015



## Comprehensive List - Completed Projects

- 1 Abrams | Morial | Abramson | Coghill Demolition <sup>(RSD)</sup>
- 2 A. D. Cross Elementary School Energy Conservation <sup>(RSD)</sup>
- 3 A. D. Crossman Elementary School and Benjamin Banneker Elementary School <sup>(RSD)</sup>
- 4 A. D. Crossman Elementary School Refurbishment <sup>(RSD)</sup>
- 5 A. P. Tureaud Elementary School Roof Repairs <sup>(RSD)</sup>
- 6 Agnes Bauduit Elementary School Boiler <sup>(RSD)</sup>
- 7 Albert Wicker Elementary School Refurbishment <sup>(RSD)</sup>
- 8 Albert Wicker Elementary School Roof Repairs <sup>(RSD)</sup>
- 9 Alfred Lawless Senior High Security Fencing <sup>(RSD)</sup>
- 10 Alice M. Harte Elementary School Demolition <sup>(OPSB)</sup>
- 11 Andrew J. Bell Junior High School Roof Replacement <sup>(RSD)</sup>
- 12 Andrew Jackson Elementary School Roof Repairs <sup>(RSD)</sup>
- 13 Andrew Jackson Elementary School Solar Panels <sup>(RSD)</sup>
- 14 Andrew H. Wilson Elementary School Cottage <sup>(RSD)</sup>
- 15 Arthur Ashe Elementary School Kitchen Renovation <sup>(OPSB)</sup>
- 16 Augustine Elementary School Roof <sup>(RSD)</sup>
- 17 Avery-Alexander Elementary School Demolition <sup>(RSD)</sup>
- 18 Barbara C. Jordan Elementary School Demolition <sup>(RSD)</sup>
- 19 Bell JH Shoring <sup>(RSD)</sup>
- 20 Benjamin Banneker Elementary School Energy Conservation <sup>(RSD)</sup>
- 21 Benjamin Franklin Senior High School <sup>(OPSB)</sup>
- 22 Bienville Elementary School Demolition <sup>(RSD)</sup>
- 23 Booker T. Washington High School Partial Demolition <sup>(RSD)</sup>
- 24 Carter G. Woodson Middle School Demolition <sup>(RSD)</sup>
- 25 Central Services Warehouse Demolition <sup>(OPSB)</sup>
- 26 Charles J. Colton Elementary Selective Demolition <sup>(RSD)</sup>
- 27 Charles J. Colton Elementary School <sup>(RSD)</sup>
- 28 Charles R. Drew Elementary Roof & Installation of Kitchen Hood <sup>(RSD)</sup>
- 29 Cohen High School Health Clinic <sup>(RSD)</sup>
- 30 Douglass High School Under Floor Utilities <sup>(RSD)</sup>
- 31 Dr. Martin Luther King School Roof Repairs <sup>(RSD)</sup>
- 32 Dr. Martin Luther King Jr. School Renovation <sup>(RSD)</sup>
- 33 Dwight D. Eisenhower Elementary School Roof Repairs <sup>(RSD)</sup>
- 34 East Bank Swing Space for Audubon Charter School <sup>(OPSB)</sup>
- 35 Edgar P. Harney Elementary School Roof Repairs <sup>(RSD)</sup>
- 36 Edna Karr High School - Gymnasium Repair <sup>(OPSB)</sup>
- 37 Edward Livingston Middle School Demolition <sup>(RSD)</sup>



- 38 Edward Henry Phillips Junior High School Demolition <sup>(OPSB)</sup>
- 39 New Edward Hynes School <sup>(OPSB)</sup>
- 40 Edwards | Hardin | Lockett | Lawless Demolition <sup>(RSD)</sup>
- 41 Eleanor L. McMain School Replacement of Existing Chillers <sup>(OPSB)</sup>
- 42 Eleanor L. McMain School Clinic <sup>(OPSB)</sup>
- 43 Ernest N. Morial Elementary Security Fencing <sup>(RSD)</sup>
- 44 Fannie C. Williams Elementary School Demolition <sup>(RSD)</sup>
- 45 Fisk-Howard Elementary School Demolition <sup>(RSD)</sup>
- 46 Florence J. Chester Elementary School Demolition <sup>(RSD)</sup>
- 47 Francis W. Gregory Demolition <sup>(RSD)</sup>
- 48 Frederick A. Douglass High Switchgear <sup>(RSD)</sup>
- 49 Frederick A. Douglass High Emergency Boiler Roof Repairs <sup>(RSD)</sup>
- 50 George Mondy Elementary School Mothball <sup>(RSD)</sup>
- 51 George Washington Carver High School Demolition <sup>(RSD)</sup>
- 52 Greater St. Stephens School <sup>(OPSB)</sup>
- 53 Henry Allen Elementary School Roof <sup>(RSD)</sup>
- 54 Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation <sup>(RSD)</sup>
- 55 Holy Cross Modular Relocation <sup>(RSD)</sup>
- 56 Israel M. Augustine Middle School Roof Replacement <sup>(RSD)</sup>
- 57 Israel M. Augustine Middle School Mothball <sup>(RSD)</sup>
- 58 James Derham Demolition <sup>(RSD)</sup>
- 59 James W. Johnson Elementary School Roof <sup>(RSD)</sup>
- 60 New Jean Batiste de Bienville School <sup>(RSD)</sup>
- 61 Jean Gordon Elementary School Demolition <sup>(RSD)</sup>
- 62 John Dibert Elementary School Roof <sup>(RSD)</sup>
- 63 John W. Hoffman Elementary School Demolition <sup>(RSD)</sup>
- 64 John F. Kennedy Modular Relocation (Schwarz Campus) <sup>(RSD)</sup>
- 65 John F. Kennedy Modular Relocation (Coghill Modular Campus) <sup>(RSD)</sup>
- 66 John F. Kennedy High School Demolition <sup>(RSD)</sup>
- 67 John McDonogh Senior High School Bleachers and Sprinklers <sup>(RSD)</sup>
- 68 John McDonogh Senior High School Roof <sup>(RSD)</sup>
- 69 John A. Shaw Elementary School Mothball <sup>(RSD)</sup>
- 70 Joseph S. Clark Senior High School Roof Repairs <sup>(RSD)</sup>
- 71 Joseph A. Craig Elementary Canopies <sup>(RSD)</sup>
- 72 Joseph A. Craig Elementary Elevator Installation <sup>(RSD)</sup>
- 73 Joseph A. Hardin Elementary Security Fencing <sup>(RSD)</sup>
- 74 Lafayette Elementary School Roof and Masonry <sup>(RSD)</sup>
- 75 Lake Area | Landry Demolition <sup>(RSD)</sup>
- 76 Langston Hughes Elementary School (Phase I) <sup>(RSD)</sup>
- 77 Langston Hughes Elementary School - New Gymnasium (Phase II) <sup>(RSD)</sup>
- 78 Langston Hughes Elementary School - Dumpster Pad <sup>(RSD)</sup>
- 79 Lawrence D. Crocker Elementary School Demolition <sup>(RSD)</sup>
- 80 L.B. Landry Annex Demolition <sup>(RSD)</sup>
- 81 Little Woods Elementary School Demolition <sup>(RSD)</sup>
- 82 Little Woods School (Dolores T. Aaron Elementary School) <sup>(RSD)</sup>

- 83 Live Oak Elementary School Roof <sup>(RSD)</sup>
- 84 Live Oak Elementary School Exterior Door Replacement <sup>(RSD)</sup>
- 85 Lorraine Hansberry Elementary School Mothball <sup>(RSD)</sup>
- 86 Louis D. Armstrong Elementary School <sup>(RSD)</sup>
- 87 Mahalia Jackson Elementary School <sup>(OPSB)</sup>
- 88 Mahalia Jackson Elementary School Dumpster / Other Improvements <sup>(OPSB)</sup>
- 89 Mahalia Jackson Elementary School Office Renovation <sup>(OPSB)</sup>
- 90 Martin Behrman Elementary School Roof <sup>(RSD)</sup>
- 91 Martin Luther King Jr. Elementary Canopy System <sup>(RSD)</sup>
- 92 Martin Luther King Jr. School Modular Building, Deck, Canopy <sup>(RSD)</sup>
- 93 Mary Church Terrell Elementary School Demolition <sup>(RSD)</sup>
- 94 Mary M. Bethune Elementary 1st Floor Replacement <sup>(OPSB)</sup>
- 95 Mary M. Bethune Elementary Rear Yard Repair/Resurfacing <sup>(OPSB)</sup>
- 96 McDonogh #7 High School Repairs <sup>(OPSB)</sup>
- 97 McDonogh #15 Elementary Exterior Masonry to SOI Standards <sup>(RSD)</sup>
- 98 McDonogh #28 Elementary School Roof <sup>(RSD)</sup>
- 99 McDonogh #32 Roof Replacement <sup>(RSD)</sup>
- 100 McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium <sup>(OPSB)</sup>
- 101 McDonogh #42 Elementary School Roof <sup>(RSD)</sup>
- 102 McDonogh #42 Elementary School HVAC Replacement <sup>(RSD)</sup>
- 103 Mildred C. Osborne Elementary School Demolition <sup>(RSD)</sup>
- 104 Mildred C. Osborne Elementary School <sup>(RSD)</sup>
- 105 Modular Campuses Close Outs <sup>(RSD)</sup>
- 106 Modular Classroom Demolition at Fannie C. Williams Elementary School <sup>(RSD)</sup>
- 107 Modular Structures at Langston Hughes Elementary School <sup>(RSD)</sup>
- 108 Morris F.X. Jeff Elementary School Demolition <sup>(RSD)</sup>
- 109 Morris F.X. Jeff Elementary School Mothball <sup>(RSD)</sup>
- 110 Murray G. Henderson Elementary School Roof <sup>(RSD)</sup>
- 111 New Andrew H. Wilson Elementary School <sup>(RSD)</sup>
- 112 New Carter G. Woodson School <sup>(RSD)</sup>
- 113 New Fannie C. Williams School <sup>(RSD)</sup>
- 114 New Joseph A. Craig Elementary School <sup>(RSD)</sup>
- 115 New L.B. Landry High School <sup>(RSD)</sup>
- 116 New Lake Area High School <sup>(RSD)</sup>
- 117 New Lawrence D. Crocker School <sup>(RSD)</sup>
- 118 New Parkview School <sup>(RSD)</sup>
- 119 New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens <sup>(RSD)</sup>
- 120 New William Frantz Elementary School <sup>(RSD)</sup>
- 121 New Orleans High School Signature Center Study <sup>(RSD)</sup>
- 122 Oretha C. Haley Demo <sup>(RSD)</sup>
- 123 Oretha C. Haley Elementary School Mothball <sup>(RSD)</sup>
- 124 Parkview Elementary School Demolition <sup>(RSD)</sup>
- 125 Paul L. Dunbar Elementary School Demolition <sup>(RSD)</sup>
- 126 Paul B. Habans Elementary School Roof Repairs <sup>(RSD)</sup>

- 127 Phillis Wheatley Elementary School Demolition <sup>(RSD)</sup>
- 128 Robert M. Lusher Elementary Roof Removal & Replacement <sup>(OPSB)</sup>
- 129 Sarah T. Reed High School Bleachers <sup>(RSD)</sup>
- 130 Sarah T. Reed High School Auditorium Wall <sup>(RSD)</sup>
- 131 Seabrook Computer Training Center Demolition <sup>(OPSB)</sup>
- 132 Schaumburg Chillers <sup>(RSD)</sup>
- 133 Schwarz Alternative Repairs <sup>(RSD)</sup>
- 134 Schwarz Alternative Modularity Demolition <sup>(RSD)</sup>
- 135 Sherwood Forest Elementary School Demolition <sup>(RSD)</sup>
- 136 Sophie B. Wright School Selective Demolition <sup>(RSD)</sup>
- 137 Sophie B. Wright Various Repairs/Restroom Renovations <sup>(OPSB)</sup>
- 138 Stuart R. Bradley Elementary School Demolition <sup>(RSD)</sup>
- 139 Sylvanie Williams Elementary School AHU Replacement <sup>(RSD)</sup>
- 140 Sylvanie Williams Elementary School Play Yard <sup>(RSD)</sup>
- 141 Sylvanie Williams Elementary School Roof Repairs <sup>(RSD)</sup>
- 142 Sylvanie Williams Elementary School HVAC/Chiller Replacement <sup>(RSD)</sup>
- 143 Temporary Campus for McDonogh #11 Expropriation <sup>(OPSB)</sup>
- 144 Thomas A. Edison Elementary School Demolition <sup>(RSD)</sup>
- 145 Thomy Lafon Elementary School Demolition <sup>(RSD)</sup>
- 146 Thomy Lafon School Interpretative Display <sup>(RSD)</sup>
- 147 Timbers Park Office Building #1 & #2 Demolition <sup>(OPSB)</sup>
- 148 Timbers HVAC <sup>(OPSB)</sup>
- 149 Village de L'est Elementary School Subsidence <sup>(RSD)</sup>
- 150 Village de L'est Elementary School Roof and Modular Demolition <sup>(RSD)</sup>
- 151 Vorice J. Waters Elementary School Demolition <sup>(RSD)</sup>
- 152 Valena C. Jones Elementary School <sup>(RSD)</sup>
- 153 Walter L. Cohen High School HVAC <sup>(RSD)</sup>
- 154 Warren Easton High School Window Replacement <sup>(OPSB)</sup>
- 155 West Bank Swing Space for Alice Harte Elementary School <sup>(OPSB)</sup>
- 156 New William J. Guste Elementary School <sup>(RSD)</sup>
- 157 William J. Guste Elementary School Science Lab <sup>(RSD)</sup>
- 158 William Frantz Elementary School Environmental Remediation & Selective Demolition <sup>(RSD)</sup>
- 159 William Frantz Elementary School Roof <sup>(RSD)</sup>

# June 2014 Program Update OPSB & RSD Phase I Projects


## Program Financial Status

The **OPSB** has \$164 million in open contracts for the Phase 1 capital program projects after issuing \$79 thousand in new contracts, change orders and amendments in June. In addition, the total change orders to date, \$2.5 million, accounts for approximately two percent (1.69%) of the total open Phase 1 construction contracts. Finally, OPSB anticipates issuing no new contracts in Phase 1 construction or professional services contracts/amendments in July.

The **RSD** has \$173 million in open contracts for the Phase 1 capital program projects after issuing \$238 thousand in new contracts and \$813 thousand in change orders and amendments in June. In addition, the total change orders to date, \$5 million, accounts for approximately three percent (3.39%) of the total open Phase 1 construction contracts. Finally, RSD anticipates issuing \$416 thousand in Phase 1 contracts, change orders, and professional services contracts/amendments in July.


Value of Projects by Phase

Design	\$	-
Procurement	\$	6,845,791
Construction	\$	165,062,829
Complete	\$	41,666,113
Future Projects	\$	-

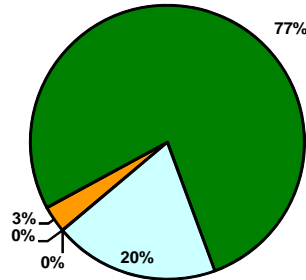

Value of Projects by Phase

Design	\$	-
Procurement	\$	-
Construction	\$	61,843,494
Complete	\$	407,017,665
Future Projects	\$	-

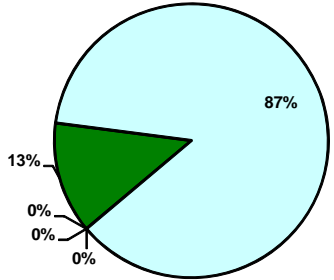

Note-The value in each phase represents the total of full project budgets.

## Program Schedule Status

OPSB Phase 1 Projects				
Group 1				
Project	Design	Procurement	Construction	Complete
Mahalia Jackson	Occupied (May 2010)			
Edward Hynes School	Occupied (January 2012)			
Group 2				
Project	Design	Procurement	Construction	Complete
Audubon School				
Alice Harte School				
McMain School - Stabilization				
- Health Clinic	Complete (August 2013)			
- Gymnasium				
McDonogh 35 HS (Phillips/Waters)				
New PK-8 at N Kenilworth (Moton)				

RSD Phase 1 Projects				
Group 1				
Project	Design	Procurement	Construction	Complete
Guste ES	Occupied (August 2008)			
Langston Hughes ES	Occupied (August 2009)			
Andrew H. Wilson ES	Occupied (January 2010)			
Lake Area HS	Occupied (January 2010)			
L.B. Landry HS	Occupied (July 2010)			
Joseph A. Craig ES	Occupied (January 2010)			
Jean Batiste de Bienville ES	Occupied (July 2012)			
Parkview ES	Occupied (August 2012)			
Lawrence D. Crocker ES	Occupied (September 2012)			
Fannie C. Williams ES	Occupied (October 2012)			
Carter G. Woodson ES	Occupied (October 2012)			
Mildred Osborne ES	Occupied (August 2012)			
William Frantz ES	Occupied (August 2013)			
Charles J. Colton ES	Occupied (June 2013)			
Group 2				
Project	Design	Procurement	Construction	Complete
Little Woods ES	Occupied (May 2013)			
Phillis Wheatley ES				
Edward Livingston HS				





# June 2014 Program Update OPSB & RSD Phase 2 Projects




## Program Financial Status

The **OPSB** has \$41 million in open contracts for the Phase 2 capital program projects after issuing no new contracts and \$63 thousand in change orders and amendments in June. In addition, the total change orders to date, \$316 thousand, account for approximately one percent (0.88%) of the total open Phase 2 construction contracts. OPSB anticipates issuing no new contracts in Phase 2 construction and \$626 thousand in professional services in July.

The **RSD** has \$362 million in open contracts for the Phase 2 capital program projects after issuing \$109 million in new contracts and \$343 thousand in change orders and amendments in June. Additionally, the total change orders to date, -\$1.1 million, account for approximately less than one percent (-0.40%) of the total open Phase 2 construction contracts. The RSD anticipates issuing \$178 thousand in Phase 2 construction contracts/change orders and no professional services contracts/amendments in July.


Value of Projects by Phase

Design	\$ 9,523,713
Procurement	\$ 64,725,169
Construction	\$ 40,606,238
Complete	\$ -
Future Projects	\$ 37,993,149

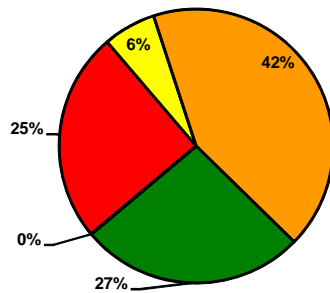

Value of Projects by Phase

Design	\$ 261,993,695
Procurement	\$ 193,602,984
Construction	\$ 240,269,446
Complete	\$ 1,071,083
Future Projects	\$ 229,280,287

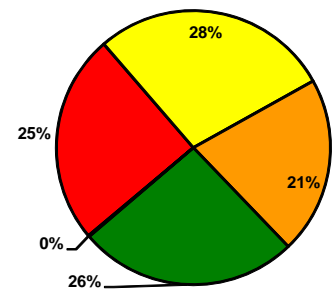

Note-The value in each phase represents the total of full project budgets.

## Program Schedule Status

OPSB Phase 2 Projects				
New Schools				
Project	Design	Procurement	Construction	Complete
Bio District HS				
Lake Forest PK-8 @ GSt Stephens				
New Karr HS @ JoEllen Smith D/B				
Full Renovations				
Project	Design	Procurement	Construction	Complete
Ben Franklin ES				
Refurbished/Renovations				
Project	Design	Procurement	Construction	Complete
Ben Franklin HS				
Bethune ES				
Warren Easton				
Fortier (Lusher) HS				
Lusher ES				
Nelson ES				

RSD Phase 2 Projects				
New Schools				
Project	Design	Procurement	Construction	Complete
Abrams HS				
Alexander ES				
Behrman ES				
Booker T. Washington HS				
Bradley				
Dunbar ES				
Fischer ES				
Fisk-Howard				
Gaudet ES				
George W. Carver HS - D/B				
Habans ES D/B				
Alfred Lawless				
Edward Livingston				
Morial				
New Algiers PreK-8				
New Orleans East (Abramson)				
Sherwood Forest ES D/B				

RSD Phase 2 Projects				
Full Renovations				
Project	Design	Procurement	Construction	Complete
Clark HS				
Drew ES				
John McDonogh HS				
Johnson ES				
Lafayette ES				
Live Oak ES				
McDonogh 42 ES				
Sophie B Wright ES				
Tubman ES				
Refurbished/Renovations				
Project	Design	Procurement	Construction	Complete
Allen ES				
Bauduit ES				
Crossman ES	Completed April, 2014			
Douglass HS				
Eisenhower HS				
Fischer ES				
Gaudet ES				
Gentilly Terrace ES				
Green MS				
Harney ES				
A. Jackson ES				
Johnson ES				
Lafayette ES				
Laurel ES				
Live Oak ES				
Marshall ES				
Martin L. King ES				
McDonogh 28 ES				
McDonogh 32 ES				
McDonogh 7 ES				
O Perry Walker HS				
Reed HS				
Rosenwald ES				
Schaumburg ES				
Schwarz HS				
Sylvanie Williams				
Village de l'est ES				
Wicker ES	Completed April, 2014			



**BESE MONTHLY REPORT**  
OPEN CONTRACTS as of 07/08/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
<b>DEMOLITIONS</b>					
Kennedy HS Demolition	Shaw Environmental & Infrastructure	FEMA	\$ 186,028.68	\$ 125,485.17	\$ 311,513.85
<b>Kennedy HS Demolition Total</b>					<b>\$ 311,513.85</b>
Booker T Washington HS Demolition - Annex & Accessory Bldgs	Shaw Environmental & Infrastructure	FEMA	\$ 49,500.00	\$ 14,640.00	\$ 64,140.00
<b>Booker T Washington HS Demolition - Annex &amp; Accessory Bldgs Total</b>					<b>\$ 64,140.00</b>
Fannie C Williams - Modular Bldgs Demolition	VergesRome Architects, APAC	FEMA	\$ 30,575.00	\$ (18,275.00)	\$ 12,300.00
<b>Fannie C Williams - Modular Bldgs Demolition Total</b>					<b>\$ 12,300.00</b>
George Mondy - Caretakers Cottage Demo	VergesRome Architects, APAC	FEMA	\$ -	\$ 1,823.00	\$ 1,823.00
<b>George Mondy - Caretakers Cottage Demo Total</b>					<b>\$ 1,823.00</b>
Andrew Bell - Caretakers Cottage Demo	VergesRome Architects, APAC	FEMA	\$ -	\$ 1,690.00	\$ 1,690.00
<b>Andrew Bell - Caretakers Cottage Demo Total</b>					<b>\$ 1,690.00</b>
Kennedy HS Modular Demolition	Harry Baker Smith Architects II, PLLC	FEMA	\$ 5,225.00	\$ -	\$ 5,225.00
<b>Kennedy HS Modular Demolition Total</b>					<b>\$ 5,225.00</b>
<b>PHASE 4 SCHOOLS</b>					
FC Williams ES Construction	Yeates & Yeates Architects, LLC Brice Building Company	FEMA FEMA	\$ - \$ 21,997,000.00	\$ 2,094,877.92 \$ 902,827.77	\$ 2,094,877.92 \$ 22,899,827.77
<b>FC Williams ES Construction Total</b>					<b>\$ 24,994,705.69</b>
FC Williams ES Playground Equipment Relocation	Mahlum Scairono Martinez Architects, LLC Hamp's Construction, LLC	FEMA FEMA	\$ 14,250.00 \$ 93,300.00	\$ - \$ -	\$ 14,250.00 \$ 93,300.00
<b>FC Williams ES Playground Equipment Relocation Total</b>					<b>\$ 107,550.00</b>
FC Williams ES Outdoor Teaching Area	Tuna Construction, LLC	Insurance Proceeds	\$ 165,000.00	\$ -	\$ 165,000.00
<b>FC Williams ES Outdoor Teaching Area Total</b>					<b>\$ 165,000.00</b>
Crocker ES Construction	Chenevert Architects, LLC Mathes Briere Architects Farnsworth Group, Inc - Building Commissioning 7 New & Reno Satterfield & Pontikes Construction Group LLC Harry Baker Smith Architects II, PLLC	FEMA FEMA FEMA FEMA FEMA	\$ - \$ 50,000.00 \$ 157,600.00 \$ 18,598,500.00 \$ 9,384.00	\$ 1,653,183.82 \$ - \$ 67,731.38 \$ 911,998.41 \$ -	\$ 1,653,183.82 \$ 50,000.00 \$ 225,331.38 \$ 19,510,498.41 \$ 9,384.00
<b>Crocker ES Construction Total</b>					<b>\$ 21,448,397.61</b>
Crocker ES Playground Equipment Relocation	Mahlum Scairono Martinez Architects, LLC Hamp's Construction, LLC	FEMA FEMA	\$ 10,695.00 \$ 70,400.00	\$ - \$ -	\$ 10,695.00 \$ 70,400.00
<b>Crocker ES Playground Equipment Relocation Total</b>					<b>\$ 81,095.00</b>
Crocker ES Demolition	Chenevert Architects, LLC	FEMA	\$ -	\$ 56,170.50	\$ 56,170.50
<b>Crocker ES Demolition Total</b>					<b>\$ 56,170.50</b>
Frantz ES Renovation/Addition	Billes Architecture, LLC Farnsworth Group, Inc - Building Commissioning Quickstart The Lathan Company Harry Baker Smith Architects II, PLLC	FEMA FEMA FEMA FEMA	\$ 855,945.00 \$ - \$ 19,537,000.00 \$ 24,522.00	\$ - \$ 213,151.48 \$ 1,242,806.32 \$ -	\$ 2,473,044.11 \$ 213,151.48 \$ 20,779,806.32 \$ 24,522.00
<b>Frantz ES Renovation/Addition Total</b>					<b>\$ 23,490,523.91</b>
Colton ES Renovation	Waggonner & Ball Architects, APC Farnsworth Group, Inc - Building Commissioning 7 New & Reno F.H. Paschen, S.N. Nielsen & Associates, LLC Harry Baker Smith Architects II, PLLC	FEMA FEMA FEMA FEMA	\$ 1,208,475.00 \$ 164,900.00 \$ 26,173,000.00 \$ 5,506.00	\$ 1,727,030.20 \$ 61,473.00 \$ 665,424.66 \$ -	\$ 2,935,505.20 \$ 226,373.00 \$ 26,838,424.66 \$ 5,506.00
<b>Colton ES Renovation Total</b>					<b>\$ 30,005,808.86</b>
Osborne ES Construction	Fauntleroy & Latham Architects, APC Farnsworth Group, Inc - Building Commissioning 7 New & Reno F.H. Paschen, S.N. Nielsen & Associates, LLC Harry Baker Smith Architects II, PLLC	FEMA FEMA FEMA FEMA	\$ 1,336,822.00 \$ 157,600.00 \$ 21,375,000.00 \$ 3,055.00	\$ 648,317.17 \$ 48,039.00 \$ 309,690.20 \$ -	\$ 1,985,139.17 \$ 205,639.00 \$ 21,684,690.20 \$ 3,055.00
<b>Osborne ES Construction Total</b>					<b>\$ 23,878,523.37</b>
Woodson ES Construction	Farnsworth Group, Inc - Building Commissioning 7 New & Reno Harry Baker Smith Architects II, PLLC	FEMA FEMA	\$ 157,600.00 \$ 1,904.00	\$ 72,075.38 \$ -	\$ 229,675.38 \$ 1,904.00
<b>Woodson ES Construction Total</b>					<b>\$ 231,579.38</b>
Parkview ES Construction	Farnsworth Group, Inc - Building Commissioning 7 New & Reno Harry Baker Smith Architects II, PLLC	FEMA FEMA	\$ 157,600.00 \$ 2,449.00	\$ 60,622.00 \$ -	\$ 218,222.00 \$ 2,449.00
<b>Parkview ES Construction Total</b>					<b>\$ 220,671.00</b>
Parkview ES Playground Equipment Relocation	Mahlum Scairono Martinez Architects, LLC Hamp's Construction, LLC	FEMA FEMA	\$ 10,695.00 \$ 73,800.00	\$ - \$ -	\$ 10,695.00 \$ 73,800.00
<b>Parkview ES Playground Equipment Relocation Total</b>					<b>\$ 84,495.00</b>
Little Woods ES Construction	Group Novak, LLC Farnsworth Group, Inc - Building Commissioning 5 plus 2 MAPP Construction, LLC	FEMA FEMA FEMA	\$ 1,498,299.00 \$ 222,742.00 \$ 21,980,000.00	\$ 391,394.41 \$ 13,506.00 \$ 143,254.21	\$ 1,889,693.41 \$ 236,248.00 \$ 22,123,254.21
<b>Little Woods ES Construction Total</b>					<b>\$ 24,249,195.62</b>



**BESE MONTHLY REPORT**  
OPEN CONTRACTS as of 07/08/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
Little Woods ES Playground Equipment Relocation	Mahlum Scairono Martinez Architects, LLC	FEMA	\$ -	\$ 10,695.00	\$ 10,695.00
<b>Little Woods ES Playground Equipment Relocation Total</b>					<b>\$ 10,695.00</b>
Wheatley ES New Construction	Holly & Smith Architects, APAC	FEMA	\$ 1,749,900.00	\$ 494,002.93	\$ 2,243,902.93
	Farnsworth Group, Inc - Building Commissioning 5 plus 2	FEMA	\$ 222,742.00	\$ -	\$ 222,742.00
	Gibbs Construction, L.L.C.	QSCB	\$ 25,275,000.00	\$ 960,577.82	\$ 26,235,577.82
<b>Wheatley ES New Construction Total</b>					<b>\$ 28,702,222.75</b>
Wheatley ES Interpretive Display	Bright Moments, LLC	FEMA	\$ 4,125.00	\$ -	\$ 4,125.00
<b>Wheatley ES Interpretive Display Total</b>					<b>\$ 4,125.00</b>
<b>PHASE 2 SCHOOLS</b>					
Fisk-Howard ES Construction	VergesRome Architects, APAC + Fanning Howey, A Joint Venture	FEMA	\$ 1,582,878.00	\$ 340,771.44	\$ 1,923,649.44
	Farnsworth Group, Inc - Building Commissioning 5 plus 2	FEMA	\$ 222,742.00	\$ 20,048.56	\$ 242,790.56
	FHP Tectonics Corp.	FEMA	\$ 25,580,947.45	\$ 235,329.64	\$ 25,816,277.09
		Insurance Proceeds	\$ 19,052.55	\$ -	\$ 19,052.55
<b>Fisk-Howard ES Construction Total</b>					<b>\$ 28,001,769.64</b>
New High School @ Alfred Lawless	Sizeler Thompson Brown Architects Project Design Group, LLC	FEMA	\$ 1,981,345.00	\$ 39,809.00	\$ 2,021,154.00
	Farnsworth Group, Inc - Building Commissioning 5 plus 2	FEMA	\$ 321,880.00	\$ (94,990.49)	\$ 226,889.51
	CORE Construction Services, L.L.C.	FEMA	\$ 35,728,664.00	\$ (364,619.78)	\$ 35,364,044.22
		Insurance Proceeds	\$ 45,336.00	\$ -	\$ 45,336.00
<b>New High School @ Alfred Lawless Total</b>					<b>\$ 37,657,423.73</b>
Dunbar ES Construction	Chenevert Architects, LLC	FEMA	\$ 1,437,088.00	\$ 409,305.28	\$ 1,846,393.28
	Farnsworth Group, Inc - Building Commissioning 5 plus 2	FEMA	\$ 222,742.00	\$ (45,060.09)	\$ 177,681.91
	The McDonnell Group, LLC	FEMA	\$ 24,457,000.00	\$ (113,540.75)	\$ 24,343,459.25
		Insurance Proceeds	\$ 35,000.00	\$ -	\$ 35,000.00
<b>Dunbar ES Construction Total</b>					<b>\$ 26,402,534.44</b>
Bradley ES Renovation/Construction	Sizeler Thompson Brown Architects Project Design Group, LLC	FEMA	\$ 1,582,878.00	\$ 42,076.05	\$ 1,624,954.05
	Farnsworth Group, Inc - Building Commissioning 1N + 4R	FEMA	\$ 223,767.17	\$ (67,638.97)	\$ 156,128.20
	Landis Construction Co., LLC	FEMA	\$ 25,424,627.00	\$ (566,090.12)	\$ 24,858,536.88
		Insurance Proceeds	\$ 21,373.00	\$ -	\$ 21,373.00
<b>Bradley ES Renovation/Construction Total</b>					<b>\$ 26,660,992.13</b>
Drew ES Renovation	Blich Knevel Architects, Inc.	FEMA	\$ 1,456,546.00	\$ 32,208.60	\$ 1,488,754.60
	Farnsworth Group, Inc - Building Commissioning 1N + 4R	FEMA	\$ 203,722.83	\$ -	\$ 203,722.83
	CORE Construction Services, L.L.C.	FEMA	\$ 15,296,000.00	\$ 491,676.30	\$ 15,787,676.30
<b>Drew ES Renovation Total</b>					<b>\$ 17,480,153.73</b>
McDonogh 42 ES Renovation	Eskew+Dumez+Ripple, APC	FEMA	\$ 1,371,659.00	\$ 235,106.05	\$ 1,606,765.05
	Farnsworth Group, Inc - Building Commissioning 1N + 4R	FEMA	\$ 204,763.03	\$ (58,536.74)	\$ 146,226.29
	CORE Construction Services, L.L.C.	Tax Credit	\$ 15,499,000.00	\$ 5,214.00	\$ 15,504,214.00
<b>McDonogh 42 ES Renovation Total</b>					<b>\$ 17,257,205.34</b>
McDonogh 42 ES Renovation - Test Pile	Eskew+Dumez+Ripple, APC	FEMA	\$ -	\$ 9,714.00	\$ 9,714.00
<b>McDonogh 42 ES Renovation - Test Pile Total</b>					<b>\$ 9,714.00</b>
Ernest 'Dutch' Morial School (New - PK-8)	Waggonner & Ball Architects, APC	FEMA	\$ 1,151,421.08	\$ 1,077,581.87	\$ 2,229,002.95
	SSRCx, LLC - Building Commissioning 1R + 4N	FEMA	\$ 111,595.00	\$ -	\$ 111,595.00
<b>Ernest 'Dutch' Morial School (New - PK-8) Total</b>					<b>\$ 2,340,597.95</b>
Edward Livingston HS Construction	Rozas-Ward/a.i.a. architects, inc.	FEMA	\$ 1,058,410.78	\$ 674,711.28	\$ 1,733,122.06
	Farnsworth Group, Inc - Building Commissioning 5 plus 2	FEMA	\$ -	\$ 213,049.90	\$ 213,049.90
	Gibbs Construction, L.L.C.	FEMA	\$ 31,479,833.27	\$ (2,164,820.65)	\$ 29,315,012.62
		Insurance Proceeds	\$ 50,166.73	\$ -	\$ 50,166.73
<b>Edward Livingston HS Construction Total</b>					<b>\$ 31,311,351.31</b>
Abrams ES Construction	Waggonner & Ball Architects, APC	FEMA	\$ 1,580,386.52	\$ 9,642.87	\$ 1,590,029.39
	SSRCx, LLC - Building Commissioning 1R + 4N	FEMA	\$ 111,595.00	\$ -	\$ 111,595.00
<b>Abrams ES Construction Total</b>					<b>\$ 1,701,624.39</b>
Avery Alexander School (New - PK-8)	Professional Services Industries, Inc	FEMA	\$ 30,581.00	\$ -	\$ 30,581.00
	Sizeler Thompson Brown Architects Project Design Group, LLC	FEMA	\$ 1,297,048.60	\$ 68,432.50	\$ 1,365,481.10
	SSRCx, LLC - Building Commissioning 1R + 4N	FEMA	\$ 106,680.00	\$ -	\$ 106,680.00
<b>Avery Alexander School (New - PK-8) Total</b>					<b>\$ 1,502,742.10</b>
Sophie B Wright HS Renovation	Waggonner & Ball Architects, APC	FEMA	\$ 1,847,676.00	\$ 453,934.50	\$ 2,301,610.50
	Farnsworth Group, Inc - Building Commissioning 1N + 4R	FEMA	\$ 212,571.51	\$ (77,988.12)	\$ 134,583.39
<b>Sophie B Wright HS Renovation Total</b>					<b>\$ 2,436,193.89</b>
Sophie B Wright HS Renovation - Test Pile & Exploratory Demo	Waggonner & Ball Architects, APC	FEMA	\$ -	\$ 4,650.20	\$ 4,650.20
<b>Sophie B Wright HS Renovation - Test Pile &amp; Exploratory Demo Total</b>					<b>\$ 4,650.20</b>



**BESE MONTHLY REPORT**  
OPEN CONTRACTS as of 07/08/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
Sophie B Wright HS Renovation - Selective Demolition and Test Pile	Waggonner & Ball Architects, APC	FEMA	\$ -	\$ 64,922.00	\$ 64,922.00
	Zimmer-Eschette Service II, LLC	FEMA	\$ 604,000.00	\$ 83,780.54	\$ 687,780.54
<b>Sophie B Wright HS Renovation - Selective Demolition and Test Pile Total</b>					<b>\$ 752,702.54</b>
John McDonogh HS Renovation	VergesRome Architects, APAC	FEMA	\$ 2,696,406.00	\$ -	\$ 2,696,406.00
<b>John McDonogh HS Renovation Total</b>					<b>\$ 2,696,406.00</b>
Tubman ES Renovation	Mahlum Scairono Martinez Architects, LLC	FEMA	\$ 1,375,942.00	\$ -	\$ 1,375,942.00
	SSRCx, LLC - Building Commissioning 1R + 4N	FEMA	\$ 61,478.00	\$ -	\$ 61,478.00
<b>Tubman ES Renovation Total</b>					<b>\$ 1,437,420.00</b>
New Orleans East HS (Abramson Site)	Rozas-Ward/a.i.a. architects, inc.	FEMA	\$ 1,056,051.52	\$ 738,853.86	\$ 1,794,905.38
	Farnsworth Group, Inc	FEMA	\$ 236,206.39	\$ (107,277.99)	\$ 128,928.40
	Gibbs Construction, L.L.C.	FEMA	\$ 27,768,550.95	\$ -	\$ 27,768,550.95
		Insurance Proceeds	\$ 31,449.05	\$ -	\$ 31,449.05
<b>New Orleans East HS (Abramson Site) Total</b>					<b>\$ 29,723,833.78</b>
New Booker T Washington HS - Test Pile	Hewitt-Washington & Associates Architects and Planners	FEMA	\$ -	\$ 9,050.00	\$ 9,050.00
<b>New Booker T Washington HS - Test Pile Total</b>					<b>\$ 9,050.00</b>
New Booker T Washington HS & Auditorium Rehabilitation	Hewitt-Washington & Associates Architects and Planners	FEMA	\$ 3,854,210.00	\$ (1,266,081.80)	\$ 2,588,128.20
<b>New Booker T Washington HS &amp; Auditorium Rehabilitation Total</b>					<b>\$ 2,588,128.20</b>
New Booker T Washington HS Interpretive Display	Bright Moments, LLC	FEMA	\$ 4,125.00	\$ -	\$ 4,125.00
<b>New Booker T Washington HS Interpretive Display Total</b>					<b>\$ 4,125.00</b>
New Booker T Washington HS - Environmental	Shaw Environmental & Infrastructure	FEMA	\$ 91,927.00	\$ -	\$ 91,927.00
<b>New Booker T Washington HS - Environmental Total</b>					<b>\$ 91,927.00</b>
New Booker T Washington Medium High School	Farnsworth Group, Inc - Building Commissioning 7 New & Reno	FEMA	\$ 239,900.00	\$ 1,802.94	\$ 241,702.94
	Hewitt-Washington & Associates Architects and Planners	FEMA	\$ -	\$ 3,180,911.02	\$ 3,180,911.02
<b>New Booker T Washington Medium High School Total</b>					<b>\$ 3,422,613.96</b>
George W. Carver HS Construction	Farnsworth Group, Inc - Building Commissioning 5 plus 2	FEMA	\$ 321,880.00	\$ (71,907.18)	\$ 249,972.82
	Broadmoor, LLC	FEMA	\$ 48,883,407.00	\$ -	\$ 48,883,407.00
		HRSA	\$ 496,170.00	\$ -	\$ 496,170.00
<b>George W. Carver HS Construction Total</b>					<b>\$ 49,629,549.82</b>
George W. Carver HS Interpretive Display	Bright Moments, LLC	FEMA	\$ 4,125.00	\$ -	\$ 4,125.00
<b>George W. Carver HS Interpretive Display Total</b>					<b>\$ 4,125.00</b>
Habans ES Construction	SSRCx, LLC	FEMA	\$ 112,014.00	\$ -	\$ 112,014.00
	CORE Construction Services, L.L.C.	FEMA	\$ 30,373,000.00	\$ -	\$ 30,373,000.00
		Insurance Proceeds	\$ 30,000.00	\$ -	\$ 30,000.00
<b>Habans ES Construction Total</b>					<b>\$ 30,515,014.00</b>
Sherwood Forest School (New - PK-8)	SSRCx, LLC - Building Commissioning 1R + 4N	FEMA	\$ 106,680.00	\$ -	\$ 106,680.00
	CORE Construction Services, L.L.C.	FEMA	\$ 29,325,000.00	\$ -	\$ 29,325,000.00
		Insurance Proceeds	\$ 30,000.00	\$ -	\$ 30,000.00
<b>Sherwood Forest School (New - PK-8) Total</b>					<b>\$ 29,461,680.00</b>
<b>REFURBISHMENTS</b>					
Frederick A Douglass HS Refurbishment	VergesRome Architects, APAC	FEMA	\$ -	\$ 741,988.15	\$ 741,988.15
	FHP Tectonics Corp.	FEMA	\$ 8,588,000.00	\$ 673,854.60	\$ 9,261,854.60
<b>Frederick A Douglass HS Refurbishment Total</b>					<b>\$ 10,003,842.75</b>
Village de L'est ES Refurb	Duplantis Design Group, PC	FEMA	\$ 48,733.00	\$ -	\$ 48,733.00
<b>Village de L'est ES Refurb Total</b>					<b>\$ 48,733.00</b>
Albert Wicker ES Refurb	SCNZ Architects, LLC	FEMA	\$ 72,114.00	\$ (7,195.80)	\$ 64,918.20
	Tuna Construction, LLC	FEMA	\$ 523,000.00	\$ 15,176.49	\$ 538,176.49
<b>Albert Wicker ES Refurb Total</b>					<b>\$ 603,094.69</b>
Thurgood Marshall ES Refurb	Hamilton Anderson Associates	FEMA	\$ 70,601.00	\$ -	\$ 70,601.00
<b>Thurgood Marshall ES Refurb Total</b>					<b>\$ 70,601.00</b>
Henry C. Schaumburg ES Refurb	N-Y Associates, Inc.	FEMA	\$ 15,193.00	\$ 18,810.00	\$ 34,003.00
<b>Henry C. Schaumburg ES Refurb Total</b>					<b>\$ 34,003.00</b>
Edgar P. Harney ES Refurb	Hamilton Anderson Associates	FEMA	\$ 27,131.00	\$ 3,294.50	\$ 30,425.50
<b>Edgar P. Harney ES Refurb Total</b>					<b>\$ 30,425.50</b>
Julius Rosenwald ES Refurb	Byron J. Stewart & Associates, APC	FEMA	\$ 105,034.00	\$ -	\$ 105,034.00
<b>Julius Rosenwald ES Refurb Total</b>					<b>\$ 105,034.00</b>
Sylvanie Williams ES Refurb	N-Y Associates, Inc.	FEMA	\$ 48,754.00	\$ 82,801.07	\$ 131,555.07
<b>Sylvanie Williams ES Refurb Total</b>					<b>\$ 131,555.07</b>
Agnes L. Bauduit ES Refurb	Duplantis Design Group, PC	FEMA	\$ 301,824.00	\$ (46,898.00)	\$ 254,926.00
<b>Agnes L. Bauduit ES Refurb Total</b>					<b>\$ 254,926.00</b>
Laurel ES Refurb	Mahlum Scairono Martinez Architects, LLC	FEMA	\$ 458,942.00	\$ -	\$ 458,942.00
<b>Laurel ES Refurb Total</b>					<b>\$ 458,942.00</b>





**BESE MONTHLY REPORT**  
OPEN CONTRACTS as of 07/08/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
McDonogh 28 ES Refurb	SCNZ Architects, LLC	FEMA	\$ 199,248.00	\$ 70,334.20	\$ 269,582.20
<b>McDonogh 28 ES Refurb Total</b>					<b>\$ 269,582.20</b>
Martin Luther King Jr. ES Refurb	VergesRome Architects, APAC	FEMA	\$ 72,295.00	\$ (11,127.00)	\$ 61,168.00
	Hamp's Construction, LLC	FEMA	\$ 342,400.00	\$ -	\$ 342,400.00
<b>Martin Luther King Jr. ES Refurb Total</b>					<b>\$ 403,568.00</b>
Henry Allen ES Refurb	N-Y Associates, Inc.	FEMA	\$ 92,546.00	\$ 95,975.77	\$ 188,521.77
<b>Henry Allen ES Refurb Total</b>					<b>\$ 188,521.77</b>
Andrew Jackson ES Refurb	N-Y Associates, Inc.	FEMA	\$ 118,872.00	\$ 151,255.51	\$ 270,127.51
<b>Andrew Jackson ES Refurb Total</b>					<b>\$ 270,127.51</b>
A.D. Crossman ES Refurb	Perez, APC	FEMA	\$ 45,212.00	\$ (8,004.00)	\$ 37,208.00
	One Construction, LLC	FEMA	\$ 239,000.00	\$ (1,925.00)	\$ 237,075.00
<b>A.D. Crossman ES Refurb Total</b>					<b>\$ 274,283.00</b>
Dwight D Eisenhower ES Refurb	Harry Baker Smith Architects II, PLLC	FEMA	\$ 154,483.00	\$ (17,229.10)	\$ 137,253.90
<b>Dwight D Eisenhower ES Refurb Total</b>					<b>\$ 137,253.90</b>
Gentilly Terrace ES Refurb	Byron J. Stewart & Associates, APC	FEMA	\$ 137,099.00	\$ (19,438.00)	\$ 117,661.00
<b>Gentilly Terrace ES Refurb Total</b>					<b>\$ 117,661.00</b>
Sarah T. Reed HS Refurb	Byron J. Stewart & Associates, APC	FEMA	\$ 105,514.00	\$ 40,266.85	\$ 145,780.85
<b>Sarah T. Reed HS Refurb Total</b>					<b>\$ 145,780.85</b>
Green ES Refurb	VergesRome Architects, APAC	FEMA	\$ 420,497.00	\$ 33,247.50	\$ 453,744.50
<b>Green ES Refurb Total</b>					<b>\$ 453,744.50</b>
Walter L Cohen Food Service	N-Y Associates, Inc.	FEMA	\$ 27,456.00	\$ -	\$ 27,456.00
<b>Walter L Cohen Food Service Total</b>					<b>\$ 27,456.00</b>
Banneker ES Food Service	SCNZ Architects, LLC	FEMA	\$ 29,528.00	\$ -	\$ 29,528.00
<b>Banneker ES Food Service Total</b>					<b>\$ 29,528.00</b>
McDonogh 32 ES Refurb	Byron J. Stewart & Associates, APC	FEMA	\$ 296,940.00	\$ -	\$ 296,940.00
<b>McDonogh 32 ES Refurb Total</b>					<b>\$ 296,940.00</b>
Live Oak ES Refurbishment	VergesRome Architects, APAC	FEMA	\$ 265,287.00	\$ 582,009.00	\$ 847,296.00
<b>Lafayette ES Refurb Total</b>					<b>\$ 324,260.00</b>
Gaudet ES Refurb	SCNZ Architects, LLC	FEMA	\$ 232,753.00	\$ -	\$ 232,753.00
<b>Gaudet ES Refurb Total</b>					<b>\$ 232,753.00</b>
Fischer ES Refurb	SCNZ Architects, LLC	FEMA	\$ 204,015.00	\$ 9,680.00	\$ 213,695.00
<b>Fischer ES Refurb Total</b>					<b>\$ 213,695.00</b>
Fischer ES Playground Equipment Relocation	Mahlum Scairono Martinez Architects, LLC	FEMA	\$ -	\$ 10,695.00	\$ 10,695.00
<b>Fischer ES Playground Equipment Relocation Total</b>					<b>\$ 10,695.00</b>
Johnson ES Refurb	SCNZ Architects, LLC	FEMA	\$ 155,901.00	\$ 10,340.00	\$ 166,241.00
<b>Johnson ES Refurb Total</b>					<b>\$ 166,241.00</b>
A.D. Crossman Food Services	SCNZ Architects, LLC	FEMA	\$ 17,519.00	\$ -	\$ 17,519.00
<b>A.D. Crossman Food Services Total</b>					<b>\$ 17,519.00</b>
Dwight D Eisenhower ES Food Services	N-Y Associates, Inc.	FEMA	\$ 32,445.00	\$ -	\$ 32,445.00
<b>Dwight D Eisenhower ES Food Services Total</b>					<b>\$ 32,445.00</b>
Andrew Jackson ES Food Services	N-Y Associates, Inc.	FEMA	\$ 19,979.00	\$ -	\$ 19,979.00
<b>Andrew Jackson ES Food Services Total</b>					<b>\$ 19,979.00</b>
Martin Luther King Jr. ES Food Services	N-Y Associates, Inc.	FEMA	\$ 11,987.00	\$ -	\$ 11,987.00
<b>Martin Luther King Jr. ES Food Services Total</b>					<b>\$ 11,987.00</b>
Gentilly Terrace ES Food Services	SCNZ Architects, LLC	FEMA	\$ 19,519.00	\$ -	\$ 19,519.00
<b>Gentilly Terrace ES Food Services Total</b>					<b>\$ 19,519.00</b>
McDonogh 28 ES Food Services	SCNZ Architects, LLC	FEMA	\$ 20,519.00	\$ -	\$ 20,519.00
<b>McDonogh 28 ES Food Services Total</b>					<b>\$ 20,519.00</b>
Henry Allen ES Food Services	N-Y Associates, Inc.	FEMA	\$ 10,983.00	\$ -	\$ 10,983.00
<b>Henry Allen ES Food Services Total</b>					<b>\$ 10,983.00</b>
Sarah T. Reed HS Food Services	N-Y Associates, Inc.	FEMA	\$ 13,985.00	\$ -	\$ 13,985.00
<b>Sarah T. Reed HS Food Services Total</b>					<b>\$ 13,985.00</b>
Albert Wicker ES Food Services	SCNZ Architects, LLC	FEMA	\$ 26,529.00	\$ -	\$ 26,529.00
<b>Albert Wicker ES Food Services Total</b>					<b>\$ 26,529.00</b>
<b>STABILIZATIONS</b>					
Andrew J Bell Roof Replacement	VergesRome Architects, APAC	FEMA	\$ -	\$ 124,357.00	\$ 124,357.00
	Crescent Commercial Construction	FEMA	\$ 1,264,000.00	\$ 267,131.35	\$ 1,531,131.35
<b>Andrew J Bell Roof Replacement Total</b>					<b>\$ 1,655,488.35</b>
John McDonogh HS - Bleachers	Trapolin-Peer Architects, APC	Insurance Proceeds	\$ 11,822.50	\$ (2,740.16)	\$ 9,082.34
	One Construction, LLC	Insurance Proceeds	\$ 68,656.00	\$ 10,100.45	\$ 78,756.45
<b>John McDonogh HS - Bleachers Total</b>					<b>\$ 87,838.79</b>



**BESE MONTHLY REPORT**  
OPEN CONTRACTS as of 07/08/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
Carbon Credit - AD Crossman (aka Esperanza Charter)	W.L. Wyman Construction Company, Inc	Harrah's	\$ 199,850.00	\$ 13,615.94	\$ 213,465.94
<b>Carbon Credit - AD Crossman (aka Esperanza Charter) Total</b>					<b>\$ 213,465.94</b>
Carbon Credit - Banneker ES	W.L. Wyman Construction Company, Inc	Harrah's	\$ 143,350.00	\$ 34,800.04	\$ 178,150.04
<b>Carbon Credit - Banneker ES Total</b>					<b>\$ 178,150.04</b>
Walter L Cohen HS - HVAC Repairs	Infinity Engineering Consultants, LLC ARC Mechanical Contractors, Inc.	FEMA FEMA	\$ 95,420.00 \$ 447,000.00	\$ (40,498.00) \$ 125,078.13	\$ 54,922.00 \$ 572,078.13
<b>Walter L Cohen HS - HVAC Repairs Total</b>					<b>\$ 627,000.13</b>
John McDonogh HS - Gymnasium Sprinkler	Fanning/Howie Associates, Inc. Coastal Fire Protection, LLC	Insurance Proceeds Insurance Proceeds	\$ 12,605.00 \$ 175,912.00	\$ 6,303.00 \$ (5,400.12)	\$ 18,908.00 \$ 170,511.88
<b>John McDonogh HS - Gymnasium Sprinkler Total</b>					<b>\$ 189,419.88</b>
<b>MOTHBALLING</b>					
Andrew J Bell Shoring Main Classroom Building	VergesRome Architects, APAC Aby Brothers, Inc.	FEMA FEMA	\$ - \$ 910,000.00	\$ 106,095.00 \$ 1,043,425.00	\$ 106,095.00 \$ 1,953,425.00
<b>Andrew J Bell Shoring Main Classroom Building Total</b>					<b>\$ 2,059,520.00</b>
Andrew J Bell Safe & Secure - Mothballing	VergesRome Architects, APAC C.D.W. Services, LLC	FEMA FEMA	\$ 92,568.00 \$ 2,058,000.00	\$ 112,194.00 \$ 443,888.90	\$ 204,762.00 \$ 2,501,888.90
<b>Andrew J Bell Safe &amp; Secure - Mothballing Total</b>					<b>\$ 2,706,650.90</b>
George Mondy ES Mothballing	VergesRome Architects, APAC	FEMA	\$ 26,023.00	\$ 40,056.00	\$ 66,079.00
<b>George Mondy ES Mothballing Total</b>					<b>\$ 66,079.00</b>
<b>BUILDING AUTOMATION SYSTEM</b>					
Building Automation System - Banneker	Synergy Building Solutions	FEMA		\$ 11,674.18	\$ 11,674.18
<b>Building Automation System - Banneker Total</b>					<b>\$ 11,674.18</b>
Building Automation System - Bienville	Moses Engineers, Inc. Synergy Building Solutions	FEMA FEMA	\$ - \$ 18,238.90	\$ 2,275.16 \$ 560.00	\$ 2,275.16 \$ 18,798.90
<b>Building Automation System - Bienville Total</b>					<b>\$ 21,074.06</b>
Building Automation System - Colton	Moses Engineers, Inc. Synergy Building Solutions	FEMA FEMA	\$ - \$ 29,127.41	\$ 3,633.41 -	\$ 3,633.41 \$ 29,127.41
<b>Building Automation System - Colton Total</b>					<b>\$ 32,760.82</b>
Building Automation System - Craig ES	Moses Engineers, Inc. Synergy Building Solutions	FEMA FEMA	\$ 10,873.76 \$ 56,716.33	\$ 2,370.11 \$ 7,701.50	\$ 13,243.87 \$ 64,417.83
<b>Building Automation System - Craig ES Total</b>					<b>\$ 77,661.70</b>
Building Automation System - Crocker	Moses Engineers, Inc. Synergy Building Solutions	FEMA FEMA	\$ - \$ 16,515.03	\$ 2,060.12 -	\$ 2,060.12 \$ 16,515.03
<b>Building Automation System - Crocker Total</b>					<b>\$ 18,575.15</b>
Building Automation System - FC Williams	Moses Engineers, Inc. Synergy Building Solutions	FEMA FEMA	\$ - \$ 17,516.91	\$ 2,185.10 \$ 560.00	\$ 2,185.10 \$ 18,076.91
<b>Building Automation System - FC Williams Total</b>					<b>\$ 20,262.01</b>
Building Automation System - Frantz	Moses Engineers, Inc. Synergy Building Solutions	FEMA FEMA	\$ - \$ 17,487.49	\$ 2,181.43 \$ 560.00	\$ 2,181.43 \$ 18,047.49
<b>Building Automation System - Frantz Total</b>					<b>\$ 20,228.92</b>
Building Automation System - L.B. Landry HS	Moses Engineers, Inc. Synergy Building Solutions	FEMA FEMA	\$ 10,873.76 \$ 50,189.62	\$ 1,555.96 \$ 560.00	\$ 12,429.72 \$ 50,749.62
<b>Building Automation System - L.B. Landry HS Total</b>					<b>\$ 63,179.34</b>
Building Automation System - Lake Area HS	Moses Engineers, Inc. Synergy Building Solutions	FEMA FEMA	\$ 10,873.76 \$ 48,450.83	\$ 1,397.88 \$ 2,720.00	\$ 12,271.64 \$ 51,170.83
<b>Building Automation System - Lake Area HS Total</b>					<b>\$ 63,442.47</b>
Building Automation System - Langston Hughes ES	Moses Engineers, Inc. Synergy Building Solutions	FEMA FEMA	\$ 10,873.76 \$ 44,855.18	\$ 890.53 \$ 560.00	\$ 11,764.29 \$ 45,415.18
<b>Building Automation System - Langston Hughes ES Total</b>					<b>\$ 57,179.47</b>
Building Automation System - Osborne	Moses Engineers, Inc. Synergy Building Solutions	FEMA FEMA	\$ - \$ 17,900.05	\$ 2,232.89 -	\$ 2,232.89 \$ 17,900.05
<b>Building Automation System - Osborne Total</b>					<b>\$ 20,132.94</b>
Building Automation System - Parkview	Moses Engineers, Inc. Synergy Building Solutions	FEMA FEMA	\$ - \$ 19,063.99	\$ 2,378.08 -	\$ 2,378.08 \$ 19,063.99
<b>Building Automation System - Parkview Total</b>					<b>\$ 21,442.07</b>
Building Automation System - Sarah T Reed	Synergy Building Solutions	FEMA	\$ -	\$ 12,587.80	\$ 12,587.80
<b>Building Automation System - Sarah T Reed Total</b>					<b>\$ 12,587.80</b>
Building Automation System - Sylvania Williams	Synergy Building Solutions	FEMA	\$ -	\$ 11,635.21	\$ 11,635.21
<b>Building Automation System - Sylvania Williams Total</b>					<b>\$ 11,635.21</b>



**BESE MONTHLY REPORT**  
OPEN CONTRACTS as of 07/08/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
Building Automation System - Wilson ES	Moses Engineers, Inc.	FEMA	\$ 10,873.76	\$ 903.44	\$ 11,777.20
	Synergy Building Solutions	FEMA	\$ 44,958.72	\$ 8,261.50	\$ 53,220.22
<b>Building Automation System - Wilson ES Total</b>					<b>\$ 64,997.42</b>
Building Automation System - Woodson	Moses Engineers, Inc.	FEMA	\$ -	\$ 2,164.90	\$ 2,164.90
	Synergy Building Solutions	FEMA	\$ 17,355.04	\$ -	\$ 17,355.04
<b>Building Automation System - Woodson Total</b>					<b>\$ 19,519.94</b>
Building Automation System - AD Crossman	Synergy Building Solutions	FEMA		\$ 12,490.68	\$ 12,490.68
<b>Building Automation System - AD Crossman Total</b>					<b>\$ 12,490.68</b>
Building Automation System - Cohen	Synergy Building Solutions	FEMA		\$ 13,252.58	\$ 13,252.58
<b>Building Automation System - Little Woods Total</b>					<b>\$ 24,064.90</b>
Building Automation System - Wicker	Synergy Building Solutions	FEMA		\$ 13,273.32	\$ 13,273.32
<b>Building Automation System - Wicker Total</b>					<b>\$ 13,273.32</b>
<b>OTHER PROFESSIONAL SERVICES</b>					
PM/CM	Jacobs Project Management Company/CSRS Consortium	FEMA	\$ 23,590,758.00	\$ 1,069,673.31	\$ 24,660,431.31
<b>PM/CM Total</b>					<b>\$ 24,660,431.31</b>
Consulting Services - Building Commissioning	GCE Services	Insurance Proceeds	\$ 50,000.00	\$ -	\$ 50,000.00
<b>Consulting Services - Building Commissioning Total</b>					<b>\$ 50,000.00</b>
Wilson ES Warranty Oversight	HMS Architects, APC	Insurance Proceeds	\$ 50,000.00	\$ -	\$ 50,000.00
<b>Wilson ES Warranty Oversight Total</b>					<b>\$ 50,000.00</b>

**GRAND TOTAL                    \$            570,698,466.75**

**OPSB OPEN CONTRACTS**  
as of  
**07/07/2014**



PROJECT	CONTRACTOR/ARCHITECT	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
<b>DEMOLITION</b>				
Alice Harte Demolition	M3A Architects, PLLC	\$ 58,061.50	\$ 8,842.00	\$ 66,903.50
<b>Alice Harte Demolition Total</b>				<b>\$ 66,903.50</b>
<b>CONSTRUCTION/RENOVATION</b>				
Hynes Elementary Construction	Farnsworth Group, Inc Woodrow Wilson Construction	\$ 200,308.00 \$ 21,108,000.00	\$ - \$ 570,066.90	\$ 200,308.00 \$ 21,678,066.90
<b>Hynes Elementary Construction Total</b>				<b>\$ 21,878,374.90</b>
New McDonogh 35 High School (Phillips Waters Site)	Sizeler Thompson Brown Architects Project Design Group, LLC Farnsworth Group, Inc Citadel Builders, LLC	\$ 3,279,219.00 \$ 321,880.00 \$ 54,984,000.00	\$ 1,193,198.16 \$ 6,620.00 \$ 616,521.79	\$ 4,472,417.16 \$ 328,500.00 \$ 55,600,521.79
<b>New McDonogh 35 High School (Phillips Waters Site) Total</b>				<b>\$ 60,401,438.95</b>
New McDonogh 35 High School (Phillips Waters Site) Site Remediation	Sizeler Thompson Brown Architects Project Design Group, LLC	\$ -	\$ 1,214,042.65	\$ 1,214,042.65
<b>New McDonogh 35 High School (Phillips Waters Site) Site Remediation Total</b>				<b>\$ 1,214,042.65</b>
Audubon School Reno/Addition	Blitch Knevel Architects Farnsworth Group, Inc FHP Technonics Corporation	\$ 995,406.90 \$ 162,212.00 \$ 12,415,000.00	\$ 513,560.90 \$ - \$ 261,076.10	\$ 1,508,967.80 \$ 162,212.00 \$ 12,676,076.10
<b>Audubon School Reno/Addition Total</b>				<b>\$ 14,347,255.90</b>
Audubon School Reno/Addition Interpretive Display	Bright Moments, LLC	\$ 4,125.00	\$ -	\$ 4,125.00
<b>Audubon School Reno/Addition Interpretive Display Total</b>				<b>\$ 4,125.00</b>
Alice Harte Elementary	WDG Architects Engineers Farnsworth Group, Inc Woodrow Wilson Construction	\$ 1,513,534.00 \$ 222,742.00 \$ 18,229,554.00	\$ 500,261.03 \$ - \$ -	\$ 2,013,795.03 \$ 222,742.00 \$ 18,229,554.00
<b>Alice Harte Elementary Total</b>		<b>\$ 8,490,446.00</b>	<b>\$ 60,663.50</b>	<b>\$ 8,551,109.50</b>
McMain New Gym & Covered Walkway	Jahncke & Burns Architects, LLC Farnsworth Group, Inc Ellis Construction, Inc.	\$ 972,951.50 \$ - \$ 9,497,800.00	\$ (142,995.12) \$ 110,156.00 \$ 935,750.56	\$ 829,956.38 \$ 110,156.00 \$ 10,433,550.56
<b>McMain New Gym &amp; Covered Walkway Total</b>				<b>\$ 11,373,662.94</b>
McMain Health Clinic Renovation	Jahncke & Burns Architects, LLC	\$ -	\$ 92,101.57	\$ 92,101.57
<b>McMain Health Clinic Renovation Total</b>				<b>\$ 92,101.57</b>
McMain Exterior Stabilization	Jahncke & Burns Architects, LLC	\$ -	\$ 969,119.38	\$ 969,119.38
<b>McMain Exterior Stabilization Total</b>				<b>\$ 969,119.38</b>
New PK-8 at Kenilworth Park (Curran Site)	Mathes Brierre Architects Farnsworth Group, Inc Woodrow Wilson Construction	\$ 1,587,671.03 \$ - \$ 22,476,000.00	\$ 149,364.00 \$ 254,729.75 \$ 35,946.05	\$ 1,737,035.03 \$ 254,729.75 \$ 22,511,946.05
<b>New PK-8 at Kenilworth Park (Curran Site) Total</b>				<b>\$ 24,503,710.83</b>
New Lake Forest School @ Greater St Stephens Site	Imre Hegedus & Associated Architects Farnsworth Group, Inc The McDonnel Group, LLC	\$ 1,382,303.00 \$ 264,670.51 \$ 34,075,000.00	\$ 875,288.50 \$ - \$ 63,094.00	\$ 2,257,591.50 \$ 264,670.51 \$ 34,138,094.00
<b>New Lake Forest School @ Greater St Stephens Site Total</b>				<b>\$ 36,660,356.01</b>
Nelson Elementary School Refurbishment	Harry Baker Smith II, PLLC	\$ 173,888.00	\$ 2,420.00	\$ 176,308.00
<b>Nelson Elementary School Refurbishment Total</b>				<b>\$ 176,308.00</b>
New Karr HS @ Jo Ellen Smith Site	Trapolin-Peer Architects, APC-VMDO Architects, PC Joint Venture Affiliated Engineers SE, Inc	\$ 442,849.32 \$ 349,100.00	\$ - \$ -	\$ 442,849.32 \$ 349,100.00
<b>New Karr HS @ Jo Ellen Smith Site Total</b>				<b>\$ 791,949.32</b>



**OPSB OPEN CONTRACTS**  
as of  
07/07/2014



PROJECT	CONTRACTOR/ARCHITECT	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
<b>STABILIZATIONS - VARIOUS</b>				
McDonogh 7 Dumpster Pad & Fence Install	GCA Education Services	\$ 29,500.00	\$ 6,690.00	\$ 36,190.00
<b>McDonogh 7 Dumpster Pad &amp; Fence Install Total</b>				<b>\$ 36,190.00</b>
McDonogh 7 LBP Remediation	Hamp's Construction, LLC	\$ 309,400.00	\$ 6,903.78	\$ 316,303.78
<b>McDonogh 7 LBP Remediation Total</b>				<b>\$ 316,303.78</b>
McDonogh 7 Modular Buildings	M Space Holdings, LLC	\$ 260,491.96	\$ -	\$ 260,491.96
<b>McDonogh 7 Modular Buildings Total</b>				<b>\$ 260,491.96</b>
Village de l'Est Modular Buildings	M Space Holdings, LLC	\$ 539,644.06	\$ 182,748.35	\$ 722,392.41
<b>Village de l'Est Modular Buildings Total</b>				<b>\$ 722,392.41</b>
McDonogh 7 Security System	Sonitrol	\$ 21,126.00	\$ 7,301.00	\$ 28,427.00
<b>McDonogh 7 Security System Total</b>				<b>\$ 28,427.00</b>
Lusher Elementary School	Meyer Engineers, LTD	\$ 139,948.00	\$ 36,300.00	\$ 176,248.00
<b>Lusher Elementary School Total</b>				<b>\$ 176,248.00</b>
McDonogh 35 HS Stabilization	Chenevert Architects, LLC	\$ 32,372.00	\$ 23,676.20	\$ 56,048.20
	Tuna Construction, LLC	\$ 352,000.00	\$ 103,183.16	\$ 455,183.16
<b>McDonogh 35 HS Stabilization Total</b>				<b>\$ 511,231.36</b>
Warren Easton HS Refurbishment	Chenevert Architects, LLC	\$ 32,372.00	\$ 208,862.94	\$ 241,234.94
<b>Warren Easton HS Refurbishment Total</b>				<b>\$ 241,234.94</b>
Audubon Charter School (Extension ES & MS) Stabilization	Chenevert Architects, LLC	\$ 32,372.00	\$ 510.53	\$ 32,882.53
<b>Audubon Charter School (Extension ES &amp; MS) Stabilization Total</b>				<b>\$ 32,882.53</b>
Fortier (Lusher) High School	SCNZ Architects, LLC	\$ 1,057,864.00	\$ 128,863.80	\$ 1,186,727.80
<b>Fortier (Lusher) High School Total</b>				<b>\$ 1,186,727.80</b>
Edna Karr HS - Gymnasium Repair	Chenevert Architects, LLC	\$ 32,372.00	\$ 43,517.98	\$ 75,889.98
	Crescent Commercial Construction	\$ 293,000.00	\$ 113,093.63	\$ 406,093.63
<b>Edna Karr HS - Gymnasium Repair Total</b>				<b>\$ 481,983.61</b>
Timbers III HVAC Repairs	Moses Engineers, Inc.	\$ 114,928.00	\$ (14,338.00)	\$ 100,590.00
<b>Timbers III HVAC Repairs Total</b>				<b>\$ 100,590.00</b>
McDonogh 7 ES Stabilization	Perez, APC	\$ 106,429.00	\$ -	\$ 106,429.00
<b>McDonogh 7 ES Stabilization Total</b>				<b>\$ 106,429.00</b>
McDonogh 7 ES Stabilization - Asphalt	Fleming Construction Company, LLC	\$ 197,000.00	\$ -	\$ 197,000.00
<b>McDonogh 7 ES Stabilization - Asphalt Total</b>				<b>\$ 197,000.00</b>
Timbers III - IT Room Relocation	N-Y Associates, Inc	\$ 4,519.00	\$ -	\$ 4,519.00
<b>Timbers III - IT Room Relocation Total</b>				<b>\$ 4,519.00</b>
Timbers III - Building Controls	N-Y Associates, Inc	\$ 3,832.00	\$ -	\$ 3,832.00
<b>Timbers III - Building Controls Total</b>				<b>\$ 3,832.00</b>
<b>OTHER PROFESSIONAL SERVICES</b>				
Program Management/Construction Management	Jacobs Project Management Company/CSRS Consortium	\$ 8,050,817.00	\$ -	\$ 8,050,817.00
<b>GRAND TOTAL</b>				<b>\$ 213,953,849.87</b>

**Orleans Parish School Board  
 BID TABULATION SHEET**

Bid Date: June 11, 2014

Project Name: Warren Easton Senior High School Stabilization  
3019 Canal Street  
New Orleans, LA 70119

Designer: Chenevert Architects LLC  
8300 Earhart Boulevard, Suite 101  
New Orleans, LA 70118

Project No.: 2011-0861 Part No.: 0001

Site Code: \_\_\_\_\_

OPSB ID: \_\_\_\_\_

OPSB Project Manager: Jacobs/CSRS Program Management

BIDDER	License Number	Addenda	Bond	Attestation Clause (Enter Date)	Base Bid	Alt. No. 1	Remarks
Battco Construction, Inc.	32179	1 <input type="checkbox"/> 2 <input type="checkbox"/>	Y <input type="checkbox"/> N <input type="checkbox"/>		—	N/A	
CDW Services	45228	1 <input checked="" type="checkbox"/> 2 <input checked="" type="checkbox"/>	Y <input checked="" type="checkbox"/> N <input type="checkbox"/>		1,790,000.00	N/A	
Dynamic Constructors, LLC	55104	1 <input checked="" type="checkbox"/> 2 <input checked="" type="checkbox"/>	Y <input checked="" type="checkbox"/> N <input type="checkbox"/>		2,800,000.00	N/A	
Landis Construction Co., LLC	35933	1 <input checked="" type="checkbox"/> 2 <input checked="" type="checkbox"/>	Y <input checked="" type="checkbox"/> N <input type="checkbox"/>	6/18/14	2,670,000.00	N/A	
J. Reed Constructors, Inc.	37085	1 <input type="checkbox"/> 2 <input type="checkbox"/>	Y <input type="checkbox"/> N <input type="checkbox"/>		—	N/A	
Kevin J. Smith Construction Co.	33374	1 <input checked="" type="checkbox"/> 2 <input checked="" type="checkbox"/>	Y <input checked="" type="checkbox"/> N <input type="checkbox"/>		2,725,510.00	N/A	
Strategic Planning & Associates	51426	1 <input type="checkbox"/> 2 <input type="checkbox"/>	Y <input type="checkbox"/> N <input type="checkbox"/>		—	N/A	
Tillage Construction, LLC	37753	1 <input checked="" type="checkbox"/> 2 <input checked="" type="checkbox"/>	Y <input checked="" type="checkbox"/> N <input type="checkbox"/>		2,800,000.00	N/A	
Tuna Construction, LLC	46529	1 <input checked="" type="checkbox"/> 2 <input checked="" type="checkbox"/>	Y <input checked="" type="checkbox"/> N <input type="checkbox"/>	6/19/14	2,407,000.00	N/A	affidavit + DBE
<i>Below Maqper</i>	<i>40066</i>	1 <input checked="" type="checkbox"/> 2 <input checked="" type="checkbox"/>	Y <input checked="" type="checkbox"/> N <input type="checkbox"/>		2,734,000.00	N/A	
		1 <input type="checkbox"/> 2 <input type="checkbox"/>	Y <input type="checkbox"/> N <input type="checkbox"/>			N/A	
		1 <input type="checkbox"/> 2 <input type="checkbox"/>	Y <input type="checkbox"/> N <input type="checkbox"/>			N/A	

**A TRUE COPY**

Signed: \_\_\_\_\_  
 Designer

Date: \_\_\_\_\_, 2014

Signed: *[Signature]*  
 Orleans Parish School Board Representative

Date: 6/23, 2014

A.F.C.: \$2,643,203.05

Construction Time: 305 Consecutive Calendar Days

Liquidated Damages: \$800.00/\$800.00 per Day

**BID RECOMMENDATIONS:** (Orleans Parish School Board Use Only.)

USER:  Reject  Award  Base Bid  Alt #1  Alt #2  Alt #3

Letter attached dated: \_\_\_\_\_, 2014

DESIGNER:  Reject  Award  Base Bid  Alt #1  Alt #2  Alt #3

Letter attached dated: \_\_\_\_\_, 2014

PROJECT MGR:  Reject  Award  Base Bid  Alt #1  Alt #2  Alt #3

Signed: \_\_\_\_\_ Date: \_\_\_\_\_, 2014

COMMENTS: \_\_\_\_\_

\_\_\_\_\_  
 Purchasing/Ancillary Services Director

Date: \_\_\_\_\_, 2014

**Orleans Parish School Board  
 BID TABULATION SHEET**

**Bid Date:** June 18, 2014

**Project Name:** Lusher (Fortier) High School Refurbishment  
5624 Freret Street, New Orleans, LA 70115

**Designer:** SCNZ Architects  
2134 Magazine Street, New Orleans, LA 70130

Project No.: 2011-0863-0001 Part No.:      Site Code:      OPSB ID:      OPSB Project Manager: Jacobs/CSRS Program Management

BIDDER	Lic. No.	Addenda	Bond	Attestation Clause (Enter Date)	Base Bid	Alt. No. 1	Alt. No. 2	Alt. No. 3	Remarks
CORE Construction Services	54378	✓	✓		14,330,000 <sup>00</sup>	94,000 <sup>00</sup>	107,000 <sup>00</sup>	21,000 <sup>00</sup>	
FHP Tectonics Corp	54077	✓	✓		15,167,000 <sup>00</sup>	102,000 <sup>00</sup>	129,000 <sup>00</sup>	81,000 <sup>00</sup>	
Gibbs Construction	10729	✓	✓		17,496,000 <sup>00</sup>	152,000 <sup>00</sup>	100,000 <sup>00</sup>	30,000 <sup>00</sup>	
Landis Construction	35933	✓	✓	6/18/14	12,140,000 <sup>00</sup>	108,000 <sup>00</sup>	98,000 <sup>00</sup>	38,000 <sup>00</sup>	
NOLA Building Group	57915								
Ryan Gootee General Contractors	43165	✓	✓		14,880,000 <sup>00</sup>	112,000 <sup>00</sup>	99,000 <sup>00</sup>	23,000 <sup>00</sup>	

**A TRUE COPY**

Signed: \_\_\_\_\_ Date: \_\_\_\_\_ Signed: \_\_\_\_\_ Date: \_\_\_\_\_  
Designer Orleans Parish School Board Representative

A.F.C.: \$18,764,383.74

Construction Time: 570 in days

Liquidated Damages: \$2,600.00 per day

**BID RECOMMENDATIONS:** (Orleans Parish School Board Use Only.)

USER:  Reject  Award:  Base Bid  Alt #1  Alt #2  Alt #3  Letter attached dated: \_\_\_\_\_

DESIGNER:  Reject  Award:  Base Bid  Alt #1  Alt #2  Alt #3  Letter attached dated: \_\_\_\_\_

PROJECT MGR:  Reject  Award:  Base Bid  Alt #1  Alt #2  Alt #3 Signed: \_\_\_\_\_ Date: \_\_\_\_\_

COMMENTS: \_\_\_\_\_

\_\_\_\_\_  
 Purchasing/Ancillary Services Director Date: \_\_\_\_\_

**Department of Education  
 BID TABULATION SHEET**

Bid Date: June 12, 2014


Project Name: Various Schools – Small Projects at RSD Schools  
 New Orleans, LA

Designer: Harry Baker Smith Architects II, A Professional LLC  
 189 Maple Ridge Drive  
 Metairie, LA 70001

Project No.: 2009-0761-0002 Part No.: \_\_\_\_\_ Site Code: \_\_\_\_\_ State ID: \_\_\_\_\_ DOE Project Manager: Jacobs/CSRS Program Management

BIDDER	Lic. No.	Addenda	Bond	Base Bid	Alt. No.1	Remarks
Hamp's Construction	31943	✓	✓	\$429,500.00		
Commander Corp.	13278	✓	✓	\$498,000.00		

A TRUE COPY

Signed:  Date: 6/26/14 Signed: \_\_\_\_\_ Date: \_\_\_\_\_  
Designer Department of Education Representative  
 A.F.C.: \$298,367.00 Construction Time 180 consecutive calendar in days Liquidated Damages: \$175.00 per day

**BID RECOMMENDATIONS:** (Department of Education Use Only.)

USER:             Reject    Award:    Base Bid    Alt #1    Alt #2    Alt #3             Letter attached dated: \_\_\_\_\_

DESIGNER:        Reject    Award:    Base Bid    Alt #1    Alt #2    Alt #3             Letter attached dated: \_\_\_\_\_

PROJECT MGR:  Reject    Award:    Base Bid    Alt #1    Alt #2    Alt #3   Signed: \_\_\_\_\_ Date: \_\_\_\_\_

COMMENTS: \_\_\_\_\_

\_\_\_\_\_ DOE Purchasing Director \_\_\_\_\_ Date: \_\_\_\_\_
