


Superintendent's Report August, 2014



Mr. Stanley C. Smith
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District

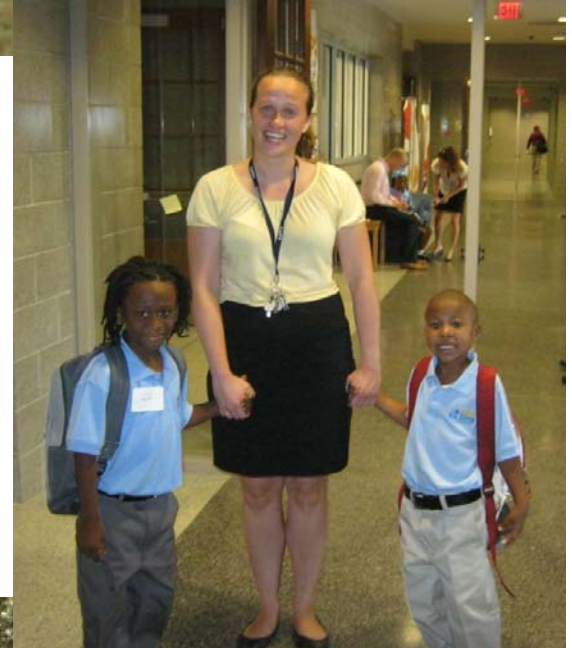

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	4
COMMUNITY MEETINGS	5
BID OPENINGS	6
DBE OVERVIEW MONTHLY SUMMARY	7
NEW & MAJOR RENOVATION	11
Ray Abrams Elementary School ^(RSD)	11
Avery Alexander Elementary School ^(RSD)	11
James Audubon School ^(OPSB)	12
Stuart R. Bradley School ^(RSD)	12
George Washington Carver School ^(RSD)	12
Charles R. Drew Elementary School ^(RSD)	13
Paul L. Dunbar School ^(RSD)	13
Fisk-Howard School ^(RSD)	13
Paul B. Habans School ^(RSD)	14
Alice Harte School ^(OPSB)	14
New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	14
Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	15
Alfred Lawless School ^(RSD)	15
Edward Livingston High School ^(RSD)	15
John McDonogh High School Selective Demolition ^(RSD)	16
John McDonogh High School Renovation ^(RSD)	16
McDonogh #35 School (Phillip/Waters Site) ^(OPSB)	16
McDonogh #42 Elementary School ^(RSD)	17
Eleanor L. McMain School Gymnasium ^(OPSB)	17
Ernest "Dutch" Morial Elementary School ^(RSD)	17
Small New Orleans East High School at Abramson ^(RSD)	18
Sherwood Forest School ^(RSD)	18
Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	18
Harriet R. Tubman Elementary School Renovation ^(RSD)	19
Booker T. Washington School Environmental Remediation ^(RSD)	19
Booker T. Washington School ^(RSD)	19
Sophie B. Wright School ^(RSD)	20

REFURBISHMENTS	21
Henry Allen Elementary School Refurbishment ^(RSD)	21
Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	21
Benjamin Banneker Elementary Kitchen School Refurbishment ^(RSD)	21
Agnes L. Bauduit Elementary School Refurbishment ^(RSD)	22
Walter L. Cohen High School Kitchen Refurbishment ^(RSD)	22
A. D. Crossman School Kitchen Refurbishment ^(RSD)	22
Frederick A. Douglass High School ^(RSD)	23
Frederick A. Douglass High School Science Lab ^(RSD)	23
Warren Easton School Refurbishment ^(OPSB)	23
Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	23
Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	24
William J. Fischer Elementary Refurbishment ^(RSD)	24
Fortier (Lusher) High School Refurbishment ^(OPSB)	24
Gaudet Elementary School Refurbishment ^(RSD)	25
Gentilly Terrace School Refurbishment ^(RSD)	25
Gentilly Terrace School Kitchen Refurbishment ^(RSD)	25
Samuel J. Green Elementary School Refurbishment ^(RSD)	26
Edgar P. Harney Elementary School Refurbishment ^(RSD)	26
Andrew Jackson School Refurbishment ^(RSD)	26
Andrew Jackson School Kitchen Refurbishment ^(RSD)	27
J. W. Johnson Elementary School Refurbishment ^(RSD)	27
Dr. Martin L. King Elementary School Refurbishment ^(RSD)	27
Dr. Martin L. King Elementary School Kitchen Refurbishment ^(RSD)	28
Lafayette Elementary School Refurbishment ^(RSD)	28
Laurel Elementary School Refurbishment ^(RSD)	28
Live Oak Elementary School Refurbishment ^(RSD)	29
Lusher Elementary School Refurbishment ^(OPSB)	29
Thurgood Marshall Elementary School Refurbishment ^(RSD)	29
McDonogh #28 School Refurbishment ^(RSD)	30
McDonogh #28 School Kitchen Refurbishment ^(RSD)	30
McDonogh #32 School Refurbishment ^(RSD)	30
Nelson Elementary School Refurbishment ^(OPSB)	31
Sarah T. Reed School Refurbishment ^(RSD)	31
Sarah T. Reed School Kitchen Refurbishment ^(RSD)	31
Rosenwald Elementary School Refurbishment ^(RSD)	32
Henry C. Schaumburg Elementary School Refurbishment ^(RSD)	32
Village de l'Est Elementary School Refurbishment ^(RSD)	32
Albert Wicker School Kitchen Refurbishment ^(RSD)	33
Sylvanie F. Williams School Refurbishment ^(RSD)	33

OTHER PROJECTS	34
Timbers III - Building Controls ^(OPSB)	34
Timbers III - IT Room Relocation ^(OPSB)	34
Building Automation System Integration At Recovery School District Central And Remote Offices ^(RSD)	35
MOTHBALL OR SAFE & SECURE OF SELECTED SCHOOLS	36
Andrew J. Bell Junior High School Shoring and Mothball ^(RSD)	36
Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School ^(RSD)	36
John F. Kennedy Modular Demolition ^(RSD)	37
Demolition of Modulares at Livingston and Schwarz ^(RSD)	37
George Mondy Elementary School Mothball ^(RSD)	37
JoEllen Smith Medical Center Demolition ^(RSD)	38
COMPLETED PROJECTS	39

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$571 million in open contracts for the capital program after issuing \$35 thousand in new contracts and \$658 thousand in change orders and amendments in August. In addition, the total change orders to date, \$6.5 million, account for approximately one percent (1.24%) of the total open construction contracts. RSD anticipates issuing approximately \$32 million in construction contracts/change orders, and no professional service contracts/amendments in September.



The OPSB has \$231 million in open contracts for the capital program after issuing \$17 million in new contracts and \$95 thousand in change orders and amendments in August. In addition, the total change orders to date, \$3 million, account for approximately two percent (1.50%) of the total open construction contracts. OPSB anticipates issuing approximately no new construction contracts/change orders and professional service contracts/amendments in September.

Community Meetings



Community meetings for the month of September

September 9, 2014

Booker T. Washington Community Meeting
3944 Martin Luther King Jr. Boulevard, New Orleans Louisiana 70125

September 10, 2014

Carver Alumni Meeting
909 Poydras Street Suite 1200, New Orleans Louisiana 70112

September 16, 2014

Sophie B. Wright Community Meeting
4238 St. Charles Avenue, New Orleans Louisiana 70115

September 23, 2014

George Washington Carver Community Meeting
3019 Higgins Boulevard, New Orleans Louisiana 70126

September 25, 2014

Sherwood Forest Elementary School Community Meeting
10501 Chef Menteur Highway, New Orleans Louisiana 70127

September 30, 2014

Avery Alexander Elementary School Community Meeting
5141 Franklin Avenue, New Orleans Louisiana 70122

Bid Openings

Bids that were opened in August 2014:

August 13, 2014

Harriet R. Tubman Elementary School Selective Demolition

August 13, 2014

Relocation of Playground Equipment at Osborne and Little Woods (Dolores T. Aaron Elementary School)

The following projects are scheduled to bid in the next 60 days:

September 3, 2014

Sylvanie Williams School Refurbishment

September 3, 2014

Timbers III - IT Room

Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District



New & Renovations:

DBE Contractors secured subcontracts on 16 projects as of August 31, 2014. The DBE subcontracts value is \$39,547,320 of the \$227,677,077 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 19 projects as of August 31, 2014. The DBE subcontracts value is \$4,841,587 of the \$15,235,276 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of August 31, 2014. The DBE subcontracts value is \$40,971,057 of the \$109,137,557 total of awarded contracts.

Total Amount of Contracts: \$ 352,049,910



Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 7 projects as of August 31, 2014. The DBE subcontracts value is \$51,703,983 of the \$191,142,360 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of August 31, 2014. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$192,045,359


* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

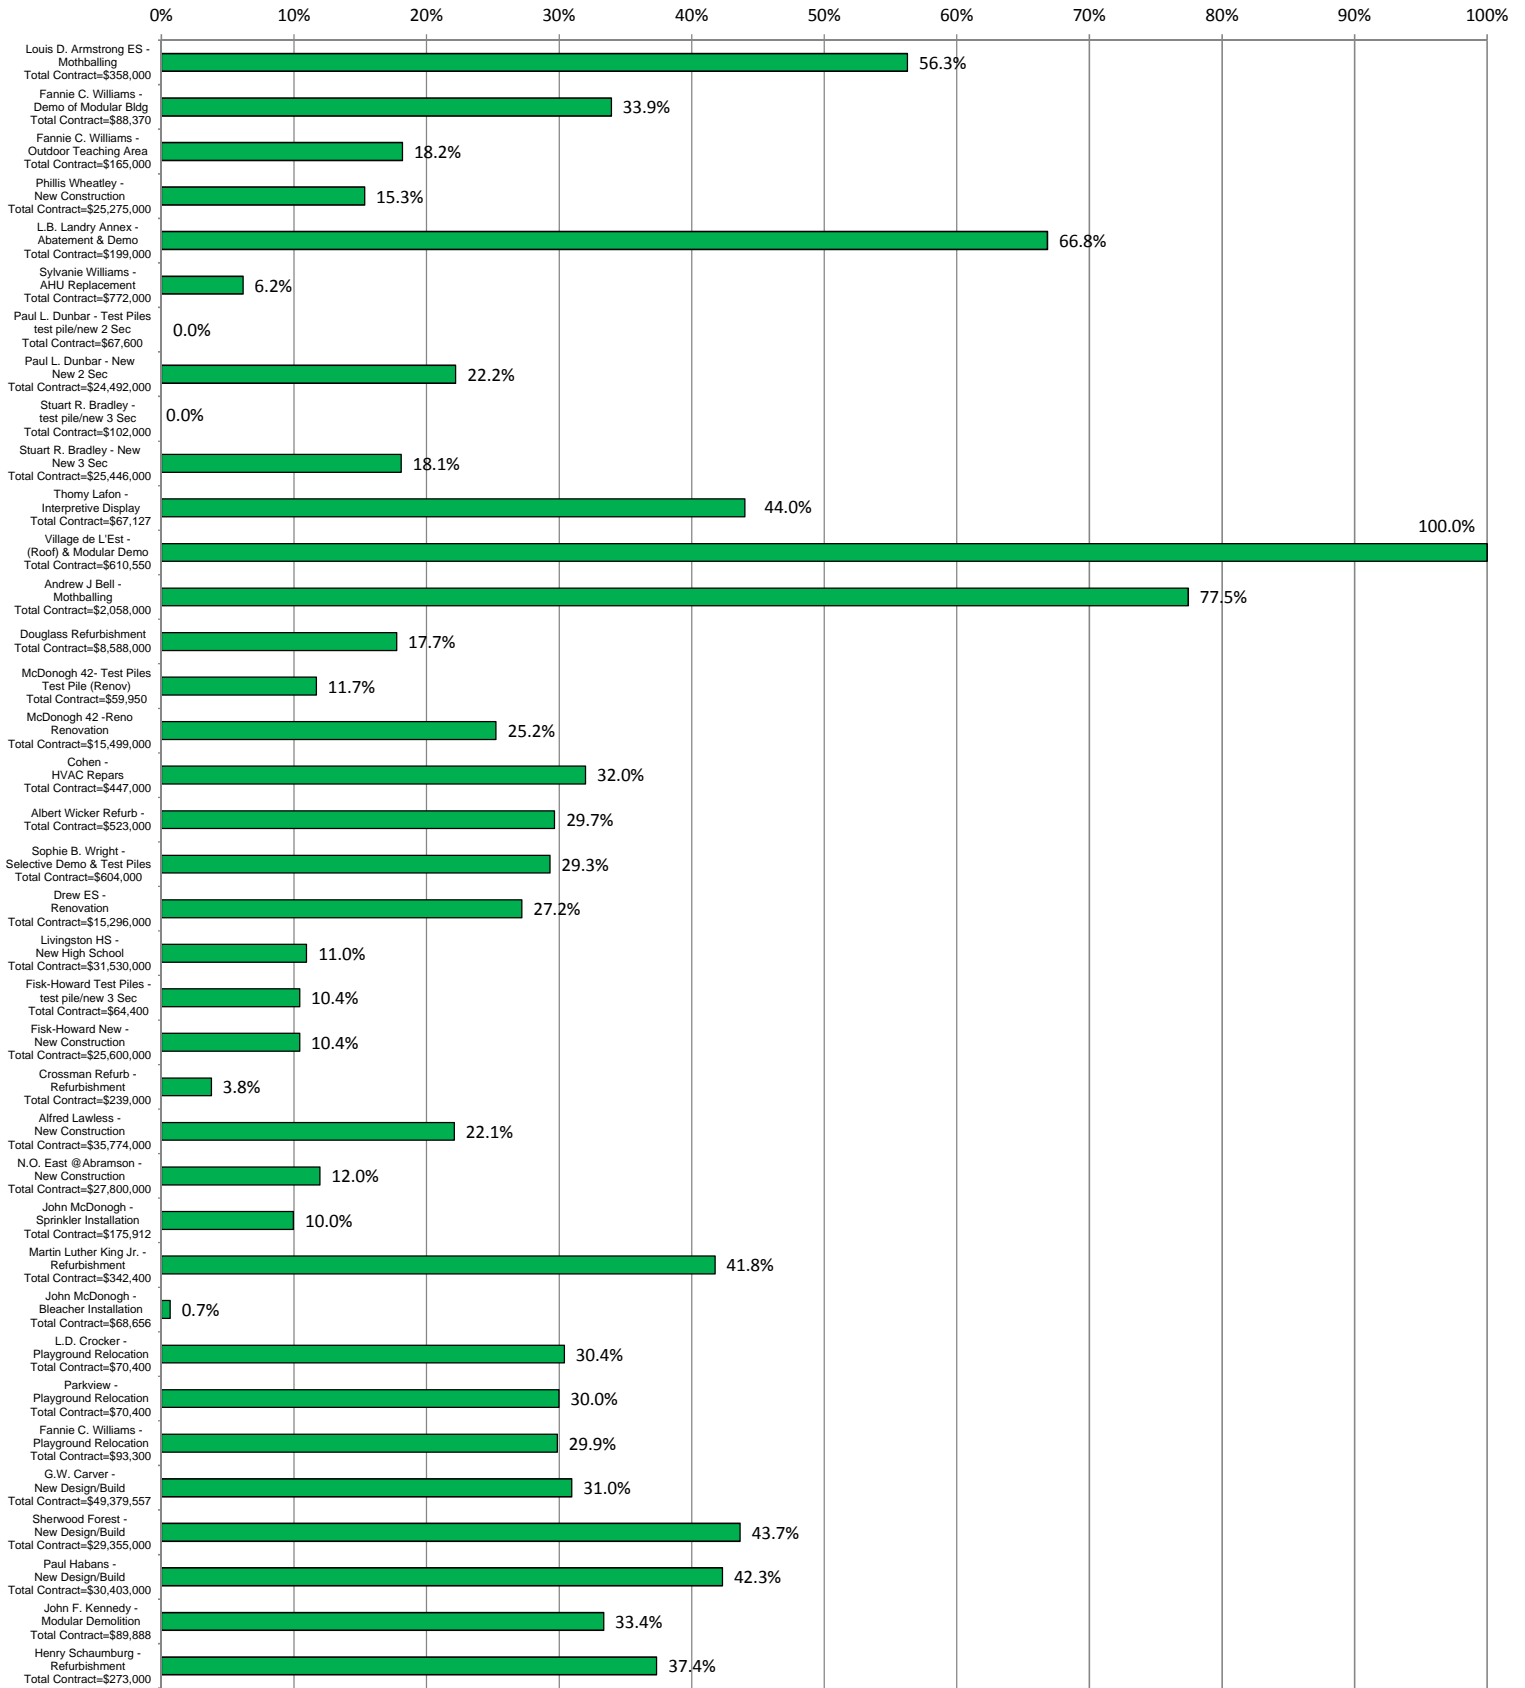

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

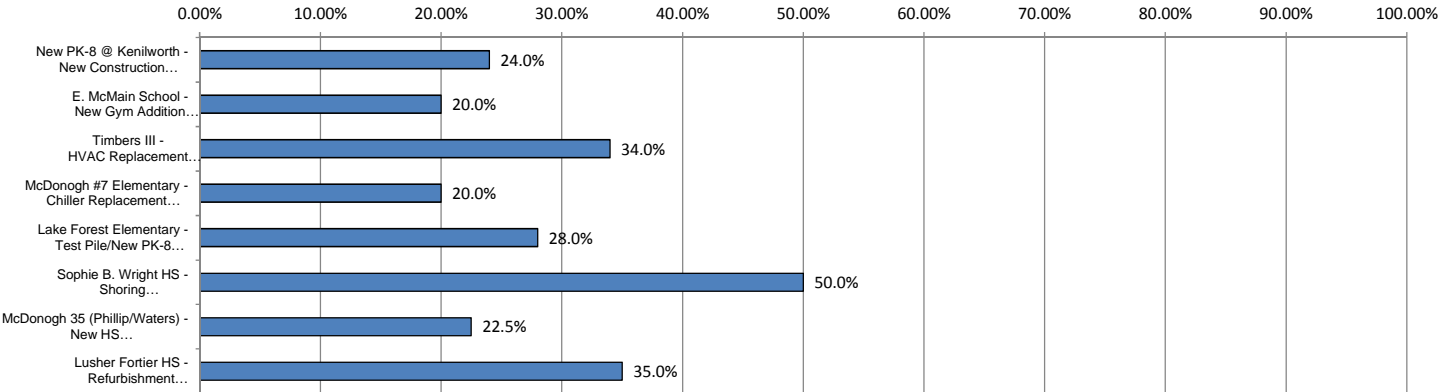

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School ^(RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – TBD

Design Phase - CD

- 100% Construction Documents were received August 25th
- Morial and Abrams will be packaged together as (1) project for the procurement process.

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



Avery Alexander Elementary School ^(RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – TBD

Design Phase - CD

- 100% Construction Documents are complete
- Procurement will be pushed by LDEQ approval of environmental issues
- Community Meeting - September 30th

Procurement Phase

- Anticipated 1st Advertisement – December 2014
- Anticipated Bid Opening – January 2015



James Audubon School (OPSB)

428 Broadway Avenue, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation of existing elementary school and new addition

Funding Source – FEMA

Architect – Blitch/Knevel Architects

Contractor – FHP Tectonics Corporation

Construction Phase

- Phase one of the corrective plan is complete
- Phase two of the corrective plan is underway
- Installation of refurbished windows is ongoing
- Installation of historic millwork and doors has started

Contractual Substantial Completion – September 2013

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – June 2015



Stuart R. Bradley School (RSD)

2401 Humanity Street, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Landis Construction Co.

Construction Phase

- Structural steel erection is 75% complete
- Installation of concrete masonry units is ongoing
- Installation of interior metal studs has started
- Pouring of roof deck is complete

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015

School Ready for Occupancy – June 2015



George Washington Carver School (RSD)

3059 Higgins Blvd., New Orleans, LA 70126 District E Ward 9

Scope of work: New High School, Design Build

Funding Source – FEMA

Contractor – Broadmoor LLC

Construction Phase

- Design Development Documents are due September 23rd
- Foundation permit is anticipated mid September
- Contractor mobilization early September
- Pile driving is anticipated to start mid September
- Forecasted Substantial Completion - March 2016



Charles R. Drew Elementary School ^(RSD)

3819 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Blitch / Knevel Architects, Inc.

Contractor – Core Construction

Construction Phase

- Stucco work on restroom tower has started
- Installation of metal studs and gypsum board continues
- MEP rough-in is ongoing
- Window refurbishment is ongoing

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015

School Ready for Occupancy – June 2015



Paul L. Dunbar School ^(RSD)

9330 Forshey Street, New Orleans, LA 70125 District A Ward 17

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor – McDonnel Group, LLC

Construction Phase

- Foundation work is 98% complete
- Subsurface drainage work is 75% complete
- Installation of CMU and metal studs is ongoing
- Roof installation is ongoing

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015

School Ready for Occupancy – June 2015



Fisk-Howard School ^(RSD)

211 South Lopez Street, New Orleans, LA 70119 District B Ward 3

Scope of work: New Pre-K – 8 School

Funding Source - FEMA

Architect - VergesRome Architects+Fanning Howey

Contractor – FHP Tectonics Corporation

Construction Phase

- Installation of interior finishes is ongoing
- Installation of HVAC ductwork is 90% complete
- Site work to start the mid September

Contractual Substantial Completion – October 2014

Forecasted Substantial Completion – December 2014

School Ready for Occupancy – January 2015



Paul B. Habans School ^(RSD)

3501 Siene Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

Construction Phase

- Design Development Documents are due September 9th
- Test pile anticipated to start late September
- Contractor mobilization mid September
- Forecasted Substantial Completion - May 2016



Alice Harte School ^(OPSB)

5300 Berkley Drive, New Orleans, La 70131 District C Ward 15

Scope of work: New Pre-K – 8 School

Funding Source – CDBG & FEMA

Architect – WDG Architects Engineers

Contractor – Woodrow Wilson Construction Company, Inc.

Construction Phase

- Site work is ongoing
- Installation of metal soffit and gutters are 98% complete
- Installation of Terrazzo Flooring is complete
- Interior painting is 85% complete
- Installation of casework is 90% complete

Contractual Substantial Completion – January 2014

Forecasted Substantial Completion – October 2104

School Ready for Occupancy – November 2014



New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)

8500 Curran Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Mathes Brierre Architects

Contractor – Woodrow Wilson Construction Company, Inc.

Construction Phase

- MEP work is ongoing
- Metal stud installation is ongoing
- Exterior masonry and metal panel installation is nearing completion
- Installation of windows at the classroom building is ongoing

Contractual Substantial Completion – September 2014

Forecasted Substantial Completion – January 2015

School Ready for Occupancy – January 2015



Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)

11110 Lake Forest Boulevard 70128 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Imre Hegedus & Associates Architects

Contractor – The McDonnell Group

Construction Phase

- MEP rough in has started
- Structural steel erection has started at the classroom building
- Concrete masonry installation is ongoing

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015

School Ready for Occupancy – August 2015



Alfred Lawless School ^(RSD)

5300 Law Street, New Orleans, LA 70117 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- Forming and pouring of columns and raised slabs is ongoing
- Installation of site utilities is ongoing
- Installation of exterior metal studs and sheathing has started
- Erection of structural steel is 90% complete
- Installation of concrete masonry has started

Contractual Substantial Completion – November 2015

Forecasted Substantial Completion – November 2015

School Ready for Occupancy – January 2016



Edward Livingston High School ^(RSD)

7301 Dwyer Road, New Orleans, LA 70126 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

Construction Phase

- Installation of interior finishes is ongoing
- Installation of metal panel is 95% complete
- Window installation is complete
- Installation of gymnasium equipment has started
- final grading of the site has started

Contractual Substantial Completion – February 2015

Forecasted Substantial Completion – February 2015

School Ready for Occupancy – June 2015



John McDonogh High School Selective Demolition ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – December 2014



John McDonogh High School Renovation ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

Design Phase - PC

- Design will start when program issues are resolved

Procurement Phase

- Anticipated 1st Advertisement – 3rd Quarter 2015
- Anticipated Bid Opening – 3rd Quarter 2015



McDonogh #35 School (Phillip/Waters Site) ^(OPSB)

1200 Senate Street, New Orleans, LA 70122 District D Ward 7

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler, Thompson, Brown Architects

Contractor – Citadel Builders, LLC

Construction Phase

- Installation of CMU walls is ongoing
- Roofing and wall sheathing is ongoing at the south classroom building
- Installation of MEP is ongoing
- Brick masonry is ongoing on the east wing

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – May 2015

School Ready for Occupancy – June 2015



McDonogh #42 Elementary School ^(RSD)

1651 North Tonti Street, New Orleans, LA 70119 District A Ward 7

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA, QSCB, NMTC, Insurance Proceeds

Architect – Eskew+Dumez+Ripple

Contractor – Core Construction

Construction Phase

- Permanent power is anticipated late September
- Installation of gypsum board is ongoing
- Steel erection is complete
- Transformer installation is complete

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – August 2015



Eleanor L. McMain School Gymnasium ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source – FEMA

Architect – Jahncke & Burns Architects

Contractor – Ellis Construction

Construction Phase

- Exterior masonry has started
- Underground utility rough-in work is ongoing
- Installation of exterior paving is ongoing
- Structural steel being installed on second floor

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015



Ernest "Dutch" Morial Elementary School ^(RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – TBD

Design Phase - CD

- Bid Documents are complete
- Morial and Abrams will be packaged together as (1) project for the procurement process.

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



Small New Orleans East High School at Abramson ^(RSD)

5552 Read Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

Construction Phase

- Masonry installation has started
- Structural steel erection is ongoing at the classroom area
- Installation of site utilities is ongoing
- Fire proofing of steel is complete in the gymnasium

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015

School Ready for Occupancy – November 2015



Sherwood Forest School ^(RSD)

4801 Maid Marion Drive, New Orleans, LA 70128 District E Ward 9

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

Construction Phase

- Design Development Documents are due September 9th
- Community Meeting September 25th
- Test pile anticipated to start late September
- Contractor mobilization mid September
- Forecasted Substantial Completion - May 2016



Harriet R. Tubman Elementary School Selective Demolition ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Procurement Phase

- Bids are being reviewed
- Anticipated Notice to Proceed - October



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- Construction Documents will be delayed due to added scope

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



Booker T. Washington School Environmental Remediation ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The remediation of the site

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – TBD

Design Phase - CD

- Community Meeting September 9th
- Bid Documents were received
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



Booker T. Washington School ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – TBD

Design Phase - CD

- Procurement will be delayed until Environmental concerns have been addressed

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



Sophie B. Wright High School Renovation ^(RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Renovation of existing school and gymnasium addition

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – TBD

Construction Phase

- Community Meeting - September 16th
- Anticipated Notice to Proceed - September 29th

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



REFURBISHMENTS

Henry Allen Elementary School Refurbishment ^(RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Bid Documents are complete
- Procurement will be delayed so that installation of windows will commence during summer break

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



Henry Allen Elementary School Kitchen Refurbishment ^(RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due October 1st
- 100% Construction Documents are due November 21st

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



Benjamin Banneker Elementary School Kitchen Refurbishment ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due October 1st
- 100% Construction Documents are due November 21st

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



Agnes L. Bauduit Elementary School Refurbishment (RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor - TBD

Design Phase - CD

- Bid Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



Walter L. Cohen High School Kitchen Refurbishment (RSD)

3520 Dryades, New Orleans Street, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due October 1st
- 100% Construction Documents are due November 21st

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



A. D. Crossman School Kitchen Refurbishment (RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due October 1st
- 100% Construction Documents are due November 21st

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



Frederick A. Douglass High School ^(RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Phased refurbishment of the existing high school

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – FHP Tectonics Corporation

Construction Phase

- Construction is 95% complete
- Contractor is working on punch list work
- Touch up painting and finish trim installation is ongoing

Contractual Substantial Completion – September 2014

Forecasted Substantial Completion – September 2014



Frederick A. Douglass High School Science Lab ^(RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovations to science lab

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

Program Completion Phase

- Program Completion Documents are due September 9th

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015

Warren Easton School ^(OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Refurbishment of existing high school, including but not limited to structure, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - Tuna Construction

Construction Phase

- Anticipated Notice to Proceed - September 16th

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Harry Baker Smith Architects II, PLLC

Contractor - TBD

Design Phase - CD

- Bid Documents are complete
- Procurement will be delayed so that installation of HVAC will commence during summer break
- Anticipated 1st Advertisement – December 2014
- Anticipated Bid Opening – February 2015



Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due October 1st
- 100% Construction Documents are due November 21st

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



William J. Fischer Elementary School Refurbishment ^(RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due September 5th
- 100% Construction Documents are due October 22nd

Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – December 2014



Fortier (Lusher) High School Refurbishment ^(OPSB)

5624 Freret Street, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation and repairs to the roof, masonry, plaster, windows, exterior doors, canopies, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Core Construction

Construction Phase

- Anticipated Notice to Proceed - September 4th
- Contractor is mobilizing

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



Gaudet Elementary School Refurbishment ^(RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - SD

- Schematic Design Documents were received August 25th
- 50% Construction Documents are due October 15th

Procurement Phase

- Anticipated 1st Advertisement – February 2015
- Anticipated Bid Opening – March 2015



Gentilly Terrace School Refurbishment ^(RSD)

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Construction Phase

- Contract is being reviewed by LDOE
- Anticipated Notice to Proceed - September 8th

Contractual Substantial Completion – March 2015

Forecasted Substantial Completion – March 2015



Gentilly Terrace School Kitchen Refurbishment ^(RSD)

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due October 1st
- 100% Construction Documents are due November 21st

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



Samuel J. Green Elementary School Refurbishment ^(RSD)

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

Construction Phase

- Owner is reviewing the contract
- Anticipated Notice to Proceed - September 24th

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



Edgar P. Harney Elementary School Refurbishment ^(RSD)

2503 Willow Street, New Orleans, LA 70113 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Hamilton Anderson Associates

Contractor - TBD

Design Phase - CD

- Bid Documents are complete

Procurement Phase

- Anticipated 1st Advertisement – September 2014
- Anticipated Bid Opening – October 2014



Andrew Jackson School Refurbishment ^(RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Bid Documents are complete
- Procurement will be delayed so that installation of windows will commence during summer break

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



Andrew Jackson School Kitchen Refurbishment ^(RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due October 1st
- 100% Construction Documents are due November 21st

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



J. W. Johnson Elementary School Refurbishment ^(RSD)

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due September 5th

Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – December 2014



Dr. Martin L. King Elementary School Refurbishment ^(RSD)

1617 Caffin Avenue, New Orleans, LA 70117 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Hamp's Construction, LLC

Construction

- Installation of screen fabric on doors has started
- Gypsum board finishing is ongoing in mechanical rooms

Contractual Substantial Completion – November 2014

Forecasted Substantial Completion – November 2014



Dr. Martin L. King Elementary School Kitchen Refurbishment ^(RSD)

1617 Caffin Avenue, New Orleans, LA 70117 District E Ward 9

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due October 1st
- 100% Construction Documents are due November 21st

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



Lafayette Elementary School Refurbishment ^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are due September 22nd

Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – December 2014



Laurel Elementary School Refurbishment ^(RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- 100% Construction Documents were received
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – December 2014



Live Oak Elementary School Refurbishment ^(RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

Design Phase - CD

- 100% Construction Documents were received
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – January 2015



Lusher Elementary School Refurbishment ^(OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source – FEMA

Architect – Meyer Engineers, LTD.


Contractor - TBD

Design Phase - CD

- 100% Construction Documents will be delayed until September 24th due to adjustments with the Design

Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – December 2014

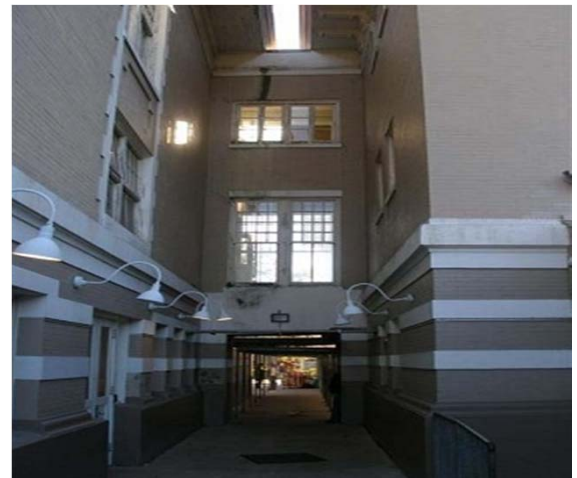

Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – TBD

Contractor - TBD

Design Phase - CD

- Project will be placed on hold until a new Architect has been selected

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



McDonogh #28 School Refurbishment ^(RSD)

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects, LLC

Contractor - TBD

Design Phase – CD

- Bid Documents are complete
- Procurement will be delayed so that installation of windows will commence during summer break

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



McDonogh #28 School Kitchen Refurbishment ^(RSD)

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due October 1st
- 100% Construction Documents are due November 21st

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



McDonogh #32 School Refurbishment (RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- 100% Construction Documents are due September 15th

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



Nelson Elementary School Refurbishment (OPSB)

3121 St. Bernard Avenue, New Orleans, LA 70119 District D Ward 7

Scope of work: Renovation and repairs to the roof, masonry, windows, exterior doors, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – Harry Baker Smith Architects

Contractor - TBD

Design Phase - CD

- Bid Documents are due end of September

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



Sarah T. Reed School Refurbishment (RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase - CD

- Bid Documents are complete

Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – December 2014



Sarah T. Reed School Kitchen Refurbishment ^(RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due October 1st
- 100% Construction Documents are due November 21st

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



Rosenwald Elementary School Refurbishment ^(RSD)

6501 Berkley Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – SD

- Schematic Design Documents were received August 28th
- 50% Construction Documents are due October 10th

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



Henry C. Schaumburg Elementary School ^(RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc

Contractor - Hernandez Consulting, LLC

Construction Phase

- Anticipated Notice to Proceed - September 22nd

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – June 2015



Village de l'Est Elementary School Refurbishment ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CBDG

Architect – Duplantis Design Group, PC

Contractor - TBD

Design Phase - CD

- 100% Construction Documents were received August 22nd

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



Albert Wicker School Kitchen Refurbishment ^(RSD)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due October 1st
- 100% Construction Documents are due November 21st

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – February 2015



Sylvanie F. Williams School Refurbishment ^(RSD)

3127 Martin Luther King Jr. Boulevard, New Orleans, LA 70125 District B Ward 2

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Bid Documents are complete

Procurement Phase

- 1st Advertisement – July 30th
- 2nd Advertisement – August 6th
- 3rd Advertisement – August 13th
- Pre-Bid Conference – August 14th
- Bid Opening – September 3rd



OTHER PROJECTS

Timbers III - Building Controls ^(OPSB)

3520 General DeGaulle Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: Design and installation of new building controls

Funding Source – OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - PC

- Owner has placed project on hold

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



Timbers III - IT Room Relocation ^(OPSB)

3520 General DeGaulle Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: Relocation of the Information Technology Room

Funding Source – OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Bid Documents are complete

Procurement Phase

- 1st Advertisement – July 23rd
- 2nd Advertisement – July 30th
- 3rd Advertisement – August 6th
- Pre-Bid Conference – August 7th
- Bid Opening – September 3rd



Building Automation System Integration At Recovery School District Central And Remote Offices ^(RSD)

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview

Funding Source – FEMA

Architect – Moses Engineers

Contractor – Synergy Building Solutions, Inc.

Construction Phase

- The five Quick Start Schools are complete, the Energy Dash Board is being implemented
- Sylvania Williams Elementary School, Sarah T. Reed Elementary School, Fannie C. Williams Elementary School, Bienville Elementary School, Charles L. Colton Elementary School, William Frantz Elementary School, Parkview Elementary School, Osborne Elementary School, Carter G. Woodson Elementary School, Walter Cohen High School, and Albert Wicker Elementary School are complete
- New integration work is ongoing on Dolores T Aaron Elementary School, A. D. Crossman Elementary School, and Benjamin Banneker Elementary School
- Lawrence D. Crocker Elementary School is anticipated to start integration to the BAS early September 2014

Contractual Substantial Completion – November 2014

Forecasted Substantial Completion – November 2014



MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

Andrew J. Bell Junior High School Mothball ^(RSD)

1010 N. Galvez St., New Orleans, LA 70119 District D Ward 6

Scope of work: Design Services to assist in determining the condition of the facilities both interior and exterior, make recommendations to stabilize the facilities and provide drawings required to provide a water barrier, ventilation, and rudimentary fire detection and to secure openings and entryways. Construction Services to stabilize the facility according to the designer's drawings and specifications.

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – CDW Services, LLC

Mothballing of Closed Schools - Safe & Secure

- Mothballing of the Gymnasium, Administration Building, Annex, Building "C", Building "D", Chapel, & E.A.Christy Building

Construction Phase

- Removal of debris from the Christy building is complete
- Roof system on the administration building is complete
- Tuck-pointing is ongoing at the Chapel and Building "B"

Contractual Substantial Completion – May 2014

Forecasted Substantial Completion – September 2014



Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School ^(RSD)

1010 N. Galvez St. & 2327 St. Philip Street, New Orleans, LA 70119 District D Ward 6

Scope of work: Demolition of existing caretakers cottages

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

Design Phase - CD

- 100% Construction Documents were received August 11th

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



John F. Kennedy Modular Demolition ^(RSD)

5700 Wisner Boulevard, New Orleans, LA 70124 District A Ward 5

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Harry Baker Smith Architects

Contractor – Hamps Construction

Construction Phase

- Contractor has mobilized
- Demolition of Modulars has started

Contractual Substantial Completion – September 2014

Forecasted Substantial Completion – September 2014



Demolition of Modular Buildings at Livingston and Schwarz ^(RSD)

7301 Dwyer Road & 709 Park Boulevard, New Orleans, LA District E Ward 9 & District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – TBD

Design Phase - CD

- 50% Construction Documents were received August 28th
- 100% Construction Documents are due October 1st

Procurement Phase

- Anticipated 1st Advertisement – November 2014
- Anticipated Bid Opening – December 2014



George Mondy Elementary School Mothball ^(RSD)

2327 St. Philip Street, New Orleans, LA 70119 District D Ward 6

Scope of work: Design Services to assist in determining the condition of the facilities both interior and exterior, make recommendations to stabilize the facilities and provide drawings required to provide a water barrier, ventilation, and rudimentary fire detection and to secure openings and entryways. Construction Services to stabilize the facility according to the designer's drawings and specifications.

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

Design Phase - CD

- Owner has placed the project on hold

Procurement Phase

- Anticipated 1st Advertisement – December 2014
- Anticipated Bid Opening – January 2015



JoEllen Smith Medical Center Demolition (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

Design Phase - CD

- 100% Construction Documents were received August 4th
- Bid Documents are due September 9th

Procurement Phase

- Anticipated 1st Advertisement – October 2014
- Anticipated Bid Opening – November 2014



Comprehensive List - Completed Projects

- 1 Abrams | Morial | Abramson | Coghill Demolition ^(RSD)
- 2 A. D. Cross Elementary School Energy Conservation ^(RSD)
- 3 A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)
- 4 A. D. Crossman Elementary School Refurbishment ^(RSD)
- 5 A. P. Tureaud Elementary School Roof Repairs ^(RSD)
- 6 Agnes Bauduit Elementary School Boiler ^(RSD)
- 7 Albert Wicker Elementary School Refurbishment ^(RSD)
- 8 Albert Wicker Elementary School Roof Repairs ^(RSD)
- 9 Alfred Lawless Senior High Security Fencing ^(RSD)
- 10 Alice M. Harte Elementary School Demolition ^(OPSB)
- 11 Andrew J. Bell Junior High School Roof Replacement ^(RSD)
- 12 Andrew Jackson Elementary School Roof Repairs ^(RSD)
- 13 Andrew Jackson Elementary School Solar Panels ^(RSD)
- 14 Andrew H. Wilson Elementary School Cottage ^(RSD)
- 15 Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)
- 16 Augustine Elementary School Roof ^(RSD)
- 17 Avery-Alexander Elementary School Demolition ^(RSD)
- 18 Barbara C. Jordan Elementary School Demolition ^(RSD)
- 19 Bell JH Shoring ^(RSD)
- 20 Benjamin Banneker Elementary School Energy Conservation ^(RSD)
- 21 Benjamin Franklin Senior High School ^(OPSB)
- 22 Bienville Elementary School Demolition ^(RSD)
- 23 Booker T. Washington High School Partial Demolition ^(RSD)
- 24 Carter G. Woodson Middle School Demolition ^(RSD)
- 25 Central Services Warehouse Demolition ^(OPSB)
- 26 Charles J. Colton Elementary Selective Demolition ^(RSD)
- 27 Charles J. Colton Elementary School ^(RSD)
- 28 Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)
- 29 Cohen High School Health Clinic ^(RSD)
- 30 Douglass High School Under Floor Utilities ^(RSD)
- 31 Dr. Martin Luther King School Roof Repairs ^(RSD)
- 32 Dr. Martin Luther King Jr. School Renovation ^(RSD)
- 33 Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)
- 34 East Bank Swing Space for Audubon Charter School ^(OPSB)
- 35 Edgar P. Harney Elementary School Roof Repairs ^(RSD)
- 36 Edna Karr High School - Gymnasium Repair ^(OPSB)
- 37 Edward Livingston Middle School Demolition ^(RSD)
- 38 Edward Henry Phillips Junior High School Demolition ^(OPSB)
- 39 New Edward Hynes School ^(OPSB)
- 40 Edwards | Hardin | Lockett | Lawless Demolition ^(RSD)
- 41 Eleanor L. McMain School Replacement of Existing Chillers ^(OPSB)
- 42 Eleanor L. McMain School Clinic ^(OPSB)

- 43 Ernest N. Morial Elementary Security Fencing ^(RSD)
- 44 Fannie C. Williams Elementary School Demolition ^(RSD)
- 45 Fisk-Howard Elementary School Demolition ^(RSD)
- 46 Florence J. Chester Elementary School Demolition ^(RSD)
- 47 Francis W. Gregory Demolition ^(RSD)
- 48 Frederick A. Douglass High Switchgear ^(RSD)
- 49 Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)
- 50 George Mondy Elementary School Mothball ^(RSD)
- 51 George Washington Carver High School Demolition ^(RSD)
- 52 Greater St. Stephens School ^(OPSB)
- 53 Henry Allen Elementary School Roof ^(RSD)
- 54 Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)
- 55 Holy Cross Modular Relocation ^(RSD)
- 56 Israel M. Augustine Middle School Roof Replacement ^(RSD)
- 57 Israel M. Augustine Middle School Mothball ^(RSD)
- 58 James Derham Demolition ^(RSD)
- 59 James W. Johnson Elementary School Roof ^(RSD)
- 60 New Jean Batiste de Bienville School ^(RSD)
- 61 Jean Gordon Elementary School Demolition ^(RSD)
- 62 John Dibert Elementary School Roof ^(RSD)
- 63 John W. Hoffman Elementary School Demolition ^(RSD)
- 64 John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)
- 65 John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)
- 66 John F. Kennedy High School Demolition ^(RSD)
- 67 John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)
- 68 John McDonogh Senior High School Roof ^(RSD)
- 69 John A. Shaw Elementary School Mothball ^(RSD)
- 70 Joseph S. Clark Senior High School Roof Repairs ^(RSD)
- 71 Joseph A. Craig Elementary Canopies ^(RSD)
- 72 Joseph A. Craig Elementary Elevator Installation ^(RSD)
- 73 Joseph A. Hardin Elementary Security Fencing ^(RSD)
- 74 Lafayette Elementary School Roof and Masonry ^(RSD)
- 75 Lake Area | Landry Demolition ^(RSD)
- 76 Langston Hughes Elementary School (Phase I) ^(RSD)
- 77 Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)
- 78 Langston Hughes Elementary School - Dumpster Pad ^(RSD)
- 79 Lawrence D. Crocker Elementary School Demolition ^(RSD)
- 80 L.B. Landry Annex Demolition ^(RSD)
- 81 Little Woods Elementary School Demolition ^(RSD)
- 82 Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)
- 83 Live Oak Elementary School Roof ^(RSD)
- 84 Live Oak Elementary School Exterior Door Replacement ^(RSD)
- 85 Lorraine Hansberry Elementary School Mothball ^(RSD)
- 86 Louis D. Armstrong Elementary School ^(RSD)
- 87 Mahalia Jackson Elementary School ^(OPSB)

- 88 Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)
- 89 Mahalia Jackson Elementary School Office Renovation ^(OPSB)
- 90 Martin Behrman Elementary School Roof ^(RSD)
- 91 Martin Luther King Jr. Elementary Canopy System ^(RSD)
- 92 Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)
- 93 Mary Church Terrell Elementary School Demolition ^(RSD)
- 94 Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)
- 95 Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)
- 96 McDonogh #7 High School Repairs ^(OPSB)
- 97 McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)
- 98 McDonogh #28 Elementary School Roof ^(RSD)
- 99 McDonogh #32 Roof Replacement ^(RSD)
- 100 McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)
- 101 McDonogh #42 Elementary School Roof ^(RSD)
- 102 McDonogh #42 Elementary School HVAC Replacement ^(RSD)
- 103 Mildred C. Osborne Elementary School Demolition ^(RSD)
- 104 Mildred C. Osborne Elementary School ^(RSD)
- 105 Modular Campuses Close Outs ^(RSD)
- 106 Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)
- 107 Modular Structures at Langston Hughes Elementary School ^(RSD)
- 108 Morris F.X. Jeff Elementary School Demolition ^(RSD)
- 109 Morris F.X. Jeff Elementary School Mothball ^(RSD)
- 110 Murray G. Henderson Elementary School Roof ^(RSD)
- 111 New Andrew H. Wilson Elementary School ^(RSD)
- 112 New Carter G. Woodson School ^(RSD)
- 113 New Fannie C. Williams School ^(RSD)
- 114 New Joseph A. Craig Elementary School ^(RSD)
- 115 New L.B. Landry High School ^(RSD)
- 116 New Lake Area High School ^(RSD)
- 117 New Lawrence D. Crocker School ^(RSD)
- 118 New Parkview School ^(RSD)
- 119 New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)
- 120 New William Frantz Elementary School ^(RSD)
- 121 New Orleans High School Signature Center Study ^(RSD)
- 122 Oretha C. Haley Demo ^(RSD)
- 123 Oretha C. Haley Elementary School Mothball ^(RSD)
- 124 Parkview Elementary School Demolition ^(RSD)
- 125 Paul L. Dunbar Elementary School Demolition ^(RSD)
- 126 Paul B. Habans Elementary School Roof Repairs ^(RSD)
- 127 Phillis Wheatley Elementary School Demolition ^(RSD)
- 128 Phillis Wheatley Elementary School ^(RSD)
- 129 Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)
- 130 Sarah T. Reed High School Bleachers ^(RSD)
- 131 Sarah T. Reed High School Auditorium Wall ^(RSD)

- 132 Seabrook Computer Training Center Demolition ^(OPSB)
- 133 Schaumburg Chillers ^(RSD)
- 134 Schwarz Alternative Repairs ^(RSD)
- 135 Schwarz Alternative Modularity Demolition ^(RSD)
- 136 Sherwood Forest Elementary School Demolition ^(RSD)
- 137 Sophie B. Wright School Selective Demolition ^(RSD)
- 138 Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)
- 139 Stuart R. Bradley Elementary School Demolition ^(RSD)
- 140 Sylvanie Williams Elementary School AHU Replacement ^(RSD)
- 141 Sylvanie Williams Elementary School Play Yard ^(RSD)
- 142 Sylvanie Williams Elementary School Roof Repairs ^(RSD)
- 143 Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)
- 144 Temporary Campus for McDonogh #11 Expropriation ^(OPSB)
- 145 Thomas A. Edison Elementary School Demolition ^(RSD)
- 146 Thomy Lafon Elementary School Demolition ^(RSD)
- 147 Thomy Lafon School Interpretative Display ^(RSD)
- 148 Timbers Park Office Building #1 & #2 Demolition ^(OPSB)
- 149 Timbers HVAC ^(OPSB)
- 150 Village de L'est Elementary School Subsidence ^(RSD)
- 151 Village de L'est Elementary School Roof and Modular Demolition ^(RSD)
- 152 Vorice J. Waters Elementary School Demolition ^(RSD)
- 153 Valena C. Jones Elementary School ^(RSD)
- 154 Walter L. Cohen High School HVAC ^(RSD)
- 155 Warren Easton High School Window Replacement ^(OPSB)
- 156 West Bank Swing Space for Alice Harte Elementary School ^(OPSB)
- 157 New William J. Guste Elementary School ^(RSD)
- 158 William J. Guste Elementary School Science Lab ^(RSD)
- 159 William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)
- 160 William Frantz Elementary School ^(RSD)
- 161 William Frantz Elementary School Roof ^(RSD)

August 2014 Program Update OPSB & RSD Phase I Projects




Program Financial Status

The **OPSB** has \$187 million in open contracts for the Phase 1 capital program projects after issuing \$95 thousand in new contracts, change orders and amendments in August. In addition, the total change orders to date, \$2.6 million, accounts for approximately two percent (1.60%) of the total open Phase 1 construction contracts. Finally, OPSB anticipates issuing no new contracts in Phase 1 construction and \$95 thousand in professional services contracts/amendments in September.

The **RSD** has \$174 million in open contracts for the Phase 1 capital program projects after issuing no new contracts and \$208 thousand in change orders and amendments in August. In addition, the total change orders to date, \$5.6 million, accounts for approximately three percent (3.54%) of the total open Phase 1 construction contracts. Finally, RSD anticipates issuing \$629 thousand in Phase 1 contracts, change orders, and professional services contracts/amendments in September.


Value of Projects by Phase

Design	\$	-
Procurement	\$	-
Construction	\$	159,877,387
Complete	\$	41,666,113
Future Projects	\$	6,850,228

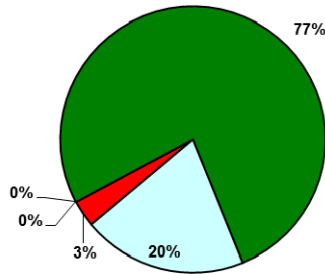

Value of Projects by Phase

Design	\$	-
Procurement	\$	-
Construction	\$	31,247,979
Complete	\$	436,243,651
Future Projects	\$	-

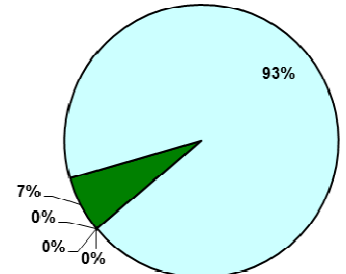

Note-The value in each phase represents the total of full project budgets.

Program Schedule Status

OPSB Phase 1 Projects				
Group 1	Design	Procurement	Construction	Complete
Project				
Mahalia Jackson	Occupied (May 2010)			
Edward Hynes School	Occupied (January 2012)			
Group 2	Design	Procurement	Construction	Complete
Project				
Audubon School				
Alice Harte School				
McMain School - Health Clinic	Complete (August 2013)			
- Gymnasium				
- Maint. Upgrade				
- Roof				
McDonogh 35 HS (Phillips/Waters)				
New PK-8 at N Kenilworth (Moton)				

RSD Phase 1 Projects				
Group 1	Design	Procurement	Construction	Complete
Project				
Guste ES	Occupied (August 2008)			
Langston Hughes ES	Occupied (August 2009)			
Andrew H. Wilson ES	Occupied (January 2010)			
Lake Area HS	Occupied (January 2010)			
L.B. Landry HS	Occupied (July 2010)			
Joseph A. Craig ES	Occupied (January 2010)			
Jean Baptiste de Bienville ES	Occupied (July 2012)			
Parkview ES	Occupied (August 2012)			
Lawrence D. Crocker ES	Occupied (September 2012)			
Fannie C. Williams ES	Occupied (October 2012)			
Carter G. Woodson ES	Occupied (October 2012)			
Mildred Osborne ES	Occupied (August 2012)			
William Frantz ES	Occupied (August 2013)			
Charles J. Colton ES	Occupied (June 2013)			
Group 2	Design	Procurement	Construction	Complete
Project				
Little Woods ES	Occupied (May 2013)			
Phillis Wheatley ES	Occupied (July 2014)			
Edward Livingston HS				

August 2014 Program Update OPSB & RSD Phase II Projects




Program Financial Status


The **OPSB** has \$57 million in open contracts for the Phase 2 capital program projects after issuing \$17 million in new contracts and no change orders and amendments in August. In addition, the total change orders to date, \$316 thousand, account for approximately one percent (0.60%) of the total open Phase 2 construction contracts. OPSB anticipates issuing no new contracts in Phase 2 construction and professional services in September.

The **RSD** has \$362 million in open contracts for the Phase 2 capital program projects after issuing no new contracts and \$413 thousand in change orders and amendments in August. Additionally, the total change orders to date, -\$304 thousand, account for approximately less than one percent (-0.28%) of the total open Phase 2 construction contracts. The RSD anticipates issuing \$32 million in Phase 2 construction contracts/change orders and no professional services contracts/amendments in September.

Value of Projects by Phase

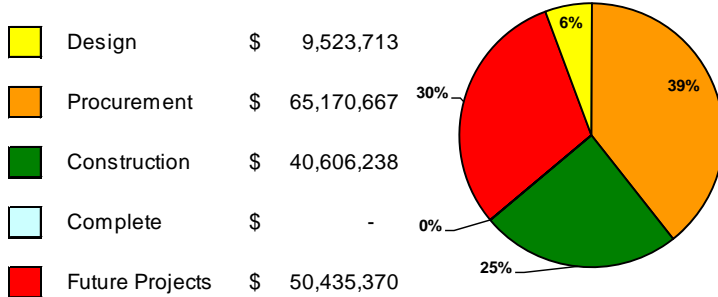

Value of Projects by Phase

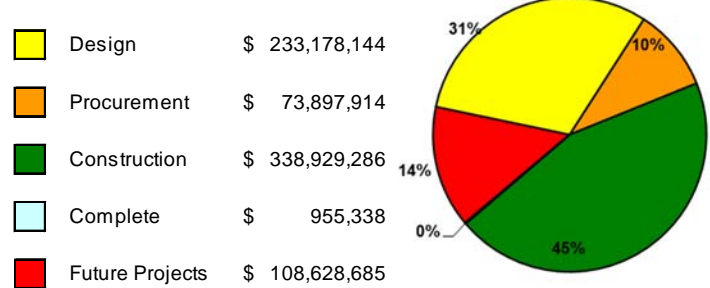

Note-The value in each phase represents the total of full project budgets.

Program Schedule Status

OPSB Phase 2 Projects				
New Schools				
Project	Design	Procurement	Construction	Complete
Bio District HS				
Lake Forest PK-8 @ GST Stephens				
New Karr HS @ JoElen Smith D/B				
Full Renovations				
Project	Design	Procurement	Construction	Complete
Ben Franklin ES - Reno I				
Refurbished/Renovations				
Project	Design	Procurement	Construction	Complete
Ben Franklin HS				
Bethune ES				
Warren Easton				
Fortier (Lusher) HS				
Lusher ES				
Nelson ES				

RSD Phase 2 Projects				
Full Renovations				
Project	Design	Procurement	Construction	Complete
Clark HS				
Drew ES				
John McDonogh HS				
Johnson ES				
Lafayette ES				
Live Oak ES				
McDonogh 42 ES				
Sophie B Wright ES				
Tubman ES				
McNair ES				
Refurbished/Renovations				
Project	Design	Procurement	Construction	Complete
Allen ES				
Bauduit ES				
Crossman ES	Completed April, 2014			
Douglass HS				
Eisenhower HS				
Fischer ES				
Gaudet ES				
Gentilly Terrace ES				
Green MS				
Harney ES				
A. Jackson ES				
Johnson ES				
Lafayette ES				
Laurel ES				
Live Oak ES				
Marshall ES				
Martin L King ES				
McDonogh 28 ES				
McDonogh 32 ES				
McDonogh 7 ES				
O Perry Walker HS				
Reed HS				
Rosenwald ES				
Schaumburg ES				
Schwartz HS				
Sylvanie Williams				
Village de l'est ES				
Wicker ES	Completed April, 2014			



BESE MONTHLY REPORT
OPEN CONTRACTS as of 09/09/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
DEMOLITIONS					
Booker T Washington HS Demolition - Annex & Accessory Bldgs	Shaw Environmental & Infrastructure	FEMA	\$ 49,500.00	\$ 51,032.00	\$ 100,532.00
Booker T Washington HS Demolition - Annex & Accessory Bldgs Total					\$ 100,532.00
George Mondy - Caretakers Cottage Demo	VergesRome Architects, APAC	FEMA	\$ -	\$ 1,823.00	\$ 1,823.00
George Mondy - Caretakers Cottage Demo Total					\$ 1,823.00
Andrew Bell - Caretakers Cottage Demo	VergesRome Architects, APAC	FEMA	\$ -	\$ 1,690.00	\$ 1,690.00
Andrew Bell - Caretakers Cottage Demo Total					\$ 1,690.00
Kennedy HS Modular Demolition	Harry Baker Smith Architects II, PLLC	FEMA	\$ 5,225.00	\$ -	\$ 5,225.00
	Hamp's Construction, LLC	FEMA	\$ 89,888.00	\$ -	\$ 89,888.00
Kennedy HS Modular Demolition Total					\$ 95,113.00
Gregory Modular Demolition	Holly & Smith Architects, APAC	FEMA	\$ 11,576.00	\$ -	\$ 11,576.00
Gregory Modular Demolition Total					\$ 11,576.00
Abramson Modular Demolition	Holly & Smith Architects, APAC	FEMA	\$ 11,576.00	\$ -	\$ 11,576.00
Abramson Modular Demolition Total					\$ 11,576.00
PHASE 1 SCHOOLS					
FC Williams ES Construction	Yeates & Yeates Architects, LLC	FEMA	\$ -	\$ 2,094,877.92	\$ 2,094,877.92
	Brice Building Company	FEMA	\$ 21,997,000.00	\$ 1,018,383.28	\$ 23,015,383.28
FC Williams ES Construction Total					\$ 25,110,261.20
FC Williams ES Playground Equipment Relocation	Mahlum Scairono Martinez Architects, LLC	FEMA	\$ 14,250.00	\$ -	\$ 14,250.00
	Hamp's Construction, LLC	FEMA	\$ 93,300.00	\$ -	\$ 93,300.00
FC Williams ES Playground Equipment Relocation Total					\$ 107,550.00
FC Williams ES Outdoor Teaching Area	Tuna Construction, LLC	Insurance Proceeds	\$ 165,000.00	\$ -	\$ 165,000.00
FC Williams ES Outdoor Teaching Area Total					\$ 165,000.00
Crocker ES Construction	Chenevert Architects, LLC	FEMA	\$ -	\$ 1,653,183.82	\$ 1,653,183.82
	Mathes Briere Architects	FEMA	\$ 50,000.00	\$ -	\$ 50,000.00
	Farnsworth Group, Inc - Building Commissioning 7 New & Reno	FEMA	\$ 157,600.00	\$ 67,731.38	\$ 225,331.38
	Satterfield & Pontikes Construction Group LLC	FEMA	\$ 18,598,500.00	\$ 911,998.41	\$ 19,510,498.41
	Harry Baker Smith Architects II, PLLC	FEMA	\$ 9,384.00	\$ -	\$ 9,384.00
Crocker ES Construction Total					\$ 21,448,397.61
Crocker ES Playground Equipment Relocation	Mahlum Scairono Martinez Architects, LLC	FEMA	\$ 10,695.00	\$ -	\$ 10,695.00
	Hamp's Construction, LLC	FEMA	\$ 70,400.00	\$ -	\$ 70,400.00
Crocker ES Playground Equipment Relocation Total					\$ 81,095.00
Crocker ES Demolition	Chenevert Architects, LLC	FEMA	\$ -	\$ 56,170.50	\$ 56,170.50
Crocker ES Demolition Total					\$ 56,170.50
Frantz ES Renovation/Addition	Billes Architecture, LLC	FEMA	\$ 855,945.00	\$ -	\$ 2,473,044.11
	Farnsworth Group, Inc - Building Commissioning Quickstart	FEMA	\$ -	\$ 213,151.48	\$ 213,151.48
	The Lathan Company	FEMA	\$ 19,537,000.00	\$ 1,300,914.89	\$ 20,837,914.89
	Harry Baker Smith Architects II, PLLC	FEMA	\$ 24,522.00	\$ -	\$ 24,522.00
Frantz ES Renovation/Addition Total					\$ 23,548,632.48
Colton ES Renovation	Waggonner & Ball Architects, APC	FEMA	\$ 1,208,475.00	\$ 1,727,030.20	\$ 2,935,505.20
	Farnsworth Group, Inc - Building Commissioning 7 New & Reno	FEMA	\$ 164,900.00	\$ 61,473.00	\$ 205,639.00
	F.H. Paschen, S.N. Nielsen & Associates, LLC	FEMA	\$ 26,173,000.00	\$ 665,424.66	\$ 26,838,424.66
	Harry Baker Smith Architects II, PLLC	FEMA	\$ 5,506.00	\$ -	\$ 5,506.00
Colton ES Renovation Total					\$ 30,005,808.86
Osborne ES Construction	Fauntleroy & Latham Architects, APC	FEMA	\$ 1,336,822.00	\$ 648,317.17	\$ 1,985,139.17
	Farnsworth Group, Inc - Building Commissioning 7 New & Reno	FEMA	\$ 157,600.00	\$ 48,039.00	\$ 205,639.00
	F.H. Paschen, S.N. Nielsen & Associates, LLC	FEMA	\$ 21,375,000.00	\$ 408,401.46	\$ 21,783,401.46
	Harry Baker Smith Architects II, PLLC	FEMA	\$ 3,055.00	\$ -	\$ 3,055.00
Osborne ES Construction Total					\$ 23,977,234.63
Woodson ES Construction	Farnsworth Group, Inc - Building Commissioning 7 New & Reno	FEMA	\$ 157,600.00	\$ 72,075.38	\$ 229,675.38
	Harry Baker Smith Architects II, PLLC	FEMA	\$ 1,904.00	\$ -	\$ 1,904.00
Woodson ES Construction Total					\$ 231,579.38
Parkview ES Construction	Farnsworth Group, Inc - Building Commissioning 7 New & Reno	FEMA	\$ 157,600.00	\$ 60,622.00	\$ 218,222.00
	Harry Baker Smith Architects II, PLLC	FEMA	\$ 2,449.00	\$ -	\$ 2,449.00
Parkview ES Construction Total					\$ 220,671.00
Parkview ES Playground Equipment Relocation	Mahlum Scairono Martinez Architects, LLC	FEMA	\$ 10,695.00	\$ -	\$ 10,695.00
	Hamp's Construction, LLC	FEMA	\$ 73,800.00	\$ -	\$ 73,800.00
Parkview ES Playground Equipment Relocation Total					\$ 84,495.00



BESE MONTHLY REPORT
OPEN CONTRACTS as of 09/09/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
Little Woods ES Construction	Group Novak, LLC Farnsworth Group, Inc - Building Commissioning 5 plus 2 MAPP Construction, LLC	FEMA	\$ 1,498,299.00	\$ 391,394.41	\$ 1,889,693.41
		FEMA	\$ 222,742.00	\$ 13,506.00	\$ 236,248.00
		FEMA	\$ 21,980,000.00	\$ 143,254.21	\$ 22,123,254.21
Little Woods ES Construction Total					\$ 24,249,195.62
Little Woods ES Playground Equipment Relocation	Mahlum Scairono Martinez Architects, LLC	FEMA	\$ -	\$ 10,695.00	\$ 10,695.00
Little Woods ES Playground Equipment Relocation Total					\$ 10,695.00
Wheatley ES New Construction	Holly & Smith Architects, APAC Farnsworth Group, Inc - Building Commissioning 5 plus 2 Gibbs Construction, L.L.C.	FEMA	\$ 1,749,900.00	\$ 494,002.93	\$ 2,243,902.93
		FEMA	\$ 222,742.00	\$ -	\$ 222,742.00
		QSCB	\$ 25,275,000.00	\$ 1,011,808.53	\$ 26,286,808.53
Wheatley ES New Construction Total					\$ 28,753,453.46
Wheatley ES Interpretive Display	Bright Moments, LLC	FEMA	\$ 4,125.00	\$ -	\$ 4,125.00
Wheatley ES Interpretive Display Total					\$ 4,125.00
PHASE 2 SCHOOLS					
Fisk-Howard ES Construction	VergesRome Architects, APAC + Fanning Howey, A Joint Venture Farnsworth Group, Inc - Building Commissioning 5 plus 2 FHP Tectonics Corp.	FEMA	\$ 1,582,878.00	\$ 340,771.44	\$ 1,923,649.44
		FEMA	\$ 222,742.00	\$ 20,048.56	\$ 242,790.56
		FEMA	\$ 25,580,947.45	\$ 245,129.29	\$ 25,826,076.74
		Insurance Proceeds	\$ 19,052.55	\$ -	\$ 19,052.55
Fisk-Howard ES Construction Total					\$ 28,011,569.29
New High School @ Alfred Lawless	Sizeler Thompson Brown Architects Project Design Group, LLC Farnsworth Group, Inc - Building Commissioning 5 plus 2 CORE Construction Services, L.L.C.	FEMA	\$ 1,981,345.00	\$ 39,809.00	\$ 2,021,154.00
		FEMA	\$ 321,880.00	\$ (94,990.49)	\$ 226,889.51
		FEMA	\$ 35,728,664.00	\$ (364,619.78)	\$ 35,364,044.22
		Insurance Proceeds	\$ 45,336.00	\$ -	\$ 45,336.00
New High School @ Alfred Lawless Total					\$ 37,657,423.73
Dunbar ES Construction	Chenevert Architects, LLC Farnsworth Group, Inc - Building Commissioning 5 plus 2 The McDonnell Group, LLC	FEMA	\$ 1,437,088.00	\$ 409,565.28	\$ 1,846,653.28
		FEMA	\$ 222,742.00	\$ (45,060.09)	\$ 177,681.91
		FEMA	\$ 24,457,000.00	\$ (113,540.75)	\$ 24,343,459.25
		Insurance Proceeds	\$ 35,000.00	\$ -	\$ 35,000.00
Dunbar ES Construction Total					\$ 26,402,794.44
Bradley ES Renovation/Construction	Sizeler Thompson Brown Architects Project Design Group, LLC Farnsworth Group, Inc - Building Commissioning 1N + 4R Landis Construction Co., LLC	FEMA	\$ 1,582,878.00	\$ 42,076.05	\$ 1,624,954.05
		FEMA	\$ 223,767.17	\$ (67,638.97)	\$ 156,128.20
		FEMA	\$ 25,424,627.00	\$ (490,611.14)	\$ 24,934,015.86
		Insurance Proceeds	\$ 21,373.00	\$ -	\$ 21,373.00
Bradley ES Renovation/Construction Total					\$ 26,736,471.11
Drew ES Renovation	Blitch Knevel Architects, Inc. Farnsworth Group, Inc - Building Commissioning 1N + 4R CORE Construction Services, L.L.C.	FEMA	\$ 1,456,546.00	\$ 32,208.60	\$ 1,488,754.60
		FEMA	\$ 203,722.83	\$ -	\$ 203,722.83
		FEMA	\$ 15,296,000.00	\$ 546,036.93	\$ 15,842,036.93
Drew ES Renovation Total					\$ 17,534,514.36
McDonogh 42 ES Renovation	Eskew+Dumez+Ripple, APC Farnsworth Group, Inc - Building Commissioning 1N + 4R CORE Construction Services, L.L.C.	FEMA	\$ 1,371,659.00	\$ 235,106.05	\$ 1,606,765.05
		FEMA	\$ 204,763.03	\$ (58,536.74)	\$ 146,226.29
		Tax Credit	\$ 15,499,000.00	\$ 103,465.50	\$ 15,602,465.50
McDonogh 42 ES Renovation Total					\$ 17,355,456.84
Ernest 'Dutch' Morial School (New - PK-8)	Waggonner & Ball Architects, APC SSRCx, LLC - Building Commissioning 1R + 4N	FEMA	\$ 1,151,421.08	\$ 1,077,581.87	\$ 2,229,002.95
		FEMA	\$ 111,595.00	\$ -	\$ 111,595.00
Ernest 'Dutch' Morial School (New - PK-8) Total					\$ 2,340,597.95
Edward Livingston HS Construction	Rozas-Ward/a.i.a. architects, inc. Farnsworth Group, Inc - Building Commissioning 5 plus 2 Gibbs Construction, L.L.C.	FEMA	\$ 1,058,410.78	\$ 676,647.28	\$ 1,735,058.06
		FEMA	\$ -	\$ 213,049.90	\$ 213,049.90
		FEMA	\$ 31,479,833.27	\$ (2,087,692.19)	\$ 29,392,141.08
		Insurance Proceeds	\$ 50,166.73	\$ -	\$ 50,166.73
Edward Livingston HS Construction Total					\$ 31,390,415.77
Abrams ES Construction	Waggonner & Ball Architects, APC SSRCx, LLC - Building Commissioning 1R + 4N	FEMA	\$ 1,580,386.52	\$ 9,642.87	\$ 1,590,029.39
		FEMA	\$ 111,595.00	\$ -	\$ 111,595.00
Abrams ES Construction Total					\$ 1,701,624.39
Avery Alexander School (New - PK-8)	Professional Services Industries, Inc Sizeler Thompson Brown Architects Project Design Group, LLC SSRCx, LLC - Building Commissioning 1R + 4N	FEMA	\$ 30,581.00	\$ -	\$ 30,581.00
		FEMA	\$ 1,297,048.60	\$ 68,432.50	\$ 1,365,481.10
		FEMA	\$ 106,680.00	\$ -	\$ 106,680.00
Avery Alexander School (New - PK-8) Total					\$ 1,502,742.10
Sophie B Wright HS Renovation	Waggonner & Ball Architects, APC Farnsworth Group, Inc - Building Commissioning 1N + 4R	FEMA	\$ 1,847,676.00	\$ 453,934.50	\$ 2,301,610.50
		FEMA	\$ 212,571.51	\$ (77,988.12)	\$ 134,583.39
Sophie B Wright HS Renovation Total					\$ 2,436,193.89
Sophie B Wright HS Renovation - Test Pile & Exploratory Demo	Waggonner & Ball Architects, APC	FEMA	\$ -	\$ 4,650.20	\$ 4,650.20
Sophie B Wright HS Renovation - Test Pile & Exploratory Demo Total					\$ 4,650.20



BESE MONTHLY REPORT
OPEN CONTRACTS as of 09/09/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
Sophie B Wright HS Renovation - Selective Demolition and Test Pile	Waggonner & Ball Architects, APC	FEMA	\$ -	\$ 64,922.00	\$ 64,922.00
	Zimmer-Eschette Service II, LLC	FEMA	\$ 604,000.00	\$ 83,780.54	\$ 687,780.54
Sophie B Wright HS Renovation - Selective Demolition and Test Pile Total					\$ 752,702.54
John McDonogh HS Renovation	VergesRome Architects, APAC	FEMA	\$ 2,696,406.00	\$ -	\$ 2,696,406.00
John McDonogh HS Renovation Total					\$ 2,696,406.00
John McDonogh HS Renovation - Selective Demolition	VergesRome Architects, APAC	FEMA	\$ -	\$ -	\$ -
John McDonogh HS Renovation - Selective Demolition Total					\$ -
Tubman ES Renovation	Mahlum Scairono Martinez Architects, LLC	FEMA	\$ 1,375,942.00	\$ -	\$ 1,375,942.00
	SSRCx, LLC - Building Commissioning 1R + 4N	FEMA	\$ 61,478.00	\$ -	\$ 61,478.00
Tubman ES Renovation Total					\$ 1,437,420.00
New Orleans East HS (Abramson Site)	Rozas-Ward/a.i.a. architects, inc.	FEMA	\$ 1,056,051.52	\$ 738,853.86	\$ 1,794,905.38
	Farnsworth Group, Inc	FEMA	\$ 236,206.39	\$ (107,277.99)	\$ 128,928.40
	Gibbs Construction, L.L.C.	FEMA	\$ 27,768,550.95	\$ -	\$ 27,768,550.95
		Insurance Proceeds	\$ 31,449.05	\$ -	\$ 31,449.05
New Orleans East HS (Abramson Site) Total					\$ 29,723,833.78
New Booker T Washington HS - Test Pile	Hewitt-Washington & Associates Architects and Planners	FEMA	\$ -	\$ 9,050.00	\$ 9,050.00
New Booker T Washington HS - Test Pile Total					\$ 9,050.00
New Booker T Washington HS & Auditorium Rehabilitation	Hewitt-Washington & Associates Architects and Planners	FEMA	\$ 3,854,210.00	\$ (1,266,081.80)	\$ 2,588,128.20
New Booker T Washington HS & Auditorium Rehabilitation Total					\$ 2,588,128.20
New Booker T Washington HS Interpretive Display	Bright Moments, LLC	FEMA	\$ 4,125.00	\$ -	\$ 4,125.00
New Booker T Washington HS Interpretive Display Total					\$ 4,125.00
New Booker T Washington HS - Environmental	Shaw Environmental & Infrastructure	FEMA	\$ 91,927.00	\$ -	\$ 91,927.00
New Booker T Washington HS - Environmental Total					\$ 91,927.00
New Booker T Washington Medium High School	Farnsworth Group, Inc - Building Commissioning 7 New & Reno	FEMA	\$ 239,900.00	\$ 1,802.94	\$ 241,702.94
	Hewitt-Washington & Associates Architects and Planners	FEMA	\$ -	\$ 3,180,911.02	\$ 3,180,911.02
New Booker T Washington Medium High School Total					\$ 3,422,613.96
George W. Carver HS Construction	Farnsworth Group, Inc - Building Commissioning 5 plus 2	FEMA	\$ 321,880.00	\$ (71,907.18)	\$ 249,972.82
	Broadmoor, LLC	FEMA	\$ 48,883,407.00	\$ -	\$ 48,883,407.00
		HRSA	\$ 496,170.00	\$ -	\$ 496,170.00
George W. Carver HS Construction Total					\$ 49,629,549.82
George W. Carver HS Interpretive Display	Bright Moments, LLC	FEMA	\$ 4,125.00	\$ -	\$ 4,125.00
George W. Carver HS Interpretive Display Total					\$ 4,125.00
Habans ES Construction	SSRCx, LLC	FEMA	\$ 112,014.00	\$ -	\$ 112,014.00
	CORE Construction Services, L.L.C.	FEMA	\$ 30,373,000.00	\$ -	\$ 30,373,000.00
		Insurance Proceeds	\$ 30,000.00	\$ -	\$ 30,000.00
Habans ES Construction Total					\$ 30,515,014.00
Sherwood Forest School (New - PK-8)	SSRCx, LLC - Building Commissioning 1R + 4N	FEMA	\$ 106,680.00	\$ -	\$ 106,680.00
	CORE Construction Services, L.L.C.	FEMA	\$ 29,325,000.00	\$ -	\$ 29,325,000.00
		Insurance Proceeds	\$ 30,000.00	\$ -	\$ 30,000.00
Sherwood Forest School (New - PK-8) Total					\$ 29,461,680.00
REFURBISHMENTS					
Frederick A Douglass HS Refurbishment	VergesRome Architects, APAC	FEMA	\$ -	\$ 741,988.15	\$ 741,988.15
	FHP Tectonics Corp.	FEMA	\$ 8,588,000.00	\$ 734,889.52	\$ 9,322,889.52
Frederick A Douglass HS Refurbishment Total					\$ 10,064,877.67
Village de L'est ES Refurb	Duplantis Design Group, PC	FEMA	\$ 48,733.00	\$ -	\$ 48,733.00
Village de L'est ES Refurb Total					\$ 48,733.00
Albert Wicker ES Refurb	SCNZ Architects, LLC	FEMA	\$ 72,114.00	\$ (7,195.80)	\$ 64,918.20
	Tuna Construction, LLC	FEMA	\$ 523,000.00	\$ 15,176.49	\$ 538,176.49
Albert Wicker ES Refurb Total					\$ 603,094.69
Thurgood Marshall ES Refurb	Hamilton Anderson Associates	FEMA	\$ 70,601.00	\$ -	\$ 70,601.00
Thurgood Marshall ES Refurb Total					\$ 70,601.00
Henry C. Schaumburg ES Refurb	N-Y Associates, Inc.	FEMA	\$ 15,193.00	\$ 18,810.00	\$ 34,003.00
Henry C. Schaumburg ES Refurb Total					\$ 34,003.00
Edgar P. Harney ES Refurb	Hamilton Anderson Associates	FEMA	\$ 27,131.00	\$ 3,294.50	\$ 30,425.50
Edgar P. Harney ES Refurb Total					\$ 30,425.50
Julius Rosenwald ES Refurb	Byron J. Stewart & Associates, APC	FEMA	\$ 105,034.00	\$ -	\$ 105,034.00
Julius Rosenwald ES Refurb Total					\$ 105,034.00
Sylvanie Williams ES Refurb	N-Y Associates, Inc.	FEMA	\$ 48,754.00	\$ 82,801.07	\$ 131,555.07
Sylvanie Williams ES Refurb Total					\$ 131,555.07
Agnes L. Bauduit ES Refurb	Duplantis Design Group, PC	FEMA	\$ 301,824.00	\$ (15,471.40)	\$ 286,352.60
Agnes L. Bauduit ES Refurb Total					\$ 286,352.60



BESE MONTHLY REPORT
OPEN CONTRACTS as of 09/09/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
Laurel ES Refurb	Mahlum Scairono Martinez Architects, LLC	FEMA	\$ 458,942.00	\$ -	\$ 458,942.00
Laurel ES Refurb Total					\$ 458,942.00
McDonogh 28 ES Refurb	SCNZ Architects, LLC	FEMA	\$ 199,248.00	\$ 70,334.20	\$ 269,582.20
McDonogh 28 ES Refurb Total					\$ 269,582.20
Martin Luther King Jr. ES Refurb	VergesRome Architects, APAC	FEMA	\$ 72,295.00	\$ (11,127.00)	\$ 61,168.00
	Hamp's Construction, LLC	FEMA	\$ 342,400.00	\$ -	\$ 342,400.00
Martin Luther King Jr. ES Refurb Total					\$ 403,568.00
Henry Allen ES Refurb	N-Y Associates, Inc.	FEMA	\$ 92,546.00	\$ 95,975.77	\$ 188,521.77
Henry Allen ES Refurb Total					\$ 188,521.77
Andrew Jackson ES Refurb	N-Y Associates, Inc.	FEMA	\$ 118,872.00	\$ 151,255.51	\$ 270,127.51
Andrew Jackson ES Refurb Total					\$ 270,127.51
A.D. Crossman ES Refurb	Perez, APC	FEMA	\$ 45,212.00	\$ (8,004.00)	\$ 37,208.00
	One Construction, LLC	FEMA	\$ 239,000.00	\$ (1,925.00)	\$ 237,075.00
A.D. Crossman ES Refurb Total					\$ 274,283.00
Dwight D Eisenhower ES Refurb	Harry Baker Smith Architects II, PLLC	FEMA	\$ 154,483.00	\$ (17,229.10)	\$ 137,253.90
Dwight D Eisenhower ES Refurb Total					\$ 137,253.90
Gentilly Terrace ES Refurb	Byron J. Stewart & Associates, APC	FEMA	\$ 137,099.00	\$ (19,438.00)	\$ 117,661.00
Gentilly Terrace ES Refurb Total					\$ 117,661.00
Sarah T. Reed HS Refurb	Byron J. Stewart & Associates, APC	FEMA	\$ 105,514.00	\$ 40,266.85	\$ 145,780.85
Sarah T. Reed HS Refurb Total					\$ 145,780.85
Green ES Refurb	VergesRome Architects, APAC	FEMA	\$ 420,497.00	\$ 33,247.50	\$ 453,744.50
Green ES Refurb Total					\$ 453,744.50
Walter L. Cohen Food Service	N-Y Associates, Inc.	FEMA	\$ 27,456.00	\$ -	\$ 27,456.00
Walter L. Cohen Food Service Total					\$ 27,456.00
Banneker ES Food Service	SCNZ Architects, LLC	FEMA	\$ 29,528.00	\$ -	\$ 29,528.00
Banneker ES Food Service Total					\$ 29,528.00
McDonogh 32 ES Refurb	Byron J. Stewart & Associates, APC	FEMA	\$ 296,940.00	\$ -	\$ 296,940.00
McDonogh 32 ES Refurb Total					\$ 296,940.00
Live Oak ES Refurbishment	VergesRome Architects, APAC	FEMA	\$ 265,287.00	\$ 582,009.00	\$ 847,296.00
Lafayette ES Refurb Total					\$ 324,260.00
Gaudet ES Refurb	SCNZ Architects, LLC	FEMA	\$ 232,753.00	\$ -	\$ 232,753.00
Gaudet ES Refurb Total					\$ 232,753.00
Fischer ES Refurb	SCNZ Architects, LLC	FEMA	\$ 204,015.00	\$ 9,680.00	\$ 213,695.00
Fischer ES Refurb Total					\$ 213,695.00
Fischer ES Playground Equipment Relocation	Mahlum Scairono Martinez Architects, LLC	FEMA	\$ -	\$ (10,695.00)	\$ (10,695.00)
Fischer ES Playground Equipment Relocation Total					\$ (10,695.00)
Johnson ES Refurb	SCNZ Architects, LLC	FEMA	\$ 155,901.00	\$ 10,340.00	\$ 166,241.00
Johnson ES Refurb Total					\$ 166,241.00
A.D. Crossman Food Services	SCNZ Architects, LLC	FEMA	\$ 17,519.00	\$ -	\$ 17,519.00
A.D. Crossman Food Services Total					\$ 17,519.00
Dwight D Eisenhower ES Food Services	N-Y Associates, Inc.	FEMA	\$ 32,445.00	\$ -	\$ 32,445.00
Dwight D Eisenhower ES Food Services Total					\$ 32,445.00
Andrew Jackson ES Food Services	N-Y Associates, Inc.	FEMA	\$ 19,979.00	\$ -	\$ 19,979.00
Andrew Jackson ES Food Services Total					\$ 19,979.00
Martin Luther King Jr. ES Food Services	N-Y Associates, Inc.	FEMA	\$ 11,987.00	\$ -	\$ 11,987.00
Martin Luther King Jr. ES Food Services Total					\$ 11,987.00
Gentilly Terrace ES Food Services	SCNZ Architects, LLC	FEMA	\$ 19,519.00	\$ -	\$ 19,519.00
Gentilly Terrace ES Food Services Total					\$ 19,519.00
McDonogh 28 ES Food Services	SCNZ Architects, LLC	FEMA	\$ 20,519.00	\$ -	\$ 20,519.00
McDonogh 28 ES Food Services Total					\$ 20,519.00
Henry Allen ES Food Services	N-Y Associates, Inc.	FEMA	\$ 10,983.00	\$ -	\$ 10,983.00
Henry Allen ES Food Services Total					\$ 10,983.00
Sarah T. Reed HS Food Services	N-Y Associates, Inc.	FEMA	\$ 13,985.00	\$ -	\$ 13,985.00
Sarah T. Reed HS Food Services Total					\$ 13,985.00
Albert Wicker ES Food Services	SCNZ Architects, LLC	FEMA	\$ 26,529.00	\$ -	\$ 26,529.00
Albert Wicker ES Food Services Total					\$ 26,529.00
Frederick A Douglass HS New Science Lab	VergesRome Architects, APAC	FEMA	\$ -	\$ 37,754.00	\$ 37,754.00
Frederick A Douglass HS New Science Lab Total					\$ 37,754.00



BESE MONTHLY REPORT
OPEN CONTRACTS as of 09/09/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
STABILIZATIONS					
Andrew J Bell Roof Replacement	VergesRome Architects, APAC	FEMA	\$ -	\$ 124,357.00	\$ 124,357.00
	Crescent Commercial Construction	FEMA	\$ 1,264,000.00	\$ 267,131.35	\$ 1,531,131.35
Andrew J Bell Roof Replacement Total					\$ 1,655,488.35
John McDonogh HS - Bleachers	Trapolin-Peer Architects, APC	Insurance Proceeds	\$ 11,822.50	\$ (2,740.16)	\$ 9,082.34
	One Construction, LLC	Insurance Proceeds	\$ 68,656.00	\$ 10,100.45	\$ 78,756.45
John McDonogh HS - Bleachers Total					\$ 87,838.79
Carbon Credit - AD Crossman (aka Esperanza Charter)	W.L. Wyman Construction Company, Inc	Harrah's	\$ 199,850.00	\$ 13,615.94	\$ 213,465.94
Carbon Credit - AD Crossman (aka Esperanza Charter) Total					\$ 213,465.94
Carbon Credit - Banneker ES	W.L. Wyman Construction Company, Inc	Harrah's	\$ 143,350.00	\$ 34,800.04	\$ 178,150.04
Carbon Credit - Banneker ES Total					\$ 178,150.04
Walter L Cohen HS - HVAC Repairs	Infinity Engineering Consultants, LLC	FEMA	\$ 95,420.00	\$ (40,498.00)	\$ 54,922.00
Walter L Cohen HS - HVAC Repairs Total					\$ 54,922.00
John McDonogh HS - Gymnasium Sprinkler	Fanning/Howie Associates, Inc.	Insurance Proceeds	\$ 12,605.00	\$ 6,303.00	\$ 18,908.00
	Coastal Fire Protection, LLC	Insurance Proceeds	\$ 175,912.00	\$ (5,400.12)	\$ 170,511.88
John McDonogh HS - Gymnasium Sprinkler Total					\$ 189,419.88
MOTHBALLING					
Andrew J Bell Shoring Main Classroom Building	VergesRome Architects, APAC	FEMA	\$ -	\$ 106,095.00	\$ 106,095.00
	Aby Brothers, Inc.	FEMA	\$ 910,000.00	\$ 1,043,425.00	\$ 1,953,425.00
Andrew J Bell Shoring Main Classroom Building Total					\$ 2,059,520.00
Andrew J Bell Safe & Secure - Mothballing	VergesRome Architects, APAC	FEMA	\$ 92,568.00	\$ 112,194.00	\$ 204,762.00
	C.D.W. Services, LLC	FEMA	\$ 2,058,000.00	\$ 443,888.90	\$ 2,501,888.90
Andrew J Bell Safe & Secure - Mothballing Total					\$ 2,706,650.90
George Mondy ES Mothballing	VergesRome Architects, APAC	FEMA	\$ 26,023.00	\$ 40,056.00	\$ 66,079.00
George Mondy ES Mothballing Total					\$ 66,079.00
BUILDING AUTOMATION SYSTEM					
Building Automation System - Banneker	Synergy Building Solutions	FEMA		\$ 11,674.18	\$ 11,674.18
Building Automation System - Banneker Total					\$ 11,674.18
Building Automation System - Bienville	Moses Engineers, Inc.	FEMA	\$ -	\$ 2,275.16	\$ 2,275.16
	Synergy Building Solutions	FEMA	\$ 18,238.90	\$ -	\$ 18,238.90
Building Automation System - Bienville Total					\$ 20,514.06
Building Automation System - Colton	Moses Engineers, Inc.	FEMA	\$ -	\$ 3,633.41	\$ 3,633.41
	Synergy Building Solutions	FEMA	\$ 29,127.41	\$ -	\$ 29,127.41
Building Automation System - Colton Total					\$ 32,760.82
Building Automation System - Craig ES	Moses Engineers, Inc.	FEMA	\$ 10,873.76	\$ 2,370.11	\$ 13,243.87
	Synergy Building Solutions	FEMA	\$ 56,716.33	\$ 7,701.50	\$ 64,417.83
Building Automation System - Craig ES Total					\$ 77,661.70
Building Automation System - Crocker	Moses Engineers, Inc.	FEMA	\$ -	\$ 2,060.12	\$ 2,060.12
	Synergy Building Solutions	FEMA	\$ 16,515.03	\$ -	\$ 16,515.03
Building Automation System - Crocker Total					\$ 18,575.15
Building Automation System - FC Williams	Moses Engineers, Inc.	FEMA	\$ -	\$ 2,185.10	\$ 2,185.10
	Synergy Building Solutions	FEMA	\$ 17,516.91	\$ -	\$ 17,516.91
Building Automation System - FC Williams Total					\$ 19,702.01
Building Automation System - Frantz	Moses Engineers, Inc.	FEMA	\$ -	\$ 2,181.43	\$ 2,181.43
	Synergy Building Solutions	FEMA	\$ 17,487.49	\$ -	\$ 17,487.49
Building Automation System - Frantz Total					\$ 19,668.92
Building Automation System - L.B. Landry HS	Moses Engineers, Inc.	FEMA	\$ 10,873.76	\$ 1,555.96	\$ 12,429.72
	Synergy Building Solutions	FEMA	\$ 50,189.62	\$ -	\$ 50,189.62
Building Automation System - L.B. Landry HS Total					\$ 62,619.34
Building Automation System - Lake Area HS	Moses Engineers, Inc.	FEMA	\$ 10,873.76	\$ 1,397.88	\$ 12,271.64
	Synergy Building Solutions	FEMA	\$ 48,450.83	\$ 2,720.00	\$ 51,170.83
Building Automation System - Lake Area HS Total					\$ 63,442.47
Building Automation System - Langston Hughes ES	Moses Engineers, Inc.	FEMA	\$ 10,873.76	\$ 890.53	\$ 11,764.29
	Synergy Building Solutions	FEMA	\$ 44,855.18	\$ -	\$ 44,855.18
Building Automation System - Langston Hughes ES Total					\$ 56,619.47
Building Automation System - Osborne	Moses Engineers, Inc.	FEMA	\$ -	\$ 2,232.89	\$ 2,232.89
	Synergy Building Solutions	FEMA	\$ 17,900.05	\$ -	\$ 17,900.05
Building Automation System - Osborne Total					\$ 20,132.94



BESE MONTHLY REPORT
OPEN CONTRACTS as of 09/09/14

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
Building Automation System - Parkview	Moses Engineers, Inc.	FEMA	\$ -	\$ 2,378.08	\$ 2,378.08
	Synergy Building Solutions	FEMA	\$ 19,063.99	\$ -	\$ 19,063.99
Building Automation System - Parkview Total					\$ 21,442.07
Building Automation System - Sarah T Reed	Synergy Building Solutions	FEMA	\$ -	\$ 12,587.80	\$ 12,587.80
Building Automation System - Sarah T Reed Total					\$ 12,587.80
Building Automation System - Sylvania Williams	Synergy Building Solutions	FEMA	\$ -	\$ 11,635.21	\$ 11,635.21
Building Automation System - Sylvania Williams Total					\$ 11,635.21
Building Automation System - Wilson ES	Moses Engineers, Inc.	FEMA	\$ 10,873.76	\$ 903.44	\$ 11,777.20
	Synergy Building Solutions	FEMA	\$ 44,958.72	\$ 8,261.50	\$ 53,220.22
Building Automation System - Wilson ES Total					\$ 64,997.42
Building Automation System - Woodson	Moses Engineers, Inc.	FEMA	\$ -	\$ 2,164.90	\$ 2,164.90
	Synergy Building Solutions	FEMA	\$ 17,355.04	\$ -	\$ 17,355.04
Building Automation System - Woodson Total					\$ 19,519.94
Building Automation System - AD Crossman	Synergy Building Solutions	FEMA		\$ 12,490.68	\$ 12,490.68
Building Automation System - AD Crossman Total					\$ 12,490.68
Building Automation System - Cohen	Synergy Building Solutions	FEMA		\$ 13,252.58	\$ 13,252.58
Building Automation System - Little Woods Total					\$ 24,064.90
Building Automation System - Wicker	Synergy Building Solutions	FEMA		\$ 13,273.32	\$ 13,273.32
Building Automation System - Wicker Total					\$ 13,273.32
OTHER PROFESSIONAL SERVICES					
PM/CM	Jacobs Project Management Company/CSRS Consortium	FEMA	\$ 23,590,758.00	\$ 1,069,673.31	\$ 24,660,431.31
PM/CM Total					\$ 24,660,431.31
Consulting Services - Building Commissioning	GCE Services	Insurance Proceeds	\$ 50,000.00	\$ -	\$ 50,000.00
Consulting Services - Building Commissioning Total					\$ 50,000.00
Wilson ES Warrantly Oversight	HMS Architects, APC	Insurance Proceeds	\$ 50,000.00	\$ -	\$ 50,000.00
Wilson ES Warrantly Oversight Total					\$ 50,000.00

GRAND TOTAL \$ 570,689,139.56

OPSB OPEN CONTRACTS
as of
09/09/2014



PROJECT	CONTRACTOR/ARCHITECT	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
CONSTRUCTION/RENOVATION				
Hynes Elementary Construction	Farnsworth Group, Inc	\$ 200,308.00	\$ -	\$ 200,308.00
	Woodrow Wilson Construction	\$ 21,108,000.00	\$ 570,066.90	\$ 21,678,066.90
Hynes Elementary Construction Total				\$ 21,878,374.90
New McDonogh 35 High School (Phillips Waters Site)	Sizeler Thompson Brown Architects Project Design Group, LLC	\$ 3,279,219.00	\$ 1,193,198.16	\$ 4,472,417.16
	Farnsworth Group, Inc	\$ 321,880.00	\$ 6,620.00	\$ 328,500.00
	Citadel Builders, LLC	\$ 54,984,000.00	\$ 711,569.79	\$ 55,695,569.79
New McDonogh 35 High School (Phillips Waters Site) Total				\$ 60,496,486.95
New McDonogh 35 High School (Phillips Waters Site) Site Remediation	Sizeler Thompson Brown Architects Project Design Group, LLC	\$ -	\$ 1,214,042.65	\$ 1,214,042.65
New McDonogh 35 High School (Phillips Waters Site) Site Remediation Total				\$ 1,214,042.65
Audubon School Reno/Addition	Blitch Knevel Architects	\$ 995,406.90	\$ 513,560.90	\$ 1,508,967.80
	Farnsworth Group, Inc	\$ 162,212.00	\$ -	\$ 162,212.00
	FHP Technics Corporation	\$ 12,415,000.00	\$ 261,076.10	\$ 12,676,076.10
Audubon School Reno/Addition Total				\$ 14,347,255.90
Audubon School Reno/Addition Interpretive Display	Bright Moments, LLC	\$ 4,125.00	\$ -	\$ 4,125.00
Audubon School Reno/Addition Interpretive Display Total				\$ 4,125.00
Alice Harte Elementary	WDG Architects Engineers	\$ 1,513,534.00	\$ 500,261.03	\$ 2,013,795.03
	Farnsworth Group, Inc	\$ 222,742.00	\$ -	\$ 222,742.00
	Woodrow Wilson Construction	\$ 18,229,554.00	\$ -	\$ 18,229,554.00
		\$ 8,490,446.00	\$ 60,663.50	\$ 8,551,109.50
Alice Harte Elementary Total				\$ 29,017,200.53
McMain New Gym & Covered Walkway	Jahncke & Burns Architects, LLC	\$ 972,951.50	\$ (142,995.12)	\$ 829,956.38
	Farnsworth Group, Inc	\$ -	\$ 110,156.00	\$ 110,156.00
	Ellis Construction, Inc.	\$ 9,497,800.00	\$ 935,750.56	\$ 10,433,550.56
McMain New Gym & Covered Walkway Total				\$ 11,373,662.94
McMain Health Clinic Renovation	Jahncke & Burns Architects, LLC	\$ -	\$ 92,101.57	\$ 92,101.57
McMain Health Clinic Renovation Total				\$ 92,101.57
McMain Exterior Stabilization	Jahncke & Burns Architects, LLC	\$ -	\$ 969,119.38	\$ 969,119.38
McMain Exterior Stabilization Total				\$ 969,119.38
New PK-8 at Kenilworth Park (Curran Site)	Mathes Brierre Architects	\$ 1,587,671.03	\$ 149,364.00	\$ 1,737,035.03
	Farnsworth Group, Inc	\$ -	\$ 254,729.75	\$ 254,729.75
	Woodrow Wilson Construction	\$ 22,476,000.00	\$ 35,946.05	\$ 22,511,946.05
New PK-8 at Kenilworth Park (Curran Site) Total				\$ 24,503,710.83
New Lake Forest School @ Greater St Stephens Site	Imre Hegedus & Associated Architects	\$ 1,382,303.00	\$ 875,288.50	\$ 2,257,591.50
	Farnsworth Group, Inc	\$ 264,670.51	\$ -	\$ 264,670.51
	The McDonnell Group, LLC	\$ 34,075,000.00	\$ 63,094.00	\$ 34,138,094.00
New Lake Forest School @ Greater St Stephens Site Total				\$ 36,660,356.01
Nelson Elementary School Refurbishment	Harry Baker Smith II, PLLC	\$ 173,888.00	\$ 2,420.00	\$ 176,308.00
Nelson Elementary School Refurbishment Total				\$ 176,308.00
New Karr HS @ Jo Ellen Smith Site	Trapolin-Peer Architects, APC-VMDO Architects, PC Joint Venture	\$ 442,849.32	\$ -	\$ 442,849.32
	Affiliated Engineers SE, Inc	\$ 349,100.00	\$ -	\$ 349,100.00
New Karr HS @ Jo Ellen Smith Site Total				\$ 791,949.32

OPSB OPEN CONTRACTS
as of
09/09/2014



PROJECT	CONTRACTOR/ARCHITECT	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
STABILIZATIONS - VARIOUS				
McDonogh 7 Dumpster Pad & Fence Install	GCA Education Services	\$ 29,500.00	\$ 6,690.00	\$ 36,190.00
McDonogh 7 Dumpster Pad & Fence Install Total				\$ 36,190.00
McDonogh 7 LBP Remediation	Hamp's Construction, LLC	\$ 309,400.00	\$ 6,903.78	\$ 316,303.78
McDonogh 7 LBP Remediation Total				\$ 316,303.78
McDonogh 7 Modular Buildings	M Space Holdings, LLC	\$ 260,491.96	\$ -	\$ 260,491.96
McDonogh 7 Modular Buildings Total				\$ 260,491.96
Village de l'Est Modular Buildings	M Space Holdings, LLC	\$ 539,644.06	\$ 182,748.35	\$ 722,392.41
Village de l'Est Modular Buildings Total				\$ 722,392.41
McDonogh 7 Security System	Sonitrol	\$ 21,126.00	\$ 7,301.00	\$ 28,427.00
McDonogh 7 Security System Total				\$ 28,427.00
Lusher Elementary School	Meyer Engineers, LTD	\$ 139,948.00	\$ 36,300.00	\$ 176,248.00
Lusher Elementary School Total				\$ 176,248.00
McDonogh 35 HS Stabilization	Chenevert Architects, LLC	\$ 32,372.00	\$ 23,676.20	\$ 56,048.20
	Tuna Construction, LLC	\$ 352,000.00	\$ 103,183.16	\$ 455,183.16
McDonogh 35 HS Stabilization Total				\$ 511,231.36
Warren Easton HS Stabilization	Chenevert Architects, LLC	\$ 32,372.00	\$ 208,862.94	\$ 241,234.94
	Tuna Construction, LLC	\$ 2,407,000.00	\$ -	\$ 2,407,000.00
Warren Easton HS Stabilization Total				\$ 2,648,234.94
Audubon Charter School (Extension ES & MS) Stabilization	Chenevert Architects, LLC	\$ 32,372.00	\$ 510.53	\$ 32,882.53
Audubon Charter School (Extension ES & MS) Stabilization Total				\$ 32,882.53
Lusher (Fortier) High School Refurbishment	SCNZ Architects, LLC	\$ 1,057,864.00	\$ 128,863.80	\$ 1,186,727.80
	CORE Construction Services, LLC	\$ 14,552,000.00	\$ -	\$ 14,552,000.00
Lusher (Fortier) High School Refurbishment Total				\$ 15,738,727.80
Edna Karr HS - Gymnasium Repair	Chenevert Architects, LLC	\$ 32,372.00	\$ 43,517.98	\$ 75,889.98
	Crescent Commercial Construction	\$ 293,000.00	\$ 113,093.63	\$ 406,093.63
Edna Karr HS - Gymnasium Repair Total				\$ 481,983.61
Timbers III HVAC Repairs	Moses Engineers, Inc.	\$ 114,928.00	\$ (14,338.00)	\$ 100,590.00
Timbers III HVAC Repairs Total				\$ 100,590.00
McDonogh 7 ES Stabilization	Perez, APC	\$ 106,429.00	\$ -	\$ 106,429.00
McDonogh 7 ES Stabilization Total				\$ 106,429.00
McDonogh 7 ES Stabilization - Asphalt	Fleming Construction Company, LLC	\$ 197,000.00	\$ -	\$ 197,000.00
McDonogh 7 ES Stabilization - Asphalt Total				\$ 197,000.00
Timbers III - IT Room Relocation	N-Y Associates, Inc	\$ 4,519.00	\$ -	\$ 4,519.00
Timbers III - IT Room Relocation Total				\$ 4,519.00
Timbers III - Building Controls	N-Y Associates, Inc	\$ 3,832.00	\$ -	\$ 3,832.00
Timbers III - Building Controls Total				\$ 3,832.00
Ben Franklin ES Renovation	N-Y Associates, Inc	\$ 186,264.00	\$ -	\$ 186,264.00
Ben Franklin ES Renovation Total				\$ 186,264.00
OTHER PROFESSIONAL SERVICES				
Program Management/Construction Management	Jacobs Project Management Company/CSRS Consortium	\$ 8,050,817.00	\$ -	\$ 8,050,817.00
			GRAND TOTAL	\$ 231,127,258.37

Department of Education
BID TABULATION SHEET

Bid Date: August 13, 2014

Project Name: Relocation of Playground Equipment at Mildred C. Osborne School and Little Woods Elementary School (Dolores T. Aaron School) Designer: Mahlum Scairono Martinez
3642 Magazine Street
New Orleans, LA 70115

Project No.: 2009-0737-0004 Part No.: _____ Site Code: _____ State ID: _____ DOE Project Manager: Jacobs/CSRS Program Management
2009-0752-0003

BIDDER	Lic. No.	Addenda	Bond	Base Bid	Remarks
Clay Construction	57313	✓	✓	\$169,000.00	
Hamp's Construction	31943	✓	✓	\$213,500.00	
Crescent City Rebuild	56117	✓	✓	\$146,237.00	

A TRUE COPY

Signed: _____ Date: _____ Signed: _____ Date: _____
Designer Department of Education Representative
 A.F.C.: \$150,000.00 Construction Time: 60 consecutive calendar in days Liquidated Damages: \$175.00 per day

BID RECOMMENDATIONS: (Department of Education Use Only.)

USER: Reject Award: Base Bid Alt #1 Alt #2 Alt #3 Letter attached dated: _____

DESIGNER: Reject Award: Base Bid Alt #1 Alt #2 Alt #3 Letter attached dated: _____

PROJECT MGR: Reject Award: Base Bid Alt #1 Alt #2 Alt #3 Signed: _____ Date: _____

COMMENTS: _____

_____ DOE Purchasing Director _____ Date: _____

Department of Education
BID TABULATION SHEET

Bid Date: August 13, 2014

Project Name: Harriet R. Tubman Elementary School Investigative Demolition
2013 General Meyer Avenue
New Orleans, LA 70127

Designer: Mahlum | Scairono Martinez Joint Venture
3642 Magazine Street
New Orleans, LA 70115

Project No.: 2012-0519-0002 Part No.: _____ Site Code: _____ State ID: _____ DOE Project Manager: Jacobs/CSRS Program Management

BIDDER	Lic. No.	Addenda	Bond	Base Bid	Alt. No.1	Remarks
<u>Insulation Technologies</u>	<u>18938</u>	<u>1</u>	<u>✓</u>	<u>\$268,000.00</u>		
<u>CDW Services</u>	<u>45228</u>	<u>1</u>	<u>✓</u>	<u>\$314,900.00</u>		
<u>Bayou General</u>	<u>29774</u>	<u>1</u>	<u>✓</u>	<u>\$275,000.00</u>		
<u>Crescent Commercial</u>	<u>49154</u>	<u>1</u>	<u>✓</u>	<u>\$389,000.00</u>		
<u>Perez APC</u>	<u>52633</u>	<u>1</u>	<u>✓</u>	<u>\$279,800.00</u>		
<u>Commander Corp.</u>	<u>13278</u>	<u>1</u>	<u>✓</u>	<u>\$347,000.00</u>		
<u>Hamp's Construction</u>	<u>31943</u>	<u>1</u>	<u>✓</u>	<u>\$283,100.00</u>		
<u>Zimmer-Eschette</u>	<u>56786</u>	<u>1</u>	<u>✓</u>	<u>\$298,700.00</u>		
<u>Construction Management</u>	<u>56068</u>	<u>1</u>	<u>✓</u>	<u>\$218,135.00</u>		

A TRUE COPY

Signed: _____ Date: _____ Signed: _____ Date: _____

Designer

Department of Education Representative

A.F.C.: \$577,343.72

Construction Time **60 consecutive calendar** in days

Liquidated Damages: **\$250.00** per day

BID RECOMMENDATIONS: (Department of Education Use Only.)

USER: Reject Award: Base Bid Alt #1 Alt #2 Alt #3 Letter attached dated: _____

DESIGNER: Reject Award: Base Bid Alt #1 Alt #2 Alt #3 Letter attached dated: _____

PROJECT MGR: Reject Award: Base Bid Alt #1 Alt #2 Alt #3 Signed: _____ Date: _____

COMMENTS: _____

_____ DOE Purchasing Director _____ Date: _____
