




Superintendent's Report April 2018



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Ms. Kunjan Narechania
Recovery School District



Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	10
Benjamin Franklin Elementary School Renovation ^(OPSB)	10
Career Technical Education High School at Kerlerec Street CMaR ^(RSD)	10
New Karr High School, CMAR ^(RSD)	10
New Orleans Charter Science and Mathematics High School ^(OPSB)	11
John McDonogh High School Renovation CMAR ^(RSD)	11
Harriet R. Tubman Elementary School Renovation ^(RSD)	11
Booker T. Washington School CMAR ^(RSD)	12
REFURBISHMENTS	13
Harney Elementary School Downspout and Gutter Repairs ^(RSD)	13
Harney Elementary School Interior Lighting ^(RSD)	13
Lafayette Elementary School Refurbishment ^(RSD)	13
Thurgood Marshall Elementary School Refurbishment ^(RSD)	14
McDonogh #28 School Flooring Refurbishment ^(RSD)	14
McDonogh #32 School Refurbishment ^(RSD)	14
McDonogh #32 School Refurbishment ^(RSD)	15
Eleanor McMMain School Envelope Repairs ^(OPSB)	15
Harriet R. Tubman Elementary School Cottage Renovation ^(RSD)	15
Schaumburg Elementary School Roof Repairs ^(RSD)	16
Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing ^(RSD)	16
Sophie B. Wright High School - Phase 2 Interior Painting and Wood Flooring Repairs ^(RSD)	16
DEMOLITIONS	17
Demolition of Modulares at Abramson 3 ^(RSD)	17
Demolition of Modulares at Coghill ^(RSD)	17
COMPLETED PROJECTS	18

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$308 million in open contracts for the capital program after issuing \$823 thousand in new contracts, change orders and amendments in April. In addition, the total change orders to date, \$6 million, account for two percent (2.43%) of the total open construction contracts. RSD anticipates issuing \$904 thousand in construction contracts/change orders, and \$28 thousand in professional service contracts/amendments in May.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$176 million in open contracts for the capital program after issuing \$0 in new contracts, change orders and amendments in April. In addition, the total change orders to date, \$7.1 million, account for approximately five percent (5.07%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 thousand in construction contracts/change orders and \$0 thousand in professional service contracts and amendments in May.

Community Meetings



Future Community Meetings

Bid Openings

Projects which are scheduled to bid in the next 60 days

May 9, 2018

McMain Envelope Repairs Bid Opening

May 23, 2018

McDonogh #42 Drainage Bid Opening

May 23, 2018

New Orleans Charter Science & Mathematics High School Bid Opening

Disadvantaged Business Enterprises (DBE) Monthly Summary



Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of April 30, 2018. The DBE subcontracts value is \$82,153,443 of the \$362,866,202 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 54 projects as of April 30, 2018. The DBE subcontracts value is \$23,174,027 of the \$73,075,270 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of April 30, 2018. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 2 projects as of April 30, 2018. The DBE subcontracts value is \$29,865,002 of the \$86,846,352 total of awarded contracts.

Total Amount of Contracts: \$ 632,202,381

Orleans Parish School Board



New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of April 30, 2018. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of April 30, 2018. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$231,354,830

* DBE provisions were included in projects bid after June 30, 2012

Disadvantaged Business Enterprises (DBE) Monthly Summary



Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 24 projects as of April 30, 2018. The DBE subcontracts value is \$82,450,426 of the \$362,866,202 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 54 projects as of April 30, 2018. The DBE subcontracts value is \$23,477,913 of the \$74,626,158 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of April 30, 2018. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 2 projects as of April 30, 2018. The DBE subcontracts value is \$29,865,002 of the \$86,846,352 total of awarded contracts.

Total Amount of Contracts: \$ 632,202,381

Orleans Parish School Board



New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of April 30, 2018. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of April 30, 2018. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$231,354,830

* DBE provisions were included in projects bid after June 30, 2012


Current RSD Program DBE Participation

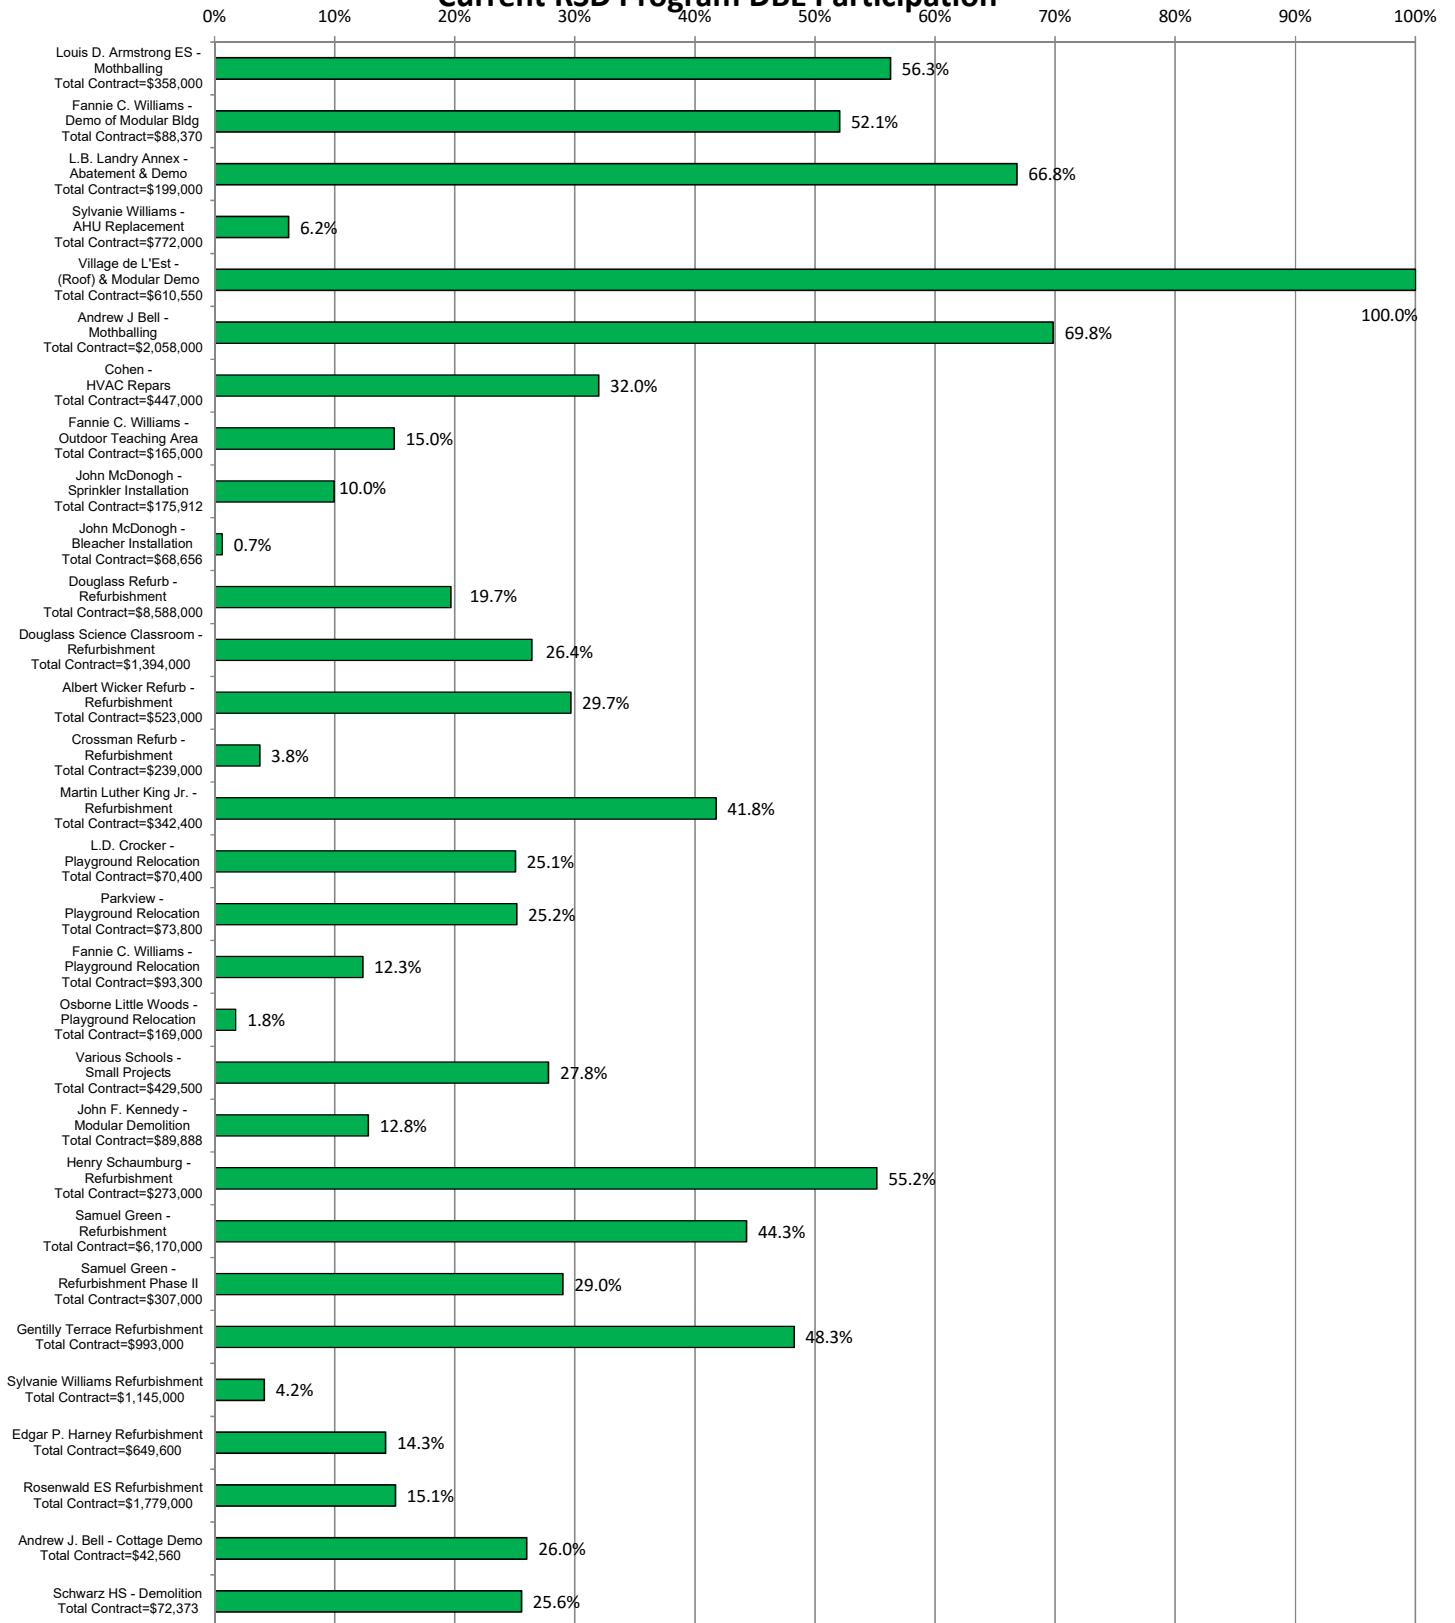

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

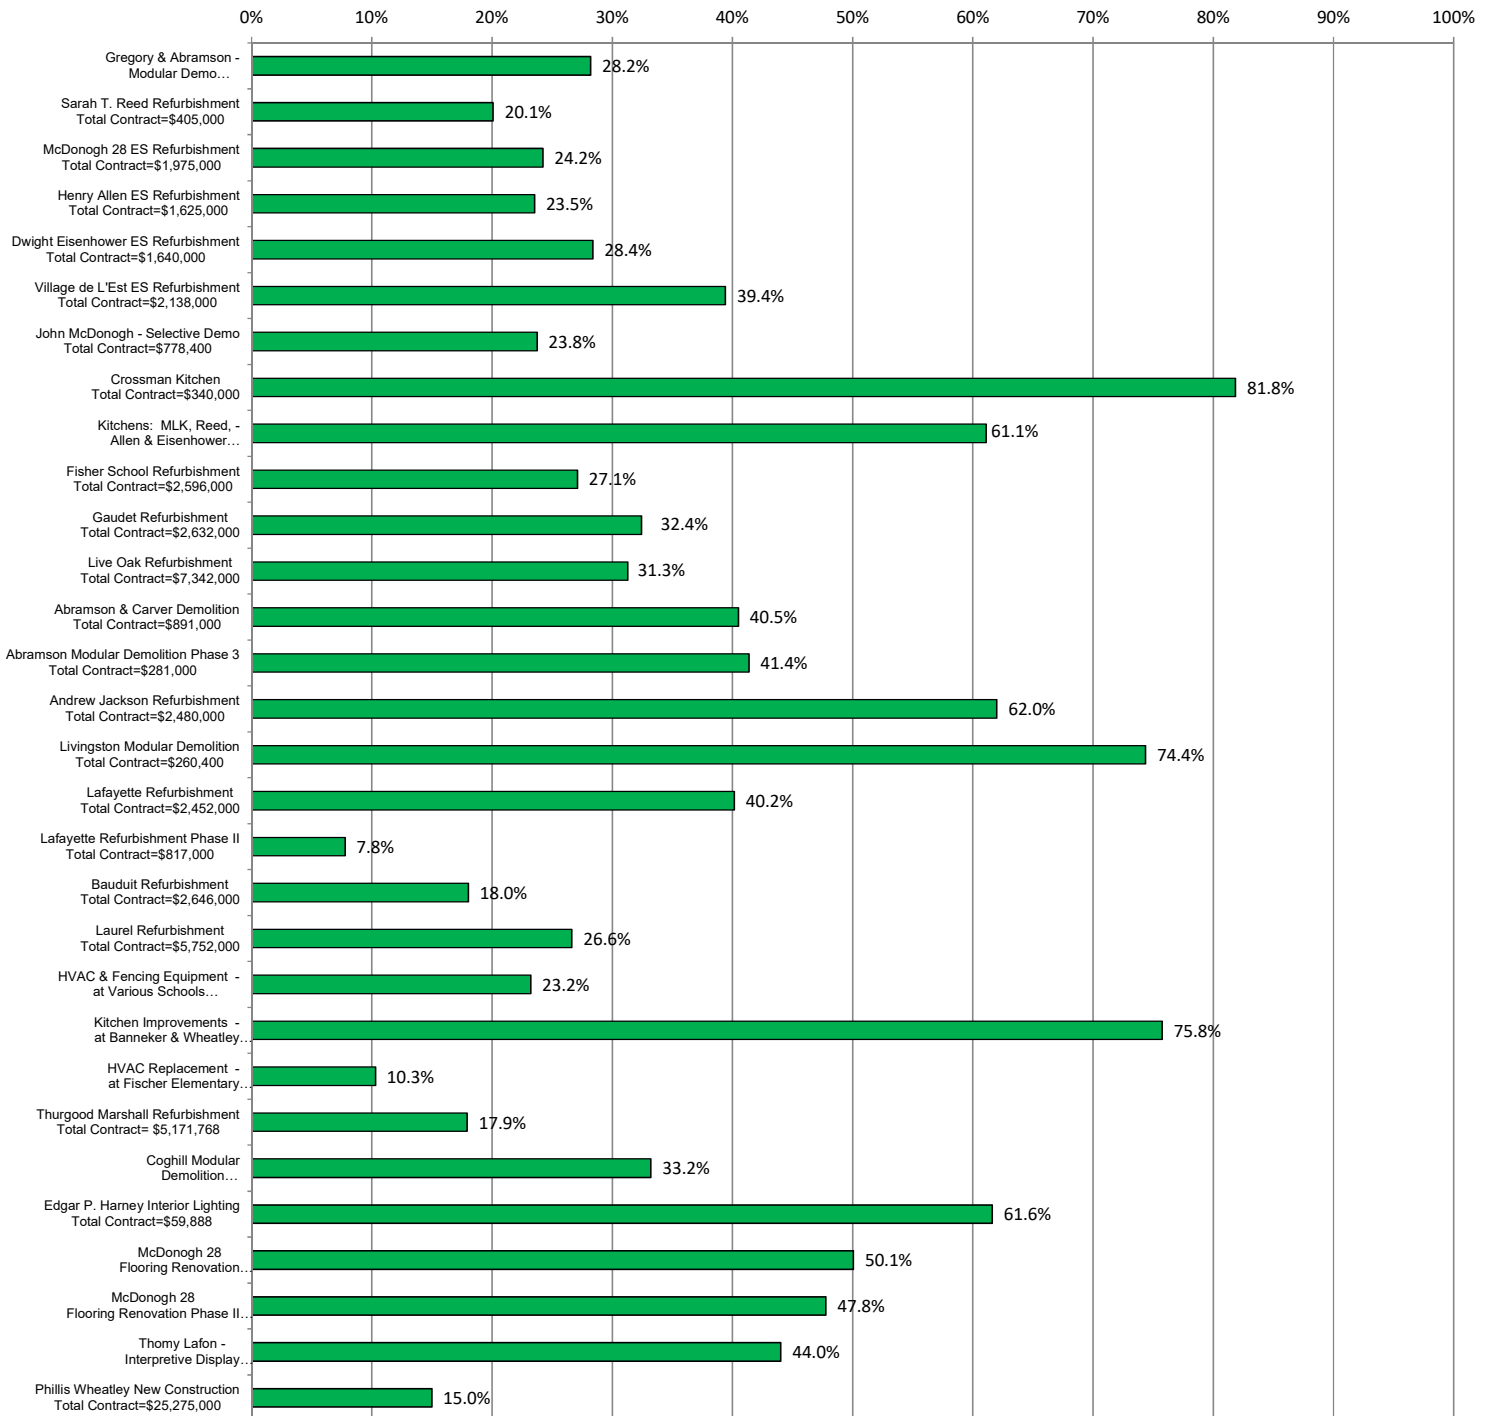


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current RSD Program DBE Participation (Continued)

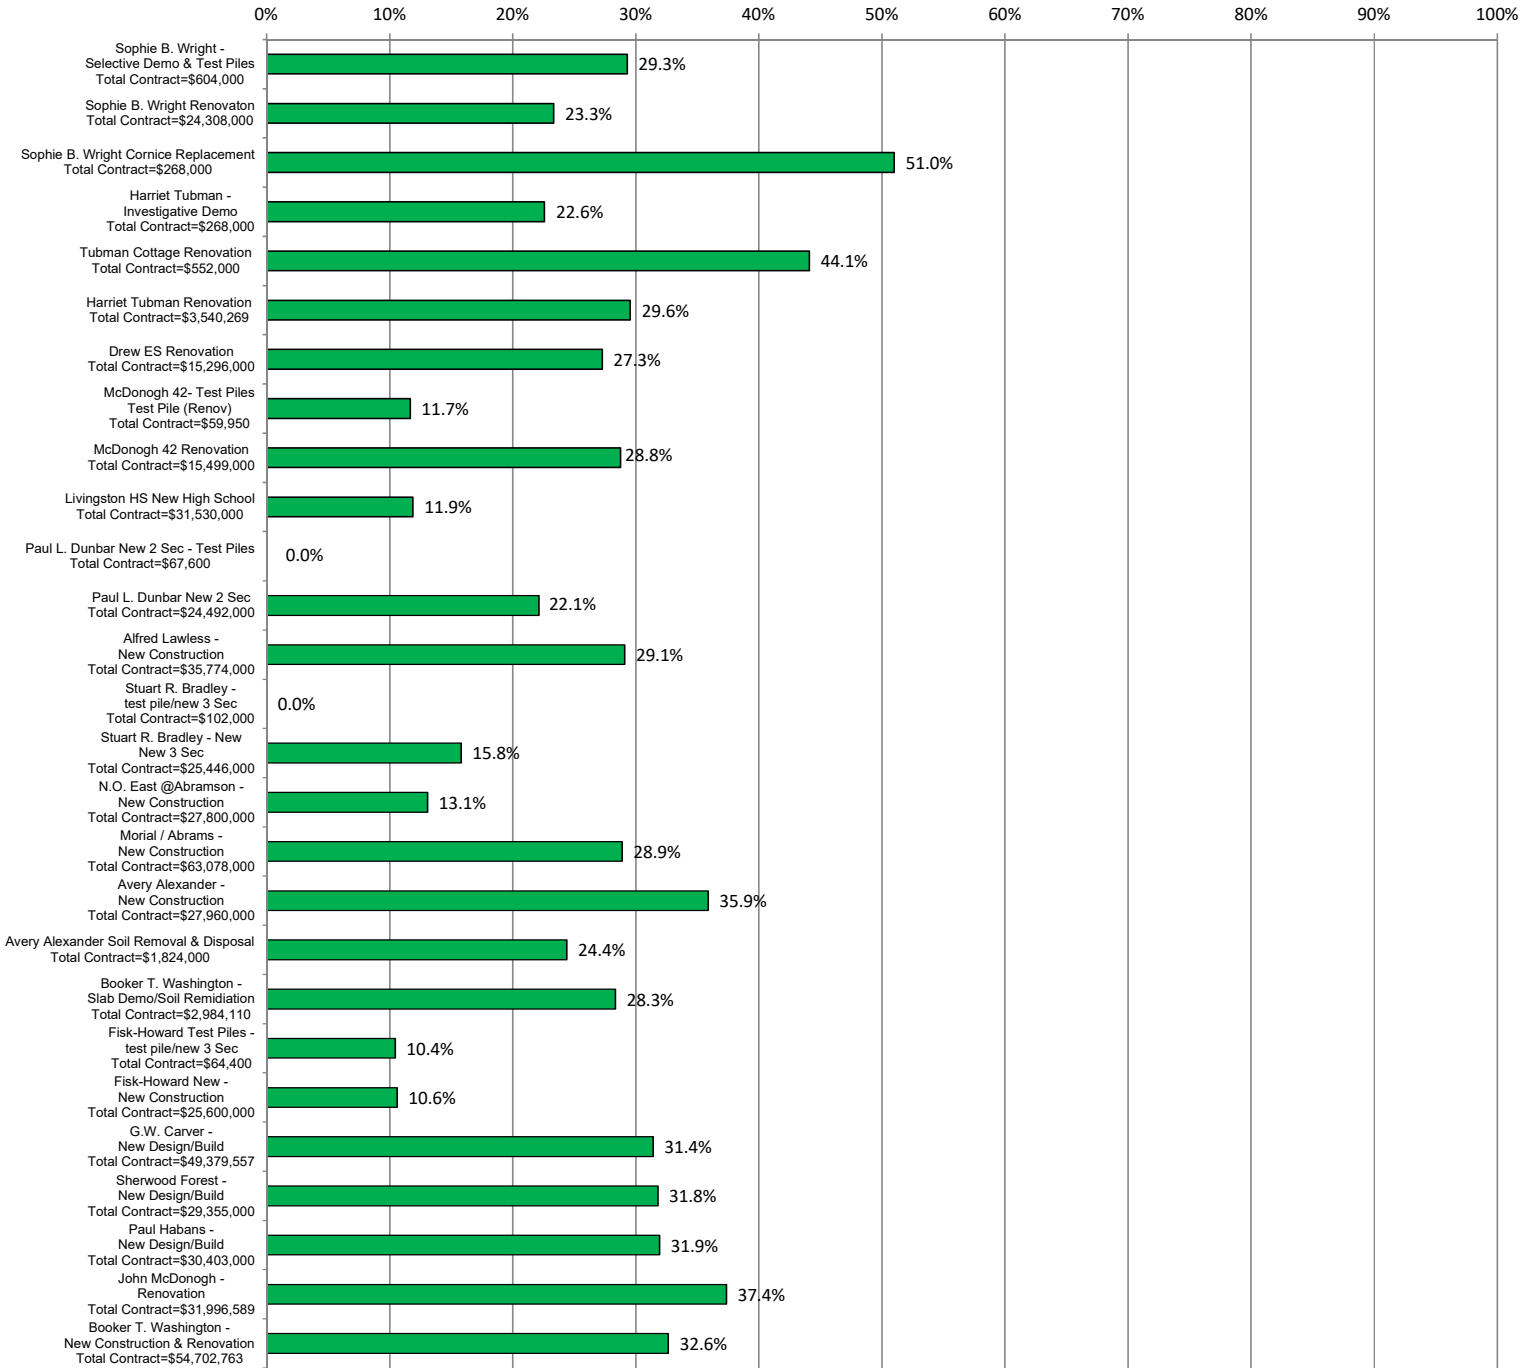

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

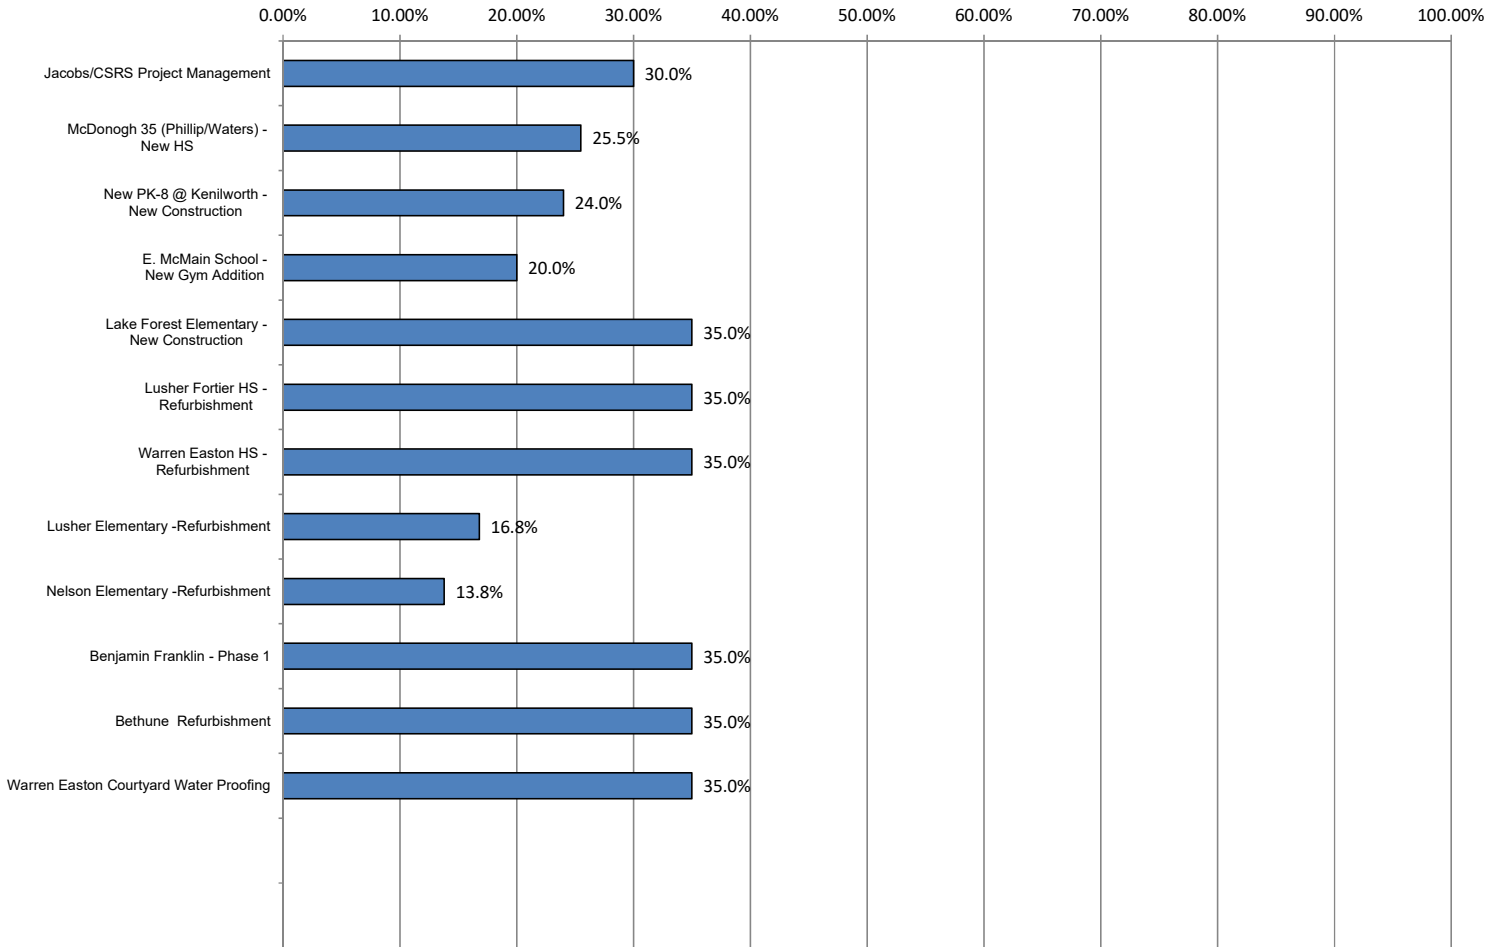

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Construction Masters

Construction Phase

- Phase 2 - 50% Construction Documents are due June 26th
- Demolition is ongoing

Contractual Substantial Completion Phase 1 – August 2018

Forecasted Substantial Completion Phase 1 – August 2018



Career Technical Education High School at Kerlerec Street CMAR ^(RSD)

1331 Kerlerec Street, New Orleans, LA 70116 District D Ward 7

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Program Phase

- Program Completion is due May 27th

New Karr High School CMAR ^(RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - Core Construction

Construction Phase

- River height is impacting the work schedule
- Above ground site demolition is finishing up
- Resteel fabrication to start in May 2018

Contractual Substantial Completion – Summer 2020

Forecasted Substantial Completion – Summer 2020



New Orleans Charter Science and Mathematics High School (OPSB)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement - April 4th
- 2nd Advertisement - April 11th
- 3rd Advertisement - April 18th
- Pre-Bid Conference - April 19th
- Bid Opening - May 23rd



John McDonogh High School Renovation CMAR (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- Installation of wood flooring continues on 2nd and 3rd floor corridors
- Site civil work is ongoing at N. Rocheblave and Barracks Street
- Flooring installation on 1st floor has started
- Exterior face brick and metal roofing has started at gymnasium

Contractual Substantial Completion – October 2018

Forecasted Substantial Completion – October 2018



Harriet R. Tubman Elementary School Renovation (RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

Construction Phase

- Wood floor refinishing continues on 2nd floor
- Windows are being installed on the west side
- HVAC is being connected
- VCT flooring installation is underway on 1st and 2nd floors

Contractual Substantial Completion – July 2018

Forecasted Substantial Completion – July 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Contractor emphasis is on closing the building envelope
- Majority of the roofing work is complete
- Sprinkler work continues
- Steel structure stabilization on the auditorium continues

Contractual Substantial Completion – January 2019

Forecasted Substantial Completion – January 2019



REFURBISHMENTS

Harney Elementary School Downspout and Gutter Repairs ^(RSD)

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of downspouts and gutters

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - Crescent Commercial

Construction Phase

- Preconstruction meeting May 22nd
- Notice to Proceed May 25th

Contractual Substantial Completion – September 2018

Forecasted Substantial Completion – September 2018



Harney Elementary School Interior Lighting ^(RSD)

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement interior lighting

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - Jack's Electric

Construction Phase

- Preconstruction meeting May 21st
- Notice to Proceed May 25th

Contractual Substantial Completion – September 2018

Forecasted Substantial Completion – September 2018



Lafayette Elementary School Refurbishment Phase 2 ^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to floor replacement

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Law Industries

Construction Phase

- Preconstruction meeting May 15th
- Notice to Proceed May 23rd

Contractual Substantial Completion – August 2018

Forecasted Substantial Completion – August 2018



Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Blanchard Mechanical Contractors

Construction Phase

- Window installation is nearing completion
- Installation of exterior sheathing on elevator is ongoing
- Exterior tuck pointing continues
- Interior painting continues

Contractual Substantial Completion – June 2018

Forecasted Substantial Completion – June 2018



McDonogh #28 School Flooring Refurbishment Phase 2 ^(RSD)

2733 Esplanade Boulevard, New Orleans, LA 70114 District A Ward 7

Scope of work: Refurbishment of existing elementary school flooring

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Insul-Tech

Construction Phase

- Preconstruction meeting May 15th
- Notice to Proceed May 25th

Contractual Substantial Completion – July 2018

Forecasted Substantial Completion – July 2018



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – HMS Architects

Contractor - TBD

Design Phase

- Owner has place project on hold



McDonogh #42 School Drainage ^(RSD)

1651 North Tonti Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Site Drainage

Funding Source – Insurance

Architect – Eskew+Dumez+Ripple

Contractor - TBD

Procurement Phase

- 1st Advertisement - April 18th
- 2nd Advertisement - April 25th
- 3rd Advertisement - May 2nd
- Pre-Bid Conference - May 3rd
- Bid Opening - May 23rd



Eleanor McMain School Envelope Repairs ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Exterior stucco and window repairs

Funding Source – General Fund & Harrah's

Architect – Concordia, LLC

Contractor – TBD

Procurement Phase

- 1st Advertisement - April 4th
- 2nd Advertisement - April 11th
- 3rd Advertisement - April 18th
- Pre-Bid Conference - April 19th
- Bid Opening - May 9th



Harriet R. Tubman Elementary School Cottage Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing cottage to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Installation of siding is ongoing
- Window and door installation continues
- MEP installation in progress

Contractual Substantial Completion – June 2018

Forecasted Substantial Completion – June 2018



Schaumburg Elementary School Roof Repairs ^(RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - Laperouse Metal Works, Inc

Construction Phase

- Fence installation will begin in May
- Metal roof submittals are being processed

Contractual Substantial Completion – August 2018

Forecasted Substantial Completion – August 2018



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

6501 Berkley Drive, New Orleans, LA 70131 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - Industrial and Mechanical Contractors, Inc

Construction Phase

- Reed - Window installation will resume in May

Contractual Substantial Completion – December 2017

Forecasted Substantial Completion – June 2018



Sophie B. Wright High School Phase 2 Interior Painting and Wood Floor Repairs ^(RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Interior painting and wood floor repairs

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – Colmex Construction

Construction Phase

- Preconstruction meeting May 21st
- Notice to Proceed May 25th

Contractual Substantial Completion – July 2018

Forecasted Substantial Completion – July 2018



DEMOLITIONS

Demolition of Modular Buildings at Abramson 3 ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – Ashley Savarino Unlimited Construction

Construction Phase

- Hydroseeding to be placed beginning of May
- Entergy to remove power poles
- Contractor working on final clean up

Contractual Substantial Completion – February 2018

Forecasted Substantial Completion – May 2018



Demolition of Modular Buildings at Coghill ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – Construction Management Enterprises

Construction Phase

- Modular componets are being prepped for transport
- Canopy has been removed

Contractual Substantial Completion – August 2018

Forecasted Substantial Completion – August 2018



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment ^(RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment ^(RSD)	10/31/2017
8	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
9	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
10	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
11	Alfred Lawless Senior ^(RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
13	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
21	Augustine Elementary School Roof ^(RSD)	04/13/2012
22	Avery-Alexander Elementary School ^(RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)	10/30/2017
25	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
26	Bell JH Shoring ^(RSD)	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
28	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
29	Bienville Elementary School Demolition ^(RSD)	05/04/2009
30	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
31	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
32	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
33	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
34	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
35	Charles J. Colton Elementary School ^(RSD)	05/23/2013
36	Charles R. Drew Elementary School ^(RSD)	04/17/2015
37	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
38	Cohen High School Health Clinic ^(RSD)	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
40	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
41	Demolition of Modular Buildings at Abramson and Carver ^(RSD)	01/18/2017
42	Demolition of Modular Buildings at Livingston ^(RSD)	01/18/2017
43	Douglass High School Under Floor Utilities ^(RSD)	

44	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
45	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
46	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
47	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
48	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
49	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011
50	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
51	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
52	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
53	Edna Karr High School - Assessment ^(OPSB)	
54	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
55	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
56	New Edward Hynes School ^(OPSB)	02/06/2012
57	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
58	Edward Livingston High School ^(RSD)	01/05/2015
59	Eleanor L. McMMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
60	Eleanor L. McMMain School Clinic ^(OPSB)	07/24/2013
61	Eleanor L. McMMain School Maintenance Upgrades ^(OPSB)	12/12/2016
62	Eleanor L. McMMain School Roof Replacement ^(OPSB)	05/13/2016
63	Ernest "Dutch" Morial Elementary ^(RSD)	03/17/2017
64	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
65	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
66	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
67	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
68	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
69	Francis W. Gregory Demolition ^(RSD)	12/21/2011
70	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
71	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
72	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
73	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
74	Gaudet Elementary School Refurbishment ^(RSD)	12/20/2016
75	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
76	George Mondy Elementary School Mothball ^(RSD)	
77	George Washington Carver School ^(RSD)	03/07/2016
78	George Washington Carver High School Demolition ^(RSD)	08/24/2011
79	Greater St. Stephens School ^(OPSB)	03/18/2013
80	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
81	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
82	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
83	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
84	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
85	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
86	Holy Cross Modular Relocation ^(RSD)	12/14/2010
87	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
88	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
89	James Derham Demolition ^(RSD)	02/23/2012

90	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
91	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
92	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
93	JoEllen Smith Medical Center Demolition ^(OPSB)	
94	John Dibert Elementary School Roof ^(RSD)	08/20/2010
95	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
96	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
97	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
98	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
99	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
100	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
101	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
102	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
103	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
104	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
105	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
106	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
107	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
108	Lake Area Landry Demolition ^(RSD)	05/01/2008
109	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
110	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
111	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
112	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
113	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
114	Laurel Elementary School Refurbishment ^(RSD)	01/03/2018
115	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
116	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
117	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
118	Live Oak Elementary School Refurbishment ^(RSD)	01/06/2017
119	Live Oak Elementary School Roof ^(RSD)	08/04/2011
120	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
121	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
122	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
123	Lusher Elementary School Refurbishment ^(OPSB)	10/31/2016
124	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
125	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
126	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
127	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
128	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
129	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
130	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
131	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
132	Mary M. Bethune Elementary School Refurbishment ^(OPSB)	10/26/2017
133	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
134	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
135	McDonogh #7 High School Repairs ^(OPSB)	

136	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
137	McDonogh #28 School Refurbishment ^(RSD)	03/15/2016
138	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
139	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
140	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
141	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
142	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
143	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
144	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
145	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
146	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
147	Modular Campuses Close Outs ^(RSD)	
148	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
149	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010
150	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
151	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
152	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
153	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
154	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
155	New Carter G. Woodson School ^(RSD)	09/14/2012
156	New Fannie C. Williams School ^(RSD)	08/24/2012
157	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
158	New L.B. Landry High School ^(RSD)	06/30/2010
159	New Lake Area High School ^(RSD)	12/28/2009
160	New Lawrence D. Crocker School ^(RSD)	04/29/2013
161	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
162	New Parkview School ^(RSD)	10/12/2012
163	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
164	New William Frantz Elementary School ^(RSD)	
165	New Orleans High School Signature Center Study ^(RSD)	
166	Oretha C. Haley Demo ^(RSD)	05/07/2012
167	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
168	Parkview Elementary School Demolition ^(RSD)	08/06/2009
169	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
170	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
171	Paul B. Habans Elementary School ^(RSD)	06/30/2016
172	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
173	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
174	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
175	Ray Abrams Elementary School ^(RSD)	03/17/2017
176	Rosenwald Elementary School Refurbishment ^(RSD)	04/07/2016
177	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
178	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
179	Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD)	02/15/2016
180	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012

181	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
182	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
183	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
184	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
185	Schaumburg Chillers ^(RSD)	11/14/2008
186	Schwarz Alternative Repairs ^(RSD)	07/14/2009
187	Schwarz Alternative Modulares Demolition ^(RSD)	04/02/2015
188	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
189	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
190	Sherwood Forest Elementary School ^(RSD)	06/30/2016
191	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
192	Sophie B. Wright School Renovation ^(RSD)	06/08/2016
193	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
194	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
195	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
196	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
197	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
198	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
199	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
200	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
201	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
202	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
203	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
204	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
205	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
206	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
207	Timbers HVAC ^(OPSB)	09/11/2013
208	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
209	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
210	Village de L'est Elementary School Refurbishment ^(RSD)	10/12/2016
211	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
212	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
213	Valena C. Jones Elementary School ^(RSD)	01/10/2013
214	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
215	Warren Easton High School Renovation ^(OPSB)	12/15/2015
216	Warren Easton School Courtyard Waterproofing ^(OPSB)	11/24/2017
217	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
218	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
219	New William J. Guste Elementary School ^(RSD)	10/06/2008
220	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
221	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
222	William Frantz Elementary School Roof ^(RSD)	08/12/2010
