Superintendent's Report August, 2017



Dr. Henderson Lewis Jr. **Orleans Parish School Board**



Mr. John White Ms. Kunjan Narehania **Recovery School District**



Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	10
Benjamin Franklin Elementary School Renovation (OPSB)	10
New Karr High School, CMAR ^(RSD)	10
John McDonogh High School Renovation CMAR (RSD)	10
Harriet R. Tubman Elementary School Renovation (RSD)	11
Booker T. Washington School CMAR (RSD)	11
REFURBISHMENTS	12
Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)	12
Agnes L. Bauduit Elementary School Refurbishment (RSD)	12
Mary M. Bethune Elementary School Refurbishment ^(OPSB)	12
Warren Easton Courtyard Waterproofing ^(OPSB)	13
William J. Fischer Elementary School HVAC Replacement ^(RSD)	13
Harney Elementary School Downspout and Gutter Repairs ^(RSD)	13
Andrew Jackson School Refurbishment (RSD)	14
Lafayette Elementary School Refurbishment ^(RSD)	14
Laurel Elementary School Refurbishment ^(RSD)	14
Thurgood Marshall Elementary School Refurbishment ^(RSD)	15
McDonogh #28 School Flooring Refurbishment ^(RSD)	15 15
McDonogh #32 School Refurbishment ^(RSD) Harriet R. Tubman Elementary School Cottage Renovation ^(RSD)	15
Schaumburg Elementary School Roof Repairs (RSD)	16
Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing ^(RSD)	16
vinage de Lot Liementary & Sarah T. Reed HVAC Equipment and Fercing	10
DEMOLITIONS	17
Demolition of Modulars at Abramson 3 (RSD)	17
Demolition of Modulars at Coghill ^(RSD)	17

COMPLETED PROJECTS

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$472 million in open contracts for the capital program after issuing \$5 million in new contracts, change orders and amendments in August. In addition, the total change orders to date, \$8.4 million, account for two percent (2.02%) of the total open construction contracts. RSD anticipates issuing \$201 thousand in construction contracts/change orders, and \$487 thousand in professional service contracts/amendments in September.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$232 million in open contracts for the capital program after issuing \$83 thousand in new contracts, change orders and amendments in August. In addition, the total change orders to date, \$9.3 million, account for approximately four percent (4.72%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 thousand in construction contracts/change orders and \$367 thousand in professional service contracts and amendments in September.

Community Meetings



Future Community Meetings

October 3, 2017

Ribbon Cutting for Ray Abrams School 6519 Virgilian Street, New Orleans LA 70126

October 5, 2017

Ribbon Cutting for Avery Alexander School 5800 St. Roch Avenue, New Orleans LA 70112

Bid Openings

Projects which are scheduled to bid in the next 60 days

September 13, 2017

Schaumberg Roof and Repairs Bid Opening

November 1, 2017

Coghill Modular Demolition Bid Opening Village de L'est Elementary School Environmental Bid Opening

November 15, 2017

Harney Roof Bid Opening



Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of August 31, 2017. The DBE subcontracts value is \$81,956,315 of the \$362,314,202 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 53 projects as of August 31, 2017. The DBE subcontracts value is \$21,827,505 of the \$73,280,853 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of August 31, 2017. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 2 projects as of August 31, 2017. The DBE subcontracts value is \$31,049,868 of the \$86,699,352 total of awarded contracts.

Total Amount of Contracts: \$631,431,352

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of August 31, 2017. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of August 31, 2017. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.


Total Amount of Contracts: \$231,354,830

* DBE provisions were included in projects bid after June 30, 2012



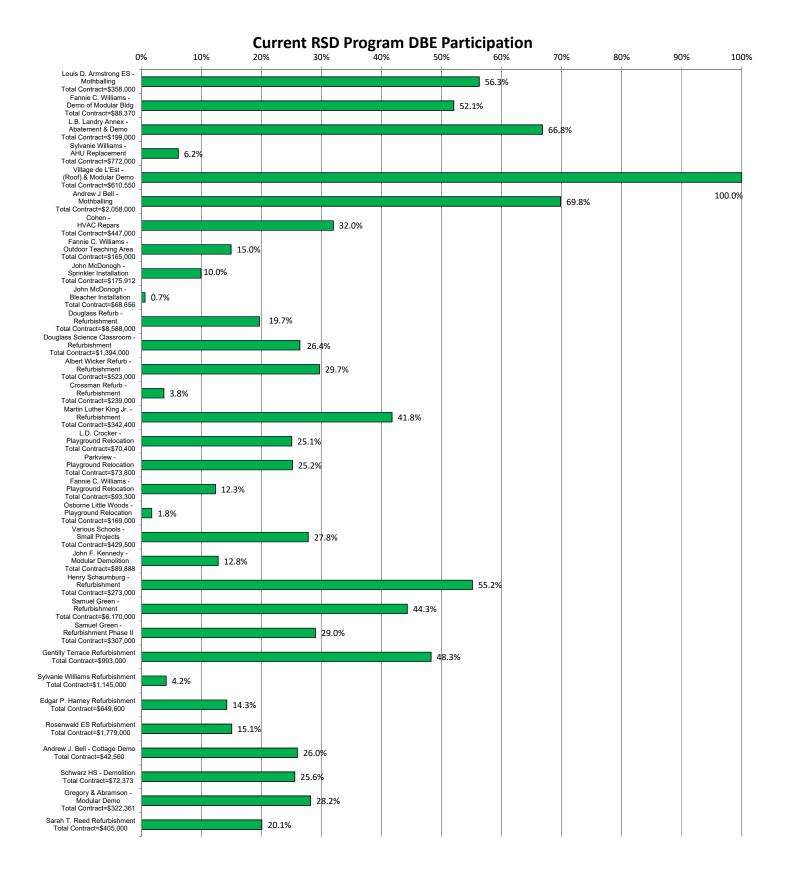


Notes: Data Based On Pre-Construction and/or monthly DBE Reports. RSD DBE Participation Target = 25% of Total Contract Amount

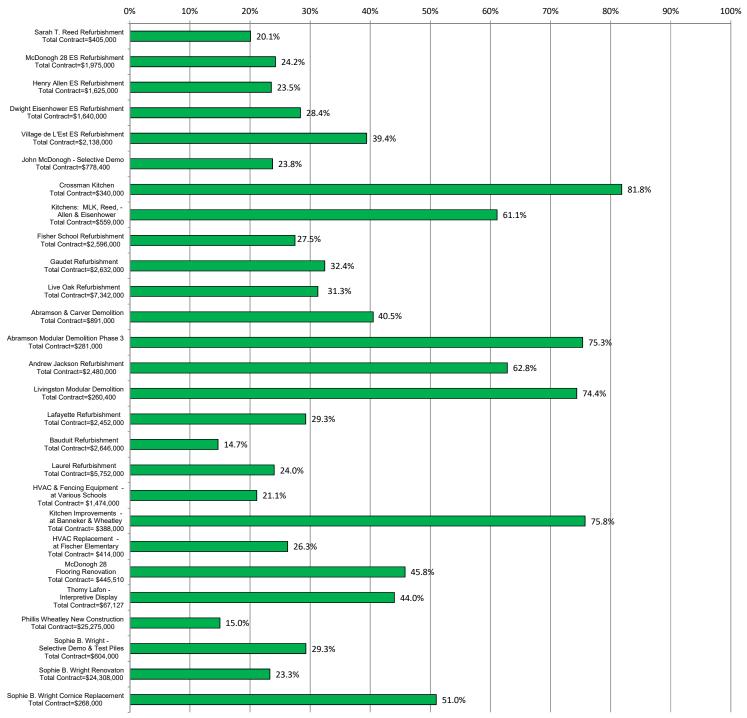

Current RSD Program DBE Participation


(Continued)

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. RSD DBE Participation Target = 25% of Total Contract Amount

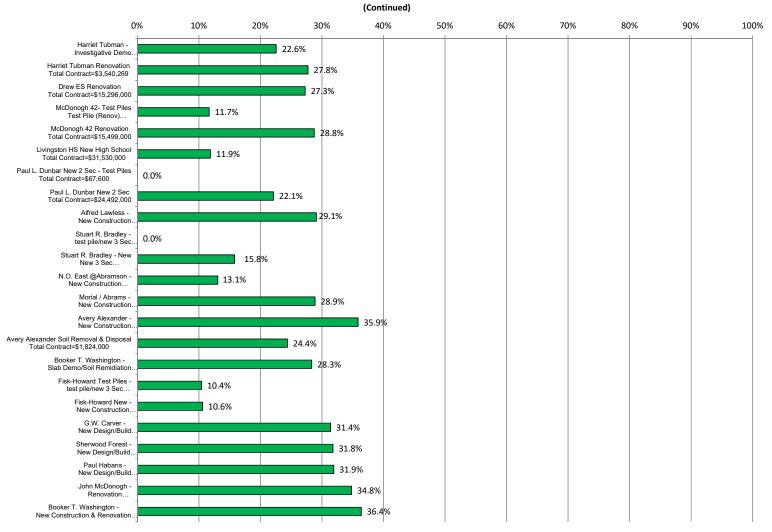

Current RSD Program DBE Participation

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. RSD DBE Participation Target = 25% of Total Contract Amount

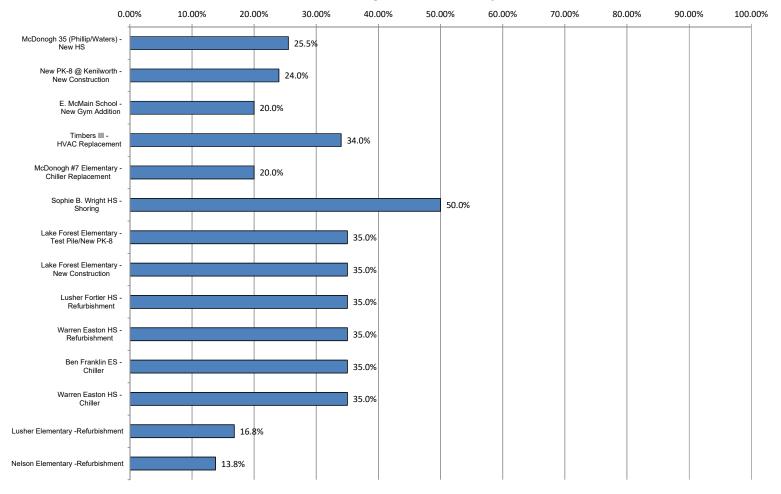

Current OPSB Program DBE Participation

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation - Project Status

(Forecasted dates only include the next project phase)

Benjamin Franklin Elementary School Renovation (OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14 Scope of work: Renovation of existing elementary school Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - TBD <u>Procurement Phase</u> • Bid Opening - August 30th

Owner is reviewing Bids



New Karr High School CMAR (RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15 Scope of work: Construction of new high school Funding Source – FEMA Architect – Trapolin Peer Architects Contractor - TBD Design Phase • A&E has submitted 90% construction documents

- A&E will submit 100% construction documents October 13th
- Test pile program is underway

Contractual Substantial Completion – TBD Forecasted Substantial Completion – TBD



John McDonogh High School Renovation CMAR ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6 Scope of work: Renovation of existing school to meet code requirements Funding Source – FEMA Architect – VergesRome Architects, APAC Contractor - Core Construction Construction Phase

Activities ongoing at the Main Building include, interior partitions, window refurbishment and MEP rough in

- · Plaster repairs and window painting continues
- · Gymnasium slab on grade will be poured in September

Contractual Substantial Completion – October 2018 Forecasted Substantial Completion – October 2018



Harriet R. Tubman Elementary School Renovation (RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA Architect – Mahlum Scairono Martinez JV Contractor - Construction Masters Inc Construction Phase

- Wood floor replacement is ongoing
- Floor replacement is ongoing on second floor
- MEP system installation is ongoing
- Exterior plaster repairs are ongoing
- · Installation of insulation has started

Contractual Substantial Completion – May 2018 Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2 Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- · Erection of steel at the gymnasium is ongoing
- Pouring of concrete columns and deck continues
- Exterior masonry removal continues

Contractual Substantial Completion – January 2019 Forecasted Substantial Completion – January 2019



REFURBISHMENTS

Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad (RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16 2300 Dumaine Street, New Orleans, LA 70119 District A Ward 3 Scope of work: Refurbishment of existing elementary school kitchen at Banneker and addition of grease trap at Wheatley Funding Source – FEMA Architect – SCNZ Architects Contractor - Commander Corp <u>Construction Phase</u>

- Wheatley dumpster pads work continues
- Banneker kitchen lighting installation has started
- Banneker dumpster pad is complete

Contractual Substantial Completion – September 2017 Forecasted Substantial Completion – September 2017



Agnes L. Bauduit Elementary School Refurbishment (RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect – Duplantis Design Group, PC Contractor – One Construction Construction Phase

- · Second floor finishes are nearing completion
- First floor ductwork and lighting installation is complete
- Exterior work is ongoing

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – September 2017



Mary M. Bethune Elementary School Refurbishment (OPSB)

4040 Eagle Street, New Orleans, LA 70118 District A Ward 17 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – Chenevert Architects Contractor – Construction Masters Inc. <u>Construction Phase</u> • Interior work has been completed

- Exterior tuck pointing continues
- Roof work is ongoing

Contractual Substantial Completion – October 2017 Forecasted Substantial Completion – October 2017



Warren Easton School Courtyard Waterproofing (OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4 Scope of work: Repairs to courtyard waterproofing Funding Source – FEMA Architect – Chenevert Architects LLC Contractor - Thigpen Construction Company <u>Construction Phase</u> • Brick and mortar repairs are ongoing Contractual Substantial Completion – November 2017 Forecasted Substantial Completion – November 2017



William J. Fischer Elementary School HVAC Replacement (RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Replacement of existing HVAC

Funding Source – FEMA Architect – SCNZ Architects Contractor - Blanchard Mechanical <u>Close-Out Phase</u> • Substantial Complete August 4th Contractual Substantial Completion – August 2017 Final Substantial Completion – August 2017

Harney Elementary School Downspout and Gutter Repairs (RSD)

2503 Willow Street New Orleans, LA 70113 District B Ward 11 Scope of work: Replacement of downspouts and gutters Funding Source – FEMA Architect – Scairono Martinez Contractor - TBD <u>Design Phase</u> • 100% Construction Documents were received August 28th <u>Procurement Phase</u> • 1st Advertisement - October 11th

- Ist Advertisement October 11th
 2nd Advertisement October 18th
- 3rd Advertisement October 25th
- 3rd Advertisement October 25th
- Pre-Bid Conference October 26th
- Bid Opening November 15th





Andrew Jackson School Refurbishment (RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services <u>Close-Out Phase</u>

Exterior stucco work is nearing completion

Substantial Complete August 23rd

Contractual Substantial Completion – August 2017 Final Substantial Completion – August 2017



Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - Tuna Construction <u>Close-Out Phase1</u>

Phase 1 Is Substantial Complete August 8th
 Design Phase 2

A&E working on second floor scope of work



Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect – Mahlum Scairono Martinez JV Contractor - Tuna Construction <u>Construction Phase</u>

- Contractor will have to move work hours to weekends due to school testing
- Exterior paving demolition and fence installation is underway
- Window installation to start in September

Contractual Substantial Completion – October 2017 Forecasted Substantial Completion – October 2017



Thurgood Marshall Elementary School Refurbishment (RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – Mahlum Scairono Martinez JV Contractor - TBD <u>Construction Phase</u> • Notice to Proceed August 23rd

Contractor is working on submittals



McDonogh #28 School Flooring Refurbishment Phase 2 (RSD)

2733 Esplanade Boulevard, New Orleans, LA 70114 District A Ward 7 Scope of work: Refurbishment of existing elementary school flooring Funding Source – FEMA, CDBG Architect – SCNZ Architects Contractor - TBD Design Phase

• A&E working on scope of work for flooring replacement on 2nd and 3rd floor



McDonogh #32 School Refurbishment (RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect – HMS Architects Contractor - TBD Design Phase • Owner is reviewing scope documents

• 90% Construction Documents are anticipated November 13th



Harriet R. Tubman Elementary School Cottage Renovation (RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing cottage to meet code requirements

Funding Source – FEMA Architect – Mahlum Scairono Martinez JV Contractor - Tuna Construction <u>Procurement Phase</u>

- Bid Opening August 2nd
- Contracts are begin signed
- Pre-Construction Conference August 26th
- Notice to Proceed October 3rd



Schaumburg Elementary School Roof Repairs (RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof Funding Source – FEMA Architect – Scairono Martinez Contractor - TBD Procurement Phase

- 1st Advertisement August 9th
- 2nd Advertisement August 16th
- 3rd Advertisement August 23rd
- Pre-Bid Conference August 24th
- Bid Opening September 13th



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing (RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

6501 Berkley Drive, New Orleans, LA 70131 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - Industrial and Mechanical Contractors, Inc Construction Phase

- HVAC equipment deliver has been delayed
- Installation of fencing at Sarah T Reed is underway
- Stripping on courts is ongoing

Contractual Substantial Completion – November 2017 Forecasted Substantial Completion – November 2017



DEMOLITIONS

Demolition of Modular Buildings at Abramson 3 (RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings Funding Source – FEMA Architect – Mahlum Scairono Martinez JV

Contractor – Ashley Savarino Unlimited Construction Construction Phase

Demolition of canopies has started

• DEQ approval is required for demolition of modulars Contractual Substantial Completion – February 2018 Forecasted Substantial Completion – February 2018



Demolition of Modular Buildings at Coghill ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA Architect – Mahlum Scairono Martinez JV

Contractor – TBD

Design Phase

100% Construction Documents were received August 14th
 Procurement Phase

- 1st Advertisement September 27th
- 2nd Advertisement October 4th
- 3rd Advertisement October 11th
- Pre-Bid Conference October 12th
- Bid Opening November 1st



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation (RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment (RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs (RSD)	06/13/2013
7	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
8	Albert Wicker Elementary School Refurbishment (RSD)	03/27/2014
9	Albert Wicker Elementary School Roof Repairs (RSD)	06/13/2013
10	Alfred Lawless Senior (RSD)	12/18/2015
11	Alfred Lawless Senior High Security Fencing (RSD)	06/15/2011
12	Alice M. Harte Elementary School (OPSB)	11/19/2014
13	Alice M. Harte Elementary School Demolition (OPSB)	12/14/2011
14	Andrew J. Bell Junior High School Roof Replacement (RSD)	02/08/2014
15	Andrew J. Bell Junior High School Mothball (RSD)	06/28/2011
16	Andrew Jackson Elementary School Roof Repairs (RSD)	07/27/2012
17	Andrew Jackson Elementary School Solar Panels (RSD)	01/14/2013
18	Andrew H. Wilson Elementary School Cottage (RSD)	10/11/2010
19	Arthur Ashe Elementary School Kitchen Renovation (OPSB)	
20	Augustine Elementary School Roof (RSD)	04/13/2012
21	Avery-Alexander Elementary School (RSD)	06/19/2017
21	Avery-Alexander Elementary School Demolition (RSD)	06/15/2012
22	Barbara C. Jordan Elementary School Demolition (RSD)	05/30/2011
23	Bell JH Shoring (RSD)	06/28/2011
24	Benjamin Banneker Elementary School Energy Conservation (RSD)	
25	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
26	Bienville Elementary School Demolition (RSD)	05/04/2009
27	Booker T. Washington High School Environmental Remediation (RSD)	12/13/2015
28	Booker T. Washington High School Partial Demolition (RSD)	04/07/2013
29	Carter G. Woodson Middle School Demolition (RSD)	02/09/2010
30	Central Services Warehouse Demolition (OPSB)	01/05/2012
31	Charles J. Colton Elementary Selective Demolition (RSD)	07/26/2010
32	Charles J. Colton Elementary School ^(RSD)	05/23/2013
33	Charles R. Drew Elementary School ^(RSD)	04/17/2015
34	Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)	06/08/2011
35	Cohen High School Health Clinic ^(RSD)	12/24/2008
36	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School (RSD)	
37	Demolition of Modular Buildings at Gregory and Abramson (RSD)	06/23/2015
38	Demolition of Modular Buildings at Abramson and Carver ^(RSD)	01/18/2017
39	Demolition of Modular Buildings at Livingston (RSD)	01/18/2017
40	Douglass High School Under Floor Utilities (RSD)	
41	Dr. Martin Luther King School Roof Repairs (RSD)	06/13/2012

10	Dr. Martin Luthan King, In Calcard Demoustion (RSD)	12/15/2014
42	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014 02/18/2016
43	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	07/27/2012
44 45	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	12/23/2015
45 46	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
40 47	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011
47 48	Edgar P. Harney Elementary School Refurbishment ^(RSD)	06/13/2012
40 49	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	12/23/2013
49 50	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
50 51	Edna Karr High School - Assessment ^(OPSB)	09/28/2010
52	Edward Livingston Middle School Demolition ^(RSD) Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
52		02/06/2012
	New Edward Hynes School ^(OPSB)	11/03/2008
54 55	Edwards Hardin Lockett Lawless Demolition ^(RSD)	01/05/2015
	Edward Livingston High School ^(RSD)	08/30/2011
56	Eleanor L. McMain School Replacement of Existing Chillers ^(OPSB)	07/24/2013
57 50	Eleanor L. McMain School Clinic ^(OPSB)	
58 50	Eleanor L. McMain School Maintenance Upgrades ^(OPSB)	12/12/2016 05/13/2016
59 60	Eleanor L. McMain School Roof Replacement ^(OPSB)	03/17/2017
60	Ernest "Dutch" Morial Elementary ^(RSD)	05/10/2011
61 42	Ernest N. Morial Elementary Security Fencing ^(RSD)	
62	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
63	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
64	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
65	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
66	Francis W. Gregory Demolition ^(RSD)	12/21/2011
67	Frederick A. Douglass High Refurbishment (RSD)	10/28/2014
68	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
69	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
70	Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)	
71	Gaudet Elementary School Refurbishment (RSD)	12/20/2016
72	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
73	George Mondy Elementary School Mothball ^(RSD)	
74	George Washington Carver School (RSD)	03/07/2016
75	George Washington Carver High School Demolition ^(RSD)	08/24/2011
76	Greater St. Stephens School ^(OPSB)	03/18/2013
77	Harriet R. Tubman Elementary School Selective Demolition (RSD)	12/14/2014
78	Henry Allen Elementary School Refurbishment (RSD)	03/08/2016
79	Henry Allen Elementary School Kitchen Refurbishment (RSD)	02/18/2016
80	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
81	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
82	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation	
83	Holy Cross Modular Relocation ^(RSD)	12/14/2010
84	Israel M. Augustine Middle School Roof Replacement (RSD)	04/13/2012
85	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
86	James Derham Demolition ^(RSD)	02/23/2012
87	James W. Johnson Elementary School Roof (RSD)	07/31/2010
	10 Statu	s Date: 31 August 2017

88	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
89	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
90	JoEllen Smith Medical Center Demolition ^(OPSB)	
91	John Dibert Elementary School Roof ^(RSD)	08/20/2010
92	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
93	John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)	11/05/2010
94	John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)	08/05/2011
95	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
96	John F. Kennedy High School Demolition (RSD)	01/12/2012
97	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
98	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
99	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
100	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
101	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
102	Joseph A. Craig Elementary Elevator Installation (RSD)	01/20/2012
103	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
104	Lafayette Elementary School Roof and Masonry (RSD)	06/22/2012
105	Lake Area Landry Demolition ^(RSD)	05/01/2008
106	Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)	11/13/2015
107	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
108	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
109	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
110	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
111	L.B. Landry Annex Demolition (RSD)	05/02/2013
112	Little Woods Elementary School Demolition (RSD)	08/09/2010
113	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
	Live Oak Elementary School Refurbishment (RSD)	01/06/2017
115	Live Oak Elementary School Roof ^(RSD)	08/04/2011
116	Live Oak Elementary School Exterior Door Replacement (RSD)	08/26/2011
117	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
118	Louis D. Armstrong Elementary School (RSD)	02/18/2013
119	Lusher Elementary School Refurbishment (OPSB)	10/31/2016
120	Mahalia Jackson Elementary School (OPSB)	05/11/2010
121	Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)	03/06/2012
122	(0000)	04/30/2013
123	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
124	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
125	Martin Luther King Jr. School Modular Building, Deck, Canopy (RSD)	07/31/2012
126	Martin Luther King Jr. School Kitchen Refurbishment (RSD)	02/18/2016
127	Mary Church Terrell Elementary School Demolition (RSD)	04/17/2013
128	Mary M. Bethune Elementary 1st Floor Replacement (OPSB)	01/24/2011
129	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)	01/21/2011
130	McDonogh #7 High School Repairs (OPSB)	
131	McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)	06/11/2012
132	McDonogh #28 School Refurbishment ^(RSD)	03/15/2016
133	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
	20	Status Data: 31 August 2017

134	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
135	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior	01/17/2014
	Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/1//2014
136	McDonogh #35 School at the Phillip/ Waters Site (OPSB)	09/23/2015
137	McDonogh #42 Elementary School Renovation (RSD)	05/28/2015
138	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
139	McDonogh #42 Elementary School HVAC Replacement (RSD)	08/09/2010
140	Mildred C. Osborne Elementary School Demolition (RSD)	02/18/2010
141	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
142		
143	Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)	05/22/2013
144	5 5 5	04/05/2010
145	Morris F.X. Jeff Elementary School Demolition (RSD)	
146	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
147	Murray G. Henderson Elementary School Roof (RSD)	06/23/2012
148	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
149	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
150	New Carter G. Woodson School ^(RSD)	09/14/2012
151	New Fannie C. Williams School ^(RSD)	08/24/2012
152	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
153	New L.B. Landry High School ^(RSD)	06/30/2010
154	New Lake Area High School ^(RSD)	12/28/2009
155	New Lawrence D. Crocker School ^(RSD)	04/29/2013
156	New PK-8 School at North Kenilworth Park at Curran Site (OPSB)	01/29/2016
157	New Parkview School ^(RSD)	10/12/2012
158	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
159	New William Frantz Elementary School ^(RSD)	
160	New Orleans High School Signature Center Study (RSD)	
161	Oretha C. Haley Demo ^(RSD)	05/07/2012
162	Oretha C. Haley Elementary School Mothball (RSD)	09/17/2012
163	Parkview Elementary School Demolition (RSD)	08/06/2009
164	Paul L. Dunbar Elementary School Demolition (RSD)	06/16/2010
165	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
166	(000)	06/30/2016
167	Paul B. Habans Elementary School Roof Repairs (RSD)	07/27/2012
168	Phillis Wheatley Elementary School Demolition (RSD)	09/26/2011
169	Phillis Wheatley Elementary School (RSD)	07/10/2014
170	Ray Abrams Elementary School (RSD)	03/17/2017
171	Rosenwald Elementary School Refurbishment (RSD)	04/07/2016
172	Robert M. Lusher Elementary Roof Removal & Replacement (OPSB)	07/14/2011
173	Samuel J. Green Elementary School Refurbishment (RSD)	02/15/2016
174	Samuel J. Green Elementary School Refurbishment Phase 2 (RSD)	02/15/2016
175	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
176	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
177	Sarah T. Reed High School Kitchen Refurbishment (RSD)	02/18/2016
178	Sarah T. Reed High School Refurbishment (RSD)	12/01/2015
		Status Data: 21 August 2017

170	OPSB)	0//05/0010
	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
180		11/14/2008
181		07/14/2009
	Schwarz Alternative Modulars Demolition (RSD)	04/02/2015
183		04/02/2015
184	· · · · · · · · · · · · · · · · · · ·	10/28/2010
185	Sherwood Forest Elementary School (RSD)	06/30/2016
186	5	09/24/2015
187	Sophie B. Wright School Renovation ^(RSD)	06/08/2016
188	Sophie B. Wright School Selective Demolition (RSD)	01/31/2014
189	Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)	07/26/2011
190	Stuart R. Bradley Elementary School Demolition (RSD)	01/27/2010
191	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
192	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
193	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
194	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
195	Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)	04/13/2012
196	(DCD)	02/18/2016
197	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
	Thomas A. Edison Elementary School Demolition (RSD)	03/25/2010
	Thomy Lafon Elementary School Demolition (RSD)	11/27/2011
200	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
201	Timbers Park Office Building #1 & #2 Demolition (OPSB)	09/18/2011
202		09/11/2013
203	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
	Village de L'est Elementary School Subsidence (RSD)	06/18/2012
	Village de L'est Elementary School Refurbishment (RSD)	10/12/2106
	Village de L'est Elementary School Roof and Modular Demolition (RSD)	06/16/2013
	Vorice J. Waters Elementary School Demolition (RSD)	01/14/2010
	Valena C. Jones Elementary School (RSD)	01/10/2013
	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
210	(0000)	12/15/2015
211	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
212	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
213		10/06/2008
214		08/04/2009
215	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
	William Frantz Elementary School Roof ^(RSD)	08/12/2010
210		00/12/2010
