
Superintendent's Report February, 2017



Dr. Henderson Lewis Jr. Orleans Parish School Board



Mr. John White Louisiana Department of Education Mr. Patrick Dobard Recovery School District

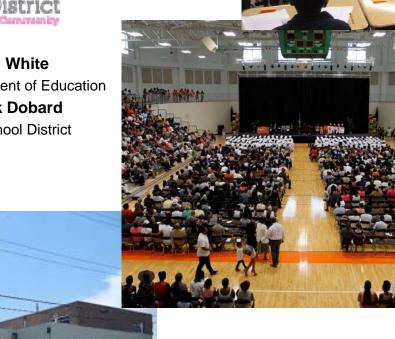



Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	3
COMMUNITY MEETINGS	4
BID OPENINGS	5
DBE OVERVIEW MONTHLY SUMMARY	6
NEW & MAJOR RENOVATION Ray Abrams Elementary School ^(RSD)	11 11
Avery Alexander Elementary School ^(RSD)	11
Benjamin Franklin Elementary School Renovation (OPSB)	11
JoEllen Smith Medical Center Demolition (OPSB)	12
New Karr High School, CMAR ^(RSD)	12
John McDonogh High School Renovation CMAR (RSD)	12
Ernest "Dutch" Morial Elementary School (RSD)	13
Harriet R. Tubman Elementary School Renovation (RSD)	13
Booker T. Washington School CMAR (RSD)	13
REFURBISHMENTS	14
Benjamin Banneker Elementary Kitchen School Refurbishment (RSD)	14
Agnes L. Bauduit Elementary School Refurbishment (RSD)	14
Mary M. Bethune Elementary School Refurbishment (OPSB)	14
William J. Fischer Elementary Refurbishment (RSD)	15
Gaudet Elementary School Refurbishment (RSD)	15
Samuel J. Green Elementary School Refurbishment ^(RSD)	15
Andrew Jackson School Refurbishment (RSD)	16
Lafayette Elementary School Refurbishment (RSD)	16
Laurel Elementary School Refurbishment ^(RSD)	16
Thurgood Marshall Elementary School Refurbishment (RSD)	17
McDonogh #28 School Flooring Refurbishment ^(RSD)	17
McDonogh #32 School Refurbishment ^(RSD)	17
Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing ^(RSD)	18

DEMOLITIONS	18
Demolition of Modulars at Abramson 3 (RSD)	18
Demolition of Modulars at Livingston (RSD)	18

COMPLETED PROJECTS

19

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$595 million in open contracts for the capital program after issuing \$161 thousand in new contracts, change orders and amendments in February. In addition, the total change orders to date, \$7.7 million, account for one percent (1.39%) of the total open construction contracts. RSD anticipates issuing approximately \$499 thousand in construction contracts/change orders, and \$72 thousand in professional service contracts/amendments in March.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$234 million in open contracts for the capital program after issuing \$133 thousand in new contracts, change orders and amendments in February. In addition, the total change orders to date, \$9.3 million, account for approximately four percent (4.72%) of the total open construction contracts. OPSB anticipates issuing approximately \$26 thousand in construction contracts/change orders and \$13 thousand in professional service contracts and amendments in March.

Community Meetings



Future Community Meetings

Bid Openings

Projects which are scheduled to bid in the next 60 days

February 1, 2017

Kitchen Improvements at Benjamin Banneker / Wheatley Grease Trap Bid Opening

March 8, 2017

HVAC Equipment Repairs at Village de l'Est, Sarah T. Reed, and Rosenwald Bid Opening

March 15, 2017

Warren Easton High School Courtyard Waterproofing Bid Opening

<u>April 5, 2017</u>

Fisher Elementary School HVAC Replacement Bid Opening

<u>April 12, 2017</u>

McDonogh #28 Flooring Renovation Bid Opening

<u>May 17, 2017</u>

Thurgood Marshall School Refurbishment Bid Opening



Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 24 projects as of February 28, 2017. The DBE subcontracts value is \$78,964,529 of the \$363,307,364 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 48 projects as of February 28, 2017. The DBE subcontracts value is \$20,269,132 of the \$65,106,535 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of February 28, 2017. The DBE subcontracts value is \$34,525,219 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 3 projects as of February 28, 2017. The DBE subcontracts value is \$11,638,373 of the \$31,996,589 total of awarded contracts.

Total Amount of Contracts: \$569,548,045

Orleans Parish School Board


New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of February 28, 2017. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.

Stabilization/Demolition/Mothballing:


DBE Contractors secured subcontracts on 2 projects as of February 28, 2017. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.


Total Amount of Contracts: \$231,354,830





Current RSD Program DBE Participation

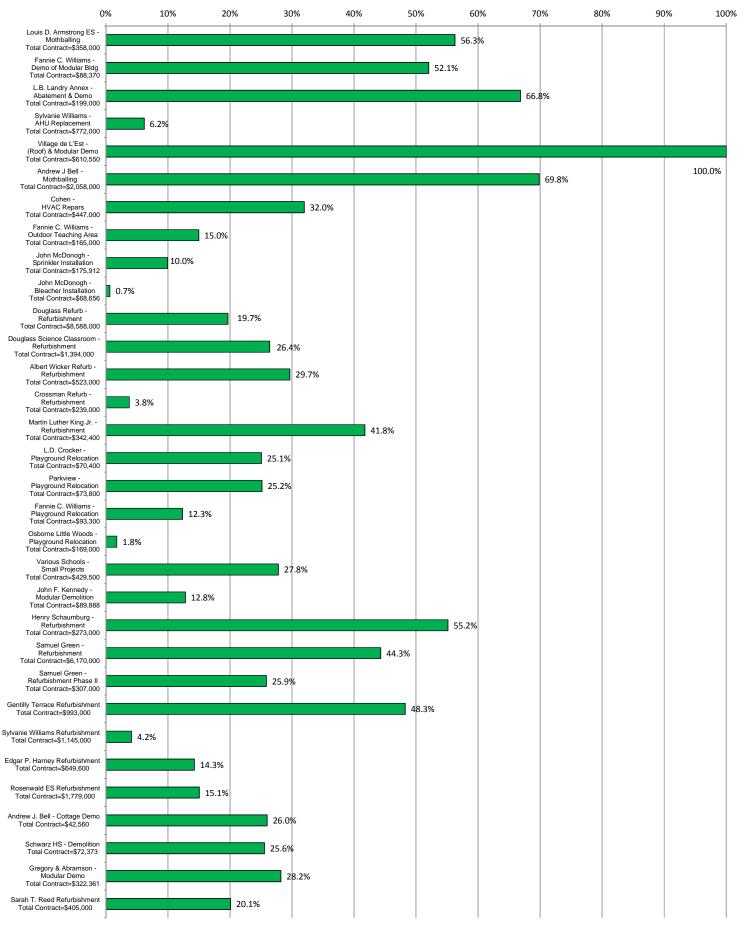


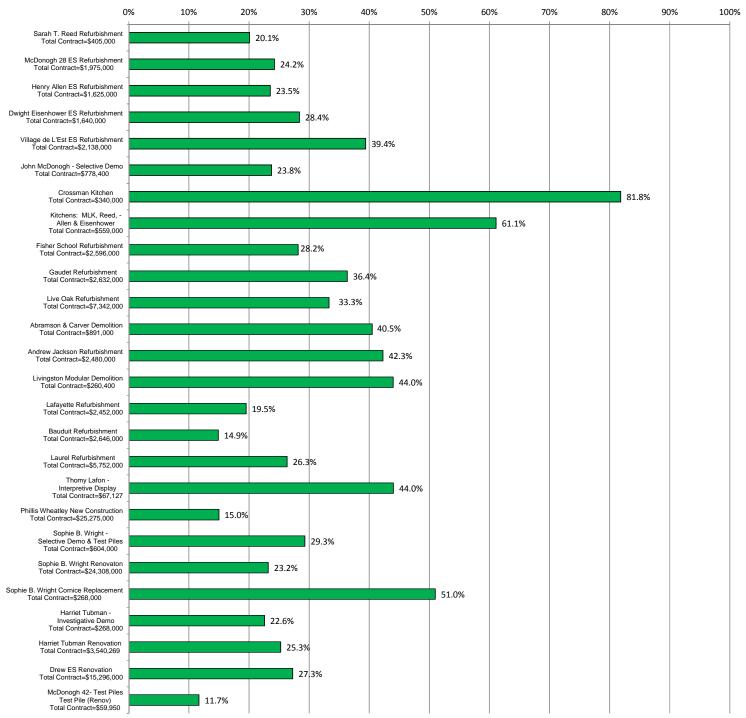

Current RSD Program DBE Participation


(Continued)

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. RSD DBE Participation Target = 25% of Total Contract Amount

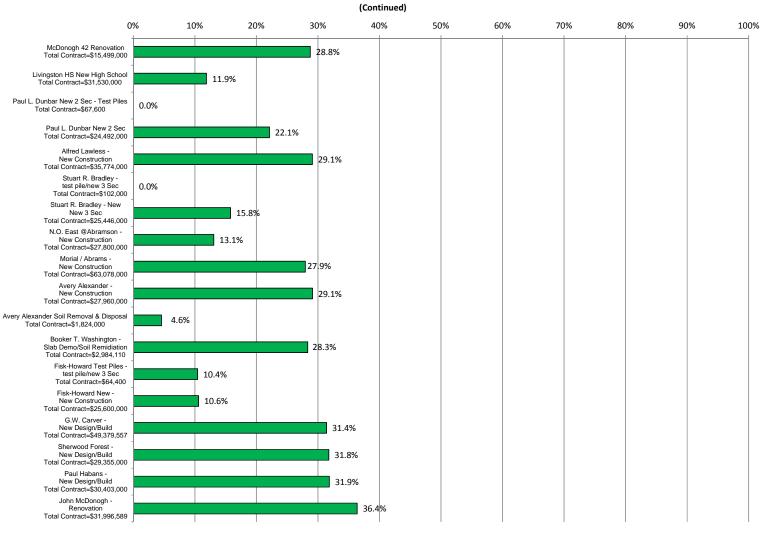

Current RSD Program DBE Participation

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. RSD DBE Participation Target = 25% of Total Contract Amount

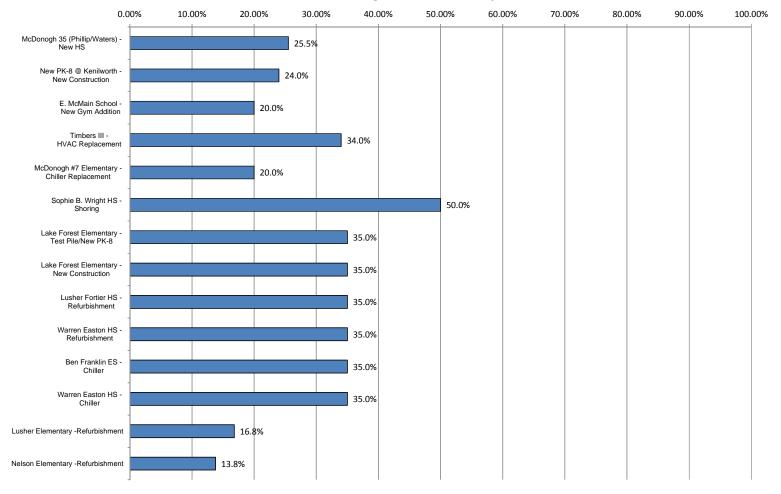

Current OPSB Program DBE Participation

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation - Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School (RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9 Scope of work: New Pre-K – 8 School Funding Source – FEMA Architect – Waggonner & Ball Architects, APC Contractor – McDonnel Group, LLC <u>Construction Phase</u> • Substantial Completion is anticipate March 17th

- GC has started their punch list
- Site clean up has started
- Contractual Substantial Completion May 2017 Forecasted Substantial Completion – March 2017



Avery Alexander Elementary School (RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8 Scope of work: New Pre-K – 8 School Funding Source – FEMA Architect – Sizeler Thompson Brown Architects Contractor – Core Construction <u>Construction Phase</u>

- Installation of exterior metal panels continue
- Exterior site work is wrapping up
- · Carpet tile installation has started
- Canopy installation continues

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – May 2017



Benjamin Franklin Elementary School Renovation (OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14 Scope of work: Renovation of existing elementary school Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - TBD Design Phase - CD

• A&E continues work on construction documents for the repairs of the exterior and the windows



JoEllen Smith Medical Center Demolition (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15 Scope of work: Demolition of existing medical center Funding Source – FEMA Architect – VergesRome Architects, APAC Contractor – Core Construction <u>Final Completion Phase</u> • Substantially Complete February 10th Contractual Substantial Completion – February 2017 Forecasted Substantial Completion – February 2017



New Karr High School CMAR (RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15 Scope of work: Construction of new high school Funding Source – FEMA Architect – Trapolin Peer Architects Contractor - TBD <u>Design Phase</u> • 90% Construction Documents are due April 26th • 100% Construction Documents are due June 7th

Contractual Substantial Completion – TBD Forecasted Substantial Completion – TBD



John McDonogh High School Renovation CMAR (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6 Scope of work: Renovation of existing school to meet code requirements Funding Source – FEMA Architect – VergesRome Architects, APAC Contractor - Core Construction <u>Construction Phase</u>

Exterior envelope repairs have started

 Main building selective demolition has started Contractual Substantial Completion – August 2018 Forecasted Substantial Completion – August 2018



Ernest "Dutch" Morial Elementary School (RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School Funding Source – FEMA Architect – Waggonner & Ball Architects, APC Contractor – McDonnel Group, LLC <u>Construction Phase</u>

- Substantial Completion is anticipate March 17th
- GC has started their punch list
- Final clean up has started

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – March 2017



Harriet R. Tubman Elementary School Renovation (RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15 Scope of work: Renovation of existing elementary school and new addition to meet code requirements Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV Contractor - Construction Masters Inc <u>Construction Phase</u>

- Roof installation is ongoing
- Refurbishment of windows continues
- Exterior Plaster repairs are ongoing
- Pouring of sidewalks has started
- MEP rough-in continues

Contractual Substantial Completion – May 2018 Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2 Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA Architect – Hewitt-Washington & Associates Contractor – Core Construction <u>Construction Phase</u>

- · Slab on grade pours continue
- Underground utility rough-in work continues
- Excavation and forming of pile caps continue

Contractual Substantial Completion – 2018 Forecasted Substantial Completion – 2018



REFURBISHMENTS

Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad (RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16 2300 Dumaine Street, New Orleans, LA 70119 District A Ward 3 Scope of work: Refurbishment of existing elementary school kitchen at Banneker and addition of grease trap at Wheatley Funding Source – FEMA Architect – SCNZ Architects Contractor - Commander Corp Procurement Phase

Contractor reviewing contract



Agnes L. Bauduit Elementary School Refurbishment (RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect – Duplantis Design Group, PC Contractor – One Construction <u>Construction Phase</u>

- Window refurbishment continues
- · Equipment curbs are being installed on the roof
- Chiller piping work continues
- Stucco and mortar mockup are under review
- Contractual Substantial Completion May 2017

Forecasted Substantial Completion – June 2017

Mary M. Bethune Elementary School Refurbishment (OPSB)

4040 Eagle Street, New Orleans, LA 70118 District A Ward 17 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – Chenevert Architects Contractor – Construction Masters Inc. <u>Procurement Phase</u>

Contractor is reviewing contracts





William J. Fischer Elementary School Refurbishment (RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect – SCNZ Architects Contractor - Perez <u>Construction Phase</u>

Work continues on intercom

 Contractor to fix rear gate and fencing issues Contractual Substantial Completion – February 2017 Forecasted Substantial Completion – April 2017



Gaudet Elementary School Refurbishment (RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – SCNZ Architects Contractor - One Construction <u>Construction Phase</u>

Substantial Completion December 20th

Contractor is working on punch list items
Contractual Substantial Completion – August 2016

Forecasted Substantial Completion – August 2016



Samuel J. Green Elementary School Refurbishment Phase 2 (RSD)

2319 Valence Street, New Orleans, LA 70115 District B Ward 13 Scope of work: Refurbishment of existing elementary school Funding Source – FEMA Architect – VergesRome Architects, APAC Contractor - Crescent Commercial <u>Construction Phase</u>

- Dumpster pad work is ongoing
- Handrail installation is progressing
- Installation of tile around water fountains has started

Contractual Substantial Completion – February 2017 Forecasted Substantial Completion – February 2017



Andrew Jackson School Refurbishment (RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen Funding Source - FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services **Construction Phase**

- Window refurb continues
- Roof and coping work inearing completion
- · Installation of new dumpster pad will start in March

Contractual Substantial Completion – June 2017 Forecasted Substantial Completion – June 2017



(RSD) Lafayette Elementary School Refurbishment

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - Tuna Construction **Construction Phase** · Window refurbishment is ongoing

• Work on Stairwell #3 continues

 Work on 3rd floor classrooms continue Contractual Substantial Completion - December 2017 Forecasted Substantial Completion – December 2017



Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect - Mahlum Scairono Martinez JV Contractor - Tuna Construction **Construction Phase** · Duct work installation has started

- · Exterior mechanical wok is ongoing
- Window replacement continues

 Work continues on 3rd classrooms Contractual Substantial Completion - October 2017 Forecasted Substantial Completion - October 2017



Thurgood Marshall Elementary School Refurbishment (RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA Architect – Mahlum Scairono Martinez JV Contractor - TBD

Procurement Phase

- 1st Advertisement April 12th
- 2nd Advertisement April 19th
- 3rd Advertisement April 26th
- Pre-Bid Conference April 27th
- Bid Opening May 17th



McDonogh #28 School Flooring Refurbishment (RSD)

2733 Esplanade Boulevard, New Orleans, LA 70114 District A Ward 7 Scope of work: Refurbishment of existing elementary school flooring Funding Source – FEMA, CDBG Architect – SCNZ Architects Contractor - TBD <u>Procurement Phase</u>

- 1st Advertisement February 22nd
- 2nd Advertisement March 1st
- 3rd Advertisement March 8th
- Pre-Bid Conference March 9th
- Bid Opening April 12th



McDonogh #32 School Refurbishment (RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof Funding Source – FEMA, CDBG Architect – SCNZ Architects Contractor - HMS Architects Design Phase - CD • A&E continues work on construction documents



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing (RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - TBD

Procurement Phase

- 1st Advertisement February 1st
- 2nd Advertisement February 8th
- 3rd Advertisement February 15th
- Pre-Bid Conference February 16th
- Bid Opening March 8th



DEMOLITIONS

Demolition of Modular Buildings at Abramson 3 (RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – TBD

Design Phase - CD

- A&E continues work on construction documents
- Anticipated 1st Advertisement April 26th

Demolition of Modular Buildings at Livingston (RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA Architect – GAEA Consultants, LLC Contractor – Concrete Busters of Louisiana <u>Construction Phase</u>

• A&E is preparing the punch list

Project is Substantially Complete

Contractual Substantial Completion – September 2016 Forecasted Substantial Completion – February 2017





Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition (RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation (RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment (RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment (RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs (RSD)	06/13/2013
7	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
8	Albert Wicker Elementary School Refurbishment (RSD)	03/27/2014
9	Albert Wicker Elementary School Roof Repairs (RSD)	06/13/2013
10	Alfred Lawless Senior (RSD)	12/18/2015
11	Alfred Lawless Senior High Security Fencing (RSD)	06/15/2011
12	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
13	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
14	Andrew J. Bell Junior High School Roof Replacement (RSD)	02/08/2014
15	Andrew J. Bell Junior High School Mothball (RSD)	06/28/2011
16	Andrew Jackson Elementary School Roof Repairs (RSD)	07/27/2012
17	Andrew Jackson Elementary School Solar Panels (RSD)	01/14/2013
18	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
19	Arthur Ashe Elementary School Kitchen Renovation (OPSB)	
20	Augustine Elementary School Roof ^(RSD)	04/13/2012
21	Avery-Alexander Elementary School Demolition (RSD)	06/15/2012
22	Barbara C. Jordan Elementary School Demolition (RSD)	05/30/2011
23	Bell JH Shoring ^(RSD)	06/28/2011
24	Benjamin Banneker Elementary School Energy Conservation (RSD)	
25	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
26	Bienville Elementary School Demolition (RSD)	05/04/2009
27	Booker T. Washington High School Environmental Remediation (RSD)	12/13/2015
28	Booker T. Washington High School Partial Demolition (RSD)	04/07/2013
29	Carter G. Woodson Middle School Demolition (RSD)	02/09/2010
30	Central Services Warehouse Demolition (OPSB)	01/05/2012
31	Charles J. Colton Elementary Selective Demolition (RSD)	07/26/2010
32	Charles J. Colton Elementary School (RSD)	05/23/2013
33	Charles R. Drew Elementary School (RSD)	04/17/2015
34	Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)	06/08/2011
35	Cohen High School Health Clinic ^(RSD)	12/24/2008
36	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School (RSD)	
37	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
38	Demolition of Modular Buildings at Abramson and Carver ^(RSD)	01/18/2017
39	Douglass High School Under Floor Utilities ^(RSD)	
40	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
41	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
42	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
43	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
		00 Falance 0017

44	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
45	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011
46	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
47	Edgar P. Harney Elementary School Roof Repairs (RSD)	06/13/2012
48	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
49	Edna Karr High School - Assessment ^(OPSB)	
50	Edward Livingston Middle School Demolition (RSD)	09/28/2010
51	Edward Henry Phillips Junior High School Demolition (OPSB)	11/19/2010
52	New Edward Hynes School ^(OPSB)	02/06/2012
53	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
54	Edward Livingston High School ^(RSD)	01/05/2015
55	Eleanor L. McMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
56	Eleanor L. McMain School Clinic ^(OPSB)	07/24/2013
57	Eleanor L. McMain School Maintenance Upgrades	12/12/2016
58	Eleanor L. McMain School Roof Replacement (OPSB)	05/13/2016
5 9	Ernest N. Morial Elementary Security Fencing (RSD)	05/10/2011
60	Fannie C. Williams Elementary School Demolition (RSD)	03/10/2009
61	Fisk-Howard Elementary School Demolition (RSD)	10/04/2011
62	Florence J. Chester Elementary School Demolition (RSD)	06/05/2011
63	Fortier (Lusher) High School Refurbishment (OPSB)	02/05/2016
64	Francis W. Gregory Demolition ^(RSD)	12/21/2011
65	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
66	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
67	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
68	Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)	
69	Gentilly Terrace Elementary School Refurbishment (RSD)	09/22/2015
70	George Mondy Elementary School Mothball ^(RSD)	
71	George Washington Carver School ^(RSD)	03/07/2016
72	George Washington Carver High School Demolition (RSD)	08/24/2011
73	Greater St. Stephens School (OPSB)	03/18/2013
74	Harriet R. Tubman Elementary School Selective Demolition (RSD)	12/14/2014
75	Henry Allen Elementary School Refurbishment (RSD)	03/08/2016
76	Henry Allen Elementary School Kitchen Refurbishment (RSD)	02/18/2016
77	Henry Allen Elementary School Roof (RSD)	05/24/2010
78	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
79	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation (RS	^{D)} 12/16/2011
80	Holy Cross Modular Relocation (RSD)	12/14/2010
81	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
82	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
83	James Derham Demolition ^(RSD)	02/23/2012
84	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
85	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
86	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
87	John Dibert Elementary School Roof ^(RSD)	08/20/2010
88	John W. Hoffman Elementary School Demolition (RSD)	05/25/2010
89	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
		e [.] 28 February 2017

00	(RSD)	00/05/0011
90	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
91	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
92 00	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
93	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
94	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
95	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
96	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
97	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
98	Joseph A. Craig Elementary Elevator Installation (RSD)	01/20/2012
99	Joseph A. Hardin Elementary Security Fencing (RSD)	05/10/2011
100	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
101	Lake Area Landry Demolition ^(RSD)	05/01/2008
102	I	11/13/2015
103	Langston Hughes Elementary School (Phase I) (RSD)	08/11/2009
104	Langston Hughes Elementary School - New Gymnasium (Phase II) (RSD)	11/10/2010
	Langston Hughes Elementary School - Dumpster Pad (RSD)	10/12/2012
106	Lawrence D. Crocker Elementary School Demolition (RSD)	04/02/2010
107	· · · · · · · ·	05/02/2013
108		08/09/2010
109	, , , , , , , , , , , , , , , , , , ,	08/01/2013
110	Live Oak Elementary School Refurbishment ^(RSD)	01/06/2017
111	Live Oak Elementary School Roof ^(RSD)	08/04/2011
112	Live Oak Elementary School Exterior Door Replacement (RSD)	08/26/2011
113	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
114	j i i j i i i j i i i j i i i j i i i j i j i i i i j i j i i i i j i j i i i i j i j i i i i j j i j i j j j i j i j j j j j j j j j j j j j j j j j j	02/18/2013
115	Lusher Elementary School Refurbishment ^(OPSB)	10/31/2016
	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
117	Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)	03/06/2012
118	Mahalia Jackson Elementary School Office Renovation (OPSB)	04/30/2013
119	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
120	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
121	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
122	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
123	Mary Church Terrell Elementary School Demolition (RSD)	04/17/2013
124	Mary M. Bethune Elementary 1st Floor Replacement (OPSB)	01/24/2011
125	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)	01/21/2011
126	McDonogh #7 High School Repairs ^(OPSB)	
127	McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)	06/11/2012
128	McDonogh #28 School Refurbishment (RSD)	03/15/2016
129	McDonogh #28 Elementary School Roof (RSD)	11/19/2011
130	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior	
131	Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
132	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
133	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
134	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
	с ,	

125	McDenergh #42 Elementary School UVAC Deplecement (RSD)	08/09/2010
135	McDonogh #42 Elementary School HVAC Replacement ^(RSD) Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
130	(202)	12/03/2012
137	Mildred C. Osborne Elemental y School	12/03/2012
130	Modular Campuses Close Outs ^(RSD)	05/22/2013
	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	03/22/2013
140	5 5 5	04/05/2010
141	Morris F.X. Jeff Elementary School Demolition ^(RSD)	01/15/2013
142	Morris F.X. Jeff Elementary School Mothball ^(RSD)	
143	· · j · · · · · j · · · · ·	06/23/2012
144 145	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
145	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
	New Carter G. Woodson School ^(RSD)	09/14/2012
	New Fannie C. Williams School ^(RSD)	08/24/2012
148	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
149		06/30/2010
	New Lake Area High School ^(RSD)	12/28/2009
151	New Lawrence D. Crocker School ^(RSD)	04/29/2013
	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
	New Parkview School ^(RSD)	10/12/2012
154		
155	New William Frantz Elementary School ^(RSD)	
156	New Orleans High School Signature Center Study (RSD)	
157	Oretha C. Haley Demo ^(RSD)	05/07/2012
158		09/17/2012
	Parkview Elementary School Demolition (RSD)	08/06/2009
	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
161	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
	Paul B. Habans Elementary School ^(RSD)	06/30/2016
163	Paul B. Habans Elementary School Roof Repairs (RSD)	07/27/2012
164	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
165	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
166	Rosenwald Elementary School Refurbishment ^(RSD)	04/07/2016
167	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
168	Samuel J. Green Elementary School Refurbishment (RSD)	02/15/2016
169	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
170	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
171	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
172	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
173	Seabrook Computer Training Center Demolition (OPSB)	06/25/2010
174	Schaumburg Chillers ^(RSD)	11/14/2008
175	Schwarz Alternative Repairs (RSD)	07/14/2009
176	(DCD)	04/02/2015
177	Schwarz Modular Building Demolition (RSD)	04/02/2015
178	Sherwood Forest Elementary School Demolition (RSD)	10/28/2010
179	Sherwood Forest Elementary School (RSD)	06/30/2016
180	Small New Orleans East High School at Abramson (RSD)	09/24/2015

181	Sophie B. Wright School Renovation (RSD)	06/08/2016
	Sophie B. Wright School Selective Demolition (RSD)	01/31/2014
183	Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)	07/26/2011
184	Stuart R. Bradley Elementary School Demolition (RSD)	01/27/2010
185	Stuart R. Bradley Elementary School (RSD)	06/26/2015
186	Sylvanie Williams Elementary School AHU Replacement (RSD)	07/30/2013
	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
188	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
189	Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)	04/13/2012
	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
191	Temporary Campus for McDonogh #11 Expropriation (OPSB)	
192	Thomas A. Edison Elementary School Demolition (RSD)	03/25/2010
193	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
196	Timbers HVAC ^(OPSB)	09/11/2013
	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
	Village de L'est Elementary School Subsidence (RSD)	06/18/2012
	Village de L'est Elementary School Refurbishment ^(RSD)	10/12/2106
	Village de L'est Elementary School Roof and Modular Demolition (RSD)	06/16/2013
201	Vorice J. Waters Elementary School Demolition (RSD)	01/14/2010
	Valena C. Jones Elementary School ^(RSD)	01/10/2013
	Walter L. Cohen High School HVAC (RSD)	04/04/2014
	Warren Easton High School Renovation (OPSB)	12/15/2015
205	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
206	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
207	5	10/06/2008
	William J. Guste Elementary School Science Lab (RSD)	08/04/2009
209	William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)	04/15/2010
210	William Frantz Elementary School Roof ^(RSD)	08/12/2010
