


Superintendent's Report September, 2016



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District

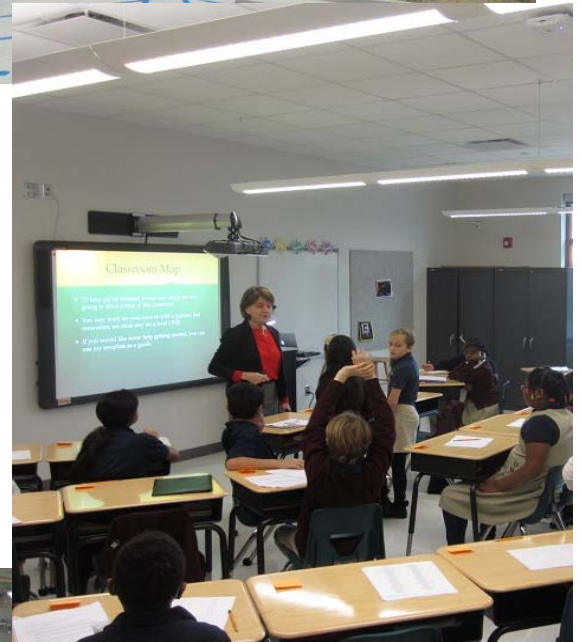

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

| | |
|---|----|
| TABLE OF CONTENTS | 1 |
| FINANCIAL OVERVIEW | 3 |
| COMMUNITY MEETINGS | 4 |
| BID OPENINGS | 5 |
| DBE OVERVIEW MONTHLY SUMMARY | 6 |
| NEW & MAJOR RENOVATION | 11 |
| Ray Abrams Elementary School ^(RSD) | 11 |
| Avery Alexander Elementary School ^(RSD) | 11 |
| Benjamin Franklin Elementary School Renovation ^(OPSB) | 11 |
| JoEllen Smith Medical Center Demolition ^(OPSB) | 12 |
| New Karr High School, CMAR ^(OPSB) | 12 |
| John McDonogh High School Renovation CMAR ^(RSD) | 12 |
| Ernest "Dutch" Morial Elementary School ^(RSD) | 13 |
| Harriet R. Tubman Elementary School Renovation ^(RSD) | 13 |
| Booker T. Washington School CMAR ^(RSD) | 13 |
| Sophie B. Wright School Cornice Replacement ^(RSD) | 14 |
| REFURBISHMENTS | 15 |
| Benjamin Banneker Elementary Kitchen School Refurbishment ^(RSD) | 15 |
| Agnes L. Bauduit Elementary School Refurbishment ^(RSD) | 15 |
| A. D. Crossman School Kitchen Refurbishment ^(RSD) | 15 |
| William J. Fischer Elementary Refurbishment ^(RSD) | 16 |
| Gaudet Elementary School Refurbishment ^(RSD) | 16 |
| Samuel J. Green Elementary School Refurbishment ^(RSD) | 16 |
| Andrew Jackson School Refurbishment ^(RSD) | 17 |
| Lafayette Elementary School Refurbishment ^(RSD) | 17 |
| Laurel Elementary School Refurbishment ^(RSD) | 17 |
| Live Oak Elementary School Refurbishment ^(RSD) | 18 |
| Lusher Elementary School Refurbishment ^(OPSB) | 18 |
| Thurgood Marshall Elementary School Refurbishment ^(RSD) | 18 |
| McDonogh #32 School Refurbishment ^(RSD) | 19 |
| Village de l'Est Elementary School Refurbishment ^(RSD) | 19 |
| Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing ^(RSD) | 19 |

| | |
|---|----|
| OTHER PROJECTS | 20 |
| Eleanor L. McMain School Maintenance Upgrades ^(OPSB) | 20 |
| DEMOLITIONS | 21 |
| Demolition of Modulares at Abramson and Carver ^(RSD) | 21 |
| Demolition of Modulares at Livingston ^(RSD) | 21 |
| COMPLETED PROJECTS | 22 |

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$551 million in open contracts for the capital program after issuing \$705 thousand in new contracts, change orders and amendments in September. In addition, the total change orders to date, \$7 million, account for one percent (1.20%) of the total open construction contracts. RSD anticipates issuing approximately \$1.5 million in construction contracts/change orders, and \$23.3 million in professional service contracts/amendments in October.



The OPSB has \$233 million in open contracts for the capital program after issuing \$0 thousand in new contracts, change orders and amendments in September. In addition, the total change orders to date, \$8.5 million, account for approximately four percent (4.29%) of the total open construction contracts. OPSB anticipates issuing approximately \$8 thousand in construction contracts/change orders and -\$189 thousand in professional service contracts and amendments in October.

Community Meetings



Future Community Meetings

October 4, 2016

Sophie B. Wright High School Ribbon Cutting
1426 Napoleon Avenue New Orleans, LA 70115

October 18, 2016

Paul B. Habans Elementary School Ribbon Cutting
3501 Seine Drive New Orleans, LA 70114

November 2, 2016

Alfred Lawless High School Ribbon Cutting
5301 North Rocheblave Street New Orleans, LA 70117

Bid Openings

No projects are scheduled to bid in the next 60 days

Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District



New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of September 30, 2016. The DBE subcontracts value is \$80,301,570 of the \$362,548,187 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 48 projects as of September 30, 2016. The DBE subcontracts value is \$19,244,420 of the \$65,106,535 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of September 30, 2016. The DBE subcontracts value is \$33,454,327 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$ 536,792,279

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of September 30, 2016. The DBE subcontracts value is \$54,086,557 of the \$199,371,360 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of September 30, 2016. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$200,274,359

* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

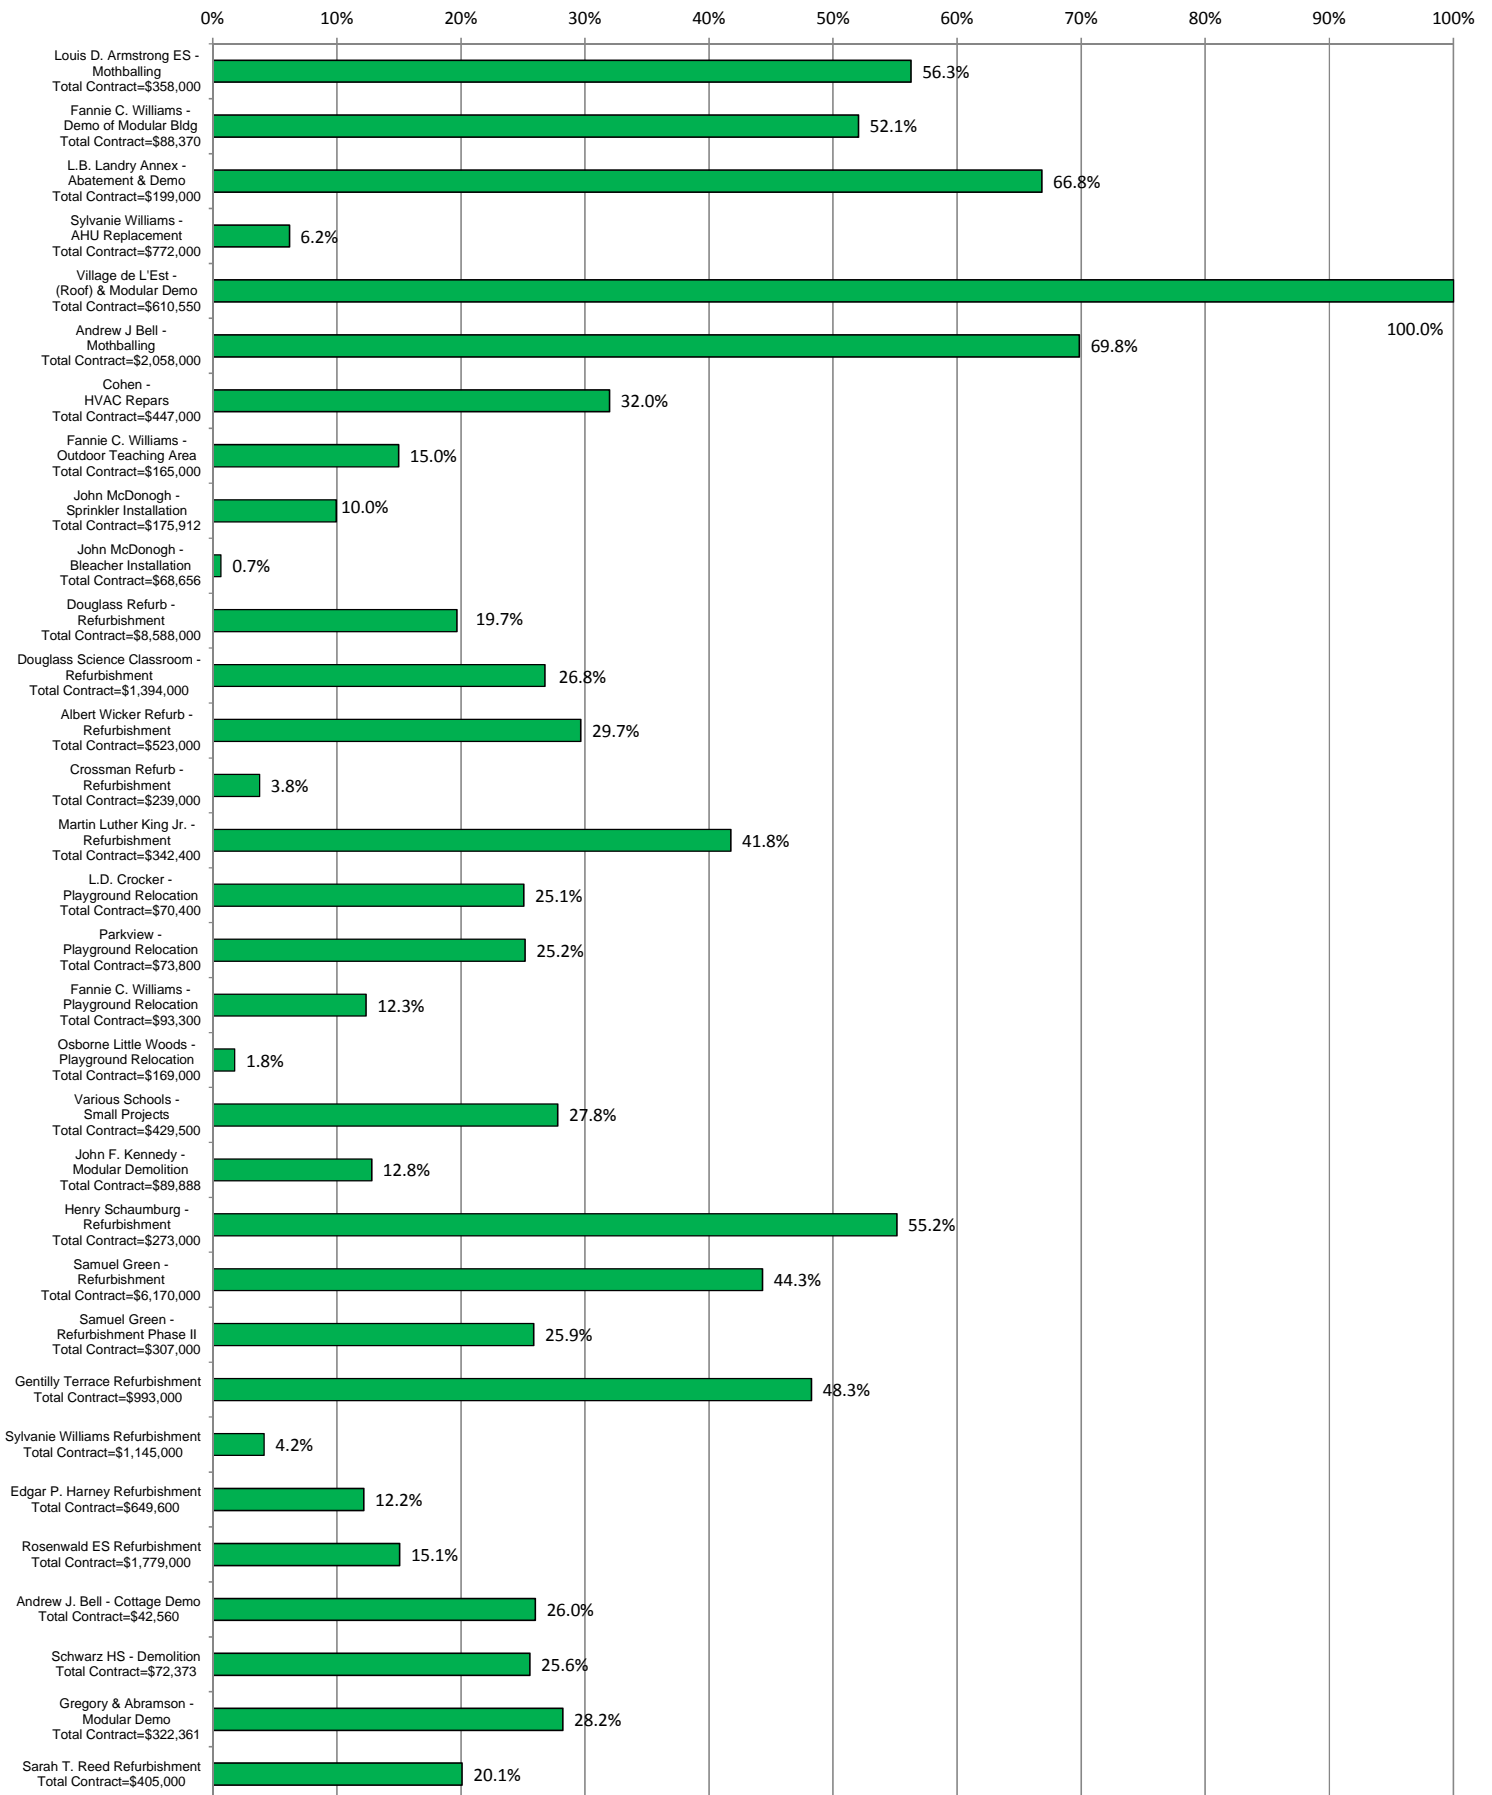


Notes: Data Based On Pre-Construction and/or 7 monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Status Date: 30 September 2016

Current RSD Program DBE Participation


(Continued)

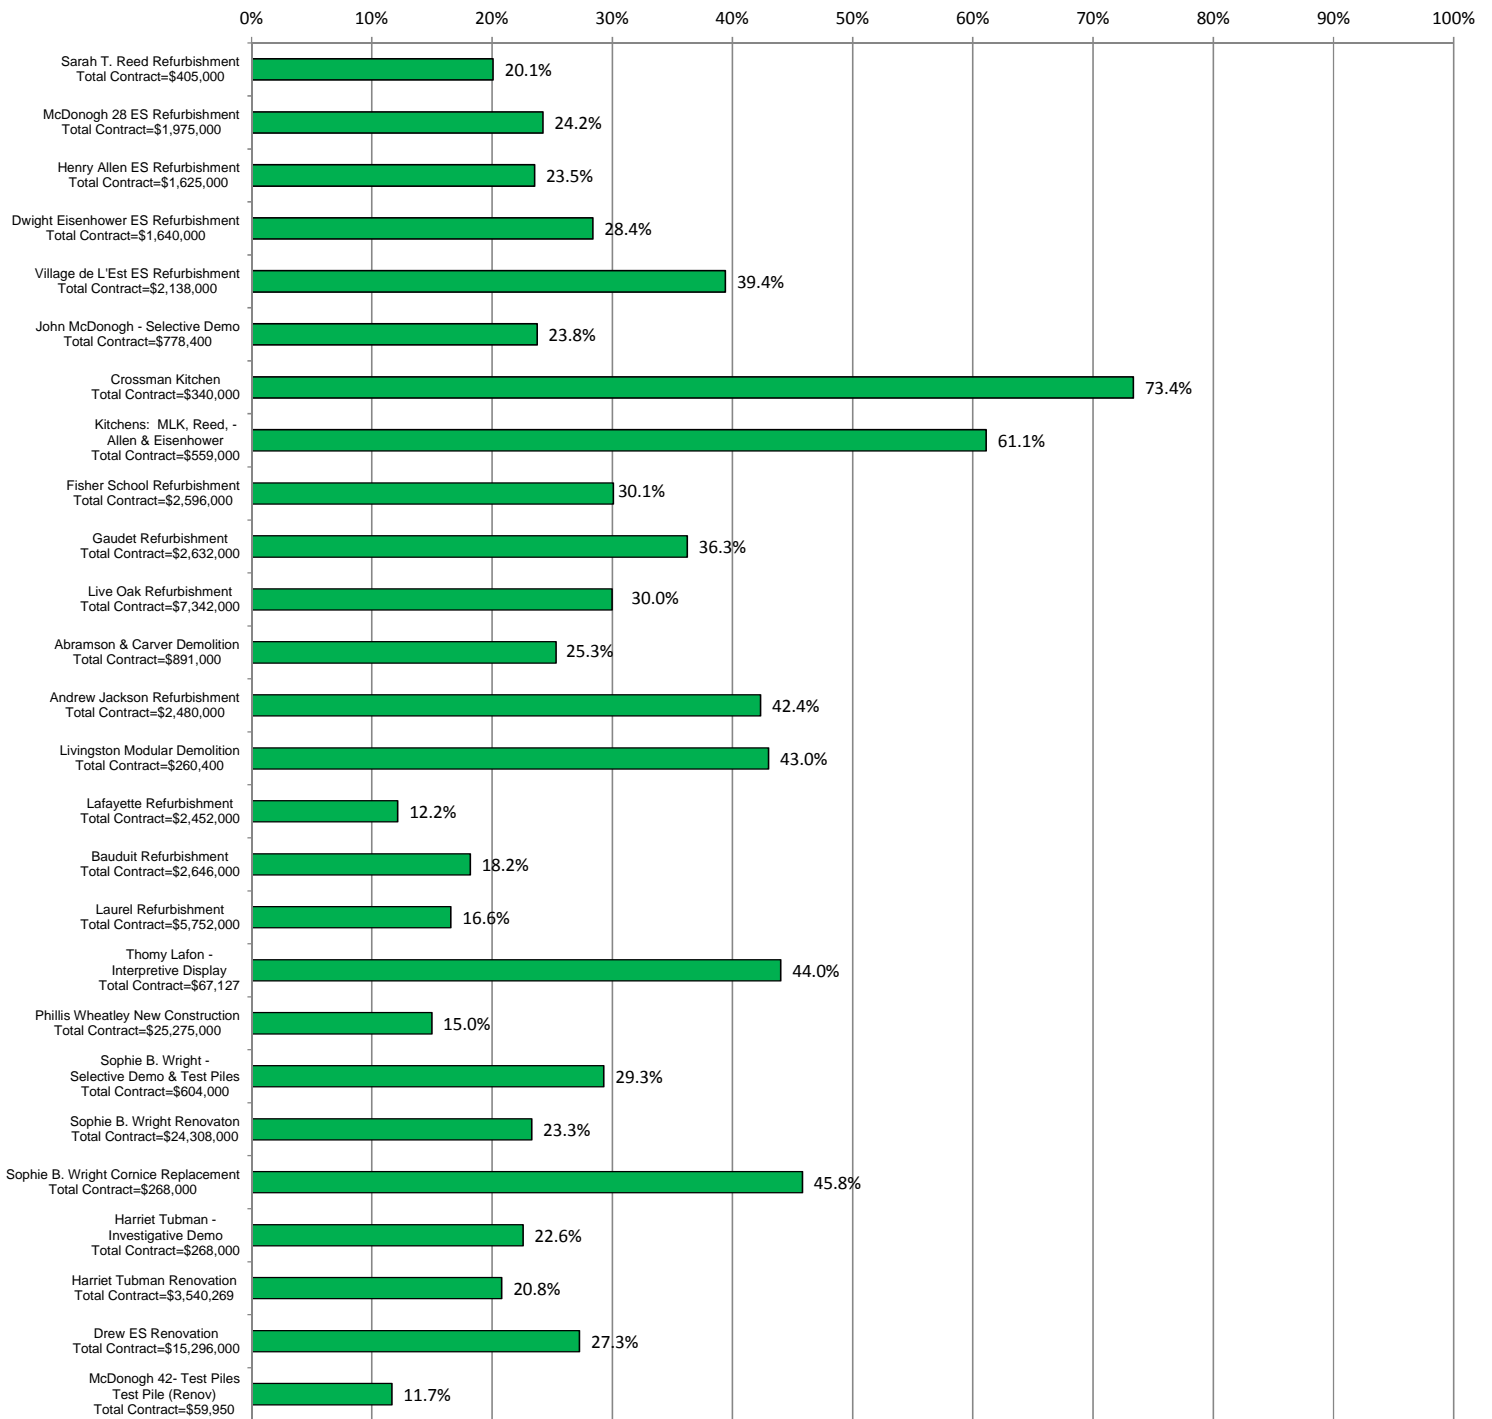

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

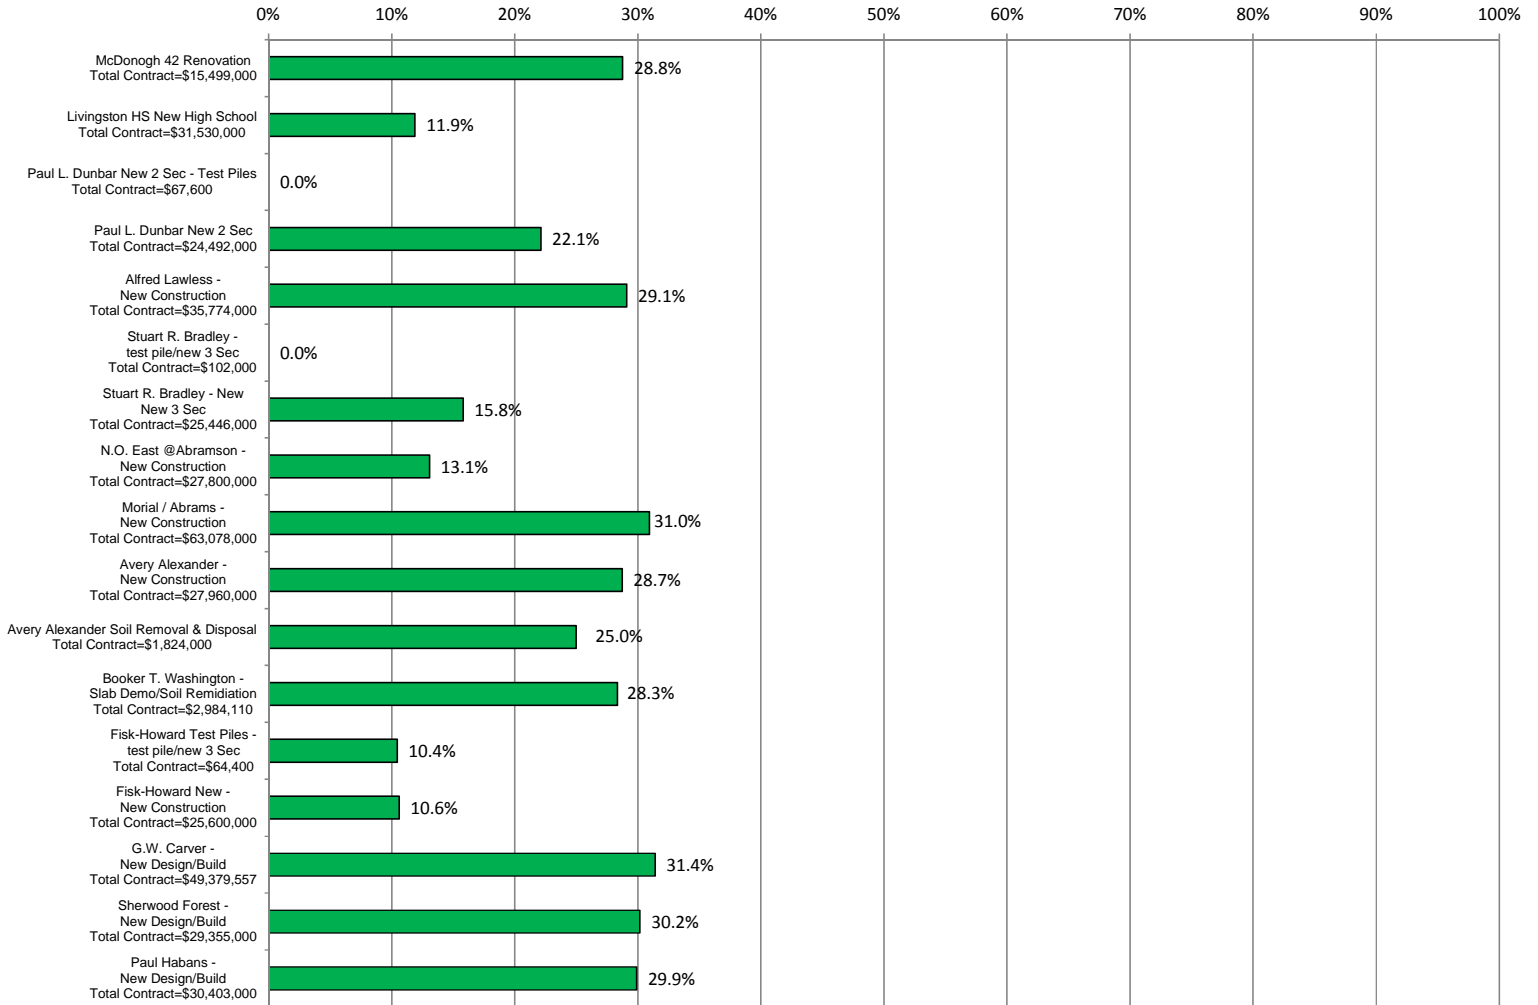

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

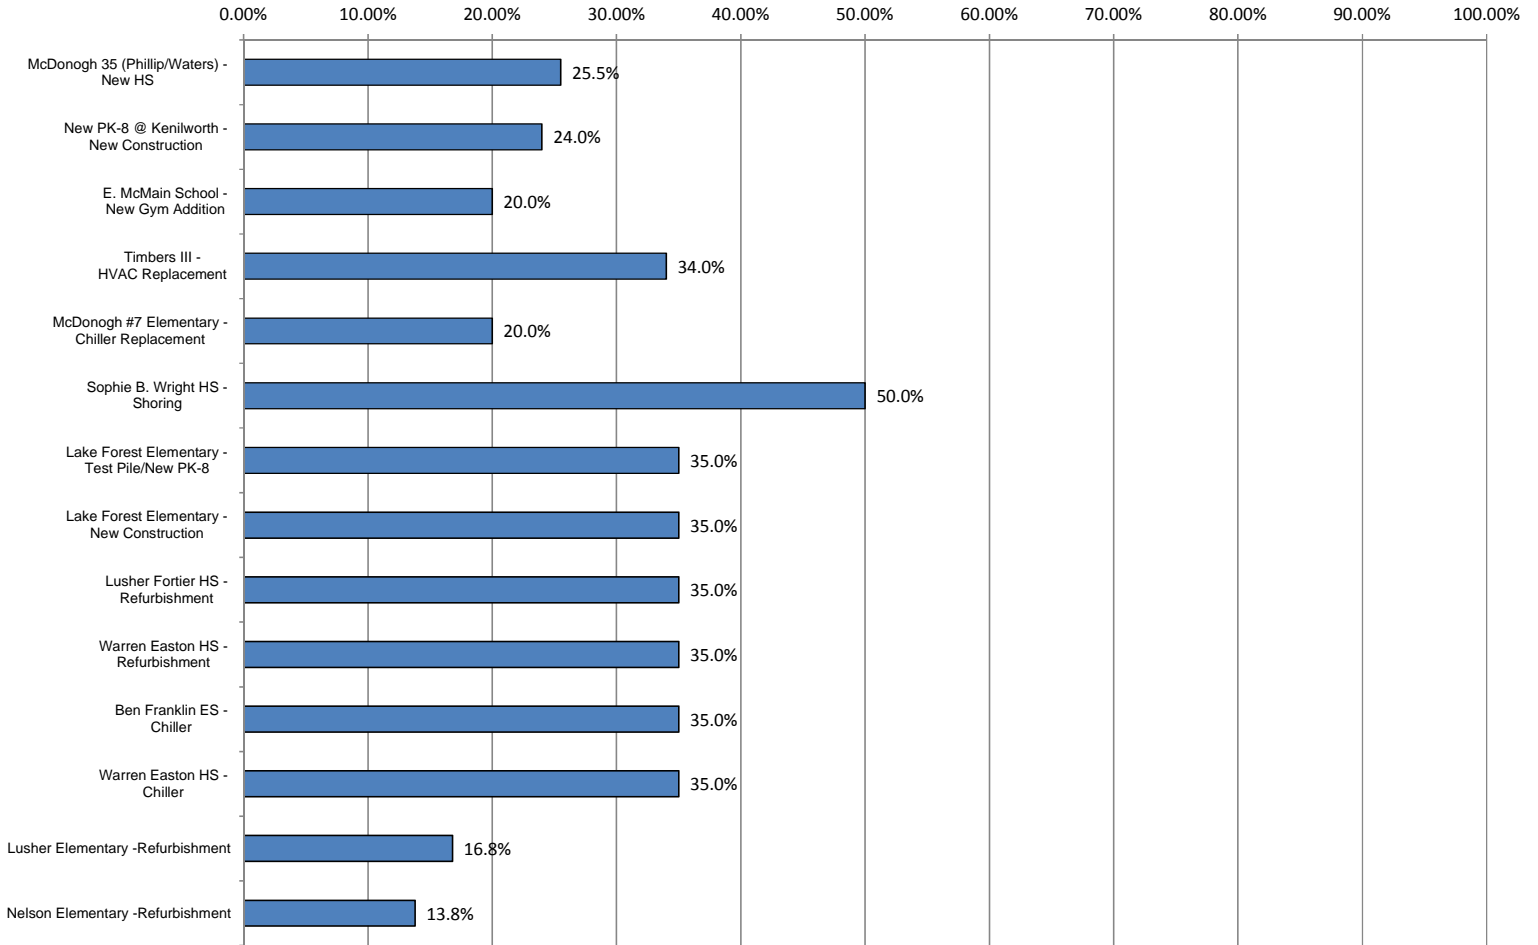

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School ^(RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Installation of interior finishes is ongoing
- HVAC installation is complete, preparation for start up in underway
- Site paving and perp work continues
- Roofing installation is nearing completion
- Special systems and data installation continues

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – March 2017



Avery Alexander Elementary School ^(RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- Installation of brick is ongoing
- Exterior metal panel installation to start in October
- Sprinkler installation is ongoing
- Window installation continues
- Ceramic tile installation has started in the restrooms

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- Owner is review scope with A&E



JoEllen Smith Medical Center Demolition (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – Core Construction

Demolition Phase

- Demolition of the main building continues
- Interior demolition continues at the medical office building

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – December 2016



New Karr High School CMAR (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – TBD

Contractor - TBD

Procurement Phase

- Attorney General to determine if OPSB is Eligible for CMAR Procurement

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



John McDonogh High School Renovation CMAR (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Design Phase

- Work on Construction Documents continues
- Test pile program to start in October
- Gymnasium Demolition is pending FEMA schedule by approval November 14th



Ernest "Dutch" Morial Elementary School ^(RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Storefront installation is complete
- Installation of all interior finishes has started
- HVAC start up prep is underway
- Lighting installation is ongoing

Contractual Substantial Completion – January 2017

Forecasted Substantial Completion – February 2017



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

Construction Phase

- plumbing rough in in kitchen area is ongoing
- Cafetorium structural steel is on site
- Window refurbishment continues
- Exterior sidewalk work is ongoing

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Test pile program is complete
- Pile driving to start in November
- Project Team is reviewing options for exterior brick work of the existing



Sophie B. Wright High School Cornice Replacement ^(RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Replace existing cornice

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – Baitco Construction

Construction Phase

- Installation of replacement cornice to follow mock up acceptance in September

Contractual Substantial Completion – December 2016

Forecasted Substantial Completion – December 2016



REFURBISHMENTS

Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

2300 Dumaine Street, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement - March 15th
- 2nd Advertisement - March 22nd
- 3rd Advertisement - March 29th
- Pre-Bid Conference - March 30th
- Bid Opening - April 19th



Agnes L. Bauduit Elementary School Refurbishment ^(RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor – One Construction

Construction Phase

- Window installation has started
- Mechanical contractor is piping new HVAC equipment
- Abatement of 3rd floor to take place October 19th
- Floor repairs continue

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



A. D. Crossman School Kitchen Refurbishment ^(RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - CDW Services

Construction Phase

- Contractor to preform corrective work on grease trap installation

Contractual Substantial Completion – July 2016

Forecasted Substantial Completion – November 2016



William J. Fischer Elementary School Refurbishment ^(RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Perez

Construction Phase

- Installation of window frames has started on first floor
- Exterior canopy columns are being installed
- Grease trap installation is complete
- Electrical work in the classrooms has started

Contractual Substantial Completion – February 2017

Forecasted Substantial Completion – February 2017



Gaudet Elementary School Refurbishment ^(RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - One Construction

Construction Phase

- Tuck point and brick cleaning is ongoing
- Testing and balance is ongoing

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – November 2016



Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD)

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school HVAC

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Crescent Commercial

Construction Phase

- Anticipated Notice to Proceed is October 17th



Andrew Jackson School Refurbishment (RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Construction Phase

- Windows on the third floor are being painted
- Stucco repairs continue near the kitchen area
- Installation of door hardware has started on first floor
- Sprinkler work continues

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Tuna Construction

Construction Phase

- Window sashes are being installed in classrooms on third floor
- Work continues in stairwell #1
- Installation of water lines at the dumpster pad continues

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Abatement and repairs to flooring has started
- Window repairs have started

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017



Live Oak Elementary School Refurbishment ^(RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- Painting continues on the exterior of the building
- Brick tuck point and stucco repairs continues
- Elevator has passed city of New Orleans inspection
- Work continues after school hours and on weekends

Contractual Substantial Completion – July 2017

Forecasted Substantial Completion – July 2017



Lusher Elementary School Refurbishment ^(OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source – FEMA

Architect – Meyer Engineers, LTD.

Contractor - Dynamic

Construction Phase

- Punch List items for elevator and bridge is ongoing

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – October 2016



Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- Securing FEMA approval on elevator location
- A&E is incorporating additional scope

Procurement Phase

- Anticipated 1st Advertisement – November 2016
- Anticipated Bid Opening – January 2017



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- A&E to revise drawings

Procurement Phase

- Anticipated 1st Advertisement – December 2016
- Anticipated Bid Opening – January 2017



Village de l'Est Elementary School Refurbishment ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

Construction Phase

- Punch list work continues
- Substantial Completion is anticipated in October

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – October 2016



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - TBD

Design Phase - CD

- 100 % Construction Documents are under review

Procurement Phase

- Anticipated 1st Advertisement – December 2016
- Anticipated Bid Opening – January 2017



OTHER PROJECTS

Eleanor L. McMain School Maintenance Upgrades ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work.

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – Tuna Construction

Construction Phase

- Testing and Balance work to be completed
- Fire alarm working is ongoing on 2nd floor
- Punch list work has started

Contractual Substantial Completion – June 2016

Forecasted Substantial Completion – November 2016



DEMOLITIONS

Demolition of Modular Buildings at Abramson and Carver ^(RSD)

5552 Read Boulevard and 3059 Higgins Boulevard, New Orleans, LA

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters, Inc.

Construction Phase

- Carver - Contractor to install new sidewalks
- Carver - Contractor to install water main shut off valve
- Abramson - Contractor to finish installing ornamental and chain link fence
- Abramson - Contractor establishing erosion control protection

Contractual Substantial Completion – October 2016

Forecasted Substantial Completion – November 2016



Demolition of Modular Buildings at Livingston ^(RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – Concrete Busters of Louisiana

Construction Phase

- Removal of modulares is ongoing
- Fence installation has started

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – October 2016



Comprehensive List - Completed Projects

| | | |
|----|---|------------|
| 1 | Abrams Morial Abramson Coghill Demolition ^(RSD) | 11/17/2008 |
| 2 | A. D. Cross Elementary School Energy Conservation ^(RSD) | |
| 3 | A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD) | 06/12/2012 |
| 4 | A. D. Crossman Elementary School Refurbishment ^(RSD) | 06/04/2014 |
| 5 | A. P. Tureaud Elementary School Roof Repairs ^(RSD) | 06/13/2013 |
| 6 | Agnes Bauduit Elementary School Boiler ^(RSD) | 12/07/2009 |
| 7 | Albert Wicker Elementary School Refurbishment ^(RSD) | 03/27/2014 |
| 8 | Albert Wicker Elementary School Roof Repairs ^(RSD) | 06/13/2013 |
| 9 | Alfred Lawless Senior ^(RSD) | 12/18/2015 |
| 10 | Alfred Lawless Senior High Security Fencing ^(RSD) | 06/15/2011 |
| 11 | Alice M. Harte Elementary School ^(OPSB) | 11/19/2014 |
| 12 | Alice M. Harte Elementary School Demolition ^(OPSB) | 12/14/2011 |
| 13 | Andrew J. Bell Junior High School Roof Replacement ^(RSD) | 02/08/2014 |
| 14 | Andrew J. Bell Junior High School Mothball ^(RSD) | 06/28/2011 |
| 15 | Andrew Jackson Elementary School Roof Repairs ^(RSD) | 07/27/2012 |
| 16 | Andrew Jackson Elementary School Solar Panels ^(RSD) | 01/14/2013 |
| 17 | Andrew H. Wilson Elementary School Cottage ^(RSD) | 10/11/2010 |
| 18 | Arthur Ashe Elementary School Kitchen Renovation ^(OPSB) | |
| 19 | Augustine Elementary School Roof ^(RSD) | 04/13/2012 |
| 20 | Avery-Alexander Elementary School Demolition ^(RSD) | 06/15/2012 |
| 21 | Barbara C. Jordan Elementary School Demolition ^(RSD) | 05/30/2011 |
| 22 | Bell JH Shoring ^(RSD) | 06/28/2011 |
| 23 | Benjamin Banneker Elementary School Energy Conservation ^(RSD) | |
| 24 | Benjamin Franklin Senior High School ^(OPSB) | 08/23/2013 |
| 25 | Bienville Elementary School Demolition ^(RSD) | 05/04/2009 |
| 26 | Booker T. Washington High School Environmental Remediation ^(RSD) | 12/13/2015 |
| 27 | Booker T. Washington High School Partial Demolition ^(RSD) | 04/07/2013 |
| 28 | Carter G. Woodson Middle School Demolition ^(RSD) | 02/09/2010 |
| 29 | Central Services Warehouse Demolition ^(OPSB) | 01/05/2012 |
| 30 | Charles J. Colton Elementary Selective Demolition ^(RSD) | 07/26/2010 |
| 31 | Charles J. Colton Elementary School ^(RSD) | 05/23/2013 |
| 32 | Charles R. Drew Elementary School ^(RSD) | 04/17/2015 |
| 33 | Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD) | 06/08/2011 |
| 34 | Cohen High School Health Clinic ^(RSD) | 12/24/2008 |
| 35 | Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD) | |
| 36 | Demolition of Modular Buildings at Gregory and Abramson ^(RSD) | 06/23/2015 |
| 37 | Douglass High School Under Floor Utilities ^(RSD) | |
| 38 | Dr. Martin Luther King School Roof Repairs ^(RSD) | 06/13/2012 |
| 39 | Dr. Martin Luther King Jr. School Renovation ^(RSD) | 12/15/2014 |
| 40 | Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD) | 02/18/2016 |
| 41 | Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD) | 07/27/2012 |
| 42 | Dwight D. Eisenhower Elementary School Refurbishment ^(RSD) | 12/23/2015 |

| | | |
|----|---|------------|
| 43 | East Bank Swing Space for Audubon Charter School ^(OPSB) | 12/30/2011 |
| 44 | Edgar P. Harney Elementary School Refurbishment ^(RSD) | |
| 45 | Edgar P. Harney Elementary School Roof Repairs ^(RSD) | 06/13/2012 |
| 46 | Edna Karr High School - Gymnasium Repair ^(OPSB) | 12/23/2013 |
| 47 | Edna Karr High School - Assessment ^(OPSB) | |
| 48 | Edward Livingston Middle School Demolition ^(RSD) | 09/28/2010 |
| 49 | Edward Henry Phillips Junior High School Demolition ^(OPSB) | 11/19/2010 |
| 50 | New Edward Hynes School ^(OPSB) | 02/06/2012 |
| 51 | Edwards Hardin Lockett Lawless Demolition ^(RSD) | 11/03/2008 |
| 52 | Edward Livingston High School ^(RSD) | 01/05/2015 |
| 53 | Eleanor L. McMains School Replacement of Existing Chillers ^(OPSB) | 08/30/2011 |
| 54 | Eleanor L. McMains School Clinic ^(OPSB) | 07/24/2013 |
| 55 | Eleanor L. McMains School Roof Replacement ^(OPSB) | 05/13/2016 |
| 56 | Ernest N. Morial Elementary Security Fencing ^(RSD) | 05/10/2011 |
| 57 | Fannie C. Williams Elementary School Demolition ^(RSD) | 03/10/2009 |
| 58 | Fisk-Howard Elementary School Demolition ^(RSD) | 10/04/2011 |
| 59 | Florence J. Chester Elementary School Demolition ^(RSD) | 06/05/2011 |
| 60 | Fortier (Lusher) High School Refurbishment ^(OPSB) | 02/05/2016 |
| 61 | Francis W. Gregory Demolition ^(RSD) | 12/21/2011 |
| 62 | Frederick A. Douglass High Refurbishment ^(RSD) | 10/28/2014 |
| 63 | Frederick A. Douglass High School Science Lab ^(RSD) | 07/05/2016 |
| 64 | Frederick A. Douglass High Switchgear ^(RSD) | 08/04/2009 |
| 65 | Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD) | |
| 66 | Gentilly Terrace Elementary School Refurbishment ^(RSD) | 09/22/2015 |
| 67 | George Mondy Elementary School Mothball ^(RSD) | |
| 68 | George Washington Carver School ^(RSD) | 03/07/2016 |
| 69 | George Washington Carver High School Demolition ^(RSD) | 08/24/2011 |
| 70 | Greater St. Stephens School ^(OPSB) | 03/18/2013 |
| 71 | Harriet R. Tubman Elementary School Selective Demolition ^(RSD) | 12/14/2014 |
| 72 | Henry Allen Elementary School Refurbishment ^(RSD) | 03/08/2016 |
| 73 | Henry Allen Elementary School Kitchen Refurbishment ^(RSD) | 02/18/2016 |
| 74 | Henry Allen Elementary School Roof ^(RSD) | 05/24/2010 |
| 75 | Henry C. Schaumburg School Refurbishment ^(RSD) | 06/26/2015 |
| 76 | Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD) | 12/16/2011 |
| 77 | Holy Cross Modular Relocation ^(RSD) | 12/14/2010 |
| 78 | Israel M. Augustine Middle School Roof Replacement ^(RSD) | 04/13/2012 |
| 79 | Israel M. Augustine Middle School Mothball ^(RSD) | 01/18/2013 |
| 80 | James Derham Demolition ^(RSD) | 02/23/2012 |
| 81 | James W. Johnson Elementary School Roof ^(RSD) | 07/31/2010 |
| 82 | New Jean Batiste de Bienville School ^(RSD) | 06/15/2012 |
| 83 | Jean Gordon Elementary School Demolition ^(RSD) | 08/16/2010 |
| 84 | John Dibert Elementary School Roof ^(RSD) | 08/20/2010 |
| 85 | John W. Hoffman Elementary School Demolition ^(RSD) | 05/25/2010 |
| 86 | John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD) | 11/05/2010 |
| 87 | John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD) | 08/05/2011 |
| 88 | John F. Kennedy Modular Demolition ^(RSD) | 09/16/2014 |

| | | |
|-----|---|------------|
| 89 | John F. Kennedy High School Demolition ^(RSD) | 01/12/2012 |
| 90 | John McDonogh Senior High School Bleachers and Sprinklers ^(RSD) | 03/27/2014 |
| 91 | John McDonogh Senior High School Roof ^(RSD) | 05/04/2010 |
| 92 | John A. Shaw Elementary School Mothball ^(RSD) | 12/12/2012 |
| 93 | Joseph S. Clark Senior High School Roof Repairs ^(RSD) | 07/27/2012 |
| 94 | Joseph A. Craig Elementary Canopies ^(RSD) | 06/06/2011 |
| 95 | Joseph A. Craig Elementary Elevator Installation ^(RSD) | 01/20/2012 |
| 96 | Joseph A. Hardin Elementary Security Fencing ^(RSD) | 05/10/2011 |
| 97 | Lafayette Elementary School Roof and Masonry ^(RSD) | 06/22/2012 |
| 98 | Lake Area Landry Demolition ^(RSD) | 05/01/2008 |
| 99 | Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB) | 11/13/2015 |
| 100 | Langston Hughes Elementary School (Phase I) ^(RSD) | 08/11/2009 |
| 101 | Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD) | 11/10/2010 |
| 102 | Langston Hughes Elementary School - Dumpster Pad ^(RSD) | 10/12/2012 |
| 103 | Lawrence D. Crocker Elementary School Demolition ^(RSD) | 04/02/2010 |
| 104 | L.B. Landry Annex Demolition ^(RSD) | 05/02/2013 |
| 105 | Little Woods Elementary School Demolition ^(RSD) | 08/09/2010 |
| 106 | Little Woods School (Dolores T. Aaron Elementary School) ^(RSD) | 08/01/2013 |
| 107 | Live Oak Elementary School Roof ^(RSD) | 08/04/2011 |
| 108 | Live Oak Elementary School Exterior Door Replacement ^(RSD) | 08/26/2011 |
| 109 | Lorraine Hansberry Elementary School Mothball ^(RSD) | 12/27/2012 |
| 110 | Louis D. Armstrong Elementary School ^(RSD) | 02/18/2013 |
| 111 | Mahalia Jackson Elementary School ^(OPSB) | 05/11/2010 |
| 112 | Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB) | 03/06/2012 |
| 113 | Mahalia Jackson Elementary School Office Renovation ^(OPSB) | 04/30/2013 |
| 114 | Martin Behrman Elementary School Roof ^(RSD) | 02/23/2010 |
| 115 | Martin Luther King Jr. Elementary Canopy System ^(RSD) | 11/05/2011 |
| 116 | Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD) | 07/31/2012 |
| 117 | Martin Luther King Jr. School Kitchen Refurbishment ^(RSD) | 02/18/2016 |
| 118 | Mary Church Terrell Elementary School Demolition ^(RSD) | 04/17/2013 |
| 119 | Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB) | 01/24/2011 |
| 120 | Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB) | 01/21/2011 |
| 121 | McDonogh #7 High School Repairs ^(OPSB) | |
| 122 | McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD) | 06/11/2012 |
| 123 | McDonogh #28 School Refurbishment ^(RSD) | 03/15/2016 |
| 124 | McDonogh #28 Elementary School Roof ^(RSD) | 11/19/2011 |
| 125 | McDonogh #32 Roof Replacement ^(RSD) | 02/24/2012 |
| 126 | McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB) | 01/17/2014 |
| 127 | McDonogh #35 School at the Phillip/ Waters Site ^(OPSB) | 09/23/2015 |
| 128 | McDonogh #42 Elementary School Renovation ^(RSD) | 05/28/2015 |
| 129 | McDonogh #42 Elementary School Roof ^(RSD) | 12/21/2011 |
| 130 | McDonogh #42 Elementary School HVAC Replacement ^(RSD) | 08/09/2010 |
| 131 | Mildred C. Osborne Elementary School Demolition ^(RSD) | 02/18/2010 |
| 132 | Mildred C. Osborne Elementary School ^(RSD) | 12/03/2012 |
| 133 | Modular Campuses Close Outs ^(RSD) | |

| | | |
|-----|---|------------|
| 134 | Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD) | 05/22/2013 |
| 135 | Modular Structures at Langston Hughes Elementary School ^(RSD) | 04/05/2010 |
| 136 | Morris F.X. Jeff Elementary School Demolition ^(RSD) | |
| 137 | Morris F.X. Jeff Elementary School Mothball ^(RSD) | 01/15/2013 |
| 138 | Murray G. Henderson Elementary School Roof ^(RSD) | 06/23/2012 |
| 139 | Nelson Elementary School Refurbishment ^(OPSB) | 04/18/2016 |
| 140 | New Andrew H. Wilson Elementary School ^(RSD) | 10/11/2009 |
| 141 | New Carter G. Woodson School ^(RSD) | 09/14/2012 |
| 142 | New Fannie C. Williams School ^(RSD) | 08/24/2012 |
| 143 | New Joseph A. Craig Elementary School ^(RSD) | 12/09/2009 |
| 144 | New L.B. Landry High School ^(RSD) | 06/30/2010 |
| 145 | New Lake Area High School ^(RSD) | 12/28/2009 |
| 146 | New Lawrence D. Crocker School ^(RSD) | 04/29/2013 |
| 147 | New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB) | 01/29/2016 |
| 148 | New Parkview School ^(RSD) | 10/12/2012 |
| 149 | New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD) | |
| 150 | New William Frantz Elementary School ^(RSD) | |
| 151 | New Orleans High School Signature Center Study ^(RSD) | |
| 152 | Oretha C. Haley Demo ^(RSD) | 05/07/2012 |
| 153 | Oretha C. Haley Elementary School Mothball ^(RSD) | 09/17/2012 |
| 154 | Parkview Elementary School Demolition ^(RSD) | 08/06/2009 |
| 155 | Paul L. Dunbar Elementary School Demolition ^(RSD) | 06/16/2010 |
| 156 | Paul L. Dunbar Elementary School ^(RSD) | 06/02/2015 |
| 157 | Paul B. Habans Elementary School ^(RSD) | 06/30/2016 |
| 158 | Paul B. Habans Elementary School Roof Repairs ^(RSD) | 07/27/2012 |
| 159 | Phillis Wheatley Elementary School Demolition ^(RSD) | 09/26/2011 |
| 160 | Phillis Wheatley Elementary School ^(RSD) | 07/10/2014 |
| 161 | Rosenwald Elementary School Refurbishment ^(RSD) | 04/07/2016 |
| 162 | Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB) | 07/14/2011 |
| 163 | Samuel J. Green Elementary School Refurbishment ^(RSD) | 02/15/2016 |
| 164 | Sarah T. Reed High School Bleachers ^(RSD) | 01/11/2012 |
| 165 | Sarah T. Reed High School Auditorium Wall ^(RSD) | 03/29/2010 |
| 166 | Sarah T. Reed High School Kitchen Refurbishment ^(RSD) | 02/18/2016 |
| 167 | Sarah T. Reed High School Refurbishment ^(RSD) | 12/01/2015 |
| 168 | Seabrook Computer Training Center Demolition ^(OPSB) | 06/25/2010 |
| 169 | Schaumburg Chillers ^(RSD) | 11/14/2008 |
| 170 | Schwarz Alternative Repairs ^(RSD) | 07/14/2009 |
| 171 | Schwarz Alternative Modulars Demolition ^(RSD) | 04/02/2015 |
| 172 | Schwarz Modular Building Demolition ^(RSD) | 04/02/2015 |
| 173 | Sherwood Forest Elementary School Demolition ^(RSD) | 10/28/2010 |
| 174 | Sherwood Forest Elementary School ^(RSD) | 06/30/2016 |
| 175 | Small New Orleans East High School at Abramson ^(RSD) | 09/24/2015 |
| 176 | Sophie B. Wright School Renovation ^(RSD) | 06/08/2016 |
| 177 | Sophie B. Wright School Selective Demolition ^(RSD) | 01/31/2014 |
| 178 | Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB) | 07/26/2011 |
| 179 | Stuart R. Bradley Elementary School Demolition ^(RSD) | 01/27/2010 |

| | | |
|-----|--|------------|
| 180 | Stuart R. Bradley Elementary School ^(RSD) | 06/26/2015 |
| 181 | Sylvanie Williams Elementary School AHU Replacement ^(RSD) | 07/30/2013 |
| 182 | Sylvanie Williams Elementary School Play Yard ^(RSD) | 09/23/2010 |
| 183 | Sylvanie Williams Elementary School Roof Repairs ^(RSD) | 07/27/2012 |
| 184 | Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD) | 04/13/2012 |
| 185 | Sylvanie Williams Elementary School Refurbishment ^(RSD) | 02/18/2016 |
| 186 | Temporary Campus for McDonogh #11 Expropriation ^(OPSB) | |
| 187 | Thomas A. Edison Elementary School Demolition ^(RSD) | 03/25/2010 |
| 188 | Thomy Lafon Elementary School Demolition ^(RSD) | 11/27/2011 |
| 189 | Thomy Lafon School Interpretative Display ^(RSD) | 10/15/2013 |
| 190 | Timbers Park Office Building #1 & #2 Demolition ^(OPSB) | 09/18/2011 |
| 191 | Timbers HVAC ^(OPSB) | 09/11/2013 |
| 192 | Timbers III - IT Room Relocation ^(OPSB) | 02/11/2015 |
| 193 | Village de L'est Elementary School Subsidence ^(RSD) | 06/18/2012 |
| 194 | Village de L'est Elementary School Roof and Modular Demolition ^(RSD) | 06/16/2013 |
| 195 | Vorice J. Waters Elementary School Demolition ^(RSD) | 01/14/2010 |
| 196 | Valena C. Jones Elementary School ^(RSD) | 01/10/2013 |
| 197 | Walter L. Cohen High School HVAC ^(RSD) | 04/04/2014 |
| 198 | Warren Easton High School Renovation ^(OPSB) | 12/15/2015 |
| 199 | Warren Easton High School Window Replacement ^(OPSB) | 09/07/2012 |
| 200 | West Bank Swing Space for Alice Harte Elementary School ^(OPSB) | 07/11/1931 |
| 201 | New William J. Guste Elementary School ^(RSD) | 10/06/2008 |
| 202 | William J. Guste Elementary School Science Lab ^(RSD) | 08/04/2009 |
| 203 | William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD) | 04/15/2010 |
| 204 | William Frantz Elementary School Roof ^(RSD) | 08/12/2010 |
