Superintendent's Report November 2018





Dr. Henderson Lewis Jr.Orleans Parish School Board



Mr. John White Louisiana Department of Education

Ms. Kunjan Narechania Recovery School District







Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	11
Benjamin Franklin Elementary School Renovation (OPSB)	11
Career Technical Education High School at Kerlerec Street CMaR (RSD)	11
New Cohen High School CMaR (RSD)	11
New Karr High School, CMAR (RSD)	12
New Orleans Charter Science and Mathematics High School (OPSB)	12
John McDonogh High School Renovation CMAR (RSD)	12
Booker T. Washington School CMAR (RSD)	13
REFURBISHMENTS	14
Fisk Howard Exterior Envelope Repairs (RSD)	14
Harney Elementary School Downspout and Gutter Repairs (RSD)	14
Lafayette Elementary School Refurbishment (RSD)	14
Eleanor McMain School Envelope Repairs (OPSB)	15
Schaumburg Elementary School Roof Repairs (RSD)	15
DEMOLITIONS	15
Demolition of Modulars at Coghill (RSD)	15
COMPLETED PROJECTS	16

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$267 million in open contracts for the capital program after issuing \$1.1 million in new contracts, change orders and amendments in November. In addition, the total change orders to date, \$3.8 million, account for one percent (1.87%) of the total open construction contracts. RSD anticipates issuing \$85 million in construction contracts/change orders, and \$327 thousand in professional service contracts/amendments in December.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$167 million in open contracts for the capital program after issuing \$-263 thousand in new contracts, change orders and amendments in November. In addition, the total change orders to date, \$5.6 million, account for approximately four percent (4.47%) of the total open construction contracts. OPSB anticipates issuing approximately \$3 million in construction contracts/change orders and \$100 thousand in professional service contracts and amendments in December.

2

Community Meetings



Future Community Meetings

DECEMBER 4, 2018

John McDonogh High School Ribbon Cutting 2426 Esplanade Avenue, New Orleans LA 70119

Bid Openings

Projects which are scheduled to bid in the next 60 days



Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 26 projects as of November 30, 2018. The DBE subcontracts value is \$82,553,475 of the \$364,282,325 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 61 projects as of November 30, 2018. The DBE subcontracts value is \$24,319,728 of the \$77,657,520 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of November 30, 2018. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 3 projects as of November 30, 2018. The DBE subcontracts value is \$45,001,673 of the 134,245,850 total of awarded contracts.

Total Amount of Contracts: \$ 685,323,252



New & Renovations:


DBE Contractors secured subcontracts on 17 projects as of November 30, 2018. The DBE subcontracts value is \$65,999,022 of the \$263,467,831 total of awarded contracts.

Stabilization/Demolition/Mothballing:


DBE Contractors secured subcontracts on 4 projects as of November 30, 2018. The DBE subcontracts value is \$569,422 of the \$1,540,999 total of awarded contracts.

Total Amount of Contracts: \$265,008,830



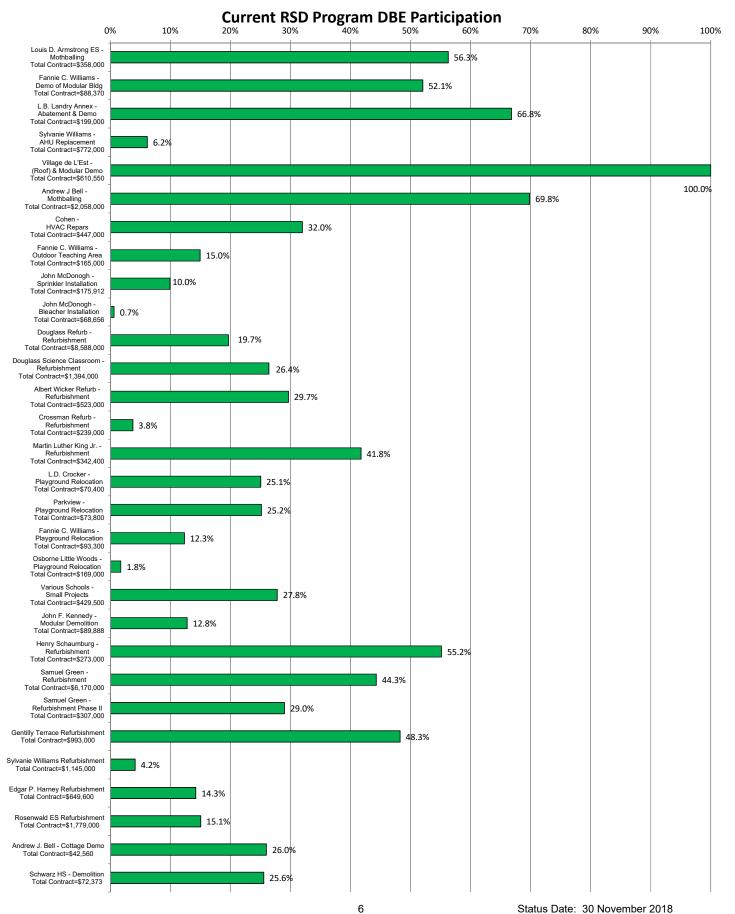


Current RSD Program DBE Participation

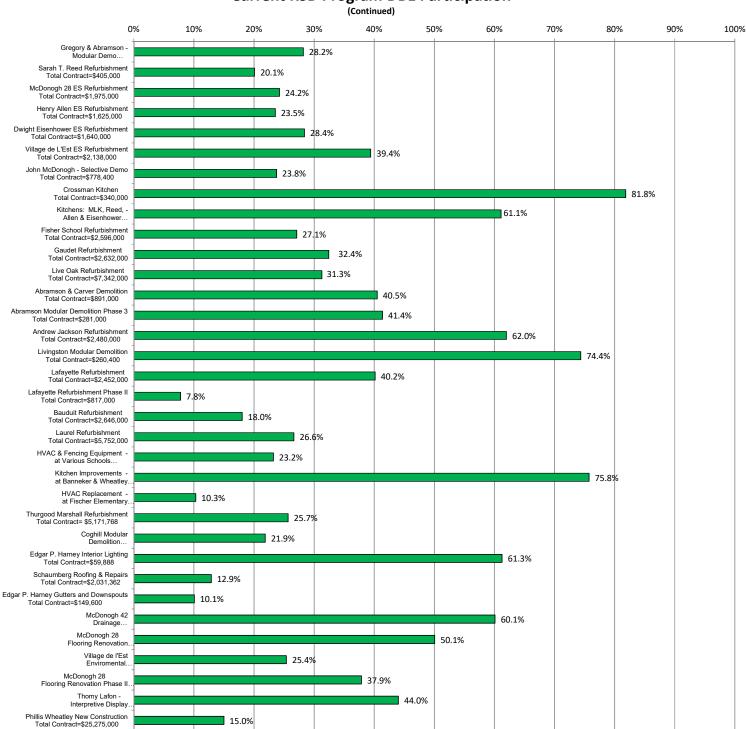

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

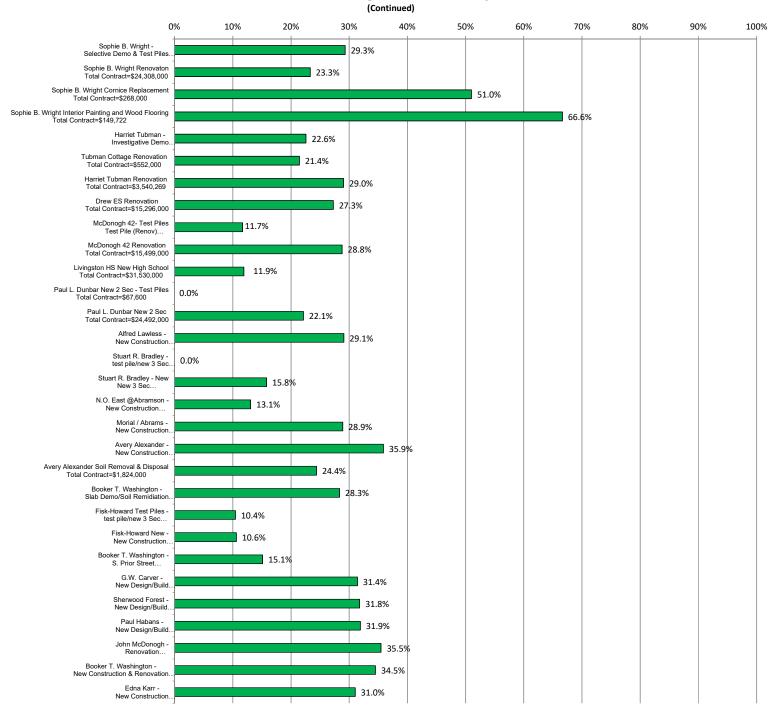

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

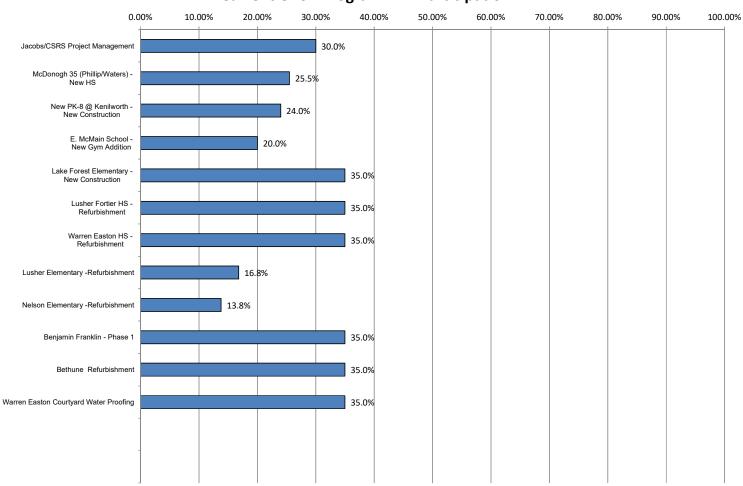

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

OPSB DBE Participation Target = 35% of Total Contract Amount

9

New & Major Renovation - Project Status

(Forecasted dates only include the next project phase)

Benjamin Franklin Elementary School Renovation Phase 2 (OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA Architect – N-Y Associates, Inc.

Contractor - TBD Procurement Phase

- 1st Advertisement October 24th
- 2nd Advertisement October 31st
- 3rd Advertisement November 7th
- Pre-Bid Conference November 8th
- Bid Opening November 28th



Career Technical Education High School at Kerlerec Street CMAR (RSD)

1331 Kerlerec Street, New Orleans, LA 70116 District D Ward 7

Scope of work: Renovation of existing high school

Funding Source – FEMA /CDBG Architect – SCNZ Architects

Contractor - TBD <u>Design Phase</u>

- · Schematic Design is due December 14th
- CMaR RFQ's are being reviewed



New Cohen High School CMAR (RSD)

3520 Dryades Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Construction of new high school

Funding Source – FEMA Architect – HMS Architects

Contractor - TBD Design Phase

- · CMaR RFQ's are being reviewed
- Space usage charts from the charter are being reviewed



New Karr High School CMAR (RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source - FEMA

Architect - Trapolin Peer Architects Contractor - Core Construction

Construction Phase

- Slabs are being poured in areas 4 and 5
- · Structural steel and decking is being installed in area 1
- Stud wall framing is underway
- Grease trap installation has started

Contractual Substantial Completion - April 2020 Forecasted Substantial Completion - April 2020



New Orleans Charter Science and Mathematics High School (OPSB)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Construction of new high school

Funding Source - FEMA

Architect - VergesRome Architects Contractor - The McDonnel Group

Construction Phase

· Demolition is ongoing

Contractual Substantial Completion – January 2021 Forecasted Substantial Completion - January 2021



John McDonogh High School Renovation CMAR (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

12

Scope of work: Renovation of existing school to meet code requirements

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor - Core Construction

Close out Phase

- · Contractor working on Gymnasium punch list
- · Ribbon Cutting December 4th
- Test and Balance reports are underway on both buildings

Contractual Substantial Completion - October 2018 Actual Substantial Completion - Main Building - September 2018 Forecasted Substantial Completion - Gymnasium - November 2018



Booker T. Washington School CMAR (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA Architect – Hewitt-Washington & Associates Contractor – Core Construction Construction Phase

- Contractor's emphasis is on closing the building envelope
- Interior finishes are ongoing at the school building
- Fireproofing is finishing at the Auditorium
- Gymnasium floor installation has started

Contractual Substantial Completion – January 2019 Forecasted Substantial Completion – May 2019



Status Date: 30 November 2018

REFURBISHMENTS

Fisk Howard Exterior Envelope Repairs (RSD)

211 South Lopez Street New Orleans, LA 70119, District B Ward 3

Scope of work: Repairs to exterior

Funding Source – FEMA

Architect - VergesRome Architects

Contractor - LLJ Environmental Construction

Construction Phase

- · Contractor has mobilized
- Contractor has started the installation of spray foam

Contractual Substantial Completion – January 2019 Forecasted Substantial Completion – January 2019



Harney Elementary School Downspout and Gutter Repairs (RSD)

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of downspouts and gutters

Funding Source – FEMA Architect – Scairono Martinez Contractor - Crescent Commercial

Construction Phase

- Contractor has started the demolition of the gutters and downspouts
- Installation of new fascia boards have started Contractual Substantial Completion – September 2018

Forecasted Substantial Completion – December 2018



Lafayette Elementary School Refurbishment Phase 2 (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to floor replacement

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Law Industries

Construction Phase

• Substandard containment exposes building to environmental contamination

14

- General Contractor has been terminated (16th July)
- Building being assessed for remediation



Eleanor McMain School Envelope Repairs (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Exterior stucco and window repairs Funding Source – General Fund & Harrah's Architect – Concordia, LLC Contractor – Tuna Construction

Construction Phase

- Exterior painting continues
- Interior lead abatement around windows is ongoing
- Plaster repairs on interior lightwells continues

Contractual Substantial Completion – April 2019 Forecasted Substantial Completion – April 2019



Schaumburg Elementary School Roof Repairs (RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA Architect – Scairono Martinez

Contractor - Laperouse Metal Works, Inc

Construction Phase

- Installation of roof panels continues
- Installation of spray foam at main roof is nearly complete
- The contractor is working on the interior water damage

Contractual Substantial Completion – August 2018 Forecasted Substantial Completion – December 2018



DEMOLITIONS

Demolition of Modular Buildings at Coghill (RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - Construction Management Enterprises

Construction Phase

- Additional topsoil is being added to the site
- Project is nearing completion

Contractual Substantial Completion – August 2018 Forecasted Substantial Completion – December 2018



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition (RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation (RSD)	11/1//2000
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School (RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment (RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment (RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs (RSD)	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment (RSD)	10/31/2017
8	Agnes Bauduit Elementary School Boiler (RSD)	12/07/2009
9	Albert Wicker Elementary School Refurbishment (RSD)	03/27/2014
10	Albert Wicker Elementary School Roof Repairs (RSD)	06/13/2013
11	Alfred Lawless Senior (RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing (RSD)	06/15/2011
13	Alice M. Harte Elementary School (OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition (OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement (RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball (RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs (RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels (RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage (RSD)	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation (OPSB)	
21	Augustine Elementary School Roof (RSD)	04/13/2012
22	Avery-Alexander Elementary School (RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition (RSD)	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad (RSD)	10/30/2017
25	Barbara C. Jordan Elementary School Demolition (RSD)	05/30/2011
26	Bell JH Shoring (RSD)	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation (RSD)	
28	Benjamin Franklin Senior High School (OPSB)	08/23/2013
29	Bienville Elementary School Demolition (RSD)	05/04/2009
30	Booker T. Washington High School Environmental Remediation (RSD)	12/13/2015
31	Booker T. Washington High School Partial Demolition (RSD)	04/07/2013
32	Carter G. Woodson Middle School Demolition (RSD)	02/09/2010
33	Central Services Warehouse Demolition (OPSB)	01/05/2012
34	Charles J. Colton Elementary Selective Demolition (RSD)	07/26/2010
35	Charles J. Colton Elementary School (RSD)	05/23/2013
36	Charles R. Drew Elementary School (RSD)	04/17/2015
37	Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)	06/08/2011
38	Cohen High School Health Clinic (RSD)	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School (RSD)	
40	Demolition of Modular Buildings at Gregory and Abramson (RSD)	06/23/2015
41	Demolition of Modular Buildings at Abramson and Carver (RSD)	01/18/2017
42	Demolition of Modular Buildings at Livingston (RSD)	01/18/2017
43	Douglass High School Under Floor Utilities (RSD)	

11	Dr. Martin Luther King Cahaal Boof Danaira (RSD)	06/13/2012
44	Dr. Martin Luther King School Roof Repairs (RSD)	
45	Dr. Martin Luther King Jr. School Renovation (RSD)	12/15/2014
46	Dwight D. Eisenhower Elementary School Kitchen Refurbishment (RSD)	02/18/2016
47	Dwight D. Eisenhower Elementary School Roof Repairs (RSD)	07/27/2012
48	Dwight D. Eisenhower Elementary School Refurbishment (RSD)	12/23/2015
49	East Bank Swing Space for Audubon Charter School (OPSB)	12/30/2011
50	Edgar P. Harney Elementary School Refurbishment (RSD)	0.4.4.0.10.0.4.0
51	Edgar P. Harney Elementary School Roof Repairs (RSD)	06/13/2012
52	Edgar P. Harney Elementary School Lighting Repairs (RSD)	08/08/2018
53	Edna Karr High School - Gymnasium Repair (OPSB)	12/23/2013
54	Edna Karr High School - Assessment (OPSB)	
55	Edward Livingston Middle School Demolition (RSD)	09/28/2010
56	Edward Henry Phillips Junior High School Demolition (OPSB)	11/19/2010
57	New Edward Hynes School (OPSB)	02/06/2012
58	Edwards Hardin Lockett Lawless Demolition (RSD)	11/03/2008
59	Edward Livingston High School (RSD)	01/05/2015
60	Eleanor L. McMain School Replacement of Existing Chillers (OPSB)	08/30/2011
61	Eleanor L. McMain School Clinic (OPSB)	07/24/2013
62	Eleanor L. McMain School Maintenance Upgrades (OPSB)	12/12/2016
63	Eleanor L. McMain School Roof Replacement (OPSB)	05/13/2016
64	Ernest "Dutch" Morial Elementary (RSD)	03/17/2017
65	Ernest N. Morial Elementary Security Fencing (RSD)	05/10/2011
66	Fannie C. Williams Elementary School Demolition (RSD)	03/10/2009
67	Fisk-Howard Elementary School Demolition (RSD)	10/04/2011
68	Florence J. Chester Elementary School Demolition (RSD)	06/05/2011
69	Fortier (Lusher) High School Refurbishment (OPSB)	02/05/2016
70	Francis W. Gregory Demolition (RSD)	12/21/2011
71	Frederick A. Douglass High Refurbishment (RSD)	10/28/2014
72	Frederick A. Douglass High School Science Lab (RSD)	07/05/2016
73	Frederick A. Douglass High Switchgear (RSD)	08/04/2009
74	Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)	
75	Gaudet Elementary School Refurbishment (RSD)	12/20/2016
76	Gentilly Terrace Elementary School Refurbishment (RSD)	09/22/2015
77	George Mondy Elementary School Mothball (RSD)	07/22/2010
78	George Washington Carver School (RSD)	03/07/2016
79	George Washington Carver High School Demolition (RSD)	08/24/2011
80	Greater St. Stephens School (OPSB)	03/18/2013
81	Harriet R. Tubman Elementary School Selective Demolition (RSD)	12/14/2014
82	Harriet R. Tubman Elementary School Renovation (RSD)	08/01/2018
83	Harriet R. Tubman Cottage Renovation (RSD)	08/02/2018
84	Henry Allen Elementary School Refurbishment (RSD)	03/08/2016
85		02/18/2016
86	Henry Allen Elementary School Kitchen Refurbishment (RSD) Henry Allen Elementary School Roof (RSD)	05/24/2010
87	Henry C. Schaumburg School Refurbishment (RSD)	06/26/2015
88	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation (RSD)	12/16/2011
		12/16/2011
89	Holy Cross Modular Relocation (RSD)	12/14/2010

90	Israel M. Augustine Middle School Roof Replacement (RSD)	04/13/2012
91	Israel M. Augustine Middle School Mothball (RSD)	01/18/2013
92	James Derham Demolition (RSD)	02/23/2012
93	James W. Johnson Elementary School Roof (RSD)	07/31/2010
94	New Jean Batiste de Bienville School (RSD)	06/15/2012
95	Jean Gordon Elementary School Demolition (RSD)	08/16/2010
96	JoEllen Smith Medical Center Demolition (OPSB)	
97	John Dibert Elementary School Roof (RSD)	08/20/2010
98	John W. Hoffman Elementary School Demolition (RSD)	05/25/2010
99	John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)	11/05/2010
100	John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)	08/05/2011
101	John F. Kennedy Modular Demolition (RSD)	09/16/2014
102	John F. Kennedy High School Demolition (RSD)	01/12/2012
103	John McDonogh Senior High School Bleachers and Sprinklers (RSD)	03/27/2014
104	John McDonogh Senior High School Roof (RSD)	05/04/2010
105	John A. Shaw Elementary School Mothball (RSD)	12/12/2012
106	Joseph S. Clark Senior High School Roof Repairs (RSD)	07/27/2012
107	Joseph A. Craig Elementary Canopies (RSD)	06/06/2011
108	Joseph A. Craig Elementary Elevator Installation (RSD)	01/20/2012
109	Joseph A. Hardin Elementary Security Fencing (RSD)	05/10/2011
110	Lafayette Elementary School Roof and Masonry (RSD)	06/22/2012
111	Lake Area Landry Demolition (RSD)	05/01/2008
112	Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)	11/13/2015
113	Langston Hughes Elementary School (Phase I) (RSD)	08/11/2009
114	Langston Hughes Elementary School - New Gymnasium (Phase II) (RSD)	11/10/2010
115	Langston Hughes Elementary School - Dumpster Pad (RSD)	10/12/2012
116	Lawrence D. Crocker Elementary School Demolition (RSD)	04/02/2010
117	Laurel Elementary School Refurbishment (RSD)	01/03/2018
118	L.B. Landry Annex Demolition (RSD)	05/02/2013
	Little Woods Elementary School Demolition (RSD)	08/09/2010
120	Little Woods School (Dolores T. Aaron Elementary School) (RSD)	08/01/2013
121	Live Oak Elementary School Refurbishment (RSD)	01/06/2017
122	Live Oak Elementary School Roof (RSD)	08/04/2011
123	Live Oak Elementary School Exterior Door Replacement (RSD)	08/26/2011
124	Lorraine Hansberry Elementary School Mothball (RSD)	12/27/2012
125	Louis D. Armstrong Elementary School (RSD)	02/18/2013
126	Lusher Elementary School Refurbishment (OPSB)	10/31/2016
127	Mahalia Jackson Elementary School (OPSB)	05/11/2010
128	Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)	03/06/2012
129	Mahalia Jackson Elementary School Office Renovation (OPSB)	04/30/2013
130	Martin Behrman Elementary School Roof (RSD)	02/23/2010
131	Martin Luther King Jr. Elementary Canopy System (RSD)	11/05/2011
132	Martin Luther King Jr. School Modular Building, Deck, Canopy (RSD)	07/31/2012
133	Martin Luther King Jr. School Kitchen Refurbishment (RSD)	02/18/2016
134	Mary Church Terrell Elementary School Demolition (RSD)	04/17/2013
135	Mary M. Bethune Elementary School Refurbishment (OPSB)	10/26/2017

124	Marrie M. Dakkerra Elementeri 1at Elem Danles mant (OPSB)	01/24/2011
	Mary M. Bethune Elementary 1st Floor Replacement (OPSB)	01/24/2011
137	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)	01/21/2011
138	McDonogh #7 High School Repairs (OPSB) McDonogh #15 Florest to Test School Repairs (RSD)	04/11/2012
139	McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)	06/11/2012
140	McDonogh #28 School Refurbishment (RSD)	03/15/2016
141	McDonogh #28 Elementary School Roof (RSD)	11/19/2011
142	McDonogh #32 Roof Replacement (RSD)	02/24/2012
143	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior	01/17/2014
111	Ramp & Handicap Seating in the Auditorium (OPSB)	00/02/0045
144	McDonogh #35 School at the Phillip/ Waters Site (OPSB)	09/23/2015
145	McDonogh #42 Elementary School Renovation (RSD)	05/28/2015
146	McDonogh #42 Elementary School Roof (RSD)	12/21/2011
147	McDonogh #42 Elementary School HVAC Replacement (RSD)	08/09/2010
148	Mildred C. Osborne Elementary School Demolition (RSD)	02/18/2010
149	Mildred C. Osborne Elementally School	12/03/2012
150	Modular Campuses Close Outs (RSD)	05/00/0040
151	Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)	05/22/2013
152	Modular Structures at Langston Hughes Elementary School (RSD)	04/05/2010
153	Morris F.X. Jeff Elementary School Demolition (RSD)	
154	Morris F.X. Jeff Elementary School Mothball (RSD)	01/15/2013
155	Murray G. Henderson Elementary School Roof (RSD)	06/23/2012
156	Nelson Elementary School Refurbishment (OPSB)	04/18/2016
157	New Andrew H. Wilson Elementary School (RSD)	10/11/2009
158	New Carter G. Woodson School (RSD)	09/14/2012
159	New Fannie C. Williams School (RSD)	08/24/2012
160	New Joseph A. Craig Elementary School (RSD)	12/09/2009
161	New L.B. Landry High School (RSD)	06/30/2010
	New Lake Area High School (RSD)	12/28/2009
163	New Lawrence D. Crocker School (RSD)	04/29/2013
164	New PK-8 School at North Kenilworth Park at Curran Site (OPSB)	01/29/2016
165	New Parkview School (RSD)	10/12/2012
166	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD)	
167	New William Frantz Elementary School (RSD)	
168	New Orleans High School Signature Center Study (RSD)	
169	Oretha C. Haley Demo (RSD)	05/07/2012
170	Oretha C. Haley Elementary School Mothball (RSD)	09/17/2012
171	Parkview Elementary School Demolition (RSD)	08/06/2009
	Paul L. Dunbar Elementary School Demolition (RSD)	06/16/2010
	Paul L. Dunbar Elementary School (RSD)	06/02/2015
174	Paul B. Habans Elementary School (RSD)	06/30/2016
175	Paul B. Habans Elementary School Roof Repairs (RSD)	07/27/2012
176	Phillis Wheatley Elementary School Demolition (RSD)	09/26/2011
177	Phillis Wheatley Elementary School (RSD)	07/10/2014
178	Ray Abrams Elementary School (RSD)	03/17/2017
179	Rosenwald Elementary School Refurbishment (RSD)	04/07/2016
180	Robert M. Lusher Elementary Roof Removal & Replacement (OPSB)	07/14/2011

101	Constant Constant Colored Defeation and (RSD)	02/15/2017
	Samuel J. Green Elementary School Refurbishment (RSD)	02/15/2016
	Samuel J. Green Elementary School Refurbishment Phase 2 (RSD)	02/15/2016
	Sarah T. Reed High School Bleachers (RSD)	01/11/2012
184		03/29/2010
185		02/18/2016
	Sarah T. Reed High School Refurbishment (RSD)	12/01/2015
187	Seabrook Computer Training Center Demolition (OPSB)	06/25/2010
188		11/14/2008
	Schwarz Alternative Repairs (RSD)	07/14/2009
	Schwarz Alternative Modulars Demolition (RSD)	04/02/2015
191	gg	04/02/2015
	Sherwood Forest Elementary School Demolition (RSD)	10/28/2010
	Sherwood Forest Elementary School (RSD)	06/30/2016
194		09/24/2015
	Sophie B. Wright School Renovation (RSD)	06/08/2016
196	Sophie B. Wright School Selective Demolition (RSD)	01/31/2014
197	3	07/26/2011
198	Stuart R. Bradley Elementary School Demolition (RSD)	01/27/2010
199	Stuart R. Bradley Elementary School (RSD)	06/26/2015
200	Sylvanie Williams Elementary School AHU Replacement (RSD)	07/30/2013
201	Sylvanie Williams Elementary School Play Yard (RSD)	09/23/2010
202	Sylvanie Williams Elementary School Roof Repairs (RSD)	07/27/2012
203	Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)	04/13/2012
204	Sylvanie Williams Elementary School Refurbishment (RSD)	02/18/2016
205	Temporary Campus for McDonogh #11 Expropriation (OPSB)	
206	Thomas A. Edison Elementary School Demolition (RSD)	03/25/2010
207	Thomy Lafon Elementary School Demolition (RSD)	11/27/2011
208	Thomy Lafon School Interpretative Display (RSD)	10/15/2013
209	Thurgood Marshall Elementary School Refurbishment (RSD)	08/10/2018
210	Timbers Park Office Building #1 & #2 Demolition (OPSB)	09/18/2011
211	Timbers HVAC (OPSB)	09/11/2013
212	Timbers III - IT Room Relocation (OPSB)	02/11/2015
213	Village de L'est Elementary School Subsidence (RSD)	06/18/2012
214	Village de L'est Elementary School Refurbishment (RSD)	10/12/2106
215	Village de L'est Elementary School Roof and Modular Demolition (RSD)	06/16/2013
216	Vorice J. Waters Elementary School Demolition (RSD)	01/14/2010
217	Valena C. Jones Elementary School (RSD)	01/10/2013
	Walter L. Cohen High School HVAC (RSD)	04/04/2014
219	(ODCD)	12/15/2015
220	Warren Easton School Courtyard Waterproofing (OPSB)	11/24/2017
221	Warren Easton High School Window Replacement (OPSB)	09/07/2012
222	West Bank Swing Space for Alice Harte Elementary School (OPSB)	07/11/1931
223	New William J. Guste Elementary School (RSD)	10/06/2008
224	(DCD)	08/04/2009
225	William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)	04/15/2010
220	William Frantz Elementary School Roof (RSD)	08/12/2010
