Superintendent's Report September 2018






Dr. Henderson Lewis Jr.Orleans Parish School Board



Mr. John White
Louisiana Department
of Education

Ms. Kunjan Narechania Recovery School District

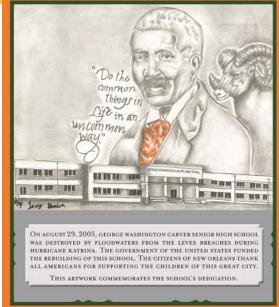





Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	11
Benjamin Franklin Elementary School Renovation (OPSB)	1′
Career Technical Education High School at Kerlerec Street CMaR (RSD)	11
New Cohen High School CMaR (RSD)	11
New Karr High School, CMAR (RSD)	12
New Orleans Charter Science and Mathematics High School (OPSB)	12
John McDonogh High School Renovation CMAR (RSD)	12
Harriet R. Tubman Elementary School Renovation (RSD)	13
Booker T. Washington School CMAR (RSD)	13
REFURBISHMENTS	14
Fisk Howard Exterior Envelope Repairs (RSD)	14
Harney Elementary School Downspout and Gutter Repairs (RSD)	14
Lafayette Elementary School Refurbishment (RSD)	14
Thurgood Marshall Elementary School Refurbishment (RSD)	15
McDonogh #42 School Refurbishment (RSD)	15
Eleanor McMain School Envelope Repairs (OPSB)	16
Schaumburg Elementary School Roof Repairs (RSD)	16
DEMOLITIONS	17
Demolition of Modulars at Coghill (RSD)	17
COMPLETED PROJECTS	18

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$265 million in open contracts for the capital program after issuing \$982 thousand in new contracts, change orders and amendments in September. In addition, the total change orders to date, \$3.4 million, account for one percent (1.71%) of the total open construction contracts. RSD anticipates issuing \$86 million in construction contracts/change orders, and \$808 thousand in professional service contracts/amendments in October.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$163 million in open contracts for the capital program after issuing \$0 thousand in new contracts, change orders and amendments in September. In addition, the total change orders to date, \$5.6 million, account for approximately four percent (4.47%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 thousand in construction contracts/change orders and \$(-23) thousand in professional service contracts and amendments in October.

Community Meetings



Future Community Meetings

OCTOBER 6, 2018

School Rebuilding Construction Industry Day Xavier University Convocation Annex

NOVEMBER 27, 2018

New Orleans Charter Science and Mathematics High School Ground
Breaking

2011 Bienville Street, New Orleans LA 70112

DECEMBER 4, 2018

John McDonogh High School Ribbon Cutting 2426 Esplanade Avenue, New Orleans LA 70119

Bid Openings

Projects which are scheduled to bid in the next 60 days

October 31, 2018

Hynes Exterior Envelope Repairs Bid Opening

November 28, 2018

Ben Franklin Elementary School Renovation Phase II

4



Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 26 projects as of September 30, 2018. The DBE subcontracts value is \$82,631,578 of the \$364,264,924 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 61 projects as of September 30, 2018. The DBE subcontracts value is \$23,954,696 of the \$76,807,120 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of September 30, 2018. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 3 projects as of September 30, 2018. The DBE subcontracts value is \$44,722,469 of the 134,245,850 total of awarded contracts.

Total Amount of Contracts: \$ 684,557,452




New & Renovations:


DBE Contractors secured subcontracts on 17 projects as of September 30, 2018. The DBE subcontracts value is \$65,999,022 of the \$263,467,831 total of awarded contracts.

Stabilization/Demolition/Mothballing:


DBE Contractors secured subcontracts on 4 projects as of September 30, 2018. The DBE subcontracts value is \$569,422 of the \$1,540,999 total of awarded contracts.

Total Amount of Contracts: \$265,008,830



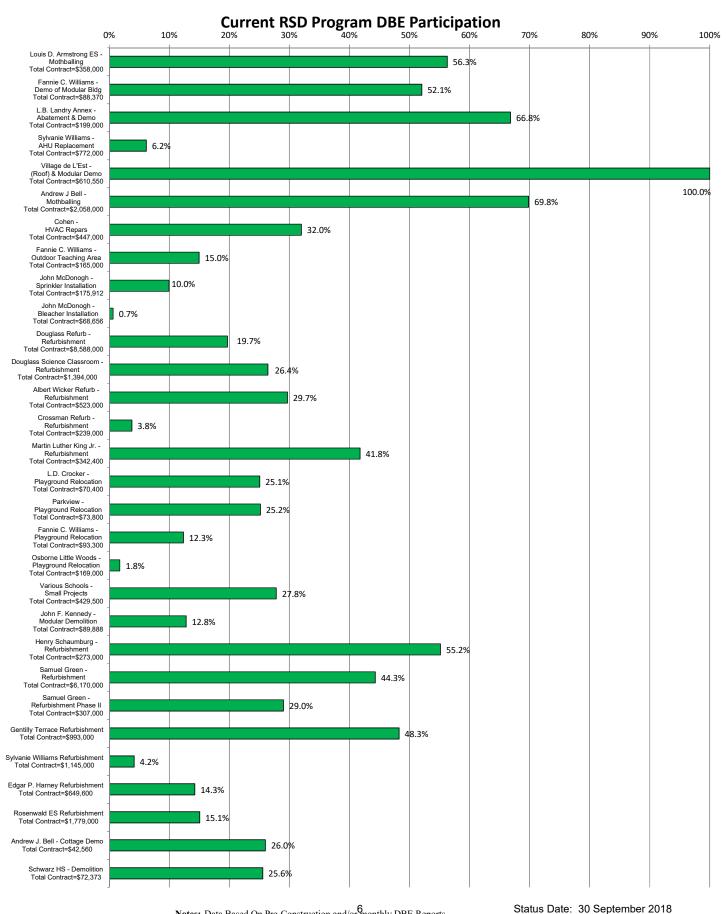


Current RSD Program DBE Participation

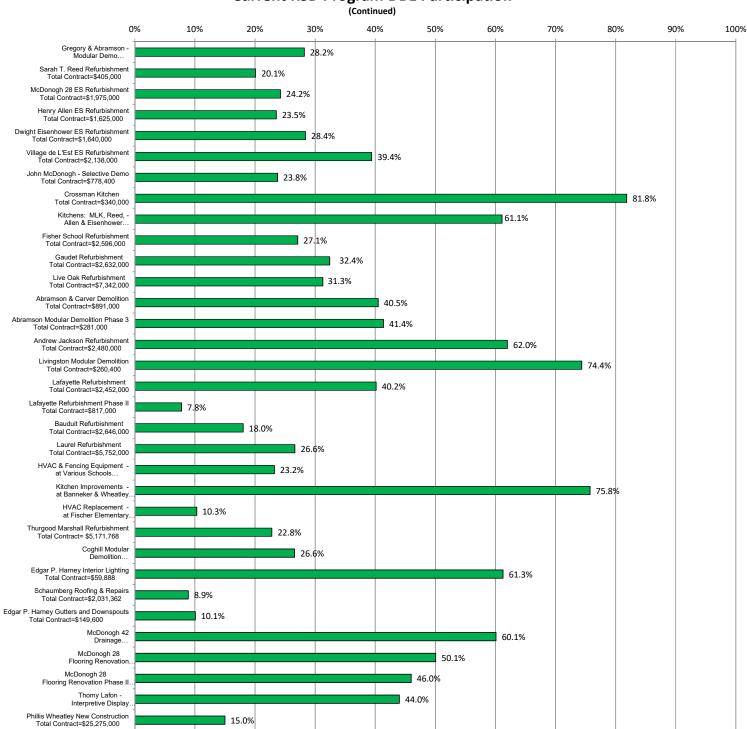

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

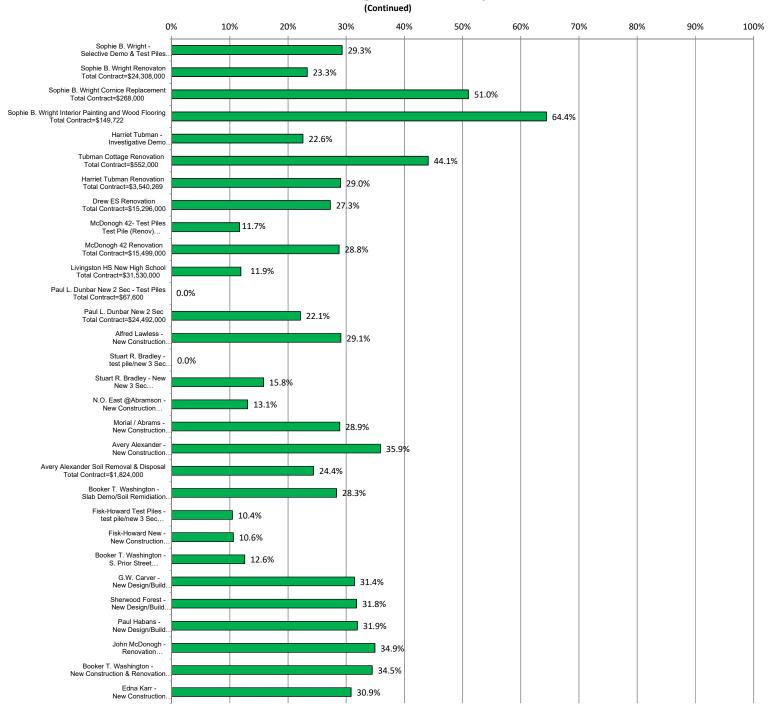

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

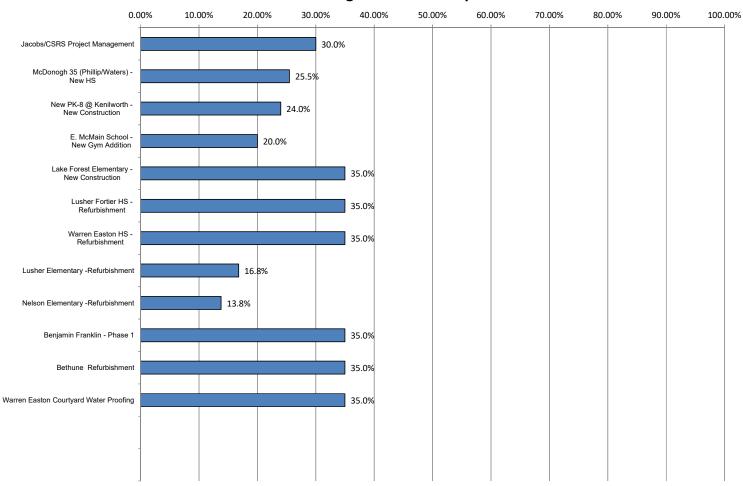

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation - Project Status

(Forecasted dates only include the next project phase)

Benjamin Franklin Elementary School Renovation (OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - Construction Masters Construction Phase

- Phase 2 A & E 100% Construction Documents received and are being
- Demolition is nearing completion
- · Lintel replacement is ongoing

Contractual Substantial Completion Phase 1 – August 2018 Forecasted Substantial Completion Phase 1 – October 2018



Career Technical Education High School at Kerlerec Street CMAR (RSD)

1331 Kerlerec Street, New Orleans, LA 70116 District D Ward 7

Scope of work: Renovation of existing high school

Funding Source – FEMA /CDBG Architect – SCNZ Architects

Contractor - TBD Design Phase

- · A&E is working on Schematic Design
- · CMaR RFQ's are being reviewed



New Cohen High School CMAR (RSD)

3520 Dryades Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Construction of new high school

Funding Source – FEMA Architect – HMS Architects Contractor - TBD

Study Phase

- Discussions are taking place with the Owner to define a final scope of work.
- · CMaR RFQ submissions are under review



4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source - FEMA

Architect – Trapolin Peer Architects Contractor - Core Construction

Construction Phase

- River level delays start by approximately 3 months
- · Pile driving is complete
- · Forming of slab continues
- · Steel is on site and erection has started

Contractual Substantial Completion – Summer 2020 Forecasted Substantial Completion – Summer 2020



New Orleans Charter Science and Mathematics High School

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Construction of new high school

Funding Source - FEMA

Architect – VergesRome Architects Contractor - The McDonnel Group

Construction Phase

- · Contractor has mobilized
- Demolition has begun

Contractual Substantial Completion – Summer 2020 Forecasted Substantial Completion – Summer 2020



John McDonogh High School Renovation CMAR (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source - FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Close out Phase

- Substantially Complete September 6th
- Ribbon Cutting December 4th
- Gymnasium Work continues

Contractual Substantial Completion - October 2018

Actual Substantial Completion - Main Building - September 2018 Forecasted Substantial Completion - Gymnasium - November 2018

Booker T. Washington School CMAR (RSD)

12

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor - Core Construction

Construction Phase

- · Contractor's emphasis is on closing the building envelope
- Exterior brick work continues
- Fireproofing the steel in the auditorium has started
- Steel structure stabilization on the auditorium is complete

Contractual Substantial Completion – January 2019

Forecasted Substantial Completion – May 2019



REFURBISHMENTS

Fisk Howard Exterior Envelope Repairs (RSD)

211 South Lopez Street New Orleans, LA 70119, District B Ward 3

Scope of work: Repairs to exterior

Funding Source - FEMA

Architect - VergesRome Architects

Contractor - TBD Procurement Phase

· Contracts are being reviewed and signed



Harney Elementary School Downspout and Gutter Repairs (RSD)

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of downspouts and gutters

Funding Source – FEMA Architect – Scairono Martinez Contractor - Crescent Commercial

Construction Phase

- · Contractor working on a recovery schedule
- A&E revising drawings for unforeseen conditions

Contractual Substantial Completion – September 2018 Forecasted Substantial Completion – December 2018



Lafayette Elementary School Refurbishment Phase 2 (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not

limited to floor replacement Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Law Industries

Construction Phase

- Substandard containment exposes building to environmental contamination
- General Contractor has been terminated (16th July)
- · Building being assessed for remediation



McDonogh #32 School Refurbishment (RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG Architect – HMS Architects Contractor - TBD Design Phase

· Owner has placed project on hold



McDonogh #42 School Drainage (RSD)

1651 North Tonti Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Site Drainage

Funding Source – Insurance / Tax Credit Architect – Eskew+Dumez+Ripple Contractor - Commander Corporation Construction Phase

- · Contractor is installing sand and gravel at the fence of the play area
- · New Catch basin has been installed

Contractual Substantial Completion – October 2018 Forecasted Substantial Completion – October 2018



Eleanor McMain School Envelope Repairs (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Exterior stucco and window repairs Funding Source – General Fund & Harrah's Architect – Concordia, LLC Contractor – Tuna Construction

Construction Phase

- Exterior painting is underway
- · Contractor is refurbishing wood windows
- Plaster repairs continue

Contractual Substantial Completion – April 2019 Forecasted Substantial Completion – April 2019



Schaumburg Elementary School Roof Repairs (RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA Architect - Scairono Martinez

Contractor - Laperouse Metal Works, Inc

Construction Phase

- · Installation of roof panels continues
- Replacement of interior ceiling has started

Contractual Substantial Completion - August 2018

Forecasted Substantial Completion - December 2018



DEMOLITIONS

Demolition of Modular Buildings at Coghill (RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source - FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - Construction Management Enterprises

Construction Phase

- New site fill is being delivered
- · Concrete paving removal is nearing completion
- Grading of site is underway

Contractual Substantial Completion – August 2018 Forecasted Substantial Completion – December 2018



16

1	Abrams Morial Abramson Coghill Demolition (RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation (RSD)	11/11/2000
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School	(RSD) 06/12/2012
4	A. D. Crossman Elementary School Refurbishment (RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment (RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs (RSD)	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment (RSD)	10/31/2017
8		12/07/2009
9	Agnes Bauduit Elementary School Boiler (RSD)	03/27/2014
9 10	Albert Wicker Elementary School Refurbishment (RSD) Albert Wicker Elementary School Roof Repairs (RSD)	06/13/2013
11	Alfred Lawless Senior (RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing (RSD)	06/15/2011
13	Alice M. Harte Elementary School (OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition (OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement (RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball (RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs (RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels (RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage (RSD)	10/11/2010
20	•	10/11/2010
21	Arthur Ashe Elementary School Kitchen Renovation (OPSB) Augustine Elementary School Roof (RSD)	04/13/2012
22	Avery-Alexander Elementary School (RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition (RSD)	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad (RSD)	10/30/2017
25	Barbara C. Jordan Elementary School Demolition (RSD)	05/30/2011
26	Bell JH Shoring (RSD)	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation (RSD)	00/20/2011
28	Benjamin Franklin Senior High School (OPSB)	08/23/2013
29	Bienville Elementary School Demolition (RSD)	05/04/2009
	(000)	12/13/2015
30	Dooker 1. Washington riigh ochool Environmental Kemedation	
31	Booker 1. Washington riigh School Fartial Demonition	04/07/2013 02/09/2010
32	Carter G. Woodson Middle School Demolition (RSD)	
33 34	Central Services Warehouse Demolition (OPSB)	01/05/2012 07/26/2010
35	Charles J. Colton Elementary Selective Demolition (RSD)	05/23/2013
36	Charles P. Drow Elementary School (RSD)	04/17/2015
37	Charles R. Drew Elementary School (RSD)	06/08/2011
38	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD) Cohen High School Health Clinic ^(RSD)	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell Sch	
40	Demolition of Modular Buildings at Gregory and Abramson (RSD)	06/23/2015
41	Demolition of Modular Buildings at Abramson and Carver (RSD)	01/18/2017
42	Demolition of Modular Buildings at Livingston (RSD)	01/18/2017
43	Douglass High School Under Floor Utilities (RSD)	01/10/2017
44	Dr. Martin Luther King School Roof Repairs (RSD)	06/13/2012
45	Dr. Martin Luther King Jr. School Renovation (RSD)	12/15/2014
70		atus Data: 30 Santambar 2018

	(DSD)	
46	Dwight D. Eisenhower Elementary School Kitchen Refurbishment (RSD)	02/18/2016
47	Dwight D. Eisenhower Elementary School Roof Repairs (RSD)	07/27/2012
48	Dwight D. Eisenhower Elementary School Refurbishment (RSD)	12/23/2015
49	East Bank Swing Space for Audubon Charter School (OPSB)	12/30/2011
50	Edgar P. Harney Elementary School Refurbishment (RSD)	
51	Edgar P. Harney Elementary School Roof Repairs (RSD)	06/13/2012
52	Edna Karr High School - Gymnasium Repair (OPSB)	12/23/2013
53	Edna Karr High School - Assessment (OPSB)	
54	Edward Livingston Middle School Demolition (RSD)	09/28/2010
55	Edward Henry Phillips Junior High School Demolition (OPSB)	11/19/2010
56	New Edward Hynes School (OPSB)	02/06/2012
57	Edwards Hardin Lockett Lawless Demolition (RSD)	11/03/2008
58	Edward Livingston High School (RSD)	01/05/2015
59	Eleanor L. McMain School Replacement of Existing Chillers (OPSB)	08/30/2011
60	Eleanor L. McMain School Clinic (OPSB)	07/24/2013
61	Eleanor L. McMain School Maintenance Upgrades (OPSB)	12/12/2016
62	Eleanor L. McMain School Roof Replacement (OPSB)	05/13/2016
63	Ernest "Dutch" Morial Elementary ^(RSD)	03/17/2017
64	Ernest N. Morial Elementary Security Fencing (RSD)	05/10/2011
65	Fannie C. Williams Elementary School Demolition (RSD)	03/10/2009
66	Fisk-Howard Elementary School Demolition (RSD)	10/04/2011
67	Florence J. Chester Elementary School Demolition (RSD)	06/05/2011
68	Fortier (Lusher) High School Refurbishment (OPSB)	02/05/2016
69	Francis W. Gregory Demolition (RSD)	12/21/2011
70	Frederick A. Douglass High Refurbishment (RSD)	10/28/2014
71	Frederick A. Douglass High School Science Lab (RSD)	07/05/2016
72	Frederick A. Douglass High Switchgear (RSD)	08/04/2009
73	Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)	
74	Gaudet Elementary School Refurbishment (RSD)	12/20/2016
75	Gentilly Terrace Elementary School Refurbishment (RSD)	09/22/2015
76	George Mondy Elementary School Mothball (RSD)	
77	George Washington Carver School (RSD)	03/07/2016
78	George Washington Carver High School Demolition (RSD)	08/24/2011
79	Greater St. Stephens School (OPSB)	03/18/2013
80	Harriet R. Tubman Elementary School Selective Demolition (RSD)	12/14/2014
81	Henry Allen Elementary School Refurbishment (RSD)	03/08/2016
82	Henry Allen Elementary School Kitchen Refurbishment (RSD)	02/18/2016
83	Henry Allen Elementary School Roof (RSD)	05/24/2010
84	Henry C. Schaumburg School Refurbishment (RSD)	06/26/2015
85	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation (RSD)	12/16/2011
86	Holy Cross Modular Relocation (RSD)	12/14/2010
87	Israel M. Augustine Middle School Roof Replacement (RSD)	04/13/2012
88	Israel M. Augustine Middle School Mothball (RSD)	01/18/2013
89	James Derham Demolition (RSD)	02/23/2012
90	James W. Johnson Elementary School Roof (RSD)	07/31/2010
91	New Jean Batiste de Bienville School (RSD)	06/15/2012

18

92	Jean Gordon Elementary School Demolition (RSD)	08/16/2010
93	JoEllen Smith Medical Center Demolition (OPSB)	00/10/2010
94	John Dibert Elementary School Roof (RSD)	08/20/2010
95	John W. Hoffman Elementary School Demolition (RSD)	05/25/2010
96	John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)	11/05/2010
97	John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)	08/05/2011
98	John F. Kennedy Modular Demolition (RSD)	09/16/2014
99	John F. Kennedy High School Demolition (RSD)	01/12/2012
100	John McDonogh Senior High School Bleachers and Sprinklers (RSD)	03/27/2014
101	John McDonogh Senior High School Roof (RSD)	05/04/2010
102	John A. Shaw Elementary School Mothball (RSD)	12/12/2012
103	Joseph S. Clark Senior High School Roof Repairs (RSD)	07/27/2012
	Joseph A. Craig Elementary Canopies (RSD)	06/06/2011
105	Joseph A. Craig Elementary Elevator Installation (RSD)	01/20/2012
106	Joseph A. Hardin Elementary Security Fencing (RSD)	05/10/2011
	Lafayette Elementary School Roof and Masonry (RSD)	06/22/2012
107	Lake Area Landry Demolition (RSD)	05/01/2008
100	Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)	11/13/2015
110	Langston Hughes Elementary School (Phase I) (RSD)	08/11/2009
	Langston Hughes Elementary School - New Gymnasium (Phase II) (RSD)	11/10/2010
	Langston Hughes Elementary School - New Gymnasium (Phase II)	10/12/2012
113	Lawrence D. Crocker Elementary School Demolition (RSD)	04/02/2010
	Laurel Elementary School Refurbishment (RSD)	01/03/2018
	L.B. Landry Annex Demolition (RSD)	05/02/2013
		08/09/2010
117	Little Woods Elementary School Demolition (RSD)	08/01/2013
	,	01/06/2017
	Live Oak Elementary School Refurbishment (RSD) Live Oak Elementary School Roof (RSD)	08/04/2011
	•	08/26/2011
121	Live Oak Elementary School Exterior Door Replacement (RSD)	12/27/2012
122	Louis D. Armstrong Elementary School (RSD)	02/18/2013
123	Lusher Elementary School Refurbishment (OPSB)	10/31/2016
124	Mahalia Jackson Elementary School (OPSB)	05/11/2010
125	Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)	03/06/2012
126	Mahalia Jackson Elementary School Office Renovation (OPSB)	04/30/2013
127	Martin Behrman Elementary School Roof (RSD)	02/23/2010
128	Martin Luther King Jr. Elementary Canopy System (RSD)	11/05/2011
129	Martin Luther King Jr. School Modular Building, Deck, Canopy (RSD)	07/31/2012
130	Martin Luther King Jr. School Kitchen Refurbishment (RSD)	02/18/2016
131		04/17/2013
132	Mary Church Terrell Elementary School Demolition (RSD) Mary M. Bethune Elementary School Refurbishment (OPSB)	10/26/2017
133	Mary M. Bethune Elementary School Refurbishment (OPSB) Mary M. Bethune Elementary 1st Floor Replacement (OPSB)	01/24/2011
134		01/21/2011
135	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB) McDonogh #7 High School Repairs (OPSB)	01/21/2011
136	McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)	06/11/2012
137	McDonogh #28 School Refurbishment (RSD)	03/15/2016
131	wichologi #20 School Kelurbishillent	03/13/2010

19

420	M. D. J. WOO EL J. D. C (RSD)	44/40/2044
138	McDonogh #28 Elementary School Roof (RSD)	11/19/2011
139	McDonogh #32 Roof Replacement (RSD)	02/24/2012
140	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium (OPSB)	01/17/2014
141	McDonogh #35 School at the Phillip/ Waters Site (OPSB)	09/23/2015
142	McDonogh #42 Elementary School Renovation (RSD)	05/28/2015
143	McDonogh #42 Elementary School Roof (RSD)	12/21/2011
144	McDonogh #42 Elementary School HVAC Replacement (RSD)	08/09/2010
145	Mildred C. Osborne Elementary School Demolition (RSD)	02/18/2010
146	Mildred C. Osborne Elementary School (RSD)	12/03/2012
147	Modular Campuses Close Outs (RSD)	
148	Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)	05/22/2013
149	Modular Structures at Langston Hughes Elementary School (RSD)	04/05/2010
150	Morris F.X. Jeff Elementary School Demolition (RSD)	
151	Morris F.X. Jeff Elementary School Mothball (RSD)	01/15/2013
152	Murray G. Henderson Elementary School Roof (RSD)	06/23/2012
153	Nelson Elementary School Refurbishment (OPSB)	04/18/2016
154	New Andrew H. Wilson Elementary School (RSD)	10/11/2009
155	New Carter G. Woodson School (RSD)	09/14/2012
156	New Fannie C. Williams School (RSD)	08/24/2012
157	New Joseph A. Craig Elementary School (RSD)	12/09/2009
158	New L.B. Landry High School (RSD)	06/30/2010
159	New Lake Area High School (RSD)	12/28/2009
160	New Lawrence D. Crocker School (RSD)	04/29/2013
161	New PK-8 School at North Kenilworth Park at Curran Site (OPSB)	01/29/2016
162	New Parkview School (RSD)	10/12/2012
163	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD)	
164	New William Frantz Elementary School (RSD)	
165	New Orleans High School Signature Center Study (RSD)	
166	Oretha C. Haley Demo (RSD)	05/07/2012
167	Oretha C. Haley Elementary School Mothball (RSD)	09/17/2012
168	Parkview Elementary School Demolition (RSD)	08/06/2009
169	Paul L. Dunbar Elementary School Demolition (RSD)	06/16/2010
170	Paul L. Dunbar Elementary School (RSD)	06/02/2015
171	Paul B. Habans Elementary School (RSD)	06/30/2016
172	Paul B. Habans Elementary School Roof Repairs (RSD)	07/27/2012
173	Phillis Wheatley Elementary School Demolition (RSD)	09/26/2011
174	· ······· , -······, -·······, · ········	07/10/2014
175	Ray Abrams Elementary School (RSD)	03/17/2017
176	Rosenwald Elementary School Refurbishment (RSD)	04/07/2016
177	Robert M. Lusher Elementary Roof Removal & Replacement (OPSB)	07/14/2011
178	Samuel J. Green Elementary School Refurbishment (RSD)	02/15/2016
179	Samuel J. Green Elementary School Refurbishment Phase 2 (RSD)	02/15/2016
180	Sarah T. Reed High School Bleachers (RSD)	01/11/2012
181	Sarah T. Reed High School Auditorium Wall (RSD)	03/29/2010
182	Sarah T. Reed High School Kitchen Refurbishment (RSD)	02/18/2016

	(DED)	
	Sarah T. Reed High School Refurbishment (RSD)	12/01/2015
184	3 · · · · · · · · · · · · · · · · · · ·	06/25/2010
185		11/14/2008
186		07/14/2009
187		04/02/2015
188		04/02/2015
189	······································	10/28/2010
190	Sherwood Forest Elementary School (RSD)	06/30/2016
191	Small New Orleans East High School at Abramson (RSD)	09/24/2015
192	Sophie B. Wright School Renovation (RSD)	06/08/2016
193	Sophie B. Wright School Selective Demolition (RSD)	01/31/2014
194	Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)	07/26/2011
195	Stuart R. Bradley Elementary School Demolition (RSD)	01/27/2010
196	Stuart R. Bradley Elementary School (RSD)	06/26/2015
197	Sylvanie Williams Elementary School AHU Replacement (RSD)	07/30/2013
198	(DOD)	09/23/2010
199	Sylvanie Williams Elementary School Roof Repairs (RSD)	07/27/2012
200	Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)	04/13/2012
201	Sylvanie Williams Elementary School Refurbishment (RSD)	02/18/2016
202	(ODOD)	
203	Thomas A. Edison Elementary School Demolition (RSD)	03/25/2010
204	Thomy Lafon Elementary School Demolition (RSD)	11/27/2011
205	Thomy Lafon School Interpretative Display (RSD)	10/15/2013
206	Timbers Park Office Building #1 & #2 Demolition (OPSB)	09/18/2011
207	Timbers HVAC (OPSB)	09/11/2013
208	Timbers III - IT Room Relocation (OPSB)	02/11/2015
209	(DOD)	06/18/2012
	Village de L'est Elementary School Refurbishment (RSD)	10/12/2106
	Village de L'est Elementary School Roof and Modular Demolition (RSD)	06/16/2013
	Vorice J. Waters Elementary School Demolition (RSD)	01/14/2010
	Valena C. Jones Elementary School (RSD)	01/10/2013
	Walter L. Cohen High School HVAC (RSD)	04/04/2014
215	(ODOD)	12/15/2015
216	(ODER)	11/24/2017
217	(ODCD)	09/07/2012
218	(ODOD)	07/11/1931
219	New William J. Guste Elementary School (RSD)	10/06/2008
220	William J. Guste Elementary School Science Lab (RSD)	08/04/2009
221	William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)	04/15/2010
	William Frantz Elementary School Roof (RSD)	08/12/2010
	William Frank Elementary School Roof	00/12/2010

21
