Superintendent's Report December 2018







Dr. Henderson Lewis Jr.Orleans Parish School Board




Mr. John White
Louisiana Department
of Education

Ms. Kunjan Narechania Recovery School District







Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	11
Benjamin Franklin Elementary School Renovation (OPSB)	11
Career Technical Education High School at Kerlerec Street CMaR (RSD)	11
New Cohen High School CMaR (RSD)	11
New Karr High School, CMAR (RSD)	12
New Orleans Charter Science and Mathematics High School (OPSB)	12
Booker T. Washington School CMAR (RSD)	12
REFURBISHMENTS	13
Fisk Howard Exterior Envelope Repairs (RSD)	13
Harney Elementary School Downspout and Gutter Repairs (RSD)	13
Lafayette Elementary School Refurbishment (RSD)	13
Eleanor McMain School Envelope Repairs (OPSB)	14
Schaumburg Elementary School Roof Repairs (RSD)	14
DEMOLITIONS	14
Demolition of Modulars at Coghill (RSD)	14
COMPLETED PROJECTS	15

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$268 million in open contracts for the capital program after issuing \$19 thousand in new contracts, change orders and amendments in December. In addition, the total change orders to date, \$4 million, account for one percent (1.88%) of the total open construction contracts. RSD anticipates issuing \$85 million in construction contracts/change orders, and \$167 thousand in professional service contracts/amendments in January.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$168 million in open contracts for the capital program after issuing \$4 million in new contracts, change orders and amendments in December. In addition, the total change orders to date, \$5.6 million, account for approximately four percent (4.31%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 million in construction contracts/change orders and \$100 thousand in professional service contracts and amendments in January.

2

Community Meetings



Future Community Meetings

3

Bid Openings

Projects which are scheduled to bid in the next 60 days

January 30, 2019

Lafayette Elementary Asbestos Abatement

4



Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 26 projects as of December 31, 2018. The DBE subcontracts value is \$82,553,475 of the \$364,282,325 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 61 projects as of December 31, 2018. The DBE subcontracts value is \$24,319,728 of the \$77,657,520 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of December 31, 2018. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 3 projects as of December 31, 2018. The DBE subcontracts value is \$45,001,673 of the 134,245,850 total of awarded contracts.

Total Amount of Contracts: \$ 685,323,252



New & Renovations:


DBE Contractors secured subcontracts on 17 projects as of December 31, 2018. . The DBE subcontracts value is \$65,999,022 of the \$263,467,831 total of awarded contracts.

Stabilization/Demolition/Mothballing:


DBE Contractors secured subcontracts on 4 projects as of December 31, 2018. The DBE subcontracts value is \$569,422 of the \$1,540,999 total of awarded contracts.

Total Amount of Contracts: \$265,008,830



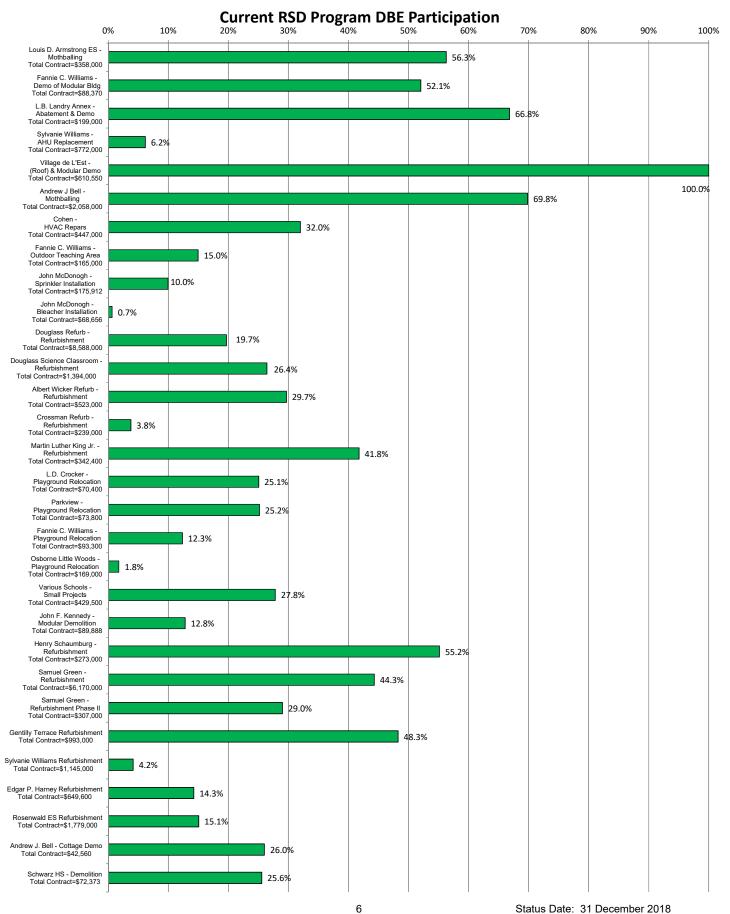

Current RSD Program DBE Participation

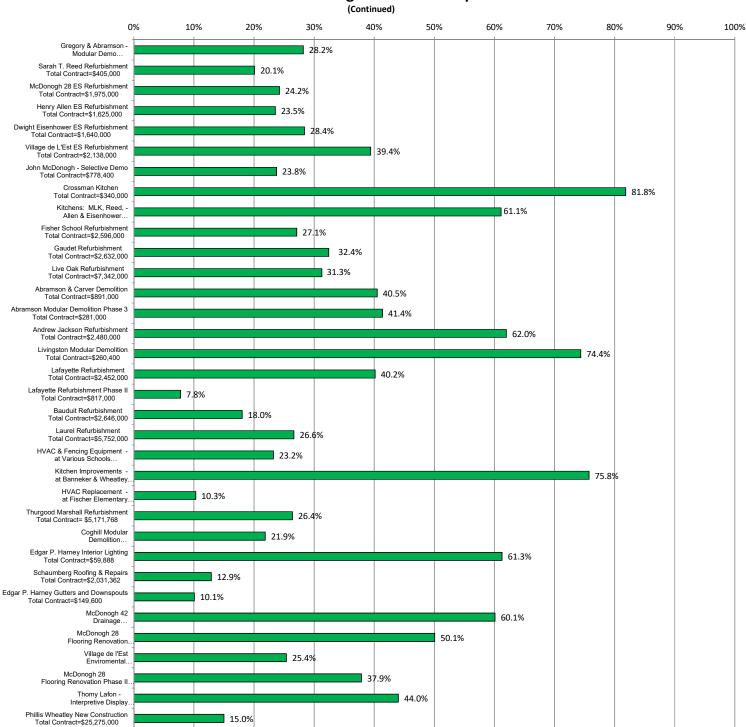


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

7

Current RSD Program DBE Participation

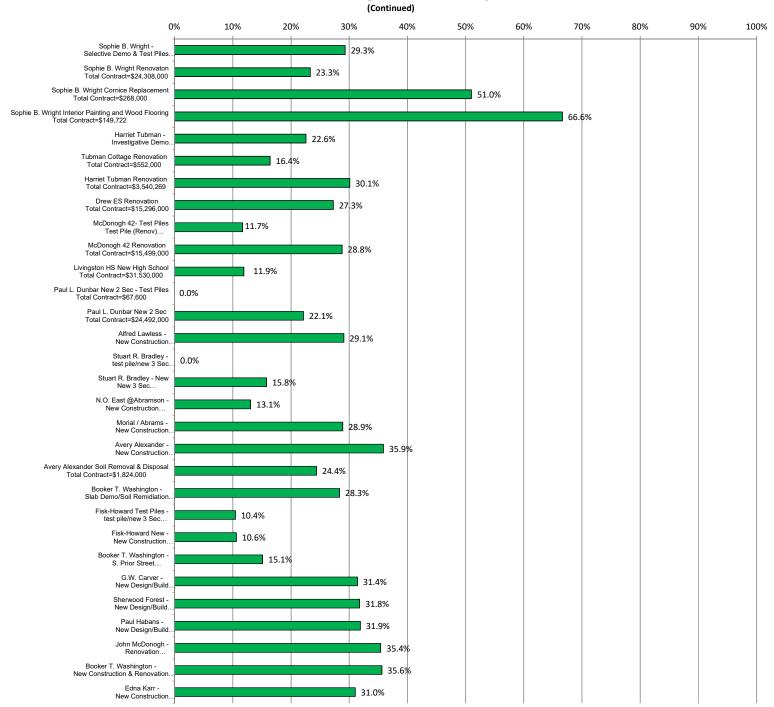


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

8

Current OPSB Program DBE Participation

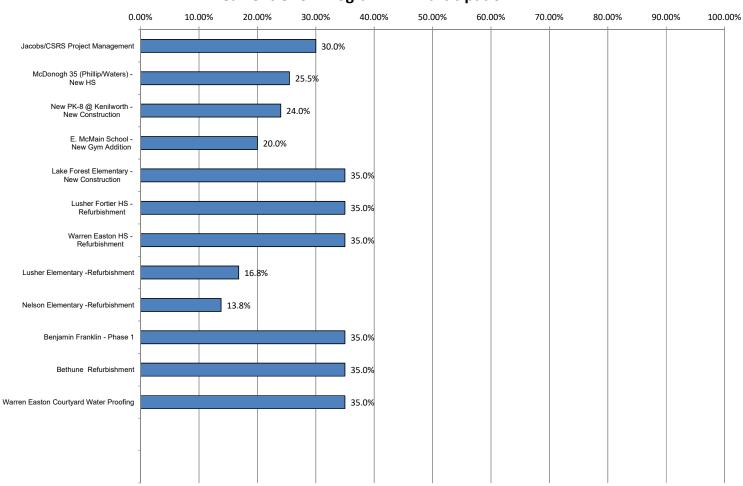

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation - Project Status

(Forecasted dates only include the next project phase)

Benjamin Franklin Elementary School Renovation Phase 2 (OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - Construction Masters

Procurement Phase

- · Bids have been reviewed
- · Contracts are being drafted and reviewed



Career Technical Education High School at Kerlerec Street CMAR (RSD)

1331 Kerlerec Street, New Orleans, LA 70116 District D Ward 7

Scope of work: Renovation of existing high school

Funding Source – FEMA /CDBG Architect – SCNZ Architects

Contractor - TBD <u>Design Phase</u>

- · Schematic Design submission was received and is being reviewed
- CMaR RFQ's are being reviewed



New Cohen High School CMAR (RSD)

3520 Dryades Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Construction of new high school

Funding Source – FEMA Architect – HMS Architects Contractor - TBD

Design Phase

- CMaR RFQ's are being reviewed
- Program Completion phase submission is due February 26th



New Karr High School CMAR (RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source - FEMA

Architect – Trapolin Peer Architects Contractor - Core Construction

Construction Phase

- Structural steel and decking is being installed in areas 4 and 5
- Stud wall framing is underway
- Roofing is starting in Area 2

Contractual Substantial Completion – April 2020 Forecasted Substantial Completion – April 2020



New Orleans Charter Science and Mathematics High School (OPSB)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – VergesRome Architects Contractor - The McDonnel Group

Construction Phase

- · Pile driving is finishing up
- · Pile caps are being formed

Contractual Substantial Completion – January 2021 Forecasted Substantial Completion – January 2021



Booker T. Washington School CMAR (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source - FEMA

Architect - Hewitt-Washington & Associates

Contractor - Core Construction

Construction Phase

- Contractor's emphasis is on closing the auditorium envelope
- Interior finishes are ongoing at the school building
- Brick work continues on auditorium
- · Gymnasium floor installation is complete, bleacher installation has started

Contractual Substantial Completion – June 2019 Forecasted Substantial Completion – June 2019

REFURBISHMENTS

Fisk Howard Exterior Envelope Repairs (RSD)

211 South Lopez Street New Orleans, LA 70119, District B Ward 3

Scope of work: Repairs to exterior

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - LLJ Environmental Construction

Construction Phase

Installation of spray foam is ongoing
 Contractual Substantial Completion – January 2019
 Forecasted Substantial Completion – January 2019



Harney Elementary School Downspout and Gutter Repairs (RSD)

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of downspouts and gutters

Funding Source – FEMA Architect – Scairono Martinez Contractor - Crescent Commercial

Construction Phase

• Gutter installation is 95% complete

Roof panel installation to start in January 2019
 Contractual Substantial Completion – September 2018
 Forecasted Substantial Completion – January 2019



Lafayette Elementary School Refurbishment Phase 2 (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not

limited to floor replacement Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD Procurement Phase

• 1st Advertisement - December 26th

2nd Advertisement - January 2nd

• 3rd Advertisement - January 9th

• Pre-Bid Conference - January 10th

· Bid Opening - January 30th



Eleanor McMain School Envelope Repairs (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Exterior stucco and window repairs Funding Source – General Fund & Harrah's Architect – Concordia, LLC Contractor – Tuna Construction

- <u>Construction Phase</u>
 Exterior painting continues
 - Interior lead abatement around windows is ongoing
 - Plaster repairs on interior lightwells continues

Contractual Substantial Completion – April 2019 Forecasted Substantial Completion – April 2019



Schaumburg Elementary School Roof Repairs (RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA Architect – Scairono Martinez

Contractor - Laperouse Metal Works, Inc

Construction Phase

- · Work on gutters and eaves is ongoing
- Grass seeding is complete

Contractual Substantial Completion – August 2018 Forecasted Substantial Completion – January 2019



DEMOLITIONS

Demolition of Modular Buildings at Coghill (RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - Construction Management Enterprises

Close Out Phase

 Project is Substantial Complete December 26th Contractual Substantial Completion – August 2018 Actual Substantial Completion – December 2018



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition (RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation (RSD)	111112000
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School (RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment (RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment (RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs (RSD)	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment (RSD)	10/31/2017
8	Agnes Bauduit Elementary School Boiler (RSD)	12/07/2009
9	Albert Wicker Elementary School Refurbishment (RSD)	03/27/2014
10	Albert Wicker Elementary School Roof Repairs (RSD)	06/13/2013
11	Alfred Lawless Senior (RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing (RSD)	06/15/2011
13	Alice M. Harte Elementary School (OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition (OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement (RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball (RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs (RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels (RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage (RSD)	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation (OPSB)	
21	Augustine Elementary School Roof (RSD)	04/13/2012
22	Avery-Alexander Elementary School (RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition (RSD)	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad (RSD)	10/30/2017
25	Barbara C. Jordan Elementary School Demolition (RSD)	05/30/2011
26	Bell JH Shoring (RSD)	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation (RSD)	
28	Benjamin Franklin Senior High School (OPSB)	08/23/2013
29	Bienville Elementary School Demolition (RSD)	05/04/2009
30	Booker T. Washington High School Environmental Remediation (RSD)	12/13/2015
31	Booker T. Washington High School Partial Demolition (RSD)	04/07/2013
32	Carter G. Woodson Middle School Demolition (RSD)	02/09/2010
33	Central Services Warehouse Demolition (PSB)	01/05/2012
34	Charles J. Colton Elementary Selective Demolition (RSD)	07/26/2010
35	Charles J. Colton Elementary School (RSD)	05/23/2013
36	Charles R. Drew Elementary School (RSD)	04/17/2015
37	Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)	06/08/2011
38	Cohen High School Health Clinic (RSD)	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School (RSD)	04/22/2015
40 41	Demolition of Modular Buildings at Abramson and Carver (RSD)	06/23/2015 01/18/2017
41	Demolition of Modular Buildings at Abramson and Carver (RSD) Demolition of Modular Buildings at Livingston (RSD)	01/18/2017
42	Douglass High School Under Floor Utilities (RSD)	01/10/2017
73	Douglass High School officer Floor offilities	

4.4	Do Martin Lather War Calcad Dar (RSD)	04/12/2012
44	Dr. Martin Luther King School Roof Repairs (RSD)	06/13/2012
45	Dr. Martin Luther King Jr. School Renovation (RSD)	12/15/2014
46	Dwight D. Eisenhower Elementary School Kitchen Refurbishment (RSD)	02/18/2016
47	Dwight D. Eisenhower Elementary School Roof Repairs (RSD)	07/27/2012
48	Dwight D. Eisenhower Elementary School Refurbishment (RSD)	12/23/2015
49	East Bank Swing Space for Audubon Charter School (OPSB)	12/30/2011
50	Edgar P. Harney Elementary School Refurbishment (RSD)	07/40/0040
51	Edgar P. Harney Elementary School Roof Repairs (RSD)	06/13/2012
52	Edgar P. Harney Elementary School Lighting Repairs (RSD)	08/08/2018
53	Edna Karr High School - Gymnasium Repair (OPSB)	12/23/2013
54	Edna Karr High School - Assessment (OPSB)	
55	Edward Livingston Middle School Demolition (RSD)	09/28/2010
56	Edward Henry Phillips Junior High School Demolition (OPSB)	11/19/2010
57	New Edward Hynes School (OPSB)	02/06/2012
58	Edwards Hardin Lockett Lawless Demolition (RSD)	11/03/2008
59	Edward Livingston High School (RSD)	01/05/2015
60	Eleanor L. McMain School Replacement of Existing Chillers (OPSB)	08/30/2011
61	Eleanor L. McMain School Clinic (OPSB)	07/24/2013
62	Eleanor L. McMain School Maintenance Upgrades (OPSB)	12/12/2016
63	Eleanor L. McMain School Roof Replacement (OPSB)	05/13/2016
64	Ernest "Dutch" Morial Elementary (RSD)	03/17/2017
65	Ernest N. Morial Elementary Security Fencing (RSD)	05/10/2011
66	Fannie C. Williams Elementary School Demolition (RSD)	03/10/2009
67	Fisk-Howard Elementary School Demolition (RSD)	10/04/2011
68	Florence J. Chester Elementary School Demolition (RSD)	06/05/2011
69	Fortier (Lusher) High School Refurbishment (OPSB)	02/05/2016
70	Francis W. Gregory Demolition (RSD)	12/21/2011
71	Frederick A. Douglass High Refurbishment (RSD)	10/28/2014
72	Frederick A. Douglass High School Science Lab (RSD)	07/05/2016
73	Frederick A. Douglass High Switchgear (RSD)	08/04/2009
74	Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)	
75	Gaudet Elementary School Refurbishment (RSD)	12/20/2016
76	Gentilly Terrace Elementary School Refurbishment (RSD)	09/22/2015
77	George Mondy Elementary School Mothball (RSD)	
78	George Washington Carver School (RSD)	03/07/2016
79	George Washington Carver High School Demolition (RSD)	08/24/2011
80	Greater St. Stephens School (OPSB)	03/18/2013
81	Harriet R. Tubman Elementary School Selective Demolition (RSD)	12/14/2014
82	Harriet R. Tubman Elementary School Renovation (RSD)	08/01/2018
83	Harriet R. Tubman Cottage Renovation (RSD)	08/02/2018
84	Henry Allen Elementary School Refurbishment (RSD)	03/08/2016
85	Henry Allen Elementary School Kitchen Refurbishment (RSD)	02/18/2016
86	Henry Allen Elementary School Roof (RSD)	05/24/2010
87	Henry C. Schaumburg School Refurbishment (RSD)	06/26/2015
88	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation (RSD)	12/16/2011
89	Holy Cross Modular Relocation (RSD)	12/14/2010
٠,	1101) 0.000 modului ttorovation	, . ,,

00	James I. M. Assessation Middle Calcast Don't Don't Don't Carry (RSD)	04/12/2012
90	Israel M. Augustine Middle School Roof Replacement (RSD)	04/13/2012
91	Israel M. Augustine Middle School Mothball (RSD)	01/18/2013
92	James Derham Demolition (RSD)	02/23/2012
93	James W. Johnson Elementary School Roof (RSD)	07/31/2010
94	New Jean Batiste de Bienville School (RSD)	06/15/2012
95 07	Jean Gordon Elementary School Demolition (RSD)	08/16/2010
96	JoEllen Smith Medical Center Demolition (OPSB)	00/00/0010
97	John Dibert Elementary School Roof (RSD)	08/20/2010
98	John W. Hoffman Elementary School Demolition (RSD)	05/25/2010
99	John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)	11/05/2010
100	John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)	08/05/2011
101	John F. Kennedy Modular Demolition (RSD)	09/16/2014
102	John F. Kennedy High School Demolition (RSD)	01/12/2012
103	John McDonogh Senior High School Bleachers and Sprinklers (RSD)	03/27/2014
104	John McDonogh Senior High School Roof (RSD)	05/04/2010
105	John A. Shaw Elementary School Mothball (RSD)	12/12/2012
106	Joseph S. Clark Senior High School Roof Repairs (RSD)	07/27/2012
107	Joseph A. Craig Elementary Canopies (RSD)	06/06/2011
108	Joseph A. Craig Elementary Elevator Installation (RSD)	01/20/2012
	Joseph A. Hardin Elementary Security Fencing (RSD)	05/10/2011
110	Lafayette Elementary School Roof and Masonry (RSD)	06/22/2012
111	Lake Area Landry Demolition (RSD)	05/01/2008
112	Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)	11/13/2015
	Langston Hughes Elementary School (Phase I) (RSD)	08/11/2009
	Langston Hughes Elementary School - New Gymnasium (Phase II) (RSD)	11/10/2010
115	Langston Hughes Elementary School - Dumpster Pad (RSD)	10/12/2012
116	Lawrence D. Crocker Elementary School Demolition (RSD)	04/02/2010
117	Laurel Elementary School Refurbishment (RSD)	01/03/2018
118	L.B. Landry Annex Demolition (RSD)	05/02/2013
	Little Woods Elementary School Demolition (RSD)	08/09/2010
120	Little Woods School (Dolores T. Aaron Elementary School) (RSD)	08/01/2013
121	Live Oak Elementary School Refurbishment (RSD)	01/06/2017
122	Live Oak Elementary School Roof (RSD)	08/04/2011
123	Live Oak Elementary School Exterior Door Replacement (RSD)	08/26/2011
124	Lorraine Hansberry Elementary School Mothball (RSD)	12/27/2012
125	Louis D. Armstrong Elementary School (RSD)	02/18/2013
126	Lusher Elementary School Refurbishment (OPSB)	10/31/2016
127	Mahalia Jackson Elementary School (OPSB)	05/11/2010
128	Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)	03/06/2012
129	Mahalia Jackson Elementary School Office Renovation (OPSB)	04/30/2013
130	Martin Behrman Elementary School Roof (RSD)	02/23/2010
131	Martin Luther King Jr. Elementary Canopy System (RSD)	11/05/2011
132	Martin Luther King Jr. School Modular Building, Deck, Canopy (RSD)	07/31/2012
133	Martin Luther King Jr. School Kitchen Refurbishment (RSD)	02/18/2016
134	Mary Church Terrell Elementary School Demolition (RSD)	04/17/2013
135	Mary M. Bethune Elementary School Refurbishment (OPSB)	10/26/2017
	,	

407	(ADSR)	04/04/0044
136	The state of the s	01/24/2011
137	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)	01/21/2011
138	McDonogh #7 High School Repairs (OPSB)	
139	McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)	06/11/2012
140	McDonogh #28 School Refurbishment (RSD)	03/15/2016
141	McDonogh #28 Elementary School Roof (RSD)	11/19/2011
142	McDonogh #32 Roof Replacement (RSD)	02/24/2012
143	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior	01/17/2014
110	Ramp & Handicap Seating in the Auditorium (OPSB)	01/1//2011
144	McDonogh #35 School at the Phillip/ Waters Site (OPSB)	09/23/2015
145	McDonogh #42 Elementary School Renovation (RSD)	05/28/2015
146	McDonogh #42 Elementary School Roof (RSD)	12/21/2011
147	McDonogh #42 Elementary School HVAC Replacement (RSD)	08/09/2010
148	Mildred C. Osborne Elementary School Demolition (RSD)	02/18/2010
149	Mildred C. Osborne Elementary School (RSD)	12/03/2012
150	Modular Campuses Close Outs (RSD)	
151	Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)	05/22/2013
152	3 3	04/05/2010
153	Morris F.X. Jeff Elementary School Demolition (RSD)	
154	Morris F.X. Jeff Elementary School Mothball (RSD)	01/15/2013
155	Murray G. Henderson Elementary School Roof (RSD)	06/23/2012
156		04/18/2016
157	New Andrew H. Wilson Elementary School (RSD)	10/11/2009
158	New Carter G. Woodson School (RSD)	09/14/2012
159		08/24/2012
160		12/09/2009
161	(DOD)	06/30/2010
162	New Lake Area High School (RSD)	12/28/2009
163	New Lawrence D. Crocker School (RSD)	04/29/2013
164	New PK-8 School at North Kenilworth Park at Curran Site (OPSB)	01/29/2016
165		10/12/2012
166	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD)	
167	New William Frantz Elementary School (RSD)	
168	New Orleans High School Signature Center Study (RSD)	
169	Oretha C. Haley Demo (RSD)	05/07/2012
170	Oretha C. Haley Elementary School Mothball (RSD)	09/17/2012
171	Parkview Elementary School Demolition (RSD)	08/06/2009
172	(DCD)	06/16/2010
173	(DCD)	06/02/2015
174	(DCD)	06/30/2016
175	(DOD)	07/27/2012
176	Phillis Wheatley Elementary School Demolition (RSD)	09/26/2011
177	Phillis Wheatley Elementary School (RSD)	07/10/2014
178	Ray Abrams Elementary School (RSD)	03/17/2017
179	Rosenwald Elementary School Refurbishment (RSD)	04/07/2016
180	Robert M. Lusher Elementary Roof Removal & Replacement (OPSB)	07/14/2011

404	(RSD)	00/45/004/
	Samuel J. Green Elementary School Refurbishment (RSD)	02/15/2016
	Samuel J. Green Elementary School Refurbishment Phase 2 (RSD)	02/15/2016
	Sarah T. Reed High School Bleachers (RSD)	01/11/2012
184	3	03/29/2010
185		02/18/2016
186	J	12/01/2015
187		06/25/2010
188		11/14/2008
189	· ·	07/14/2009
190	Schwarz Alternative Modulars Demolition (RSD)	04/02/2015
191	3 · · · · · · · · · · · · · · · · · · ·	04/02/2015
	Sherwood Forest Elementary School Demolition (RSD)	10/28/2010
193	Sherwood Forest Elementary School (RSD)	06/30/2016
194	Small New Orleans East High School at Abramson (RSD)	09/24/2015
195	Sophie B. Wright School Renovation (RSD)	06/08/2016
196	\mathbf{I}	01/31/2014
197	Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)	07/26/2011
198	Stuart R. Bradley Elementary School Demolition (RSD)	01/27/2010
199	Stuart R. Bradley Elementary School (RSD)	06/26/2015
200	Sylvanie Williams Elementary School AHU Replacement (RSD)	07/30/2013
201	Sylvanie Williams Elementary School Play Yard (RSD)	09/23/2010
202	Sylvanie Williams Elementary School Roof Repairs (RSD)	07/27/2012
203	Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)	04/13/2012
204	Sylvanie Williams Elementary School Refurbishment (RSD)	02/18/2016
205	Temporary Campus for McDonogh #11 Expropriation (OPSB)	
	Thomas A. Edison Elementary School Demolition (RSD)	03/25/2010
207	Thomy Lafon Elementary School Demolition (RSD)	11/27/2011
208	Thomy Lafon School Interpretative Display (RSD)	10/15/2013
209	Thurgood Marshall Elementary School Refurbishment (RSD)	08/10/2018
210	Timbers Park Office Building #1 & #2 Demolition (OPSB)	09/18/2011
211	Timbers HVAC (OPSB)	09/11/2013
212	Timbers III - IT Room Relocation (OPSB)	02/11/2015
213	Village de L'est Elementary School Subsidence (RSD)	06/18/2012
214	Village de L'est Elementary School Refurbishment (RSD)	10/12/2106
215	Village de L'est Elementary School Roof and Modular Demolition (RSD)	06/16/2013
216	Vorice J. Waters Elementary School Demolition (RSD)	01/14/2010
217	(DCD)	01/10/2013
218	(DCD)	04/04/2014
219	(ODCD)	12/15/2015
220	Warren Easton School Courtyard Waterproofing (OPSB)	11/24/2017
221	Warren Easton High School Window Replacement (OPSB)	09/07/2012
222	(ODCD)	07/11/1931
223	New William J. Guste Elementary School (RSD)	10/06/2008
224	(DCD)	08/04/2009
225	William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)	04/15/2010
	William Frantz Elementary School Roof (RSD)	08/12/2010
220	William France Elementary School (1901)	3011212010
