Superintendent's Report June 2020







Dr. Cade BrumleyLouisiana Department
of Education





Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
FUTURE COMMUNITY MEETINGS	3
BID OPENINGS	3
DBE OVERVIEW MONTHLY SUMMARY	4
NEW & MAJOR RENOVATION	9
Behrman Elementary School CMaR (RSD)	9
Career Technical Education High School at Kerlerec Street CMaR (RSD)	9
New Cohen High School CMaR (RSD)	9
New Karr High School, CMAR (RSD)	10
Lafayette Elementary School Renovation (RSD)	10
Booker T. Washington School CMAR (RSD)	10
Sarah T. Reed Modular Demolition (RSD)	11
COMPLETED PROJECTS	12

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$256 million in open contracts for the capital program after issuing \$10.3 million in new contracts, change orders and amendments in June. In addition, the total change orders to date, \$3.7 million, account for one percent (1.89%) of the total open construction contracts. RSD anticipates issuing \$95.5 million in construction contracts/change orders, and \$389 thousand in professional service contracts/amendments in July.

Status Date: June 30, 2020

Future Community Meetings

None Scheduled

Bid Openings

None Scheduled



Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 27 projects as of June 30, 2020. The DBE subcontracts value is \$83,897,632 of the \$372,057,325 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 65 projects as of June 30, 2020. The DBE subcontracts value is \$24,730,053 of the \$78,177,771 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of June 30, 2020. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.


CMAR New:

DBE Contractors secured subcontracts on 5 projects as of June 30, 2020. The DBE subcontracts value is \$51,254,998 of the \$146,019,056 total of awarded contracts.

Total Amount of Contracts: \$705,391,709

4


^{*} DBE provisions were included in projects bid after June 30, 2012

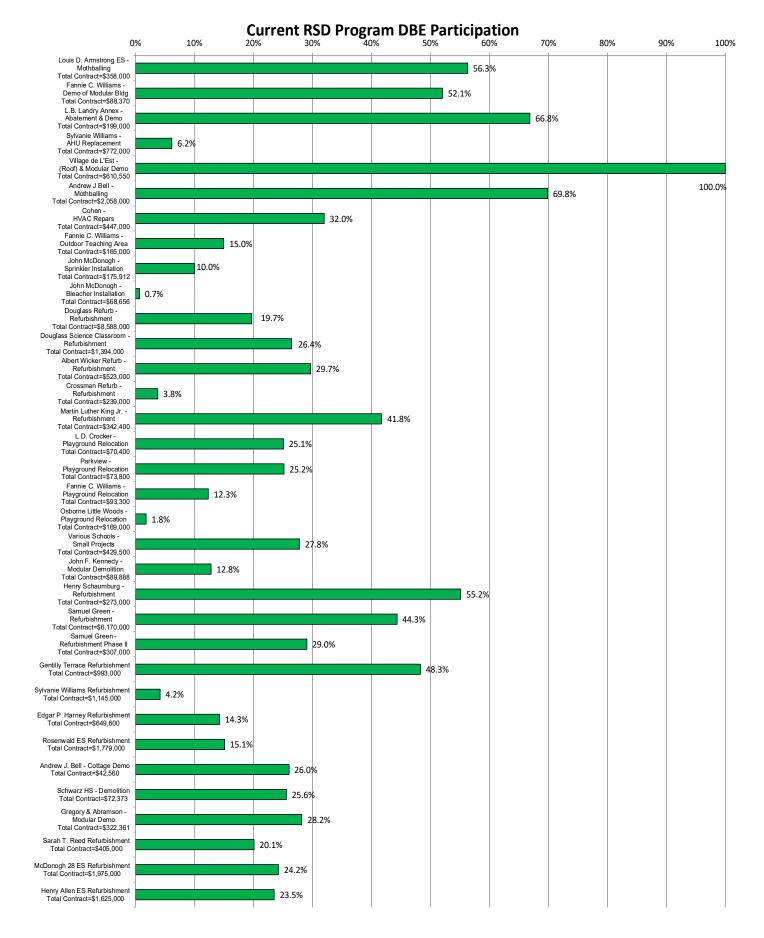

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

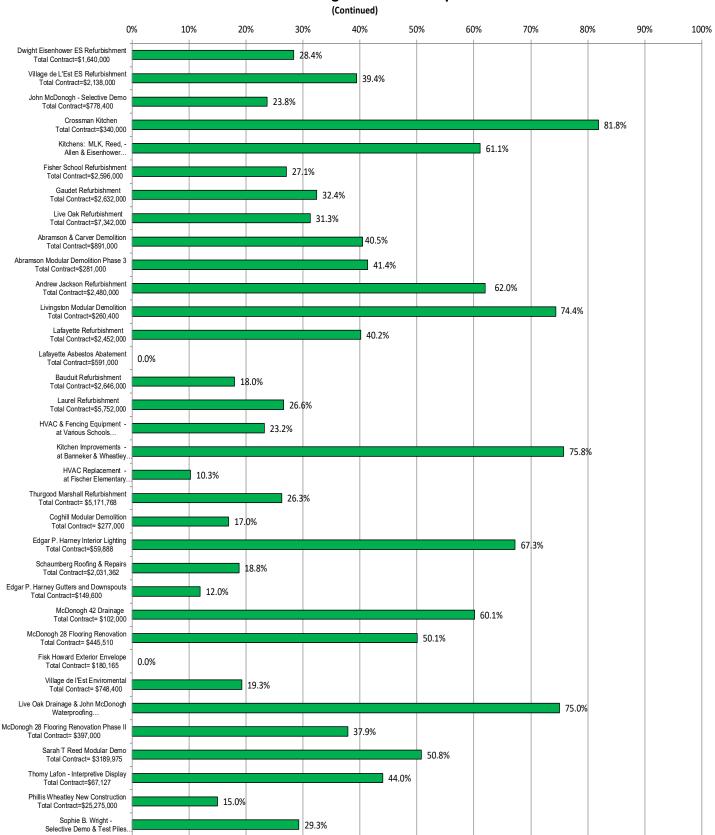

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Current RSD Program DBE Participation

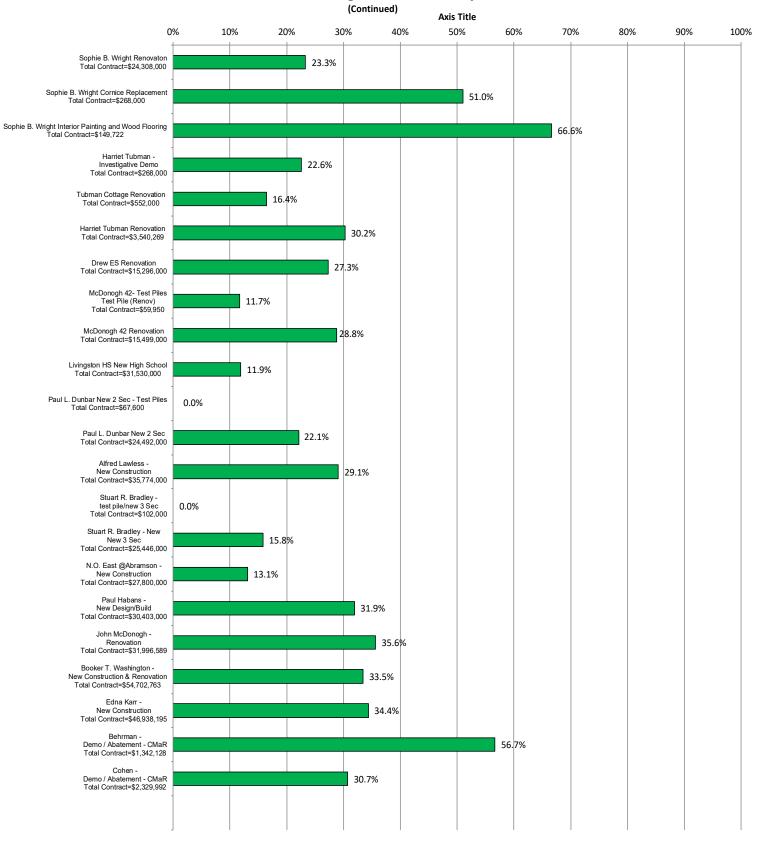

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Behrm	
0	
Scope o Funding	
Architect	
Contract <u>Design F</u>	
• A	
• S • F	
Career	
Scope o	
Funding	
Architect Contract	
<u>Design</u> F	
• C	
• 0	
• D	
New C	
Scope o Funding	
Architect	
Contract <u>Design F</u>	
• A	
• G • D	
• N	

9

4400 G	
Scope of wo	
Funding So	
Architect T	
Architect – T	
Contractor -	
Close Out P	
• Contr	
L	
2727 S	
Scope of wo	
Funding So	
Architect – N	
Contractor -	
<u>Procuremen</u>	
• Notice	
• Contr	
1201	
Scope of wo	
school	
Funding Sol	
Funding Sol Architect – H	
Contractor -	
Construction	
• Interp	
• Hand	
• Painti	
• Stage	
• Punc	
Contractual	
Forecasted	

Sarah T. Reed Modular Demolition (RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Demolition of existing modulars

Funding Source – FEMA
Architect – Scairono Martinez Architects
Contractor – Insultech
Construction Phase

- Contractor started canopy removal
- · Building removal to start in September

Contractual Substantial Completion – November 2020 Forecasted Substantial Completion – November 2020



Status Date: June 30, 2020

Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition (RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation (RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School (RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment (RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment (RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs (RSD)	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment (RSD)	10/31/2017
8	Agnes Bauduit Elementary School Boiler (RSD)	12/07/2009
9	Albert Wicker Elementary School Refurbishment (RSD)	03/27/2014
10	Albert Wicker Elementary School Roof Repairs (RSD)	06/13/2013
11	Alfred Lawless Senior (RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing (RSD)	06/15/2011
13	Alice M. Harte Elementary School (OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition (OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement (RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball (RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs (RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels (RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage (RSD)	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation (OPSB)	
21	Augustine Elementary School Roof (RSD)	04/13/2012
22	Avery-Alexander Elementary School (RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition (RSD)	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad (RSD)	10/30/2017
25	Barbara C. Jordan Elementary School Demolition (RSD)	05/30/2011
26	Bell JH Shoring (RSD)	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation (RSD)	
28	Benjamin Franklin Senior High School (OPSB)	08/23/2013
29	Bienville Elementary School Demolition (RSD)	05/04/2009
30	Booker T. Washington High School Environmental Remediation (RSD)	12/13/2015
31	Booker T. Washington High School Partial Demolition (RSD)	04/07/2013
32	Carter G. Woodson Middle School Demolition (RSD)	02/09/2010
33	Central Services Warehouse Demolition (OPSB)	01/05/2012
34	Charles J. Colton Elementary Selective Demolition (RSD)	07/26/2010
35	Charles J. Colton Elementary School (RSD)	05/23/2013
36	Charles R. Drew Elementary School (RSD)	04/17/2015
37	Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)	06/08/2011
38	Cohen High School Health Clinic (RSD)	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School (RSD)	
40	Demolition of Modular Buildings at Coghill (RSD)	12/26/2018
41	Demolition of Modular Buildings at Gregory and Abramson (RSD)	06/23/2015
42	Demolition of Modular Buildings at Abramson and Carver (RSD)	01/18/2017

40	(RSD)	04/40/0047
43	Demolition of Modular Buildings at Livingston (RSD)	01/18/2017
44	Douglass High School Under Floor Utilities (RSD)	00/40/0040
45 46	Dr. Martin Luther King School Roof Repairs (RSD)	06/13/2012 12/15/2014
	Dr. Martin Luther King Jr. School Renovation (RSD)	
47	Dwight D. Eisenhower Elementary School Kitchen Refurbishment (RSD)	02/18/2016
48	Dwight D. Eisenhower Elementary School Roof Repairs (RSD)	07/27/2012
49	Dwight D. Eisenhower Elementary School Refurbishment (RSD)	12/23/2015
50	East Bank Swing Space for Audubon Charter School (PSD)	12/30/2011
51	Edgar P. Harney Elementary School Refurbishment (RSD)	00/40/0040
52	Edgar P. Harney Elementary School Roof Repairs (RSD)	06/13/2012
53	Edgar P. Harney Elementary School Downspouts and Gutters (RSD)	01/09/2019
54	Edgar P. Harney Elementary School Lighting Repairs (RSD)	08/08/2018
55	Edna Karr High School - Gymnasium Repair (OPSB)	12/23/2013
56	Edna Karr High School - Assessment (OPSB)	
57	Edward Livingston Middle School Demolition (RSD)	09/28/2010
58	Edward Henry Phillips Junior High School Demolition (OPSB)	11/19/2010
59	New Edward Hynes School (OPSB)	02/06/2012
60	Edwards Hardin Lockett Lawless Demolition (RSD)	11/03/2008
61	Edward Livingston High School (RSD)	01/05/2015
62	Eleanor L. McMain School Replacement of Existing Chillers (OPSB)	08/30/2011
63	Eleanor L. McMain School Clinic (OPSB)	07/24/2013
64	Eleanor L. McMain School Maintenance Upgrades (OPSB)	12/12/2016
65	Eleanor L. McMain School Roof Replacement (OPSB)	05/13/2016
66	Ernest "Dutch" Morial Elementary (RSD)	03/17/2017
67	Ernest N. Morial Elementary Security Fencing (RSD)	05/10/2011
68	Fannie C. Williams Elementary School Demolition (RSD)	03/10/2009
69	Fisk-Howard Elementary School Demolition (RSD)	10/04/2011
70	Florence J. Chester Elementary School Demolition (RSD)	06/05/2011
71	Fortier (Lusher) High School Refurbishment (OPSB)	02/05/2016
72	Francis W. Gregory Demolition (RSD)	12/21/2011
73	Frederick A. Douglass High Refurbishment (RSD)	10/28/2014
74	Frederick A. Douglass High School Science Lab (RSD)	07/05/2016
75	Frederick A. Douglass High Switchgear (RSD)	08/04/2009
76	Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)	
77	Gaudet Elementary School Refurbishment (RSD)	12/20/2016
78	Gentilly Terrace Elementary School Refurbishment (RSD)	09/22/2015
79	George Mondy Elementary School Mothball (RSD)	
80	George Washington Carver School (RSD)	03/07/2016
81	George Washington Carver High School Demolition (RSD)	08/24/2011
82	Greater St. Stephens School (OPSB)	03/18/2013
83	Harriet R. Tubman Elementary School Selective Demolition (RSD)	12/14/2014
84	Harriet R. Tubman Elementary School Renovation (RSD)	08/01/2018
85	Harriet R. Tubman Cottage Renovation (RSD)	08/02/2018
86	Henry Allen Elementary School Refurbishment (RSD)	03/08/2016
87	Henry Allen Elementary School Kitchen Refurbishment (RSD)	02/18/2016
88	Henry Allen Elementary School Roof (RSD)	05/24/2010
	,,	

89	Henry C. Schaumburg School Refurbishment (RSD)	06/26/2015
90	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation (RSD)	12/16/2011
91	Holy Cross Modular Relocation (RSD)	12/14/2010
92	Israel M. Augustine Middle School Roof Replacement (RSD)	04/13/2012
93	Israel M. Augustine Middle School Mothball (RSD)	01/18/2013
94	James Derham Demolition (RSD)	02/23/2012
95		07/31/2010
96	James W. Johnson Elementary School Roof (RSD)	06/15/2012
97	New Jean Batiste de Bienville School (RSD)	08/16/2010
	Jean Gordon Elementary School Demolition (RSD)	00/10/2010
98	JoEllen Smith Medical Center Demolition (OPSB)	00/20/2040
99	John Dibert Elementary School Roof (RSD)	08/20/2010
100	John W. Hoffman Elementary School Demolition (RSD)	05/25/2010
101	John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)	11/05/2010
	John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)	08/05/2011
103	John F. Kennedy Modular Demolition (RSD)	09/16/2014
104	oom of the same of	01/12/2012
	John McDonogh Senior High School Bleachers and Sprinklers (RSD)	03/27/2014
106	John McDonogh Senior High School Roof (RSD)	05/04/2010
107	John 7. Char Elementary Concor Methodi	12/12/2012
108	occopii di diani domoi mgii domoi nooi nopamb	07/27/2012
	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
110	Joseph A. Craig Elementary Elevator Installation (RSD)	01/20/2012
111	Joseph A. Hardin Elementary Security Fencing (RSD)	05/10/2011
112	Lafayette Elementary School Roof and Masonry (RSD)	06/22/2012
113	Lake Area Landry Demolition (RSD)	05/01/2008
114	Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)	11/13/2015
115	Langston Hughes Elementary School (Phase I) (RSD)	08/11/2009
116	Langston Hughes Elementary School - New Gymnasium (Phase II) (RSD)	11/10/2010
	Langston Hughes Elementary School - Dumpster Pad (RSD)	10/12/2012
118	Lawrence D. Crocker Elementary School Demolition (RSD)	04/02/2010
119	Laurel Elementary School Refurbishment (RSD)	01/03/2018
120	L.B. Landry Annex Demolition (RSD)	05/02/2013
	Little Woods Elementary School Demolition (RSD)	08/09/2010
	Little Woods School (Dolores T. Aaron Elementary School) (RSD)	08/01/2013
	Live Oak Elementary School Refurbishment (RSD)	01/06/2017
	Live Oak Elementary School Roof (RSD)	08/04/2011
	Live Oak Elementary School Exterior Door Replacement (RSD)	08/26/2011
	Lorraine Hansberry Elementary School Mothball (RSD)	12/27/2012
127	(DOD)	02/18/2013
128	Lusher Elementary School Refurbishment (OPSB)	10/31/2016
129	Mahalia Jackson Elementary School (OPSB)	05/11/2010
130	Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)	03/06/2012
131	Mahalia Jackson Elementary School Office Renovation (OPSB)	04/30/2013
132	Martin Behrman Elementary School Roof (RSD)	02/23/2010
133	Martin Luther King Jr. Elementary Canopy System (RSD)	11/05/2011
134	(000)	07/31/2012
	maran Easter rang on contour modular ballang, bear, callopy	

135	Martin Luther King Jr. School Kitchen Refurbishment (RSD)	02/18/2016
136	Mary Church Terrell Elementary School Demolition (RSD)	04/17/2013
137	Mary M. Bethune Elementary School Refurbishment (OPSB)	10/26/2017
138	Mary M. Bethune Elementary 1st Floor Replacement (OPSB)	01/24/2011
139	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)	01/21/2011
140	McDonogh #7 High School Repairs (OPSB)	
141	McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)	06/11/2012
142		03/15/2016
143	McDonogh #28 Elementary School Roof (RSD)	11/19/2011
144	McDonogh #32 Roof Replacement (RSD)	02/24/2012
445	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior	04/47/2044
145	Ramp & Handicap Seating in the Auditorium (OPSB)	01/17/2014
146	McDonogh #35 School at the Phillip/ Waters Site (OPSB)	09/23/2015
147	McDonogh #42 Elementary School Renovation (RSD)	05/28/2015
148	McDonogh #42 Elementary School Roof (RSD)	12/21/2011
149	McDonogh #42 Elementary School HVAC Replacement (RSD)	08/09/2010
150	Mildred C. Osborne Elementary School Demolition (RSD)	02/18/2010
151	Mildred C. Osborne Elementary School (RSD)	12/03/2012
152	Modular Campuses Close Outs (RSD)	
153	Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)	05/22/2013
154	Modular Structures at Langston Hughes Elementary School (RSD)	04/05/2010
155	Morris F.X. Jeff Elementary School Demolition (RSD)	
156	Morris F.X. Jeff Elementary School Mothball (RSD)	01/15/2013
157		06/23/2012
158	Nelson Elementary School Refurbishment (OPSB)	04/18/2016
159	New Andrew H. Wilson Elementary School (RSD)	10/11/2009
160		09/14/2012
161	New Fannie C. Williams School (RSD)	08/24/2012
162	New Joseph A. Craig Elementary School (RSD)	12/09/2009
	New L.B. Landry High School (RSD)	06/30/2010
	New Lake Area High School (RSD)	12/28/2009
	New Lawrence D. Crocker School (RSD)	04/29/2013
166	(2-2-)	01/29/2016
167	(===)	10/12/2012
168	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD)	
169	New William Frantz Elementary School (RSD)	
170	New Orleans High School Signature Center Study (RSD)	
171	Oretha C. Haley Demo (RSD)	05/07/2012
172	Oretha C. Haley Elementary School Mothball (RSD)	09/17/2012
	Parkview Elementary School Demolition (RSD)	08/06/2009
	Paul L. Dunbar Elementary School Demolition (RSD)	06/16/2010
	Paul L. Dunbar Elementary School (RSD)	06/02/2015
	Paul B. Habans Elementary School (RSD)	06/30/2016
	Paul B. Habans Elementary School Roof Repairs (RSD)	07/27/2012
178	(DOD)	09/26/2011
179	Phillis Wheatley Elementary School (RSD)	07/10/2014
	•	

180	Down Allerson Element (SSD)	03/17/2017
181	Ray Abrams Elementary School (RSD)	04/07/2016
	Rosenwald Elementary School Refurbishment (RSD)	07/14/2011
	Robert M. Lusher Elementary Roof Removal & Replacement (OPSB) Samuel J. Green Elementary School Refurbishment (RSD)	02/15/2016
	Samuel J. Green Elementary School Refurbishment Phase 2 (RSD)	02/15/2016
185		02/13/2010
	Sarah T. Reed High School Bleachers (RSD)	
186	Sarah T. Reed High School Auditorium Wall (RSD)	03/29/2010 02/18/2016
187		
188	Sarah T. Reed High School Refurbishment (RSD)	12/01/2015
189	Seabrook Computer Training Center Demolition (OPSB)	06/25/2010
190	onium and on more	11/14/2008
	Schaumburg Elementary School Roof Repairs (RSD)	05/09/2019
	Schwarz Alternative Repairs (RSD)	07/14/2009
	Schwarz Alternative Modulars Demolition (RSD)	04/02/2015
	Schwarz Modular Building Demolition (RSD)	04/02/2015
	Sherwood Forest Elementary School Demolition (RSD)	10/28/2010
196	Sherwood Forest Elementary School (RSD)	06/30/2016
	Small New Orleans East High School at Abramson (RSD)	09/24/2015
198	Sophie B. Wright School Renovation (RSD)	06/08/2016
199	Sophie B. Wright School Selective Demolition (RSD)	01/31/2014
200	Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)	07/26/2011
201	Stuart R. Bradley Elementary School Demolition (RSD)	01/27/2010
202	Stuart R. Bradley Elementary School (RSD)	06/26/2015
203	Sylvanie Williams Elementary School AHU Replacement (RSD)	07/30/2013
204	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
	Sylvanie Williams Elementary School Roof Repairs (RSD)	07/27/2012
206	Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)	04/13/2012
207	Sylvanie Williams Elementary School Refurbishment (RSD)	02/18/2016
208	Temporary Campus for McDonogh #11 Expropriation (OPSB)	
209	Thomas A. Edison Elementary School Demolition (RSD)	03/25/2010
210	Thomy Lafon Elementary School Demolition (RSD)	11/27/2011
211	Thomy Lafon School Interpretative Display (RSD)	10/15/2013
212	Thurgood Marshall Elementary School Refurbishment (RSD)	08/10/2018
213	Timbers Park Office Building #1 & #2 Demolition (OPSB)	09/18/2011
214	Timbers HVAC (OPSB)	09/11/2013
215	Timbers III - IT Room Relocation (OPSB)	02/11/2015
216	Village de L'est Elementary School Subsidence (RSD)	06/18/2012
217	Village de L'est Elementary School Refurbishment (RSD)	10/12/2106
218	Village de L'est Elementary School Roof and Modular Demolition (RSD)	06/16/2013
	Vorice J. Waters Elementary School Demolition (RSD)	01/14/2010
	Valena C. Jones Elementary School (RSD)	01/10/2013
221	Walter L. Cohen High School HVAC (RSD)	04/04/2014
222	Warren Easton High School Renovation (OPSB)	12/15/2015
	Warren Easton School Courtyard Waterproofing (OPSB)	11/24/2017
	Warren Easton High School Window Replacement (OPSB)	09/07/2012
	West Bank Swing Space for Alice Harte Elementary School (OPSB)	07/11/1931
	3	


226	New William J. Guste Elementary School (RSD)	10/06/2008
227	William J. Guste Elementary School Science Lab (RSD)	08/04/2009
228	William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)	04/15/2010
229	William Frantz Elementary School Roof (RSD)	08/12/2010




RSD Program Summary-Phase II







Value of Projects by Phase



Design

Behrman Elementary School CMaR

Career Technical Education High School at Kerlerec Street CMaR

New Cohen High School CMaR

Total: 3

Procurement

Lafayette ES - Refurb

Reed Modular Demolition

Total: 2

Construction

Booker T. Washington - New New Karr High School CMAR

Total: 2

Complete

A Jackson ES - Refurb Abrams ES - New

Allen ES - Refurb

Avery Alexander ES - New

Bauduit ES - Refurb

Bradley ES - New

Carver HS - New D/B

Crossman ES - Refurb

Douglass HS - Refurb

Drew ES - Reno

Dunbar ES - New

Eisenhower ES - Refurb

Fischer ES-Refurb

Fisk Howard - Exterior Envelope

Fisk-Howard ES - New

Gaudet ES-Refurb

Gentilly Terrace ES - Refurb

Green MS - Refurb Phase I & Phase II

Habans ES - New D/B

Harney ES - Gutters & Downspouts

Harney ES - Interior Lighting

Harney ES - Refurb

John McDonogh HS - Reno

Laurel ES - Refurb

Lawless HS - New

Live Oak Drainage & John McDonogh

Waterproofing

Live Oak ES - Refurb & Exploratory

Demolition

Marshall ES - Refurb

Martin L King ES - Refurb

McDonogh 28 - Flooring Renovation Phase 2

McDonogh 28 ES - Refurb

McDonogh 32 ES - Refurb

McDonogh 42 ES - Reno Morial ES - New

NO East HS @Abramson - New

Reed HS - Refurb

Rosenwald ES - Refurb

Schaumburg ES - Refurb

Schaumburg Roof

Sherwood Forest ES - New D/B

Sophie B Wright HS - Phase 2 Interior

Painting and Wood Floor Repairs

Sophie B Wright HS - Reno Sylvanie Williams - Refurb

_ . __ _

Tubman ES - Reno

Village de L'Est ES - Environmental

Village de L'Est ES - Refurb

Wicker ES - Refurb

Total: 47



BESE MONTHLY REPORT OPEN CONTRACTS as of 06/30/2020

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE	ORIGINAL CONTRACT AMOUNTS	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
DEMOLITIONS					
Reed Modular Demolition	Mahlum Scairono Martinez Architects, LLC	FEMA			\$ 34,710.00
Reed Modular Demolition Total	Insulation Technologies, Inc	FEMA			\$ 189,975.00 \$ 224,685.00
Reed Modular Demontion Total					\$ 224,665.00
PHASE 1 SCHOOLS					
Crocker ES Construction	Mathes Brierre Architects	FEMA	\$ 50,000.00	\$ -	\$ 50,000.00
Crocker ES Construction Total					\$ 50,000.00
PHASE 2 SCHOOLS					
Project Name	CONTRACTOR/ARCHITECT	FUNDING SOURCE	CONTRACT AMOUNT	Change Orders/Amendments	Sum of Total Contract
New Booker T Washington HS Interpretive Display New Booker T Washington HS Interpretive Display Total	Bright Moments, LLC	FEMA	\$ 4,125.00	\$ 58,712.51	\$ 62,837.51 \$ 62.837.51
New Booker T Washington Medium High School	Farnsworth Group, Inc - Building Commissioning 7 New & Reno	FEMA	\$ 239,900.00	\$ -	\$ 239,900.00
·	Hewitt-Washington & Associates Architects and Planners	FEMA	\$ -	\$ 5,021,113.93	\$ 5,021,113.93
	CORE Construction Services, L.L.C.				\$ 63,095,152.00
New Booker T Washington Medium High School Total New Booker T Washington Medium High School - S. Prieur St.	Durr Heavy Construction, LLC	FEMA	\$ 1,249,000,00	\$ 67.491.93	\$ 68,356,165.93 \$ 1.316.491.93
New Booker T Washington Medium High School - S. Prieur St. New Booker T Washington Medium High School - S. Prieur St. Total	Duli Reavy Construction, EEC	FEWA	\$ 1,249,000.00	\$ 67,491.93	\$ 1,316,491.93
Fisk-Howard ES Construction	VergesRome Architects + Fanning Howey, A Joint Venture	FEMA	\$ 1,582,878.00	\$ 469,603.58	\$ 2,052,481.58
Fisk-Howard ES Construction Total					\$ 2,052,481.58
McDonogh 42 AHERA Asbestos Inspection/Mgmt	Terracon Consultants, Inc	FEMA	\$ 6,710.00	\$ 21,505.89	
McDonogh 42 AHERA Asbestos Inspection/Mgmt Total Behrman ES Construction	SSRCx, LLC	FEMA	\$ 325.056.00	¢ -	\$ 28,215.89 \$ 325,056.00
Behrman ES Construction Total	SSRCX, EEC	FEMA	\$ 323,030.00	-	\$ 325,056.00
Behrman ES Construction Gym Demo	Waggonner & Ball Architects, APC	FEMA	\$ -	\$ 29,482.00	
Behrman ES Construction Gym Demo Total	•				\$ 29,482.00
Behrman ES Construction New Gym Behrman ES Construction New Gym Total	Waggonner & Ball Architects, APC	FEMA	\$ -	\$ 244,351.00	\$ 244,351.00 \$ 244,351.00
Behrman ES Construction New Gym Total Behrman ES Construction New Gym Total	Waggonner & Ball Architects, APC	FEMA	\$ -	\$ 63,932.00	
Behrman ES Construction Selective Demo Total		TEMA	-	ψ 03,332.00	\$ 63,932.00
Behrman ES Construction Selective Demo/Gym Demo	Landis Construction Co., LLC	FEMA	\$ 1,342,128.00	\$ -	\$ 1,342,128.00
Behrman ES Construction Selective Demo/Gym Demo Total					\$ 1,342,128.00
Behrman ES Construction(CMAR) Behrman ES Construction(CMAR) Total	Waggonner & Ball Architects, APC	FEMA	\$ 2,345,881.00	\$ 312,629.50	\$ 2,658,510.50 \$ 2,658,510.50
Behrman ES Construction(CMAR) PreConstruction	Landis Construction Co., LLC	FEMA	\$ 170,000.00	\$ -	\$ 170,000.00
Behrman ES Construction(CMAR) PreConstruction Total			*	· •	\$ 170,000.00
Avery Alexander School (New - PK-8)	Sizeler Thompson Brown Architects Project Design Group, LLC	FEMA	\$ 1,297,048.60	\$ 241,665.57	
Avery Alexander School (New - PK-8) Total Sophie B Wright HS Renovation	Waggonner & Ball Architects, APC	FEMA	\$ 1,847,676.00	\$ 610,892.81	\$ 1,538,714.17
Sopnie B Wright HS Renovation	Waggonner & Ball Architects, APC	Tax Credit	\$ 1,847,676.00	\$ 610,892.81	\$ 1,986,794.95 \$ 471,773.86
	CORE Construction Services, L.L.C.	Tun Grount			\$ 25,821,328.80
Sophie B Wright HS Renovation Total					\$ 28,279,897.61
Sophie B Wright HS Renovation Phase II -Interior Painting & Wood Flooring	Waggonner & Ball Architects, APC	Tax Credit	\$ -	\$ 22,454.00	
Sophie B Wright HS Renovation Phase II -Interior Painting & Wood Flooring Total John McDonogh HS Renovation	VergesRome Architects, APAC	FEMA	\$ 2,696,406.00	\$ 454,655.15	\$ 22,454.00 \$ 2,627,322.03
Som mesonogn no Kenovation	volgestome Alomeous, Al Ao	Tax Credit	\$ -	Ψ 404,000.10	\$ 523,739.12
	CORE Construction Services, L.L.C.				\$ 32,418,681.24
John McDonogh HS Renovation Total					\$ 35,569,742.39
New Cohen HS (CMAR)	HMS Architects, APC Thompson Builders	FEMA FEMA	\$ 1,955,818.00 \$ 154,175.00		\$ 2,047,747.25 \$ 154,175.00
New Cohen HS (CMAR) Total		FEMA	3 134,173.00		\$ 2,201,922.25
New Cohen HS (CMAR) PreConstruction	Lemoine Company, LLC	CDBG	\$ 140,000.00	\$ -	\$ 140,000.00
New Cohen HS (CMAR) PreConstruction Total	·				\$ 140,000.00
New Cohen HS (CMAR) Selective Demo	Lemoine Company, LLC	FEMA	\$ 2,329,992.00	\$ -	\$ 2,329,992.00
New Cohen HS (CMAR) Selective Demo Total Kerelec CTE Renovation(CMAR)	AE Selec Demo - TBD	FEMA			\$ 2,329,992.00
No. 51.5 Ton 51.5 Home In The Indian In Indian I	SCNZ Architects, LLC	FEMA	\$ 2,198,720.00	\$ 136,338.70	\$ 2,335,058.70
	SSRCx, LLC	FEMA	\$ 226,473.00	\$ -	\$ 226,473.00
	Broadmoor, LLC (Pre Construction)	FEMA	\$ 125,000.00	\$ -	\$ 125,000.00
Kerelec CTE Renovation(CMAR) Total					\$ 2,686,531.70



BESE MONTHLY REPORT OPEN CONTRACTS as of 06/30/2020

PROJECT	CONTRACTOR/ARCHITECT	FUNDING SOURCE		IAL CONTRACT	CHANGE ORDERS/ AMENDMENTS	CONTRACT AMOUNTS
Lafayette ES Renovation	N-Y Associates, Inc. Building Commissioning-TBD	FEMA FEMA	\$	-	\$ 747,929.00	\$ 747,929.00
	Gibbs Construction, L.L.C.	FEMA OPSB	\$	2,631,413.00 5.143.587.00		\$ 2,631,413.00 \$ 5.143.587.00
Lafayette ES Re	novation Total	0,05	<u> </u>	3,143,307.00		\$ 8,522,929.00
Tubman ES Renovation - Cottage	Mahlum Scairono Martinez Architects, LLC	FEMA Tax Credit	\$		\$ 124,533.00	
Tubman ES Renovation	- Cottage Total					\$ 124,533.00
REFURBISHMENTS						
Thurgood Marshall ES Refurb					9	5,829,416.56
Lafayette ES Refurb	N-Y Associates, Inc.	FEMA	\$	324,260.00	\$ 90,978.90	415,238.90
	Tuna Construction, LLC	FEMA	\$	2,452,000.00	\$ 777,993.44	
Lafayette ES Refurb (Phase II)	S Refurb Total N-Y Associates, Inc.	FEMA	s		\$ 845.687.60	\$ 3,645,232.34 8 845.687.60
Lafayette ES Refurb (Phase II) Lafayette ES Refurb		FEWA	3		\$ 645,067.00	\$ 845.687.60
Lafayette Asbestos Abatement	Ritter Consulting Engineers LTD	FEMA	S	20.135.00	\$ 13,300.00	
Editifotio Nobolio Nationioni	Insulation Technologies, Inc	FEMA	Š	591,000.00		
Lafavette Asbestos Al				,		\$ 1,131,607.00
•						
STABILIZATIONS - Various						
Live Oak ES Drainange	VergesRome Architects, APAC	FEMA	\$	-		
	Alfaro Bro. Concrete Construction	FEMA	\$	162,192.00		
Live Oak ES D						\$ 209,627.10
John McDonogh Waterproofing	VergesRome Architects, APAC	FEMA	\$			
John McDonogh Water	Alfaro Bro. Concrete Construction	FEMA	\$	213,919.00		\$ 255,283.70 \$ 303.994.42
John McDonogh Water	proofing Total					\$ 303,994.42
OTHER PROFESSIONAL SERVICES						
Program Management/Construction Management	Jacobs Project Management Company/CSRS Consortium	FEMA	\$	13,582,445.95		
			\$	9,047,221.05		
		Insurance Proceeds			\$ - 5	127,600.00
Program Management/Construction Man						\$ 37,429,423.92
E-Rate Documentation	Educational Professional Services, LLC	Insurance Proceeds	\$	18,000.00		
E-Rate Docum	nentation Total					
					:	37,447,423.92
					Grand Total	256,530,859.30
