Superintendent's Report September, 2015



Dr. Henderson Lewis Jr.Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District



Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	4
COMMUNITY MEETINGS	5
BID OPENINGS	6
DBE OVERVIEW MONTHLY SUMMARY	7
NEW & MAJOR RENOVATION	13
Ray Abrams Elementary School (RSD)	13
Avery Alexander Elementary School (RSD)	13
George Washington Carver School (RSD)	13
Benjamin Franklin Elementary School Renovation (OPSB)	14
Paul B. Habans School (RSD)	14
New Karr High School, CMAR (OPSB)	14
New PK-8 School at North Kenilworth Park at Curran Site (OPSB)	15
Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)	15
Alfred Lawless School (RSD)	15
John McDonogh High School Selective Demolition (RSD)	16
John McDonogh High School Renovation (RSD)	16
McDonogh #35 School (Phillip/Waters Site) (OPSB)	16
Eleanor L. McMain School Gymnasium (OPSB)	17
Ernest "Dutch" Morial Elementary School (RSD)	17
Small New Orleans East High School at Abramson (RSD)	17
Sherwood Forest School (RSD)	18
Harriet R. Tubman Elementary School Renovation (RSD)	18
Booker T. Washington School Environmental Remediation (RSD)	18
Booker T. Washington School (RSD)	19
Sophie B. Wright School (RSD)	19

REFURBISHMENTS	20
Henry Allen Elementary School Refurbishment (RSD)	20
Henry Allen Elementary School Kitchen Refurbishment (RSD)	20
Benjamin Banneker Elementary Kitchen School Refurbishment (RSD)	20
Agnes L. Bauduit Elementary School Refurbishment (RSD)	21
Bethune and Tureaud Elementary School Refurbishment (OPSB)	21
Walter L. Cohen High School Kitchen Refurbishment (RSD)	21
A. D. Crossman School Kitchen Refurbishment (RSD)	22
Frederick A. Douglass High School Science Lab (RSD)	22
Warren Easton School Refurbishment (OPSB)	22
Dwight D. Eisenhower Elementary School Refurbishment (RSD)	23
Dwight D. Eisenhower Elementary School Kitchen Refurbishment (RSD)	23
William J. Fischer Elementary Refurbishment (RSD)	23
Fortier (Lusher) High School Refurbishment (OPSB)	24
Gaudet Elementary School Refurbishment (RSD)	24
Gentilly Terrace School Refurbishment (RSD)	24
Samuel J. Green Elementary School Refurbishment (RSD)	25
Edgar P. Harney Elementary School Refurbishment (RSD)	25
Andrew Jackson School Refurbishment (RSD)	25
J. W. Johnson Elementary School Refurbishment (RSD)	26
Dr. Martin L. King Elementary School Kitchen Refurbishment (RSD)	26
Lafayette Elementary School Refurbishment (RSD)	26
Laurel Elementary School Refurbishment (RSD)	27
Live Oak Elementary School Refurbishment (RSD)	27
Lusher Elementary School Refurbishment (OPSB)	27
Thurgood Marshall Elementary School Refurbishment (RSD)	28
McDonogh #28 School Refurbishment (RSD)	28
McDonogh #32 School Refurbishment (RSD)	28
Nelson Elementary School Refurbishment (OPSB)	29
Sarah T. Reed School Refurbishment (RSD)	29
Sarah T. Reed School Kitchen Refurbishment (RSD)	29
Rosenwald Elementary School Refurbishment (RSD)	30
Village de l'Est Elementary School Refurbishment (RSD)	30
Albert Wicker School Kitchen Refurbishment (RSD)	30
Sylvanie F. Williams School Refurbishment (RSD)	31

2

OTHER PROJECTS	32
Eleanor L. McMain School Roof Replacement (OPSB)	32
Eleanor L. McMain School Maintenance Upgrades (OPSB)	32
Timbers III - Building Controls (OPSB)	32
Building Automation System Integration At Recovery School District Central And Remote Offices (RSD)	33
MOTHBALL OR SAFE & SECURE OF SELECTED SCHOOLS	34
Demolition of Modulars at Abramson and Carver (RSD)	34
Demolition of Modulars at Livingston (RSD)	34
COMPLETED PROJECTS	35

3

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$537 million in open contracts for the capital program after issuing no new contracts, change orders and amendments in September. In addition, the total change orders to date, \$3.7 million, account for less than one percent (0.80%) of the total open construction contracts. RSD anticipates issuing approximately \$802 thousand in construction contracts/change orders, and \$834 thousand in professional service contracts/amendments in October.



The OPSB has \$225 million in open contracts for the capital program after issuing \$1.9 million in new contracts and \$4.2 million in change orders and amendments in September. In addition, the total change orders to date, \$4.8 million, account for approximately two percent (2.48%) of the total open construction contracts. OPSB anticipates issuing approximately \$108 thousand in construction contracts/change orders and -\$258 thousand in professional service contracts/amendments in October.

Community Meetings



Future Community Meetings

Bid Openings

Bids which were opened in September, 2015

September 2, 2015

• Kitchen Improvement at A. D. Crossman School

September 23, 2015

• Bethune School Refurbishment and Tureaud School Refurbishment

The following projects are scheduled to bid in the next 60 days

November 24, 2015

• Fisher Elementary School Refurbishment

December 2, 2015

• Gaudet Elementary School Refurbishment

December 2, 2015

• Abramson and Carver Modular Demolition

December 9, 2015

Live Oak Elementary School Refurbishment

December 9, 2015

• Livingston Modular Demolition

December 16, 2015

• Bauduit Elementary School Refurbishment

December 22, 2015

• Andrew Jackson Elementary School Refurbishment

Disadvantaged Business Enterprises (DBE) Monthly Summary





New & Renovations:

DBE Contractors secured subcontracts on 20 projects as of September 30, 2015. The DBE subcontracts value is \$73,113,989 of the \$346,275,187 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 37 projects as of September 30, 2015. The DBE subcontracts value is \$10,833,115 of the \$37,301,890 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of September 30, 2015. The DBE subcontracts value is \$34,691,592 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$492,714,634

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 12 projects as of September 30, 2015. The DBE subcontracts value is \$54,086,557 of the \$199,371,360 total of awarded contracts.

Stabilization/Demolition/Mothballing:


7

DBE Contractors secured subcontracts on 2 projects as of September 30, 2015. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$200,274,359

^{*} DBE provisions were included in projects bid after June 30, 2012


Current RSD Program DBE Participation

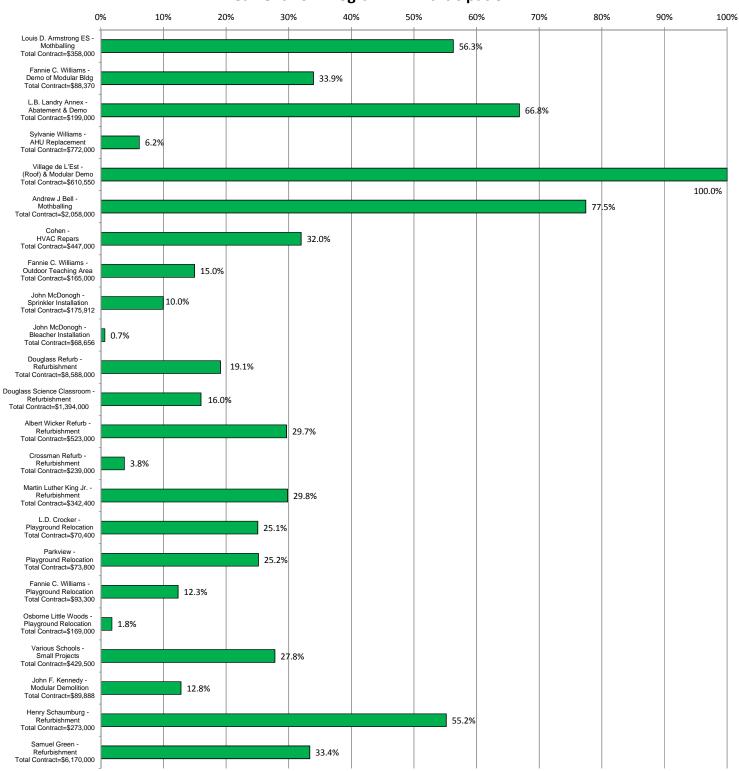

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

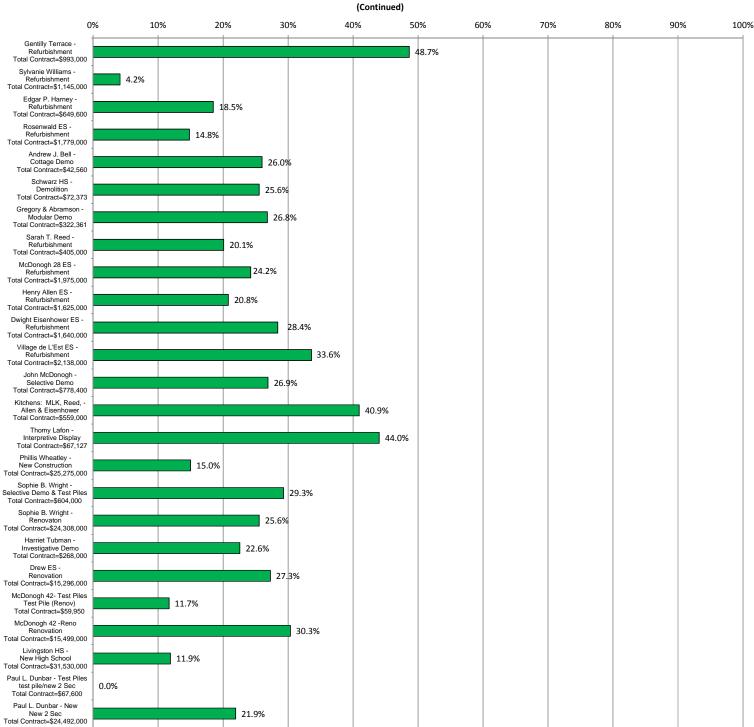

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. $RSD\ DBE\ Participation\ Target = 25\%\ of\ Total\ Contract\ Amount$

Current RSD Program DBE Participation

(Continued)

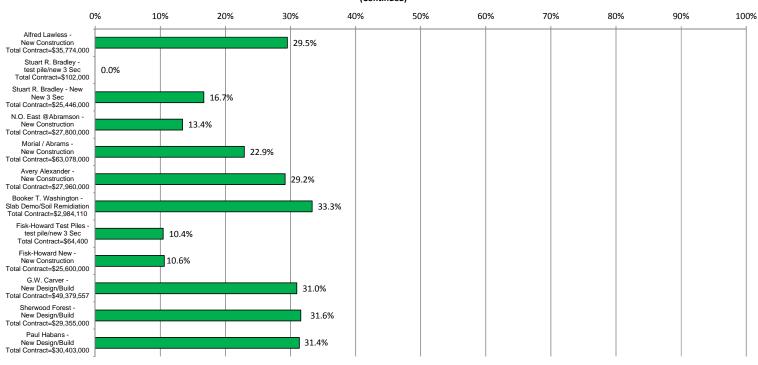


10

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

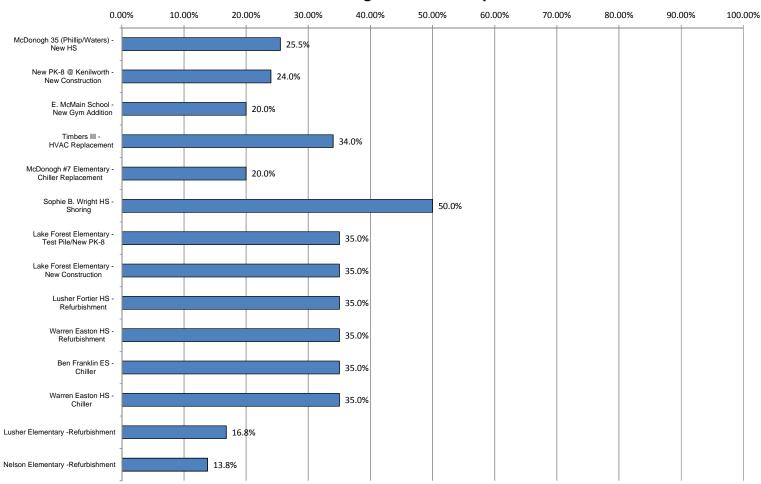

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation - Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School (RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect - Waggonner & Ball Architects, APC

Contractor – McDonnel Group, LLC

Construction Phase

- Forming and pouring of pile caps and grade beams continues
- Under slab rough-in work is ongoing
- · Installation of site drainage is ongoing
- · CMU block layout has started

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – May 2017



Avery Alexander Elementary School (RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect – Sizeler Thompson Brown Architects

Contractor - Core Construction

Construction Phase

- · Auger cast pile work 90% complete
- Underground electrical and plumbing rough-ins continues
- Pile caps are being formed and poured

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – May 2017



George Washington Carver School (RSD)

3059 Higgins Blvd., New Orleans, LA 70126 District E Ward 9

Scope of work: New High School, Design Build

Funding Source – FEMA Contractor – Broadmoor LLC

Construction Phase

· Insulation and gypsum board installation is ongoing at convocation center

13

- · Ceiling installation has started in classroom building
- · Terrazzo installation ins ongoing
- Installation of lighting continues
- Site drainage is ongoing

Contractual Substantial Completion – March 2016 Forecasted Substantial Completion – March 2016



Benjamin Franklin Elementary School Renovation (OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA Architect – N-Y Associates, Inc.

Contractor - TBD Design Phase - CD

- Selective demolition on two banks of windows is complete
- Architect updating scope for interior and exterior stabilization

Procurement Phase

- Anticipated 1st Advertisement TBD
- · Anticipated Bid Opening TBD



Paul B. Habans School (RSD)

3501 Siene Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: New School, Design Build

Funding Source – FEMA Architect – Grace Hebert Contractor – Core Construction

Construction Phase

- · Installation of masonry continues
- Exterior sheathing and waterproofing is complete
- · Interior framing and gypsum board installation is ongoing
- · Curtain wall installation continues
- · Ductwork testing has started

Contractual Substantial Completion – May 2016 Forecasted Substantial Completion – May 2016



New Karr High School CMAR (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center and construction of new high Funding Source – FEMA

14

Architect – VergesRome Architects, APAC

Contractor – TBD

Procurement Phase

- A/E contract is complete
- CMAR contract 90% complete
- · Demolition Subcontractor site visit Sept 29th



New PK-8 School at North Kenilworth Park at Curran Site (OPSB)

8500 Curran Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect - Mathes Brierre Architects

Contractor - Woodrow Wilson Construction Company, Inc.

Construction Phase

- · Exterior glazing is complete
- State Fire Marshal Certificate of Occupancy is anticipated September 29th
- · Commissioning has started

Contractual Substantial Completion – September 2014 Forecasted Substantial Completion – October 2015 School Ready for Occupancy – January 2016



Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)

11110 Lake Forest Boulevard 70128 District E Ward 9

Scope of work: New Pre-K - 8 School

Funding Source – FEMA

Architect – Imre Hegedus & Associates Architects

Contractor - The McDonnel Group

Construction Phase

- Installation of interior finishes is 93% complete
- Site work is 93% complete
- · Substantial completion September 24th
- · School to move in October 21st

Contractual Substantial Completion – July 2015 Forecasted Substantial Completion – September 2015 School Ready for Occupancy – October 2015



Alfred Lawless School (RSD)

5300 Law Street, New Orleans, LA 70117 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- Interior painting is finishing
- Gymnasium equipment installation complete
- Interior storefront installation underway
- Installation of site paving and curb installation continues

Contractual Substantial Completion – November 2015 Forecasted Substantial Completion – November 2015 School Ready for Occupancy – January 2016



Status Date: 30 September 2015

John McDonogh High School Selective Demolition

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Exploratory and selective demolition of the existing school

Funding Source - FEMA

Architect – VergesRome Architects, APAC Contractor - Zimmer-Eschette Services Construction Phase

- 2nd and 3rd floor demolition is complete
- 1st floor demolition is 95% complete
- Exterior items to be removed to start mid September

Contractual Substantial Completion – October 2015

Forecasted Substantial Completion – October 2015



John McDonogh High School Renovation (RSI

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

Contracts are being reviewed by both parties



McDonogh #35 School (Phillip/Waters Site) (OPSB)

1200 Senate Street, New Orleans, LA 70122 District D Ward 7

16

Scope of work: New High School Funding Source – FEMA

Architect – Sizeler, Thompson, Brown Architects

Contractor - Citadel Builders, LLC

Construction Phase

- Punch list is 98% complete
- · Life skills classroom being redesigned
- · Gymnasium bleacher installations complete
- · Ribbon Cutting September 23rd

Contractual Substantial Completion – May 2015 Forecasted Substantial Completion – August 2015 School Ready for Occupancy – August 2015



Eleanor L. McMain School Gymnasium (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source - FEMA

Architect – Jahncke & Burns Architects

Contractor – Gibbs Construction

Construction Phase

- · Stucco installation continues
- Gypsum board installation continues
- Mechanical and electrical rough in is ongoing
- · Window frames at the gymnasium are being installed

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion - February 2016



Ernest "Dutch" Morial Elementary School (RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect - Waggonner & Ball Architects, APC

Contractor – McDonnel Group, LLC

Construction Phase

- · Installation if site drainage is ongoing
- Slab on grade pouring is ongoing
- · CMU block installation has started
- Above slab plumbing has started

Contractual Substantial Completion – January 2017 Forecasted Substantial Completion – January 2017



Small New Orleans East High School at Abramson (RSD)

5552 Read Boulevard, New Orleans, LA 70127 District E Ward 9

17

Scope of work: New High School Funding Source – FEMA

Architect – RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

Construction Phase

- Substantial completion September 2015
- Commissioning to start mid of October
- Punch List in progress
- Exterior grading and landscape is nearly complete

Contractual Substantial Completion – June 2015 Forecasted Substantial Completion – September 2015 School Ready for Occupancy – October 2015



Sherwood Forest School (RSD)

4801 Maid Marion Drive, New Orleans, LA 70128 District E Ward 9

Scope of work: New School, Design Build

Funding Source – FEMA Architect – Grace Hebert Contractor – Core Construction

Construction Phase

- · Masonry installation at the classroom wing is ongoing
- MEP work is ongoing throughout
- Roof work is ongoing
- Exterior sheathing is complete

Contractual Substantial Completion – May 2016 Forecasted Substantial Completion – May 2016



Harriet R. Tubman Elementary School Renovation (RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source - FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

• 100% Construction Documents are due November 17th

Procurement Phase

- Anticipated 1st Advertisement December 2015
- Anticipated Bid Opening January 2016



Booker T. Washington School Environmental Remediation (R:

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

18

Scope of work: The remediation of the site

Funding Source – FEMA

Architect - CB&I

Contractor - SEMS, Inc

Construction Phase

- Area 1 is complete
- · Area 2 is complete
- · Area 3, backfill and grading is ongoing
- · Area 4 site grading ongoing
- Area 5 driveway is being demolished
- Area 6 will start when are 5 is complete

Contractual Substantial Completion – December 2015

Forecasted Substantial Completion – December 2015



Booker T. Washington School (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor - TBD

Design Phase - SD

Successful Proposal will be announced October 2015



Sophie B. Wright High School Renovation (RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Renovation of existing school and gymnasium addition

Funding Source - FEMA

Architect - Waggonner & Ball Architects, APC

Contractor – Core Construction

Construction Phase

- MEP rough-in on 1st and 2nd floors is 75% complete
- Installation of roofing continues
- · Window refurbishment is ongoing
- Plaster work continues in stairwells

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – June 2016



Status Date: 30 September 2015

REFURBISHMENTS

Henry Allen Elementary School Refurbishment (RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - N-Y Associates, Inc.

Contractor - Tuna Construction

Construction Phase

- Exterior door replacement continues
- Mechanical work is 85% complete
- Tuck pointing is 70% complete
- Replacement of hardware continues

Contractual Substantial Completion – February 2016 Forecasted Substantial Completion – February 2016



Henry Allen Elementary School Kitchen Refurbishment (RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services

Construction Phase

- Interior work to begin October 19th
- Exterior work to begin October 22nd

Contractual Substantial Completion – March 2016 Forecasted Substantial Completion – March 2016



Benjamin Banneker Elementary School Kitchen Refurbishment (RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – SCNZ Architects

Contractor - TBD Design Phase - CD

• Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase

20

- Anticipated 1st Advertisement January 2016
- Anticipated Bid Opening March 2016



Agnes L. Bauduit Elementary School Refurbishment (RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor - TBD

Procurement Phase

- 1st Advertisement November 11th
- 2nd Advertisement November 18th
- 3rd Advertisement November 25th
- · Pre-Bid Conference December 1st
- Bid Opening December 16th



Bethune and Tureaud Elementary School Refurbishment (OPSB)

4040 Eagle Street & 2021 Pauger Street, New Orleans, LA District A Ward 3 & District D Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Chenevert Architects LLC

Contractor - TBD

Procurement Phase

Owner is reviewing bids



Walter L. Cohen High School Kitchen Refurbishment (RSD)

3520 Dryades, New Orleans Street, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

• Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase

21

- Anticipated 1st Advertisement January 2016
- Anticipated Bid Opening March 2016



A. D. Crossman School Kitchen Refurbishment (RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – SCNZ Architects Contractor - CDW Services <u>Procurement Phase</u>

Contracts to be signed and returned by contractor



Frederick A. Douglass High School Science Lab (RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovations to science lab

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor – One Construction

Construction Phase

- Wood floor repairs are ongoing in classrooms
- · Repairs to skylights has started
- · Elevator shaft is ongoing

Contractual Substantial Completion – January 2016 Forecasted Substantial Completion – January 2016



Warren Easton School (OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Refurbishment of existing high school, including but not limited to structure, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects LLC Contractor - Tuna Construction

Construction Phase

- Restroom renovations continues
- Exterior tuck pointing 65% complete
- Sprinkler work at the Gymnasium will continue during summer break

Contractual Substantial Completion – September 2015 Forecasted Substantial Completion – September 2015

Status Date: 30 September 2015

Dwight D. Eisenhower Elementary School Refurbishment (RSD)

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - Harry Baker Smith Architects II, PLLC

Contractor - CDW Construction

Construction Phase

- · Site grading is ongoing
- Ceiling repairs continues
- Painting has started on the clear stories

Contractual Substantial Completion – January 2016 Forecasted Substantial Completion – January 2016



Dwight D. Eisenhower Elementary School Kitchen Refurbishment

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services Construction Phase

Contractor is revising his schedule because of permit delay

Contractual Substantial Completion – March 2016 Forecasted Substantial Completion – March 2016



William J. Fischer Elementary School Refurbishment (RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA, CDBG

Architect - SCNZ Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement October 21st
- 2nd Advertisement October 28th
- 3rd Advertisement November 4th
- Pre-Bid Conference November 5th
- Bid Opening November 24th



Status Date: 30 September 2015

Fortier (Lusher) High School Refurbishment (OPSB)

5624 Freret Street, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation and repairs to the roof, masonry, plaster, windows, exterior doors, canopies, mechanical systems, and electrical systems.

Funding Source – FEMA Architect – SCNZ Architects Contractor - Core Construction Construction Phase

- · Contractor is working on punch list from phase one and three
- Modular buildings to be removed in November
- Phase two is 50% complete
- · Repairs to exterior brick work is ongoing

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion - March 2016



Gaudet Elementary School Refurbishment (RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA Architect – SCNZ Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement October 28th
- 2nd Advertisement November 4th
- 3rd Advertisement November 11th
- Pre-Bid Conference November 12th
- Bid Opening December 2nd



Gentilly Terrace School Refurbishment (RSD)

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

24

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners Contractor - One Construction

Construction Phase

· Substantial Completion September 22nd



Samuel J. Green Elementary School Refurbishment $^{(RSD)}$

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect – VergesRome Architects, APAC Contractor - Hernandez Consulting, LLC

Construction Phase

- Fire Alarm work is 95% complete
- Window replacement is 95% complete
- Dumpster pad 80% complete
- Exterior brick repairs is 75% complete
- Restroom repairs are nearing completion

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – October 2015



Edgar P. Harney Elementary School Refurbishment (RSD)

2503 Willow Street, New Orleans, LA 70113 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect – VergesRome Architects, APAC Contractor - Hamp's Construction, LLC

Construction Phase

- Schedule to be adjusted for cooler/freezer install
- · Dumpster work is ongoing
- · Painting of exterior doors is ongoing

Contractual Substantial Completion – September 2015 Forecasted Substantial Completion – October 2015



Andrew Jackson School Refurbishment (RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

25

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- 1st Advertisement November 11th
- · 2nd Advertisement November 18th
- 3rd Advertisement November 25th
- Pre-Bid Conference December 3rd
- · Bid Opening December 22nd



J. W. Johnson Elementary School Refurbishment (RSD)

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA, CDBG

Architect - SCNZ Architects

Contractor - TBD Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval
 Procurement Phase
 - Anticipated 1st Advertisement TBD
 - Anticipated Bid Opening TBD



Dr. Martin L. King Elementary School Kitchen Refurbishment (RSD)

1617 Caffin Avenue, New Orleans, LA 70117 District E Ward 9

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services

Construction Phase

- Existing dumpster pad has been removed
- Excavating for new water lines
- Forming of the dumpster pad has started

Contractual Substantial Completion – March 2016 Forecasted Substantial Completion – March 2016



Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16 Scope of work: Refurbishment of existing elementary school, including but not

limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD Design Phase - CD

• Procurement schedule has been adjusted pending FEMA funding approval Procurement Phase

26

- Anticipated 1st Advertisement February 2016
- Anticipated Bid Opening March 2016



Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect - Mahlum Scairono Martinez JV

Contractor - TBD Procurement Phase

- · All bids were rejected
- Owner is reviewing added scope of work



Live Oak Elementary School Refurbishment (RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

Procurement Phase

- 1st Advertisement November 4th
- 2nd Advertisement November 11th
- 3rd Advertisement November 18th
- Pre-Bid Conference November 19th
- · Bid Opening December 9th



Lusher Elementary School Refurbishment (OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source - FEMA

Architect – Meyer Engineers, LTD.

Contractor - Dynamic

- Construction Phase
 - Annex 3rd floor renovation is underway
 - Bridge completion is projected for December

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – August 2016



Status Date: 30 September 2015

Thurgood Marshall Elementary School Refurbishment (RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - TBD Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval
 Procurement Phase
 - Anticipated 1st Advertisement December 2015
 - Anticipated Bid Opening January 2016



McDonogh #28 School Refurbishment (RSD)

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source - FEMA

Architect – SCNZ Architects, LLC

Contractor - Tuna Construction

Construction Phase

- Kitchen scope change order is being reviewed work to be preformed during Christmas
- Window replacement is nearing completion
- Exterior painting is 35% complete
- Stairwell work to start beginning of October

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



McDonogh #32 School Refurbishment (RSD)

800 DeArmas Street, New Orleans, LA $\,$ 70114 $\,$ District C $\,$ Ward 15 $\,$

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners Contractor - TBD

Design Phase – CD

- Bid Documents were received August 18th
- Procurement schedule has been adjusted pending FEMA funding approval
 Procurement Phase

28

- Anticipated 1st Advertisement December 2015
- Anticipated Bid Opening January 2016



Nelson Elementary School Refurbishment (OPSB)

3121 St. Bernard Avenue, New Orleans, LA 70119 District D Ward 7

Scope of work: Renovation and repairs to the roof, masonry, windows, exterior doors, mechanical systems, and electrical systems.

Funding Source - FEMA

Architect – Harry Baker Smith Architects Contractor - Blanchard Mechanical Contractor

Construction Phase

- Excavation and site drainage work is ongoing
- · Roofing and parapet work is complete
- Masonry work has started

Contractual Substantial Completion – March 2016 Forecasted Substantial Completion – March 2016



Sarah T. Reed School Refurbishment (RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - Tuna Construction

Construction Phase

- All work is complete except for the dining floor which will be complete over the Thanksqiving break
- Dumpster pad work is ongoing
- Electrical work to start in October

Contractual Substantial Completion – December 2015

Forecasted Substantial Completion – December 2015



Sarah T. Reed School Kitchen Refurbishment

5316 Michoud Boulevard, New Orleans, LA $\,$ 70129 $\,$ District E $\,$ Ward 9 $\,$

Scope of work: Refurbishment of existing high school kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services Construction Phase

- Existing dumpster pad has been removed
- New water lines have been installed
- Forming of the dumpster pad has started

Contractual Substantial Completion – March 2016 Forecasted Substantial Completion – March 2016



Status Date: 30 September 2015

Rosenwald Elementary School Refurbishment (RSD)

6501 Berkley Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect - Byron J. Stewart & Associates, APC Architects & Planners

Contractor - One Construction

Construction Phase

- HVAC controls are 55% complete
- · Cafeteria and kitchen sprinkler system installation is ongoing
- Electrical work is 95% complete
- Installation of new ceiling grid and tiles is nearing completion

Contractual Substantial Completion – January 2016

Forecasted Substantial Completion – January 2016



Village de l'Est Elementary School Refurbishment (RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA, CBDG

Architect – Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

Construction Phase

- Work continues on dumpster pad and grease trap
- Replacement of AHU's Continues
- Replacement of restroom stalls and fixtures is 50% Complete
- Interior painting is nearing completion

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – April 2016



Albert Wicker School Kitchen Refurbishment (R

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA Architect – SCNZ Architects

Contractor - TBD Design Phase - CD

Procurement schedule has been adjusted pending FEMA funding approval
 Procurement Phase

30

- Anticipated 1st Advertisement January 2016
- Anticipated Bid Opening March 2016



Sylvanie F. Williams School Refurbishment $^{(RSD)}$

3127 Martin Luther King Jr. Boulevard, New Orleans, LA 70125 District B Ward 2 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect – N-Y Associates, Inc.

Construction Phase

- Exterior door repairs are 60% complete
- Work on parking resurfacing is 95% complete
- Kitchen repairs are ongoing
- Brick tuck-pointing is ongoing

Contractual Substantial Completion – December 2015

Forecasted Substantial Completion – December 2015



Status Date: 30 September 2015

OTHER PROJECTS

Eleanor L. McMain School Roof Replacement (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Roof replacement

Funding Source – General Fund & Harrah's

Architect - Duplantis Design Group

Contractor – Rycars Construction

Construction Phase

- Notice to proceed September 9th
- Contractor is mobilizing



Eleanor L. McMain School Maintenance Upgrades (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work.
Funding Source – General Fund & Harrah's
Architect – Duplantis Design Group
Contractor – Tuna Construction

Procurement Phase

• Environmental testing to start September 18th



Timbers III - Building Controls (OPSB)

3520 General DeGaulle Drive, New Orleans, LA 70114 District C Ward 15

32

Scope of work: Design and installation of new building controls

Funding Source – OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - TBD Design Phase - PC

Owner has placed project on hold

Procurement Phase

- Anticipated 1st Advertisement TBD
- · Anticipated Bid Opening TBD



Building Automation System Integration At Recovery School

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview ES

Funding Source – FEMA Architect – Moses Engineers Contractor – Synergy Building Solutions, Inc.

Construction Phase

- The five Quick Start Schools are complete, the Energy Dash Board is being implemented
- Sylvanie Williams Elementary School, Sarah T. Reed Elementary School, Fannie C. Williams Elementary School, Bienville Elementary School, Charles L. Colton Elementary School, William Frantz Elementary School, Parkview Elementary School, Osborne Elementary School, Carter G.
 Woodson Elementary School, Walter Cohen High School, Dolores T Aaron Elementary School, A. D. Crossman Elementary School, and Albert Wicker Elementary School are complete
- Benjamin Banneker Elementary School is complete
- Synergy is compiling training docs and O&M manuals

Contractual Substantial Completion – May 2015 Forecasted Substantial Completion – January 2016



Status Date: 30 September 2015

MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

Demolition of Modular Buildings at Abramson and Carver (RSD)

5552 Read Boulevard and 3059 Higgins Boulevard, New Orleans, LA Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - TBD

Procurement Phase

- 1st Advertisement October 28th
- 2nd Advertisement November 4th
- 3rd Advertisement November 11th
- Pre-Bid Conference November 12th
- · Bid Opening December 2nd

Demolition of Modular Buildings at Livingston (RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source - FEMA

Architect - GAEA Consultants, LLC

Contractor - TBD

Procurement Phase

- 1st Advertisement November 4th
- 2nd Advertisement November 11th
- 3rd Advertisement November 18th
- Pre-Bid Conference November 19th
- Bid Opening December 9th



Status Date: 30 September 2015

Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition (RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation (RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School (RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment (RSD)	06/04/2014
5	A. P. Tureaud Elementary School Roof Repairs (RSD)	06/13/2013
6	Agnes Bauduit Elementary School Boiler (RSD)	12/07/2009
7	Albert Wicker Elementary School Refurbishment (RSD)	03/27/2014
8	Albert Wicker Elementary School Roof Repairs (RSD)	06/13/2013
9	Alfred Lawless Senior High Security Fencing (RSD)	06/15/2011
10	Alice M. Harte Elementary School (OPSB)	11/19/2014
11	Alice M. Harte Elementary School Demolition (OPSB)	12/14/2011
12	Andrew J. Bell Junior High School Roof Replacement (RSD)	02/08/2014
13	Andrew J. Bell Junior High School Mothball (RSD)	06/28/2011
14	Andrew Jackson Elementary School Roof Repairs (RSD)	07/27/2012
15	Andrew Jackson Elementary School Solar Panels (RSD)	01/14/2013
16	Andrew H. Wilson Elementary School Cottage (RSD)	10/11/2010
17	Arthur Ashe Elementary School Kitchen Renovation (OPSB)	
18	Augustine Elementary School Roof (RSD)	04/13/2012
19	Avery-Alexander Elementary School Demolition (RSD)	06/15/2012
20	Barbara C. Jordan Elementary School Demolition (RSD)	05/30/2011
21	Bell JH Shoring (RSD)	06/28/2011
22	Benjamin Banneker Elementary School Energy Conservation (RSD)	
23	Benjamin Franklin Senior High School (OPSB)	08/23/2013
24	Bienville Elementary School Demolition (RSD)	05/04/2009
25	Booker T. Washington High School Partial Demolition (RSD)	04/07/2013
26	Carter G. Woodson Middle School Demolition (RSD)	02/09/2010
27	Central Services Warehouse Demolition (OPSB)	01/05/2012
28	Charles J. Colton Elementary Selective Demolition (RSD)	07/26/2010
29	Charles J. Colton Elementary School (RSD)	05/23/2013
30	Charles R. Drew Elementary School (RSD)	04/17/2015
31	Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)	06/08/2011
32	Cohen High School Health Clinic (RSD)	12/24/2008
33	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School (RSD)	
34	Demolition of Modular Buildings at Gregory and Abramson (RSD)	06/23/2015
35	Douglass High School Under Floor Utilities (RSD)	
36	Dr. Martin Luther King School Roof Repairs (RSD)	06/13/2012
37	Dr. Martin Luther King Jr. School Renovation (RSD)	12/15/2014
38	Dwight D. Eisenhower Elementary School Roof Repairs (RSD)	07/27/2012
39	East Bank Swing Space for Audubon Charter School (OPSB)	12/30/2011
40	Edgar P. Harney Elementary School Roof Repairs (RSD)	06/13/2012
41	Edna Karr High School - Gymnasium Repair (OPSB)	12/23/2013
42	Edna Karr High School - Assessment (OPSB)	
43	Edward Livingston Middle School Demolition (RSD)	09/28/2010

4.4	Edward Harman Blatting a land and think Colored Bounding (OPSB)	11/10/2010
44	Edward Henry Phillips Junior High School Demolition (OPSB)	11/19/2010
45	New Edward Hynes School (OPSB)	02/06/2012
46	Edwards Hardin Lockett Lawless Demolition (RSD)	11/03/2008
47	Edward Livingston High School (RSD)	01/05/2015
48	Eleanor L. McMain School Replacement of Existing Chillers (OPSB)	08/30/2011
49	Eleanor L. McMain School Clinic (OPSB)	07/24/2013
50	Ernest N. Morial Elementary Security Fencing (RSD)	05/10/2011
51	Fannie C. Williams Elementary School Demolition (RSD)	03/10/2009
52	Fisk-Howard Elementary School Demolition (RSD)	10/04/2011
53	Florence J. Chester Elementary School Demolition (RSD)	06/05/2011
54	Francis W. Gregory Demolition (RSD)	12/21/2011
55	Frederick A. Douglass High Refurbishment (RSD)	10/28/2014
56	Frederick A. Douglass High Switchgear (RSD)	08/04/2009
57	Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)	
58	George Mondy Elementary School Mothball (RSD)	
59	George Washington Carver High School Demolition (RSD)	08/24/2011
60	Greater St. Stephens School (OPSB)	03/18/2013
61	Harriet R. Tubman Elementary School Selective Demolition (RSD)	12/14/2014
62	Henry Allen Elementary School Roof (RSD)	05/24/2010
63	Henry C. Schaumburg School Refurbishment (RSD)	06/26/2015
64	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation (RSD)	12/16/2011
65	Holy Cross Modular Relocation (RSD)	12/14/2010
66	Israel M. Augustine Middle School Roof Replacement (RSD)	04/13/2012
67	Israel M. Augustine Middle School Mothball (RSD)	01/18/2013
68	James Derham Demolition (RSD)	02/23/2012
69	James W. Johnson Elementary School Roof (RSD)	07/31/2010
70	New Jean Batiste de Bienville School (RSD)	06/15/2012
71	Jean Gordon Elementary School Demolition (RSD)	08/16/2010
72	John Dibert Elementary School Roof (RSD)	08/20/2010
73	John W. Hoffman Elementary School Demolition (RSD)	05/25/2010
74	John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)	11/05/2010
75	John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)	08/05/2011
76	John F. Kennedy Modular Demolition (RSD)	09/16/2014
77	John F. Kennedy High School Demolition (RSD)	01/12/2012
78	John McDonogh Senior High School Bleachers and Sprinklers (RSD)	03/27/2014
79	John McDonogh Senior High School Roof (RSD)	05/04/2010
80	John A. Shaw Elementary School Mothball (RSD)	12/12/2012
81	Joseph S. Clark Senior High School Roof Repairs (RSD)	07/27/2012
82	Joseph A. Craig Elementary Canopies (RSD)	06/06/2011
83	Joseph A. Craig Elementary Elevator Installation (RSD)	01/20/2012
84	Joseph A. Hardin Elementary Security Fencing (RSD)	05/10/2011
85	Lafayette Elementary School Roof and Masonry (RSD)	06/22/2012
86	Lake Area Landry Demolition (RSD)	05/01/2008
87	Langston Hughes Elementary School (Phase I) (RSD)	08/11/2009
88	Langston Hughes Elementary School - New Gymnasium (Phase II) (RSD)	11/10/2010
89	Langston Hughes Elementary School - Dumpster Pad (RSD)	10/12/2012
	J - J J	-

00	(RSD)	0.4/0.0/0.04.0
90	Lawrence D. Crocker Elementary School Demolition (RSD)	04/02/2010
91	L.B. Landry Annex Demolition (RSD)	05/02/2013
92	Little Woods Elementary School Demolition (RSD)	08/09/2010
93	Little Woods School (Dolores T. Aaron Elementary School) (RSD)	08/01/2013
94	Live Oak Elementary School Roof (RSD)	08/04/2011
95	Live Oak Elementary School Exterior Door Replacement (RSD)	08/26/2011
96	Lorraine Hansberry Elementary School Mothball (RSD)	12/27/2012
97	Louis D. Armstrong Elementary School (RSD)	02/18/2013
98	Mahalia Jackson Elementary School (OPSB)	05/11/2010
99	Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)	03/06/2012
100	Mahalia Jackson Elementary School Office Renovation (OPSB)	04/30/2013
101	Martin Behrman Elementary School Roof (RSD)	02/23/2010
	Martin Luther King Jr. Elementary Canopy System (RSD)	11/05/2011
103	3	07/31/2012
104	Mary Church Terrell Elementary School Demolition (RSD)	04/17/2013
105	Mary M. Bethune Elementary 1st Floor Replacement (OPSB)	01/24/2011
106	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)	01/21/2011
107	McDonogh #7 High School Repairs (OPSB)	07/14/10040
	McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)	06/11/2012
109	McDonogh #28 Elementary School Roof (RSD)	11/19/2011
110	McDonogh #32 Roof Replacement (RSD)	02/24/2012
111	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior	01/17/2014
440	Ramp & Handicap Seating in the Auditorium (OPSB)	05/00/0045
	McDonogh #42 Elementary School Renovation (RSD)	05/28/2015
	McDonogh #42 Elementary School Roof (RSD)	12/21/2011
	McDonogh #42 Elementary School HVAC Replacement (RSD)	08/09/2010
115	Mildred C. Osborne Elementary School Demolition (RSD)	02/18/2010
116	Mildred C. Osborne Elementary School	12/03/2012
11/	Modular Campuses Close Outs (RSD)	05/00/0040
118	Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)	05/22/2013
119	3 3	04/05/2010
120	Morris F.X. Jeff Elementary School Demolition (RSD)	04/45/2042
121	Morris F.X. Jeff Elementary School Mothball (RSD)	01/15/2013
	Murray G. Henderson Elementary School Roof (RSD)	06/23/2012
	New Andrew H. Wilson Elementary School (RSD)	10/11/2009
	New Carter G. Woodson School (RSD)	09/14/2012
	New Fannie C. Williams School (RSD)	08/24/2012
	New Joseph A. Craig Elementary School (RSD)	12/09/2009
127	New L.B. Landry High School (RSD)	06/30/2010 12/28/2009
	New Lake Area High School (RSD)	
	New Lawrence D. Crocker School (RSD)	04/29/2013
130 131	New Parkview School ^(RSD) New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	10/12/2012
	New William Frantz Elementary School (RSD)	
133	New Orleans High School Signature Center Study (RSD)	05/07/2012
134	Oretha C. Haley Demo (RSD)	03/07/2012

125	O III O III II (RSD)	00/17/2012
	Oretha C. Haley Elementary School Mothball (RSD)	09/17/2012
	Parkview Elementary School Demolition (RSD)	08/06/2009
	Paul L. Dunbar Elementary School Demolition (RSD)	06/16/2010
	Paul L. Dunbar Elementary School (RSD)	06/02/2015
	Paul B. Habans Elementary School Roof Repairs (RSD)	07/27/2012
	Phillis Wheatley Elementary School Demolition (RSD)	09/26/2011
141	Phillis Wheatley Elementary School (RSD)	07/10/2014
142	3	07/14/2011
143	3 · · · · · · · · · · · · · · · · · · ·	01/11/2012
144	Sarah T. Reed High School Auditorium Wall (RSD)	03/29/2010
145	Seabrook Computer Training Center Demolition (OPSB)	06/25/2010
146	Schaumburg Chillers (RSD)	11/14/2008
147	· ·	07/14/2009
148		04/02/2015
149	3 · · · · · · · · · · · · · · · · · · ·	04/02/2015
150	Sherwood Forest Elementary School Demolition (RSD)	10/28/2010
151	\mathbf{I}	01/31/2014
152	Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)	07/26/2011
153	Stuart R. Bradley Elementary School Demolition (RSD)	01/27/2010
154	· · · · · · · · · · · · · · · · · · ·	06/26/2015
155	Sylvanie Williams Elementary School AHU Replacement (RSD)	07/30/2013
156	Sylvanie Williams Elementary School Play Yard (RSD)	09/23/2010
157	Sylvanie Williams Elementary School Roof Repairs (RSD)	07/27/2012
158		04/13/2012
159	Temporary Campus for McDonogh #11 Expropriation (OPSB)	
160	Thomas A. Edison Elementary School Demolition (RSD)	03/25/2010
161	Thomy Lafon Elementary School Demolition (RSD)	11/27/2011
162	Thomy Lafon School Interpretative Display (RSD)	10/15/2013
163	Timbers Park Office Building #1 & #2 Demolition (OPSB)	09/18/2011
	Timbers HVAC (OPSB)	09/11/2013
165	Timbers III - IT Room Relocation (OPSB)	02/11/2015
166	Village de L'est Elementary School Subsidence (RSD)	06/18/2012
	Village de L'est Elementary School Roof and Modular Demolition (RSD)	06/16/2013
	Vorice J. Waters Elementary School Demolition (RSD)	01/14/2010
	Valena C. Jones Elementary School (RSD)	01/10/2013
	Walter L. Cohen High School HVAC (RSD)	04/04/2014
171	Warren Easton High School Window Replacement (OPSB)	09/07/2012
172	West Bank Swing Space for Alice Harte Elementary School (OPSB)	07/11/1931
173	New William J. Guste Elementary School (RSD)	10/06/2008
174	(DCD)	08/04/2009
	William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)	04/15/2010
	William Frantz Elementary School Roof (RSD)	08/12/2010
.,,	William France Elementary School Roof	55/12/2010

38
