


Superintendent's Report December, 2016



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District

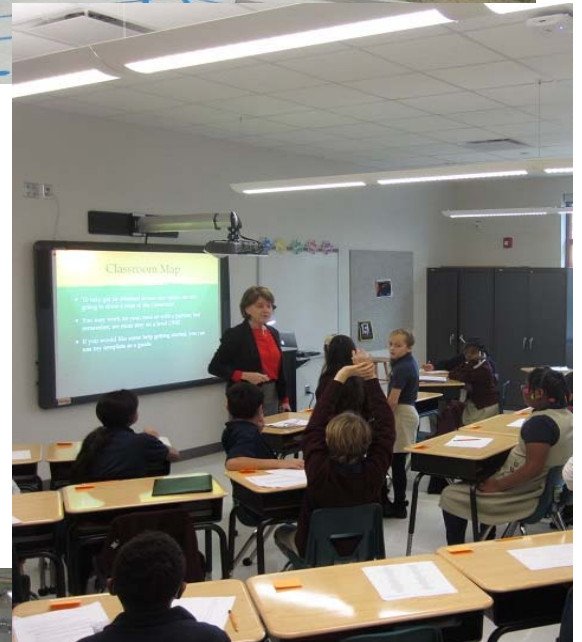

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	3
COMMUNITY MEETINGS	4
BID OPENINGS	5
DBE OVERVIEW MONTHLY SUMMARY	6
NEW & MAJOR RENOVATION	11
Ray Abrams Elementary School ^(RSD)	11
Avery Alexander Elementary School ^(RSD)	11
Benjamin Franklin Elementary School Renovation ^(OPSB)	11
JoEllen Smith Medical Center Demolition ^(OPSB)	12
New Karr High School, CMAR ^(RSD)	12
John McDonogh High School Renovation CMAR ^(RSD)	12
Ernest "Dutch" Morial Elementary School ^(RSD)	13
Harriet R. Tubman Elementary School Renovation ^(RSD)	13
Booker T. Washington School CMAR ^(RSD)	13
Sophie B. Wright School Cornice Replacement ^(RSD)	14
REFURBISHMENTS	15
Benjamin Banneker Elementary Kitchen School Refurbishment ^(RSD)	15
Agnes L. Bauduit Elementary School Refurbishment ^(RSD)	15
A. D. Crossman School Kitchen Refurbishment ^(RSD)	15
William J. Fischer Elementary Refurbishment ^(RSD)	16
Gaudet Elementary School Refurbishment ^(RSD)	16
Samuel J. Green Elementary School Refurbishment ^(RSD)	16
Andrew Jackson School Refurbishment ^(RSD)	17
Lafayette Elementary School Refurbishment ^(RSD)	17
Laurel Elementary School Refurbishment ^(RSD)	17
Live Oak Elementary School Refurbishment ^(RSD)	18
Thurgood Marshall Elementary School Refurbishment ^(RSD)	18
McDonogh #32 School Refurbishment ^(RSD)	18
Village de l'Est Elementary School Refurbishment ^(RSD)	19
Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing ^(RSD)	19

DEMOLITIONS	20
Demolition of Modulares at Abramson and Carver ^(RSD)	20
Demolition of Modulares at Livingston ^(RSD)	20
 COMPLETED PROJECTS	 21

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$595 million in open contracts for the capital program after issuing \$23 million in new contracts, change orders and amendments in December. In addition, the total change orders to date, \$7.7 million, account for one percent (1.40%) of the total open construction contracts. RSD anticipates issuing approximately \$719 thousand in construction contracts/change orders, and \$815 thousand in professional service contracts/amendments in January.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$231 million in open contracts for the capital program after issuing -\$296 thousand in new contracts, change orders and amendments in December. In addition, the total change orders to date, \$9.2 million, account for approximately four percent (4.67%) of the total open construction contracts. OPSB anticipates issuing approximately \$774 thousand in construction contracts/change orders and \$792 dollars in professional service contracts and amendments in January.

Community Meetings



Future Community Meetings

Bid Openings

Projects which are scheduled to bid in the next 60 days

January 25, 2017

Bethune School Refurbishment Bid Opening

February 1, 2017

Kitchen Improvements at Benjamin Banneker / Wheatley Grease Trap Bid Opening

March 8, 2017

HVAC Equipment Repairs at Village de l'Est, Sarah T. Reed, and Rosenwald Bid Opening

March 22, 2017

Thurgood Marshall School Refurbishment Bid Opening

Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District



New & Renovations:

DBE Contractors secured subcontracts on 24 projects as of December 31, 2016. The DBE subcontracts value is \$89,745,976 of the \$394,544,776 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 48 projects as of December 31, 2016. The DBE subcontracts value is \$19,547,610 of the \$65,106,535 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of December 31, 2016. The DBE subcontracts value is \$34,525,219 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$ 568,788,868

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of December 31, 2016. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of December 31, 2016. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$231,354,830

* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

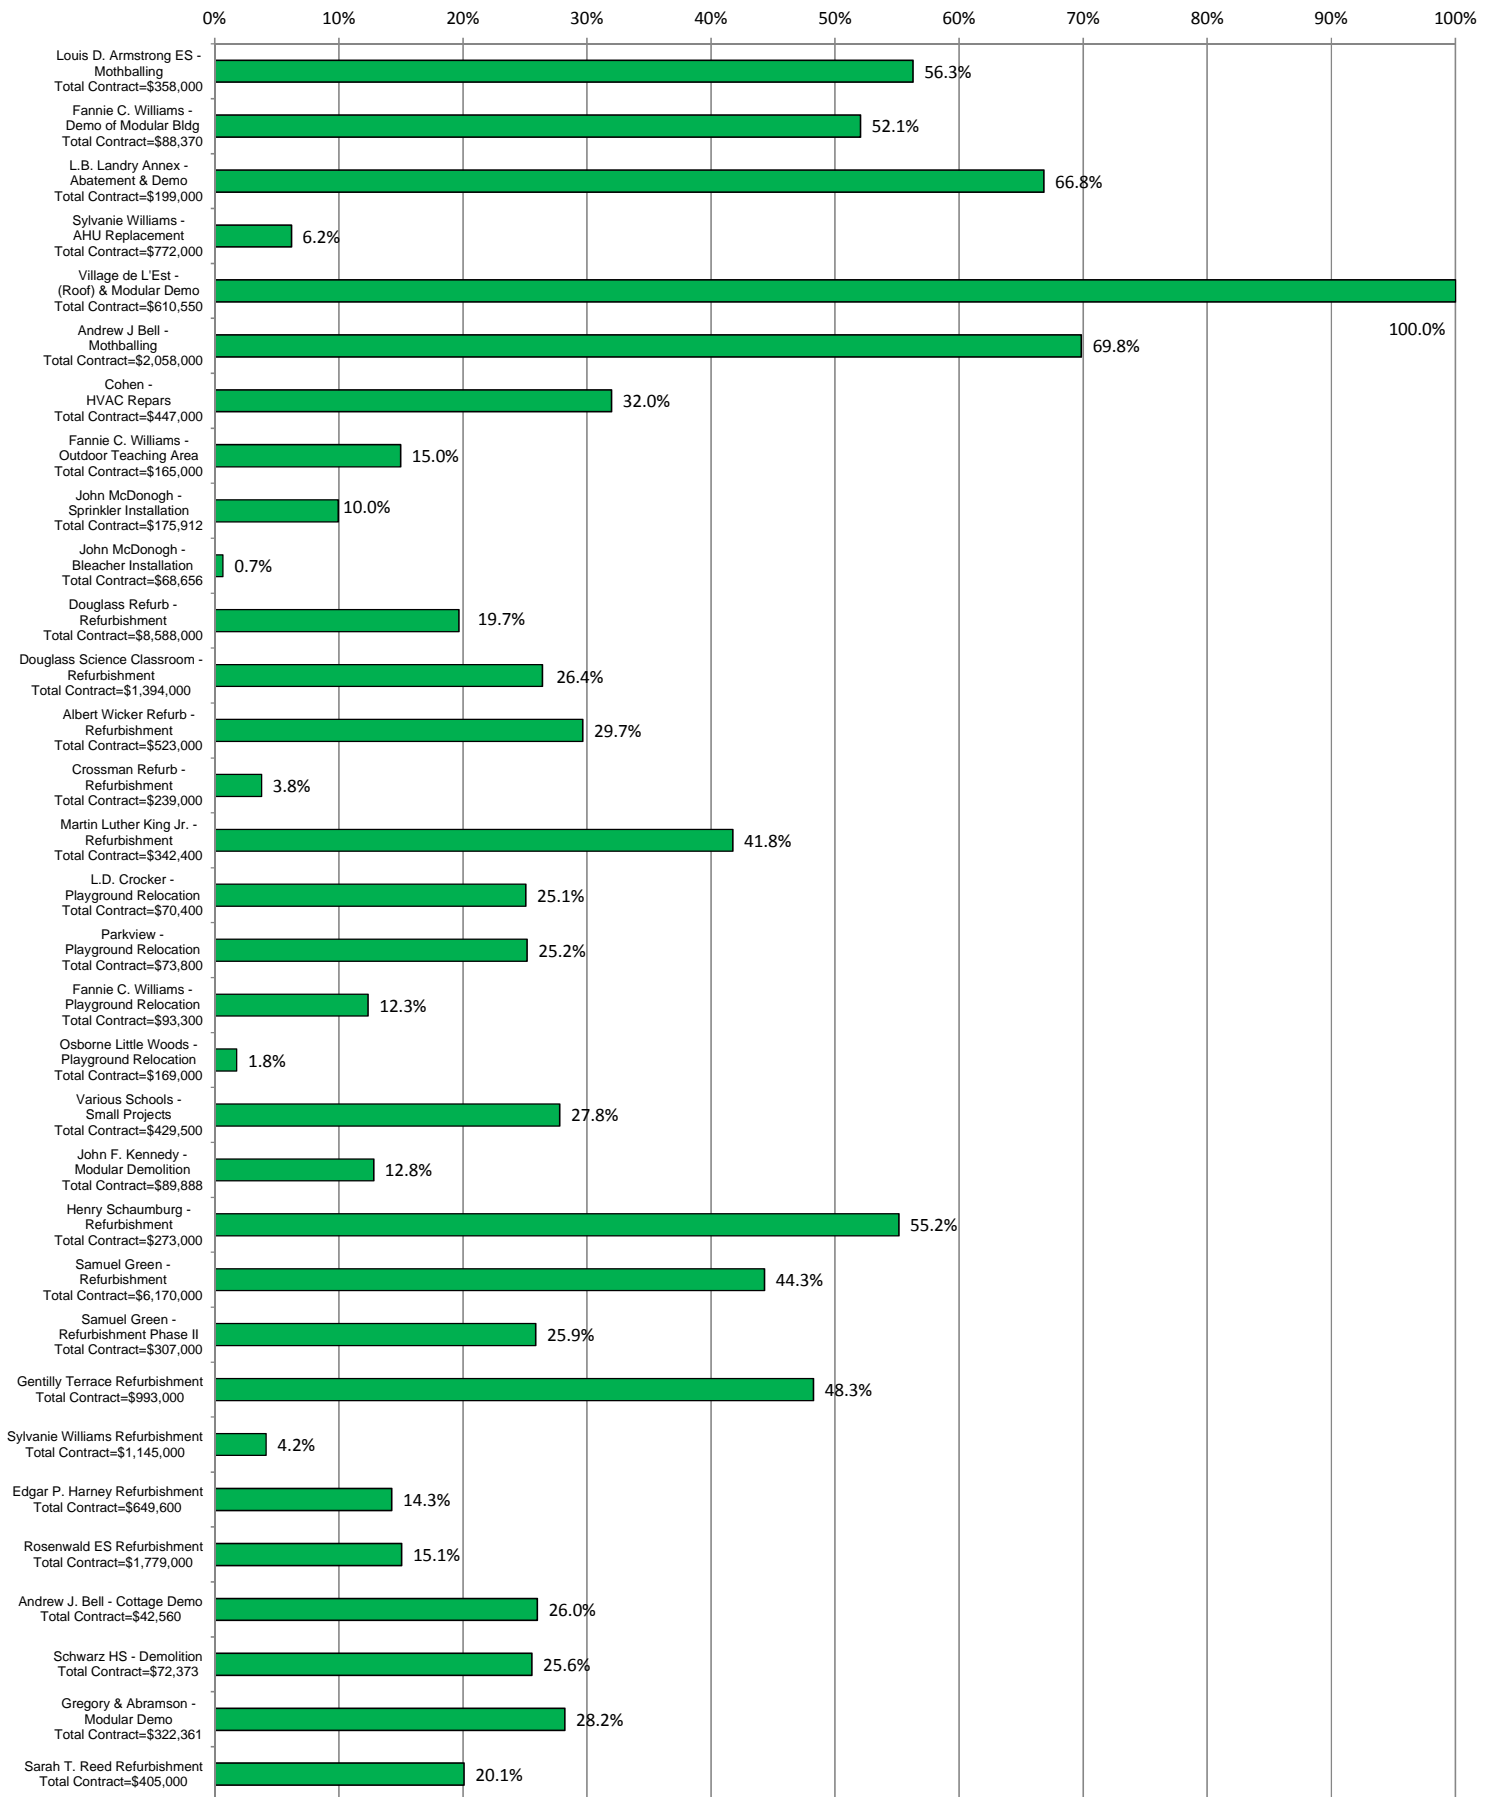


Notes: Data Based On Pre-Construction and/or 7 monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Status Date: 31 December 2016

Current RSD Program DBE Participation


(Continued)

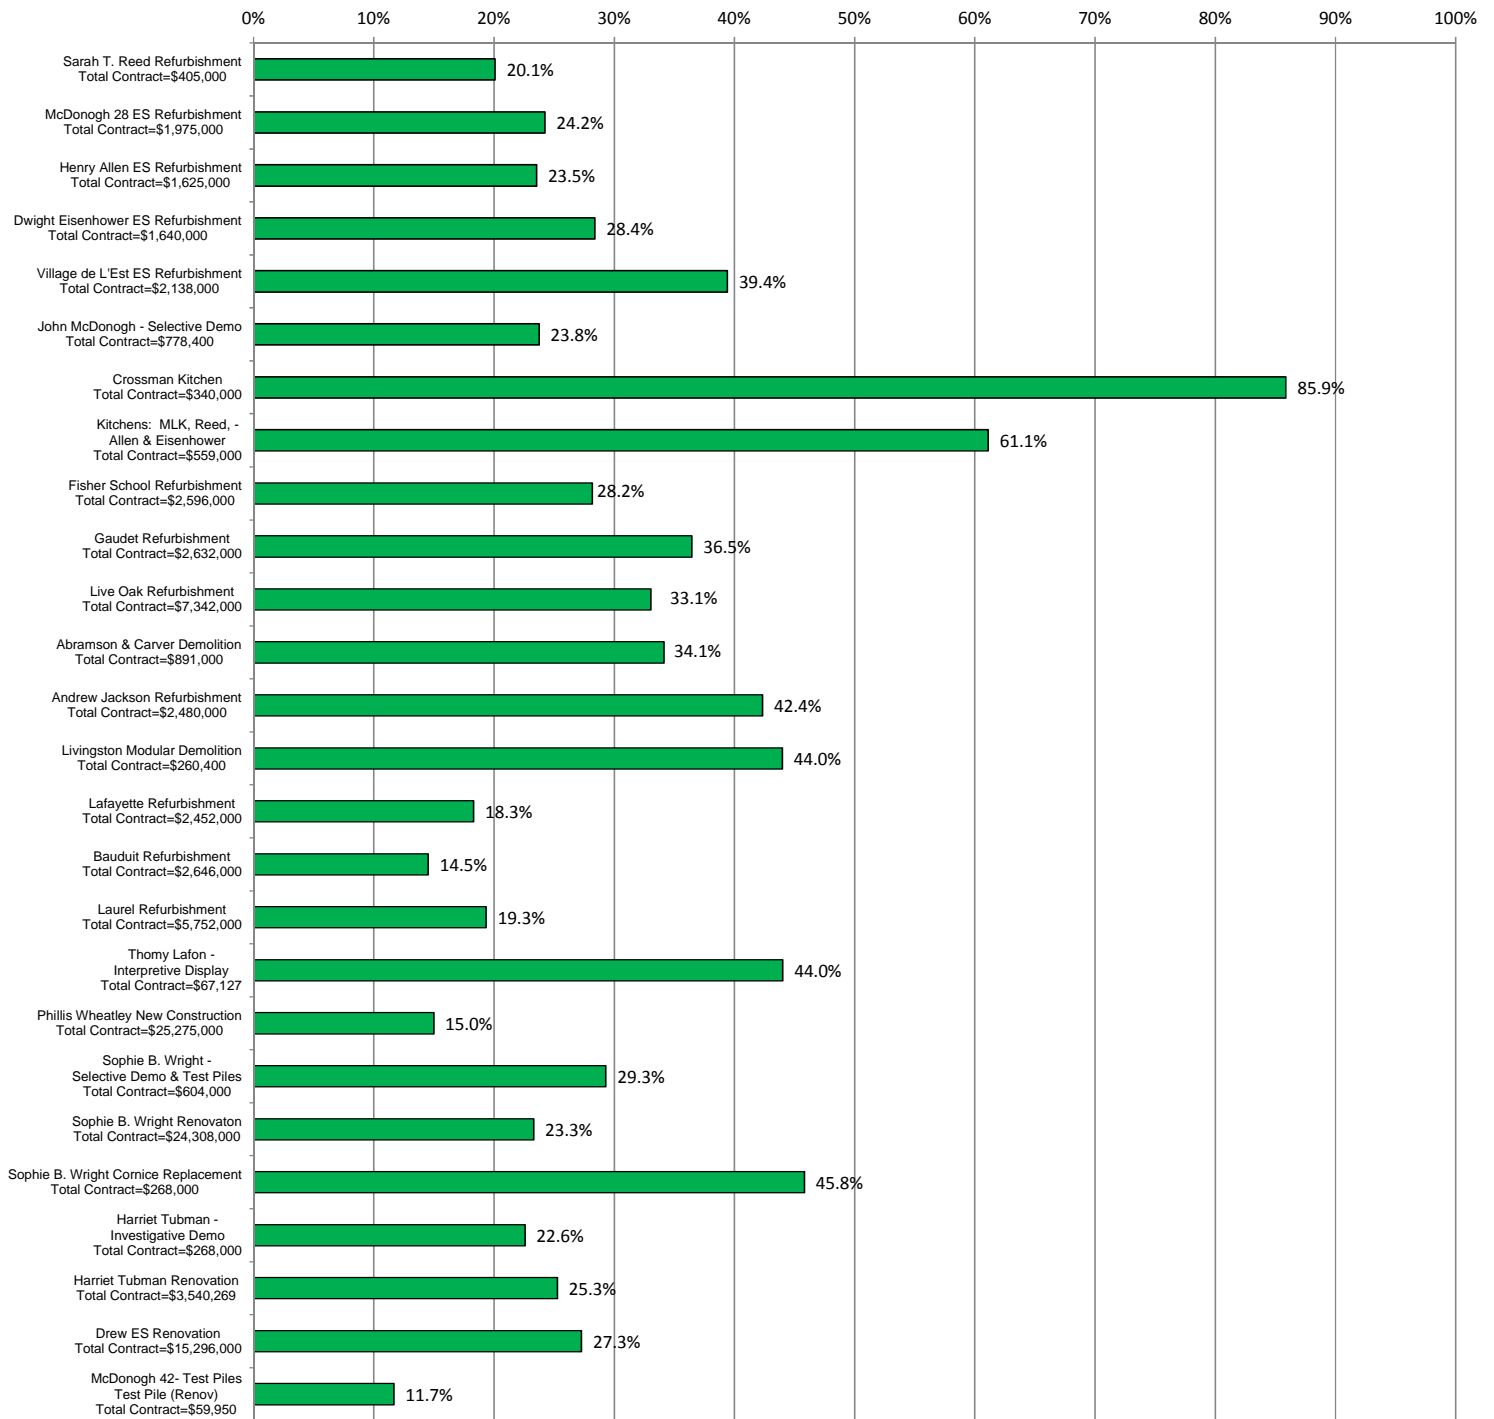

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

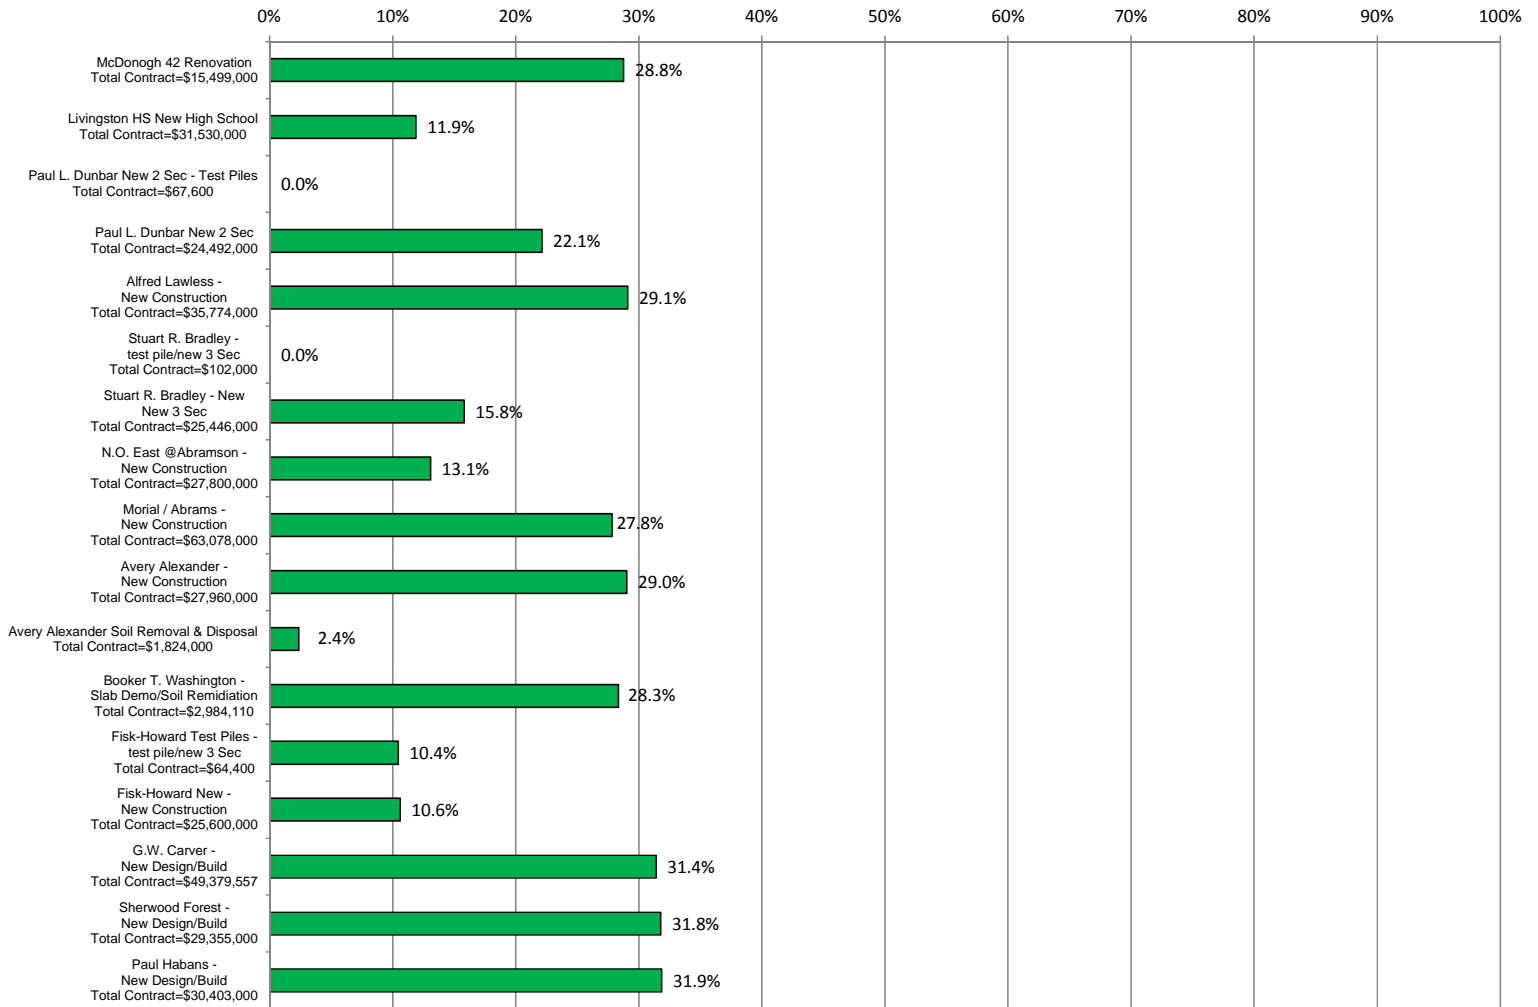

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

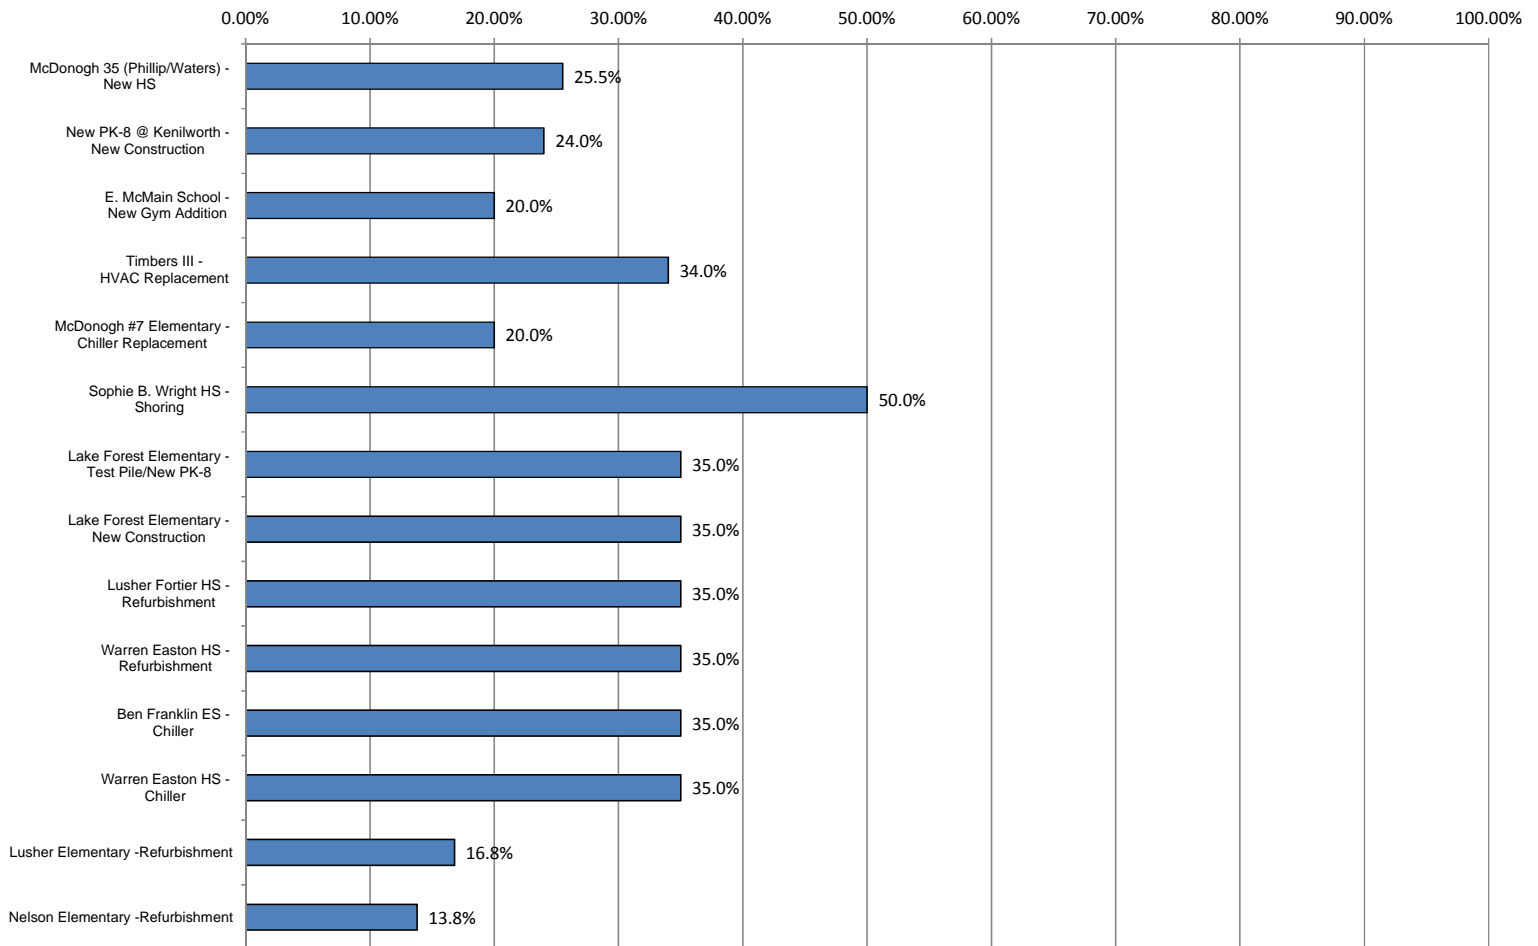

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School ^(RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Gymnasium flooring installation will start in January
- Interior painting continues
- Plumbing fixture installation ongoing
- Roofing cap sheet installation almost complete
- Casework installation has started

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – March 2017



Avery Alexander Elementary School ^(RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- Installation of ceiling tile has started
- Metal panel installation continues
- Kitchen equipment hookup is underway
- HVAC is being prepped for start up
- Millwork installation is ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- A&E continues work on construction documents for the repairs of the exterior and the windows



JoEllen Smith Medical Center Demolition (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – Core Construction

Demolition Phase

- Foundation removal continues
- Pile survey due in January 2017

Contractual Substantial Completion – January 2017

Forecasted Substantial Completion – January 2017



New Karr High School CMAR (RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - TBD

Procurement Phase

- 50% Construction Documents were received December 20th

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



John McDonogh High School Renovation CMAR (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Design Phase

- Work on Construction Documents is ongoing
- Archaeological exploration work continues
- Gymnasium demolition is ongoing

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



ESPLANADE AVENUE



NEW GYMNASIUM - BARRACKS STREET



NEW GYMNASIUM - N. ROCHELAVE STREET



NEW GYMNASIUM - N. ROCHELAVE STREET

Ernest "Dutch" Morial Elementary School ^(RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Gymnasium flooring installation will start in January
- Interior painting continues
- Plumbing fixture installation ongoing
- Roofing cap sheet installation almost complete
- Casework installation has started

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – March 2017



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

Construction Phase

- Electrical rough-in ongoing
- Second floor slab has been poured at the cafetorium
- Exterior Plaster repairs are underway
- Installation of refurbished windows continues
- Mechanical rough in is underway

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Pile driving is complete
- Underground utility rough in's has started
- Excavation and forming of pile caps continues

Contractual Substantial Completion – 2018

Forecasted Substantial Completion – 2018



Sophie B. Wright High School Cornice Replacement ^(RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Replace existing cornice

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – Battco Construction

Construction Phase

- Substantial completion December 29th

Contractual Substantial Completion – December 2016

Forecasted Substantial Completion – December 2016



REFURBISHMENTS

Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

2300 Dumaine Street, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement - December 28th
- 2nd Advertisement - January 4th
- 3rd Advertisement - January 11th
- Pre-Bid Conference - January 12th
- Bid Opening - February 1st



Agnes L. Bauduit Elementary School Refurbishment ^(RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor – One Construction

Construction Phase

- Window installation continues
- Installation of ducts is ongoing
- Work on the dumpster pad continues
- VCT flooring installation continues

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



A. D. Crossman School Kitchen Refurbishment ^(RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects


Contractor - CDW Services

Construction Phase

- Corrective work on grease trap to occur in January
- Anticipated Substantial January 2017

Contractual Substantial Completion – July 2016

Forecasted Substantial Completion – January 2017

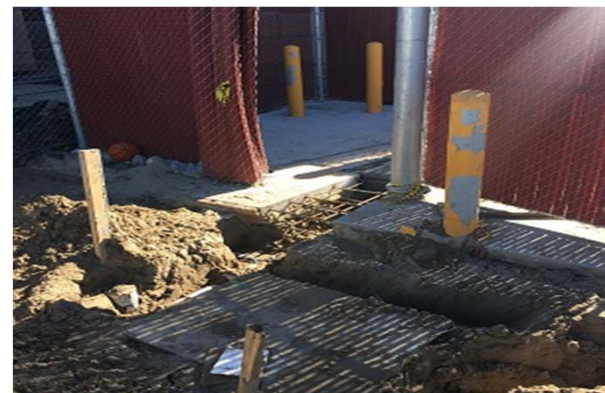

William J. Fischer Elementary School Refurbishment ^(RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Perez

Construction Phase

- Window installation continues
- Lighting installation is ongoing
- Contractor anticipated to request substantial completion in January

Contractual Substantial Completion – February 2017

Forecasted Substantial Completion – February 2017



Gaudet Elementary School Refurbishment ^(RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - One Construction

Construction Phase

- Contractor is working fire alarm system

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – January 2017



Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD)

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Crescent Commercial

Construction Phase

- Installation of new VCT will be removed from the contractor's scope
- Stair landings were poured over the Christmas break

Contractual Substantial Completion – February 2017

Forecasted Substantial Completion – February 2017



Andrew Jackson School Refurbishment (RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Construction Phase

- Contractor has moved on to the second floor and started window
- Exterior stucco repairs continue
- Exterior doors and frames are being installed
- New grease trap has been installed

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Tuna Construction

Construction Phase

- Window refurbishment is ongoing
- Work on stairwell #3 is nearing completion
- Dumpster pad work is 90% complete
- Sidewalk replacement continues

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Roof work was performed over Christmas Break
- Mechanical work continues
- Window replacement is ongoing

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017



Live Oak Elementary School Refurbishment ^(RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- Substantial Completion is anticipated in January
- Contractor is replacing damaged paved areas
- Contractor to repair asphalt at utility tie-in
- Work continues after school hours and on weekends

Contractual Substantial Completion – July 2017

Forecasted Substantial Completion – January 2017



Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- A&E to submit Bid Documents January 31st
- Anticipated Bid Opening – March 22nd

Procurement Phase

- Anticipated 1st Advertisement – February 2017
- Anticipated Bid Opening – March 2017



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- A&E to revise drawings

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



Village de l'Est Elementary School Refurbishment ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CBDG

Architect – Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

Construction Phase

- Substantial Completion October 12th

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – October 2016



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - TBD

Procurement Phase

- 1st Advertisement - February 1st
- 2nd Advertisement - February 8th
- 3rd Advertisement - February 15th
- Pre-Bid Conference - February 16th
- Bid Opening - March 8th



DEMOLITIONS

Demolition of Modular Buildings at Abramson and Carver ^(RSD)

5552 Read Boulevard and 3059 Higgins Boulevard, New Orleans, LA

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters, Inc.

Construction Phase

- Carver - Punch list walk December 8th
- Carver - Contractor to install water main shut off valve
- Abramson - Contractor to adjust ornamental fence

Contractual Substantial Completion – October 2016

Forecasted Substantial Completion – January 2017



Demolition of Modular Buildings at Livingston ^(RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – Concrete Busters of Louisiana

Construction Phase

- Removal of limestone continues
- Concrete sidewalks and canopy to be removed

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – February 2017



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
6	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
7	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
8	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
9	Alfred Lawless Senior ^(RSD)	12/18/2015
10	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
11	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
12	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
13	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
14	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
15	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
16	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
17	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
18	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
19	Augustine Elementary School Roof ^(RSD)	04/13/2012
20	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
21	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
22	Bell JH Shoring ^(RSD)	06/28/2011
23	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
24	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
25	Bienville Elementary School Demolition ^(RSD)	05/04/2009
26	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
27	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
28	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
29	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
30	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
31	Charles J. Colton Elementary School ^(RSD)	05/23/2013
32	Charles R. Drew Elementary School ^(RSD)	04/17/2015
33	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
34	Cohen High School Health Clinic ^(RSD)	12/24/2008
35	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
36	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
37	Douglass High School Under Floor Utilities ^(RSD)	
38	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
39	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
40	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
41	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
42	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
43	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011

44	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
45	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
46	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
47	Edna Karr High School - Assessment ^(OPSB)	
48	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
49	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
50	New Edward Hynes School ^(OPSB)	02/06/2012
51	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
52	Edward Livingston High School ^(RSD)	01/05/2015
53	Eleanor L. McMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
54	Eleanor L. McMain School Clinic ^(OPSB)	07/24/2013
55	Eleanor L. McMain School Maintenance Upgrades ^(OPSB)	12/12/2016
56	Eleanor L. McMain School Roof Replacement ^(OPSB)	05/13/2016
57	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
58	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
59	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
60	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
61	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
62	Francis W. Gregory Demolition ^(RSD)	12/21/2011
63	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
64	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
65	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
66	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
67	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
68	George Mondy Elementary School Mothball ^(RSD)	
69	George Washington Carver School ^(RSD)	03/07/2016
70	George Washington Carver High School Demolition ^(RSD)	08/24/2011
71	Greater St. Stephens School ^(OPSB)	03/18/2013
72	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
73	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
74	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
75	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
76	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
77	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
78	Holy Cross Modular Relocation ^(RSD)	12/14/2010
79	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
80	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
81	James Derham Demolition ^(RSD)	02/23/2012
82	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
83	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
84	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
85	John Dibert Elementary School Roof ^(RSD)	08/20/2010
86	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
87	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
88	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
89	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014

90	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
91	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
92	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
93	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
94	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
95	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
96	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
97	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
98	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
99	Lake Area Landry Demolition ^(RSD)	05/01/2008
100	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
101	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
102	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
103	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
104	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
105	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
106	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
107	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
108	Live Oak Elementary School Roof ^(RSD)	08/04/2011
109	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
110	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
111	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
112	Lusher Elementary School Refurbishment ^(OPSB)	10/31/2016
113	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
114	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
115	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
116	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
117	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
118	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
119	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
120	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
121	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
122	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
123	McDonogh #7 High School Repairs ^(OPSB)	
124	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
125	McDonogh #28 School Refurbishment ^(RSD)	03/15/2016
126	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
127	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
128	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
129	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
130	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
131	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
132	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
133	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
134	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012

135	Modular Campuses Close Outs ^(RSD)	
136	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
137	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010
138	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
139	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
140	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
141	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
142	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
143	New Carter G. Woodson School ^(RSD)	09/14/2012
144	New Fannie C. Williams School ^(RSD)	08/24/2012
145	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
146	New L.B. Landry High School ^(RSD)	06/30/2010
147	New Lake Area High School ^(RSD)	12/28/2009
148	New Lawrence D. Crocker School ^(RSD)	04/29/2013
149	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
150	New Parkview School ^(RSD)	10/12/2012
151	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
152	New William Frantz Elementary School ^(RSD)	
153	New Orleans High School Signature Center Study ^(RSD)	
154	Oretha C. Haley Demo ^(RSD)	05/07/2012
155	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
156	Parkview Elementary School Demolition ^(RSD)	08/06/2009
157	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
158	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
159	Paul B. Habans Elementary School ^(RSD)	06/30/2016
160	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
161	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
162	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
163	Rosenwald Elementary School Refurbishment ^(RSD)	04/07/2016
164	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
165	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
166	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
167	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
168	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
169	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
170	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
171	Schaumburg Chillers ^(RSD)	11/14/2008
172	Schwarz Alternative Repairs ^(RSD)	07/14/2009
173	Schwarz Alternative Modulares Demolition ^(RSD)	04/02/2015
174	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
175	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
176	Sherwood Forest Elementary School ^(RSD)	06/30/2016
177	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
178	Sophie B. Wright School Renovation ^(RSD)	06/08/2016
179	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
180	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011

181	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
182	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
183	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
184	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
185	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
186	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
187	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
188	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
189	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
190	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
191	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
192	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
193	Timbers HVAC ^(OPSB)	09/11/2013
194	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
195	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
196	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
197	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
198	Valena C. Jones Elementary School ^(RSD)	01/10/2013
199	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
200	Warren Easton High School Renovation ^(OPSB)	12/15/2015
201	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
202	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
203	New William J. Guste Elementary School ^(RSD)	10/06/2008
204	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
205	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
206	William Frantz Elementary School Roof ^(RSD)	08/12/2010
