Superintendent's Report May, 2017



Dr. Henderson Lewis Jr.Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Ms. Kunjan Narehania
Recovery School District



Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION Avery Alexander Elementary School (RSD) Benjamin Franklin Elementary School Renovation (OPSB) New Karr High School, CMAR (RSD) John McDonogh High School Renovation CMAR (RSD) Harriet R. Tubman Elementary School Renovation (RSD) Booker T. Washington School CMAR (RSD)	10 10 10 10 11 11
REFURBISHMENTS Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad (RSD) Agnes L. Bauduit Elementary School Refurbishment (OPSB) Mary M. Bethune Elementary School Refurbishment (OPSB) Warren Easton Courtyard Waterproofing (OPSB) William J. Fischer Elementary Refurbishment (RSD) William J. Fischer Elementary School HVAC Replacement (RSD) Andrew Jackson School Refurbishment (RSD) Lafayette Elementary School Refurbishment (RSD) Laurel Elementary School Refurbishment (RSD) Thurgood Marshall Elementary School Refurbishment (RSD) McDonogh #28 School Flooring Refurbishment (RSD) McDonogh #32 School Refurbishment (RSD) Harriet R. Tubman Elementary School Cottage Renovation (RSD) Schaumburg Roof & Harney Gutters & Downspouts (RSD) Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing (RSD)	12 12 12 13 13 13 14 14 14 15 15 15 16 16
DEMOLITIONS Demolition of Madulare at Abramaan 2 (RSD)	17
Demolition of Modulars at Abramson 3 (RSD) COMPLETED PROJECTS	17 18

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$562 million in open contracts for the capital program after issuing \$768 thousand in new contracts, change orders and amendments in May. In addition, the total change orders to date, \$10 million, account for one percent (1.88%) of the total open construction contracts. RSD anticipates issuing approximately \$896 thousand in construction contracts/change orders, and \$358 thousand in professional service contracts/amendments in June.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$232 million in open contracts for the capital program after issuing \$96 thousand in new contracts, change orders and amendments in May. In addition, the total change orders to date, \$9.1 million, account for approximately four percent (4.65%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 thousand in construction contracts/change orders and \$0 thousand in professional service contracts and amendments in June.

Status Date: 31 May 2017

2

Community Meetings



Future Community Meetings

3

Bid Openings

Projects which are scheduled to bid in the next 60 days

June 7, 2017

Abramson Modular Demolition Phase 3 Bid Opening

June 14, 2017

Benjamin Franklin Elementary School Renovation Bid Opening

July 6, 2017

Thurgood Marshall School Refurbishment Bid Opening

August 2, 2017

Harriet Tubman School Cottage Renovation Bid Opening



Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of May 31, 2017. The DBE subcontracts value is \$81,330,678 of the \$363,307,364 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 52 projects as of May 31, 2017. The DBE subcontracts value is \$21,479,653 of the \$67,828,085 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of May 31, 2017. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 2 projects as of May 31, 2017. The DBE subcontracts value is \$32,624,001 of the \$86,699,352 total of awarded contracts.

Total Amount of Contracts: \$626,972,358



New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of May 31, 2017. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.

Stabilization/Demolition/Mothballing:

5


DBE Contractors secured subcontracts on 2 projects as of May 31, 2017. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$231,354,830


* DBE provisions were included in projects bid after June 30, 2012



DDE provisions were included in projects bld diter suite 50, 2012

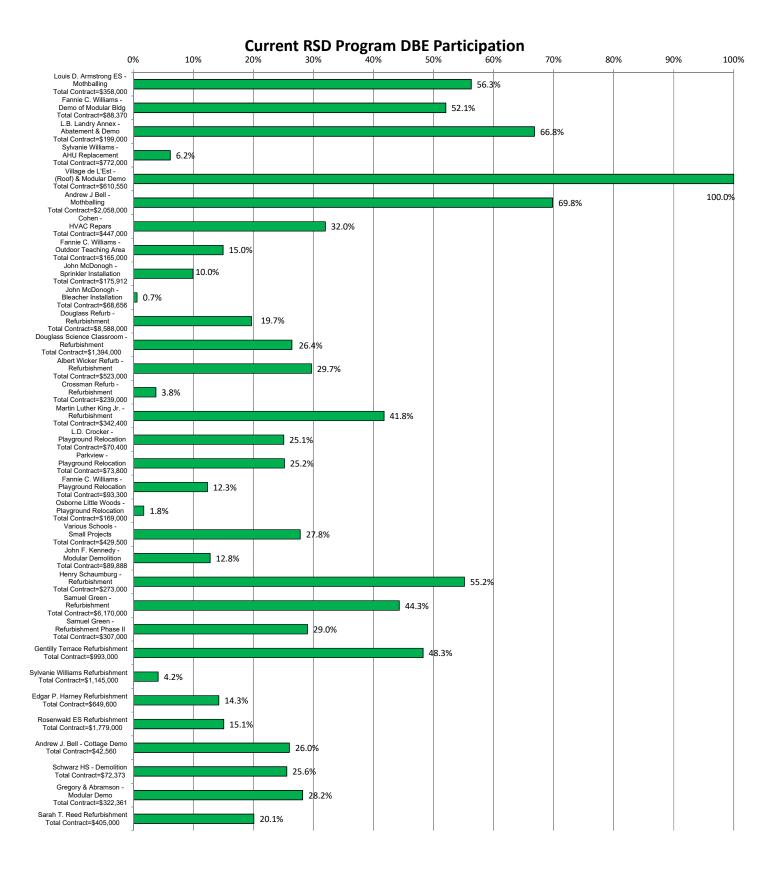


Current RSD Program DBE Participation

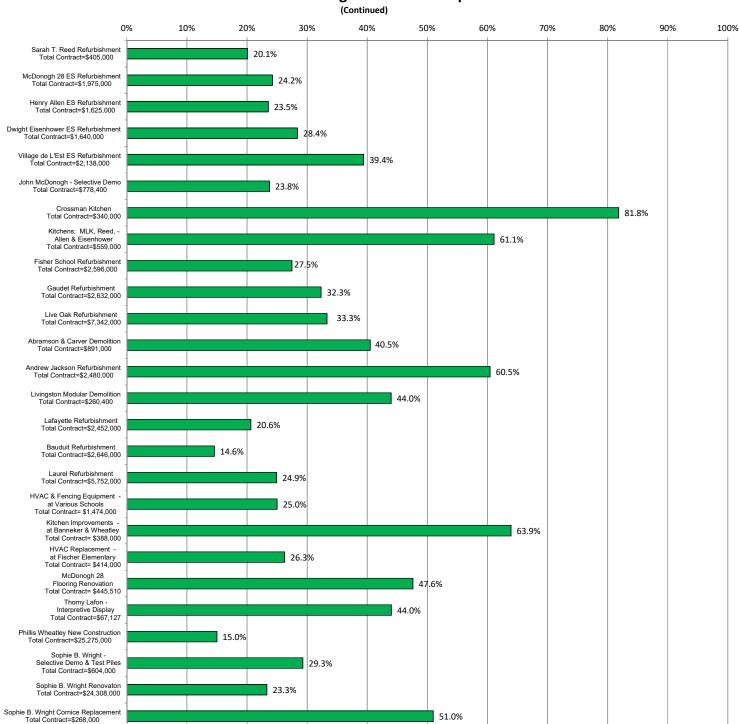

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

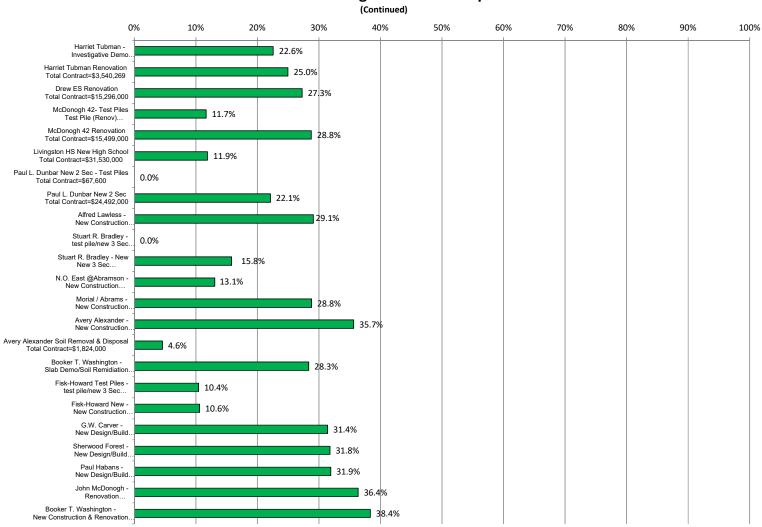

Notes: Data Based On Pre-Construction and/or monthly DBE Reports. RSD DBE Participation Target = 25% of Total Contract Amount

8

Current OPSB Program DBE Participation

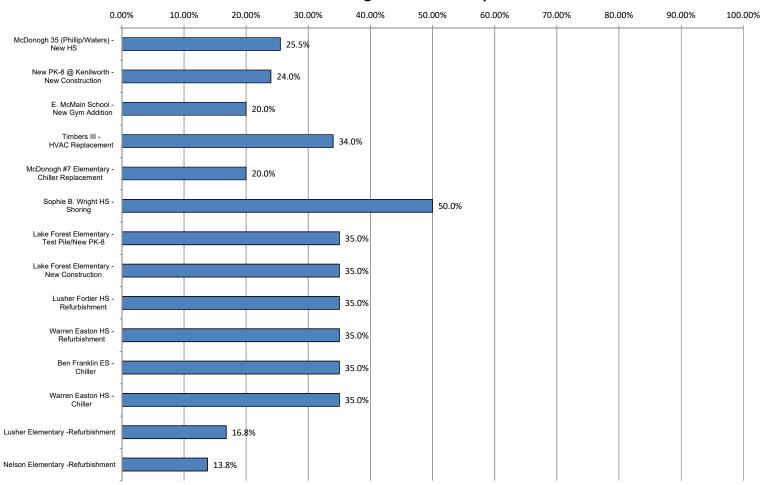

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

OPSB DBE Participation Target = 35% of Total Contract Amount

9

New & Major Renovation - Project Status

(Forecasted dates only include the next project phase)

Avery Alexander Elementary School (RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K - 8 School

Funding Source - FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- · Installation of landscaping and fencing is finishing
- Contractor is working in the punch list
- Commissioning and tab is underway

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – June 2017



Benjamin Franklin Elementary School Renovation (OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA Architect – N-Y Associates, Inc.

Contractor - TBD Procurement Phase

- 1st Advertisement May 10th
- 2nd Advertisement May 17th
- 3rd Advertisement May 24th
- · Pre-Bid Conference May 25th
- Bid Opening June 14th



New Karr High School CMAR (RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - TBD Design Phase

- 90% Construction Documents were received May 10th
- 100% Construction Documents are due June 14th

Contractual Substantial Completion – TBD Forecasted Substantial Completion – TBD



Status Date: 31 May 2017

10

John McDonogh High School Renovation CMAR (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source - FEMA

Architect - VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- · Installation of pile caps is underway
- Masonry tuckpointing is ongoing
- · Mechanical and electrical rough-in work is ongoing
- Interior wall framing continues on main building

Contractual Substantial Completion - October 2018

Forecasted Substantial Completion – October 2018



Harriet R. Tubman Elementary School Renovation (RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source - FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

Construction Phase

- · Repairs to sidewalks is ongoing
- · Refurbishment of windows continue
- · Floor replacement is ongoing on second floor
- Elevator trim out is underway
- · Exterior plaster repairs ongoing

Contractual Substantial Completion - May 2018

Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

11

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source - FEMA

Architect – Hewitt-Washington & Associates

Contractor - Core Construction

Construction Phase

- Slab on grade pours nearing completion
- Selective demolition has started in the Auditorium

Contractual Substantial Completion – January 2019

Forecasted Substantial Completion - January 2019



REFURBISHMENTS

Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad (RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16 2300 Dumaine Street. New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen at Banneker

and addition of grease trap at Wheatley

Funding Source – FEMA Architect – SCNZ Architects Contractor - Commander Corp Construction Phase

- Demolition at both schools is complete
- · A&E is reviewing the location of the exhaust hood at Banneker

Contractual Substantial Completion – September 2017

Forecasted Substantial Completion – September 2017



Agnes L. Bauduit Elementary School Refurbishment (RS

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect - Duplantis Design Group, PC

Contractor – One Construction

Construction Phase

- Window refurbishment is ongoing
- HVAC work is nearing completion
- · Interior finishes are being installed on the third floor
- Roof working is ongoing

Contractual Substantial Completion – May 2017 Forecasted Substantial Completion – July 2017



Mary M. Bethune Elementary School Refurbishment (OPSB)

4040 Eagle Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect – Chenevert Architects

Contractor – Construction Masters Inc.

Construction Phase

Interior demolition has started

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017



Warren Easton School Courtyard Waterproofing (OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Repairs to courtyard waterproofing

Funding Source - FEMA

Architect – Chenevert Architects LLC Contractor - Thigpen Construction Company

Construction Phase

- Contractor has mobilized
- Brick and mortar repairs have started

Contractual Substantial Completion – November 2017 Forecasted Substantial Completion – November 2017



William J. Fischer Elementary School Refurbishment (RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG Architect – SCNZ Architects

Contractor - Perez
Construction Phase

- · Project is in warranty period
- Contractor to fix fencing issues

Contractual Substantial Completion – January 2017 Actual Substantial Completion – January 2017



William J. Fischer Elementary School HVAC Replacement (RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Replacement of existing HVAC

Funding Source – FEMA Architect – SCNZ Architects Contractor - Blanchard Mechanical

Construction Phase

Notice to Proceed has been issued
 Contractual Substantial Completion – August 2017
 Forecasted Substantial Completion – August 2017



Andrew Jackson School Refurbishment (RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - CDW Services Construction Phase

- 2nd floor and 3rd floor window refurbishment is complete
- Contractor is finishing exterior envelope work
- Work on the dumpster pads continues

Contractual Substantial Completion – June 2017 Forecasted Substantial Completion – July 2017



Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16 Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA Architect – N-Y Associates, Inc. Contractor - Tuna Construction

Construction Phase

- Window sash refurbishment continues
- · Main stairwell work is finishing up
- · Work in the 2nd floor classrooms is finishing
- Abatement is nearing completion

Contractual Substantial Completion – July 2017 Forecasted Substantial Completion – July 2017



Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA, CDBG

Architect - Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Installation of VCT continues
- HVAC units are being installed
- Window replacement continues
- · Ceiling grid in the cafeteria is underway

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017



Status Date: 31 May 2017

14

Thurgood Marshall Elementary School Refurbishment (RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source - FEMA

Architect - Mahlum Scairono Martinez JV

Contractor - TBD

Procurement Phase

- 1st Advertisement May 31st
- 2nd Advertisement June 7th
- 3rd Advertisement June 14th
- Pre-Bid Conference June 15th
- · Bid Opening July 6th



McDonogh #28 School Flooring Refurbishment (RSD)

2733 Esplanade Boulevard, New Orleans, LA 70114 District A Ward 7

Scope of work: Refurbishment of existing elementary school flooring

Funding Source – FEMA, CDBG Architect – SCNZ Architects Contractor - Insultech Construction Phase

- Notice to Proceed is anticipated June 12th
- Contractor is mobilizing

Contractual Substantial Completion – August 2017 Forecasted Substantial Completion – August 2017



McDonogh #32 School Refurbishment (RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects Contractor - TBD

Design Phase - CD

· Project place "On Hold"



Harriet R. Tubman Elementary School Cottage Renovation (RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing cottage to meet code requirements

Funding Source - FEMA Architect - Mahlum Scairono Martinez JV Contractor - TBD

- **Procurement Phase**
 - 1st Advertisement June 28th
 - 2nd Advertisement July 5th
 - 3rd Advertisement July 12th
 - Pre-Bid Conference June 13th
 - · Bid Opening August 2nd



Schaumburg Roof & Harney Gutters & Downspouts (RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9 2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of roof at Schaumberg and gutters at Harney

Funding Source - FEMA Architect – Scairono Martinez Contractor - TBD

Design Phase

- 50% Construction Documents are due June 30th
- 100% Construction Documents are due August 7th

Contractual Substantial Completion - TBD Forecasted Substantial Completion - TBD



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing (RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source - FEMA

Architect - Marrero Couvillion & Associates

Contractor - Industrial and Mechanical Contractors, Inc.

Construction Phase

- Notice to Proceed is anticipated June 14th
- Contractor is mobilizing

Contractual Substantial Completion - November 2017 Forecasted Substantial Completion - November 2017



DEMOLITIONS

Demolition of Modular Buildings at Abramson 3 $\,^{(RSD)}$

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – TBD <u>Procurement Phase</u>

- 1st Advertisement May 3rd
- 2nd Advertisement May 10th
- 3rd Advertisement May 17th
- Pre-Bid Conference May 18th
- Bid Opening June 7th



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition (RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation (RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School (RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment (RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment (RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs (RSD)	06/13/2013
7	Agnes Bauduit Elementary School Boiler (RSD)	12/07/2009
8	Albert Wicker Elementary School Refurbishment (RSD)	03/27/2014
9	Albert Wicker Elementary School Roof Repairs (RSD)	06/13/2013
10	Alfred Lawless Senior (RSD)	12/18/2015
11	Alfred Lawless Senior High Security Fencing (RSD)	06/15/2011
12	Alice M. Harte Elementary School (OPSB)	11/19/2014
13	Alice M. Harte Elementary School Demolition (OPSB)	12/14/2011
14	Andrew J. Bell Junior High School Roof Replacement (RSD)	02/08/2014
15	Andrew J. Bell Junior High School Mothball (RSD)	06/28/2011
16	Andrew Jackson Elementary School Roof Repairs (RSD)	07/27/2012
17	Andrew Jackson Elementary School Solar Panels (RSD)	01/14/2013
18	Andrew H. Wilson Elementary School Cottage (RSD)	10/11/2010
19	Arthur Ashe Elementary School Kitchen Renovation (OPSB)	
20	Augustine Elementary School Roof (RSD)	04/13/2012
21	Avery-Alexander Elementary School Demolition (RSD)	06/15/2012
22	Barbara C. Jordan Elementary School Demolition (RSD)	05/30/2011
23	Bell JH Shoring (RSD)	06/28/2011
24	Benjamin Banneker Elementary School Energy Conservation (RSD)	
25	Benjamin Franklin Senior High School (OPSB)	08/23/2013
26	Bienville Elementary School Demolition (RSD)	05/04/2009
27	Booker T. Washington High School Environmental Remediation (RSD)	12/13/2015
28	Booker T. Washington High School Partial Demolition (RSD)	04/07/2013
29	Carter G. Woodson Middle School Demolition (RSD)	02/09/2010
30	Central Services Warehouse Demolition (OPSB)	01/05/2012
31	Charles J. Colton Elementary Selective Demolition (RSD)	07/26/2010
32	Charles J. Colton Elementary School (RSD)	05/23/2013
33	Charles R. Drew Elementary School (RSD)	04/17/2015
34	Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)	06/08/2011
35	Cohen High School Health Clinic (RSD)	12/24/2008
36	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School (RSD)	
37	Demolition of Modular Buildings at Gregory and Abramson (RSD)	06/23/2015
38	Demolition of Modular Buildings at Abramson and Carver (RSD)	01/18/2017
39	Demolition of Modular Buildings at Livingston (RSD)	01/18/2017
40	Douglass High School Under Floor Utilities (RSD)	0//40/0040
41	Dr. Martin Luther King School Roof Repairs (RSD)	06/13/2012
42	Dr. Martin Luther King Jr. School Renovation (RSD)	12/15/2014
43	Dwight D. Eisenhower Elementary School Kitchen Refurbishment (RSD)	02/18/2016

4.4	Decision Decision of the Color of Decision (RSD)	07/27/2012
44	Dwight D. Eisenhower Elementary School Roof Repairs (RSD)	07/27/2012
45 44	Dwight D. Eisenhower Elementary School Refurbishment (RSD)	12/23/2015
46 47	East Bank Swing Space for Audubon Charter School (OPSB)	12/30/2011
47	Edgar P. Harney Elementary School Refurbishment (RSD)	04/12/2012
48	Edgar P. Harney Elementary School Roof Repairs (RSD)	06/13/2012
49	Edna Karr High School - Gymnasium Repair (OPSB)	12/23/2013
50	Edna Karr High School - Assessment (OPSB)	00/20/2010
51	Edward Livingston Middle School Demolition (RSD)	09/28/2010
52	Edward Henry Phillips Junior High School Demolition (OPSB)	11/19/2010
53 E4	New Edward Hynes School (OPSB) Edwards Hynes School (RSD)	02/06/2012 11/03/2008
54	Edwards Hardin Lockett Lawless Demolition (RSD)	
55 54	Edward Livingston High School (RSD)	01/05/2015
56	Eleanor L. McMain School Replacement of Existing Chillers (OPSB)	08/30/2011
57	Eleanor L. McMain School Clinic (OPSB)	07/24/2013
58	Eleanor L. McMain School Maintenance Upgrades (OPSB)	12/12/2016
59	Eleanor L. McMain School Roof Replacement (OPSB)	05/13/2016
60	Ernest "Dutch" Morial Elementary (RSD)	03/17/2017
61	Ernest N. Morial Elementary Security Fencing (RSD)	05/10/2011
62	Fannie C. Williams Elementary School Demolition (RSD)	03/10/2009
63	Fisk-Howard Elementary School Demolition (RSD)	10/04/2011
64	Florence J. Chester Elementary School Demolition (RSD)	06/05/2011
65	Fortier (Lusher) High School Refurbishment (OPSB)	02/05/2016
66	Francis W. Gregory Demolition (RSD)	12/21/2011
67	Frederick A. Douglass High Refurbishment (RSD)	10/28/2014
68	Frederick A. Douglass High School Science Lab (RSD)	07/05/2016
69	Frederick A. Douglass High Switchgear (RSD)	08/04/2009
70	Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)	
71	Gaudet Elementary School Refurbishment (RSD)	12/20/2016
72	Gentilly Terrace Elementary School Refurbishment (RSD)	09/22/2015
73	George Mondy Elementary School Mothball (RSD)	
74	George Washington Carver School (RSD)	03/07/2016
75	George Washington Carver High School Demolition (RSD)	08/24/2011
76	Greater St. Stephens School (OPSB)	03/18/2013
77	Harriet R. Tubman Elementary School Selective Demolition (RSD)	12/14/2014
78	Henry Allen Elementary School Refurbishment (RSD)	03/08/2016
79	Henry Allen Elementary School Kitchen Refurbishment (RSD)	02/18/2016
80	Henry Allen Elementary School Roof (RSD)	05/24/2010
81	Henry C. Schaumburg School Refurbishment (RSD)	06/26/2015
82	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation (RSD)	12/16/2011
83	Holy Cross Modular Relocation (RSD)	12/14/2010
84	Israel M. Augustine Middle School Roof Replacement (RSD)	04/13/2012
85	Israel M. Augustine Middle School Mothball (RSD)	01/18/2013
86	James Derham Demolition (RSD)	02/23/2012
87	James W. Johnson Elementary School Roof (RSD)	07/31/2010
88	New Jean Batiste de Bienville School (RSD)	06/15/2012
89	Jean Gordon Elementary School Demolition (RSD)	08/16/2010

90	JoEllen Smith Medical Center Demolition (OPSB)	
91	John Dibert Elementary School Roof (RSD)	08/20/2010
92	John W. Hoffman Elementary School Demolition (RSD)	05/25/2010
93	John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)	11/05/2010
94	John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)	08/05/2011
95	John F. Kennedy Modular Demolition (RSD)	09/16/2014
96		01/12/2012
	John F. Kennedy High School Demolition (RSD)	03/27/2014
97	John McDonogh Senior High School Bleachers and Sprinklers (RSD)	
98	John McDonogh Senior High School Roof (RSD)	05/04/2010
99	John A. Shaw Elementary School Mothball (RSD)	12/12/2012
100	Joseph S. Clark Senior High School Roof Repairs (RSD)	07/27/2012
101	Joseph A. Craig Elementary Canopies (RSD)	06/06/2011
	Joseph A. Craig Elementary Elevator Installation (RSD)	01/20/2012
103	Joseph A. Hardin Elementary Security Fencing (RSD)	05/10/2011
	Lafayette Elementary School Roof and Masonry (RSD)	06/22/2012
	Lake Area Landry Demolition (RSD)	05/01/2008
	Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)	11/13/2015
	Langston Hughes Elementary School (Phase I) (RSD)	08/11/2009
	Langston Hughes Elementary School - New Gymnasium (Phase II) (RSD)	11/10/2010
	Langston Hughes Elementary School - Dumpster Pad (RSD)	10/12/2012
	Lawrence D. Crocker Elementary School Demolition (RSD)	04/02/2010
	L.B. Landry Annex Demolition (RSD)	05/02/2013
	Little Woods Elementary School Demolition (RSD)	08/09/2010
	Little Woods School (Dolores T. Aaron Elementary School) (RSD)	08/01/2013
	Live Oak Elementary School Refurbishment (RSD)	01/06/2017
	Live Oak Elementary School Roof (RSD)	08/04/2011
116	Live Oak Elementary School Exterior Door Replacement (RSD)	08/26/2011
117	Lorraine Hansberry Elementary School Mothball (RSD)	12/27/2012
118	Louis D. Armstrong Elementary School (RSD)	02/18/2013
119	Lusher Elementary School Refurbishment (OPSB)	10/31/2016
120	Mahalia Jackson Elementary School (OPSB)	05/11/2010
121	Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)	03/06/2012
122	Mahalia Jackson Elementary School Office Renovation (OPSB)	04/30/2013
123	Martin Behrman Elementary School Roof (RSD)	02/23/2010
124	Martin Luther King Jr. Elementary Canopy System (RSD)	11/05/2011
125	Martin Luther King Jr. School Modular Building, Deck, Canopy (RSD)	07/31/2012
126	Martin Luther King Jr. School Kitchen Refurbishment (RSD)	02/18/2016
127	Mary Church Terrell Elementary School Demolition (RSD)	04/17/2013
128	Mary M. Bethune Elementary 1st Floor Replacement (OPSB)	01/24/2011
129	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)	01/21/2011
130	McDonogh #7 High School Repairs (OPSB)	
131	McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)	06/11/2012
132	McDonogh #28 School Refurbishment (RSD)	03/15/2016
133	McDonogh #28 Elementary School Roof (RSD)	11/19/2011
134	McDonogh #32 Roof Replacement (RSD)	02/24/2012
		5=.= 24.2

	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior	
135	Ramp & Handicap Seating in the Auditorium (OPSB)	01/17/2014
136	McDonogh #35 School at the Phillip/ Waters Site (OPSB)	09/23/2015
137	McDonogh #42 Elementary School Renovation (RSD)	05/28/2015
138	McDonogh #42 Elementary School Roof (RSD)	12/21/2011
139	McDonogh #42 Elementary School HVAC Replacement (RSD)	08/09/2010
140	Mildred C. Osborne Elementary School Demolition (RSD)	02/18/2010
141	Mildred C. Osborne Elementary School (RSD)	12/03/2012
142	(DCD)	
143	Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)	05/22/2013
144	Modular Structures at Langston Hughes Elementary School (RSD)	04/05/2010
145	Morris F.X. Jeff Elementary School Demolition (RSD)	
146	Morris F.X. Jeff Elementary School Mothball (RSD)	01/15/2013
147	Murray G. Henderson Elementary School Roof (RSD)	06/23/2012
148	Nelson Elementary School Refurbishment (OPSB)	04/18/2016
149	New Andrew H. Wilson Elementary School (RSD)	10/11/2009
150	New Carter G. Woodson School (RSD)	09/14/2012
151	New Fannie C. Williams School (RSD)	08/24/2012
152	New Joseph A. Craig Elementary School (RSD)	12/09/2009
153	New L.B. Landry High School (RSD)	06/30/2010
154	New Lake Area High School (RSD)	12/28/2009
155	New Lawrence D. Crocker School (RSD)	04/29/2013
156		01/29/2016
157	New Parkview School (RSD)	10/12/2012
158	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD)	
159	New William Frantz Elementary School (RSD)	
160	New Orleans High School Signature Center Study (RSD)	
161	· · · · · · · · · · · · · · · · · · ·	05/07/2012
	Oretha C. Haley Elementary School Mothball (RSD)	09/17/2012
	Parkview Elementary School Demolition (RSD)	08/06/2009
164	Paul L. Dunbar Elementary School Demolition (RSD)	06/16/2010
165	Paul L. Dunbar Elementary School (RSD)	06/02/2015
166	Paul B. Habans Elementary School (RSD)	06/30/2016
167	Paul B. Habans Elementary School Roof Repairs (RSD)	07/27/2012
168	Phillis Wheatley Elementary School Demolition (RSD)	09/26/2011
169	Phillis Wheatley Elementary School (RSD)	07/10/2014
170	Ray Abrams Elementary School (RSD)	03/17/2017
171	Rosenwald Elementary School Refurbishment (RSD)	04/07/2016
172	Robert M. Lusher Elementary Roof Removal & Replacement (OPSB)	07/14/2011
173	Samuel J. Green Elementary School Refurbishment (RSD) Samuel J. Green Elementary School Refurbishment rnase 2	02/15/2016
174	(RSD)	02/15/2016
175	Sarah T. Reed High School Bleachers (RSD)	01/11/2012
176	Sarah T. Reed High School Auditorium Wall (RSD)	03/29/2010
177	Sarah T. Reed High School Kitchen Refurbishment (RSD)	02/18/2016
178	Sarah T. Reed High School Refurbishment (RSD)	12/01/2015
179	Seabrook Computer Training Center Demolition (OPSB)	06/25/2010

100	Calculation (RSD)	11/14/2000
	Schaumburg Chillers (RSD)	11/14/2008 07/14/2009
181	Schwarz Alternative Repairs (RSD)	
	Schwarz Alternative Modulars Demolition (RSD)	04/02/2015
183	Schwarz Modular Building Demolition (RSD)	04/02/2015
184	Sherwood Forest Elementary School Demolition (RSD)	10/28/2010
185	,	06/30/2016
186	Small New Orleans East High School at Abramson (RSD)	09/24/2015
187	Sophie B. Wright School Renovation (RSD)	06/08/2016
188	Sophie B. Wright School Selective Demolition (RSD)	01/31/2014
189	Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)	07/26/2011
190	Stuart R. Bradley Elementary School Demolition (RSD)	01/27/2010
191	Stuart R. Bradley Elementary School (RSD)	06/26/2015
	Sylvanie Williams Elementary School AHU Replacement (RSD)	07/30/2013
193	Sylvanie Williams Elementary School Play Yard (RSD)	09/23/2010
194	Sylvanie Williams Elementary School Roof Repairs (RSD)	07/27/2012
195	Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)	04/13/2012
196	Sylvanie Williams Elementary School Refurbishment (RSD)	02/18/2016
197	Temporary Campus for McDonogh #11 Expropriation (OPSB)	
	Thomas A. Edison Elementary School Demolition (RSD)	03/25/2010
199	Thomy Lafon Elementary School Demolition (RSD)	11/27/2011
200	Thomy Lafon School Interpretative Display (RSD)	10/15/2013
201	Timbers Park Office Building #1 & #2 Demolition (OPSB)	09/18/2011
202	Timbers HVAC (OPSB)	09/11/2013
203	Timbers III - IT Room Relocation (OPSB)	02/11/2015
	Village de L'est Elementary School Subsidence (RSD)	06/18/2012
	Village de L'est Elementary School Refurbishment (RSD)	10/12/2106
	Village de L'est Elementary School Roof and Modular Demolition (RSD)	06/16/2013
	Vorice J. Waters Elementary School Demolition (RSD)	01/14/2010
	Valena C. Jones Elementary School (RSD)	01/10/2013
209	(DCD)	04/04/2014
210	Warren Easton High School Renovation (OPSB)	12/15/2015
211	Warren Easton High School Window Replacement (OPSB)	09/07/2012
	West Bank Swing Space for Alice Harte Elementary School (OPSB)	07/11/1931
213	New William J. Guste Elementary School (RSD)	10/06/2008
214	William J. Guste Elementary School Science Lab (RSD)	08/04/2009
	William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)	04/15/2010
210	William Frantz Elementary School Roof (RSD)	08/12/2010
