
# Superintendent's Report October 2022







**Dr. Cade Brumley**Louisiana Department
of Education





## **Table of Contents**

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
FUTURE COMMUNITY MEETINGS	3
BID OPENINGS	3
DBE OVERVIEW MONTHLY SUMMARY	4
NEW & MAJOR RENOVATION	8
Behrman Elementary School CMaR (RSD)	8
Career Technical Education High School at Kerlerec Street CMaR (RSD)	8
New Cohen High School CMaR (RSD)	8
COMPLETED PROJECTS	g

## **Overview**

### **FINANCIAL OVERVIEW - ALL PROJECTS**



The RSD has \$152 million in open contracts for the capital program after issuing \$72 thousand in new contracts, change orders and amendments in October. In addition, the total change orders to date, \$ 234 thousand, account for less than one percent (0.23%) of the total open construction contracts. RSD anticipates issuing approximately \$0 thousand in construction contracts/change orders, and \$408 thousand in professional service contracts/amendments in November.

# **Future Community Meetings**

**None Scheduled** 

# **Bid Openings**

**None Scheduled** 



# **Disadvantaged Business Enterprises (DBE) Monthly Summary**

## **Recovery School District**

#### New & Renovations:

DBE Contractors secured subcontracts on 27 projects as of October 31, 2022. The DBE subcontracts value is \$84,866,010 of the \$372,937,728 total of awarded contracts.

### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 65 projects as of October 31, 2022. The DBE subcontracts value is \$24,723,075 of the \$78,177,771 total of awarded contracts.

### **Design-Build New:**


DBE Contractors secured subcontracts on 3 projects as of October 31, 2022. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

#### CMAR New:

DBE Contractors secured subcontracts on 6 projects as of October 31, 2022. The DBE subcontracts value is \$88,312,336 of the \$241,997,237 total of awarded contracts.

Total Amount of Contracts: \$802,250,293


<sup>\*</sup> DBE provisions were included in projects bid after June 30, 2012

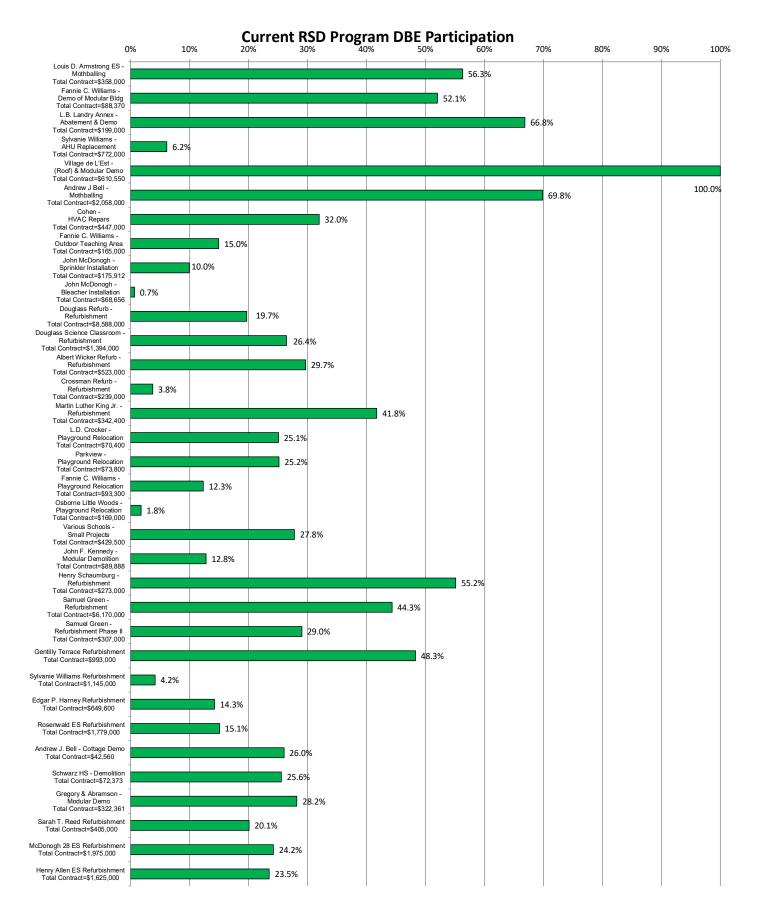

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount


## **Current RSD Program DBE Participation**

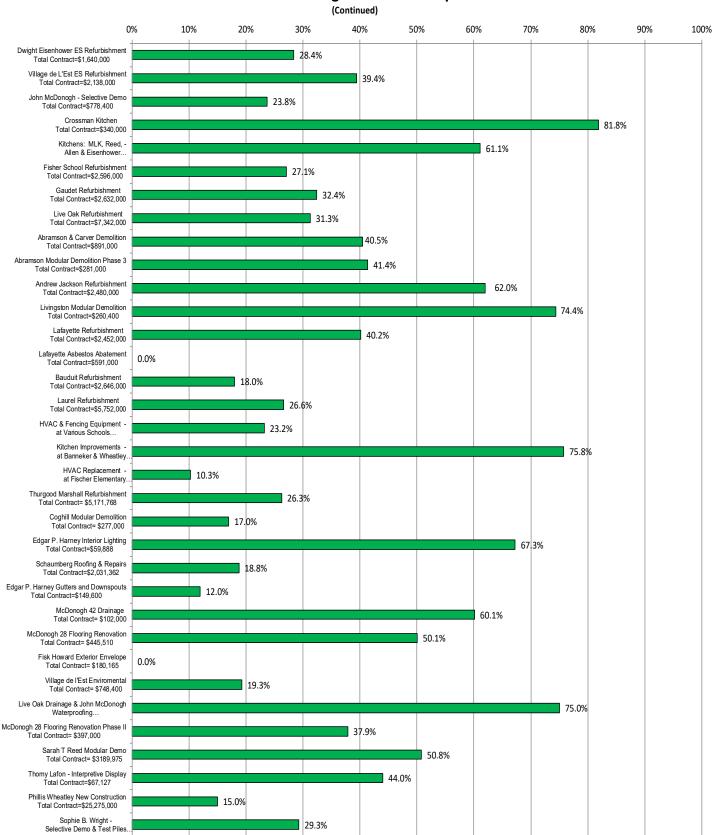

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

## **Current RSD Program DBE Participation**

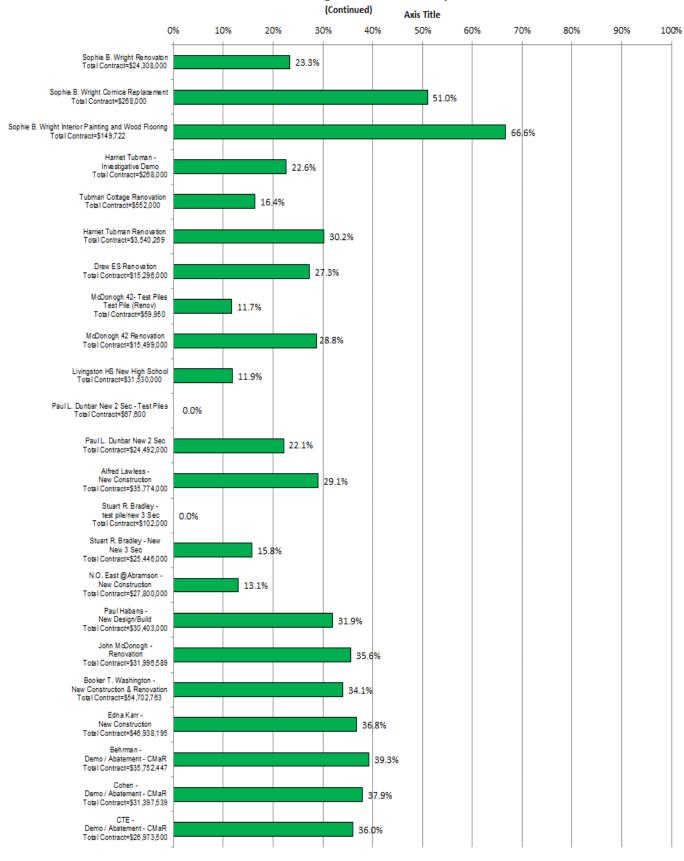

## **New & Major Renovation - Project Status**

(Forecasted dates only include the next project phase)

## Behrman Elementary School CMaR (RSD)

3819 Hershel Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect - Waggonner & Ball Architects

Contractor - Landis Construction

#### Construction Phase

- Walk-in cooler/freezer near completion
- Landscaping continues
- Punchlist work ongoing
- Terrazzo floor installation underway at ELC
- Gym equipment installation near completion



# Career Technical Education High School at Kerlerec Street CMAR (RSD)

1331 Kerlerec Street, New Orleans, LA 70116 District D Ward 7

Scope of work: Renovation of existing high school

Funding Source - CDBG

Architect - SCNZ Architects

Contractor - Broadmoor Construction

### Construction Phase

- Storm drainage ongoing
- Interior signage near completion
- Storefront entrance hardware installation in progress
- · Security and access control wiring near completion



## New Cohen High School CMAR (RSD)

3520 Dry ades Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Construction of new high school

Funding Source - FEMA / CDBG

Architect - HMS Architects

Contractor - The Lemoine Company

#### Construction Phase

- · Commissioning of HVAC continues
- Installation of exterior landscaping continues
- Final cleaning on 2nd and 3rd floor
- TCO issued 10/25/2022



## **Comprehensive List - Completed Projects**

1	Abrams   Morial   Abramson   Coghill Demolition (RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation (RSD)	11/11/2000
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School (RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment (RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment (RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs (RSD)	06/13/2013
_		10/31/2017
7	Agnes Bauduit Elementary School Refurbishment (RSD)	
8	Agnes Bauduit Elementary School Boiler (RSD)	12/07/2009
9	Albert Wicker Elementary School Refurbishment (RSD)	03/27/2014
10	Albert Wicker Elementary School Roof Repairs (RSD)	06/13/2013
11	Alfred Lawless Senior (RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing (RSD)	06/15/2011
13	Alice M. Harte Elementary School (OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition (OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement (RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball (RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs (RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels (RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage (RSD)	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation (OPSB)	
21	Augustine Elementary School Roof (RSD)	04/13/2012
22	Avery-Alexander Elementary School (RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition (RSD)	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad (RSD)	10/30/2017
25	Barbara C. Jordan Elementary School Demolition (RSD)	05/30/2011
26	Bell JH Shoring (RSD)	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation (RSD)	
28	Benjamin Franklin Senior High School (OPSB)	08/23/2013
29	Bienville Elementary School Demolition (RSD)	05/04/2009
30	Booker T. Washington High School Environmental Remediation (RSD)	12/13/2015
31	Booker T. Washington High School Partial Demolition (RSD)	04/07/2013
32	Carter G. Woodson Middle School Demolition (RSD)	02/09/2010
33	Central Services Warehouse Demolition (OPSB)	01/05/2012
34	Charles J. Colton Elementary Selective Demolition (RSD)	07/26/2010
35	Charles J. Colton Elementary School (RSD)	05/23/2013
36	Charles R. Drew Elementary School (RSD)	04/17/2015
37	Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)	06/08/2011
38	Cohen High School Health Clinic (RSD)	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School (RSD)	
40	Demolition of Modular Buildings at Coghill (RSD)	12/26/2018
41	Demolition of Modular Buildings at Gregory and Abramson (RSD)	06/23/2015
42	Demolition of Modular Buildings at Abramson and Carver (RSD)	01/18/2017

43	Demolition of Modular Buildings at Livingston (RSD)	01/18/2017
44	Douglass High School Under Floor Utilities (RSD)	
45	Dr. Martin Luther King School Roof Repairs (RSD)	06/13/2012
46	Dr. Martin Luther King Jr. School Renovation (RSD)	12/15/2014
47	Dwight D. Eisenhower Elementary School Kitchen Refurbishment (RSD)	02/18/2016
48	Dwight D. Eisenhower Elementary School Roof Repairs (RSD)	07/27/2012
49	Dwight D. Eisenhower Elementary School Refurbishment (RSD)	12/23/2015
50	East Bank Swing Space for Audubon Charter School (OPSB)	12/30/2011
51	Edgar P. Harney Elementary School Refurbishment (RSD)	
52	Edgar P. Harney Elementary School Roof Repairs (RSD)	06/13/2012
53	Edgar P. Harney Elementary School Downspouts and Gutters (RSD)	01/09/2019
54	Edgar P. Harney Elementary School Lighting Repairs (RSD)	08/08/2018
55	Edna Karr High School - Gymnasium Repair (OPSB)	12/23/2013
56	Edna Karr High School - Assessment (OPSB)	
57	Edward Livingston Middle School Demolition (RSD)	09/28/2010
58	Edward Henry Phillips Junior High School Demolition (OPSB)	11/19/2010
59	New Edward Hynes School (OPSB)	02/06/2012
60	Edwards   Hardin   Lockett   Lawless Demolition (RSD)	11/03/2008
61	Edward Livingston High School (RSD)	01/05/2015
62	Eleanor L. McMain School Replacement of Existing Chillers (OPSB)	08/30/2011
63	Eleanor L. McMain School Clinic (OPSB)	07/24/2013
64	Eleanor L. McMain School Maintenance Upgrades (OPSB)	12/12/2016
65	Eleanor L. McMain School Roof Replacement (OPSB)	05/13/2016
66	Ernest "Dutch" Morial Elementary (RSD)	03/17/2017
67	Ernest N. Morial Elementary Security Fencing (RSD)	05/10/2011
68	Fannie C. Williams Elementary School Demolition (RSD)	03/10/2009
69	Fisk-Howard Elementary School Demolition (RSD)	10/04/2011
70	Florence J. Chester Elementary School Demolition (RSD)	06/05/2011
71	Fortier (Lusher) High School Refurbishment (OPSB)	02/05/2016
72	Francis W. Gregory Demolition (RSD)	12/21/2011
73	Frederick A. Douglass High Refurbishment (RSD)	10/28/2014
74	Frederick A. Douglass High School Science Lab (RSD)	07/05/2016
75	Frederick A. Douglass High Switchgear <sup>(RSD)</sup>	08/04/2009
76	Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)	
77	Gaudet Elementary School Refurbishment (RSD)	12/20/2016
78	Gentilly Terrace Elementary School Refurbishment (RSD)	09/22/2015
79	George Mondy Elementary School Mothball (RSD)	
80	George Washington Carver School (RSD)	03/07/2016
81	George Washington Carver High School Demolition (RSD)	08/24/2011
82	Greater St. Stephens School (OPSB)	03/18/2013
83	Harriet R. Tubman Elementary School Selective Demolition (RSD)	12/14/2014
84	Harriet R. Tubman Elementary School Renovation (RSD)	08/01/2018
85	Harriet R. Tubman Cottage Renovation (RSD)	08/02/2018
86	Henry Allen Elementary School Refurbishment (RSD)	03/08/2016
87	Henry Allen Elementary School Kitchen Refurbishment (RSD)	02/18/2016
88	Henry Allen Elementary School Roof (RSD)	05/24/2010

	(PSD)	00/00/0045
89	Henry C. Schaumburg School Refurbishment (RSD)	06/26/2015
90	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation (RSD)	12/16/2011
91	Holy Cross Modular Relocation (RSD)	12/14/2010
92	Israel M. Augustine Middle School Roof Replacement (RSD)	04/13/2012
93	Israel M. Augustine Middle School Mothball (RSD)	01/18/2013
94	James Derham Demolition (RSD)	02/23/2012
95	James W. Johnson Elementary School Roof <sup>(RSD)</sup>	07/31/2010
96	New Jean Batiste de Bienville School (RSD)	06/15/2012
97	Jean Gordon Elementary School Demolition (RSD)	08/16/2010
98	JoEllen Smith Medical Center Demolition (OPSB)	
99	John Dibert Elementary School Roof <sup>(RSD)</sup>	08/20/2010
100	John W. Hoffman Elementary School Demolition (RSD)	05/25/2010
101	John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)	11/05/2010
102	John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)	08/05/2011
103	John F. Kennedy Modular Demolition (RSD)	09/16/2014
104	John F. Kennedy High School Demolition (RSD)	01/12/2012
105	John McDonogh Senior High School Bleachers and Sprinklers (RSD)	03/27/2014
106	John McDonogh Senior High School Roof (RSD)	05/04/2010
107	John A. Shaw Elementary School Mothball (RSD)	12/12/2012
108	Joseph S. Clark Senior High School Roof Repairs (RSD)	07/27/2012
109	Joseph A. Craig Elementary Canopies (RSD)	06/06/2011
110	Joseph A. Craig Elementary Elevator Installation (RSD)	01/20/2012
111	Joseph A. Hardin Elementary Security Fencing (RSD)	05/10/2011
112	Lafayette Elementary School Roof and Masonry (RSD)	06/22/2012
	Lake Area   Landry Demolition (RSD)	05/01/2008
	Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)	11/13/2015
	Langston Hughes Elementary School (Phase I) (RSD)	08/11/2009
	Langston Hughes Elementary School - New Gymnasium (Phase II) (RSD)	11/10/2010
117		10/12/2012
	Lawrence D. Crocker Elementary School Demolition (RSD)	04/02/2010
	Laurel Elementary School Refurbishment (RSD)	01/03/2018
120	L.B. Landry Annex Demolition (RSD)	05/02/2013
121	Little Woods Elementary School Demolition (RSD)	08/09/2010
	Little Woods School (Dolores T. Aaron Elementary School) (RSD)	08/01/2013
123		01/06/2017
124	Live Oak Elementary School Roof (RSD)	08/04/2011
125	-	08/26/2011
126	Lorraine Hansberry Elementary School Mothball (RSD)	12/27/2012
127		02/18/2013
128	,,,,,	10/31/2016
129	Lusher Elementary School Refurbishment (OPSB)	05/11/2010
130	Mahalia Jackson Elementary School (OPSB)	03/06/2012
	Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)	
131	Mahalia Jackson Elementary School Office Renovation (OPSB)	04/30/2013
132	Martin Behrman Elementary School Roof (RSD)	02/23/2010
133	Martin Luther King Jr. Elementary Canopy System (RSD)	11/05/2011
134	Martin Luther King Jr. School Modular Building, Deck, Canopy (RSD)	07/31/2012

135	Martin Laster Wines In Cale at Witches Defeated in Language (RSD)	02/18/2016
136	Martin Luther King Jr. School Kitchen Refurbishment (RSD)	04/17/2013
	Mary Church Terrell Elementary School Demolition (RSD)	
137	Mary M. Bethune Elementary School Refurbishment (OPSB)	10/26/2017
138	Mary M. Bethune Elementary 1st Floor Replacement (OPSB)	01/24/2011
139	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)	01/21/2011
140	McDonogh #7 High School Repairs (OPSB)	00/44/0040
141	McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)	06/11/2012
142		03/15/2016
143		11/19/2011
144	moboliogii #02 Roof Replacement	02/24/2012
145	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior	01/17/2014
	Ramp & Handicap Seating in the Auditorium (OPSB)	
146	mosoriogn 700 concor at the 1 mmp/ vatoro one	09/23/2015
147	McDonogh #42 Elementary School Renovation (RSD)	05/28/2015
148	McDonogh #42 Elementary School Roof (RSD)	12/21/2011
149	McDonogh #42 Elementary School HVAC Replacement (RSD)	08/09/2010
150	Mildred C. Osborne Elementary School Demolition (RSD)	02/18/2010
151	Mildred C. Osborne Elementary School (RSD)	12/03/2012
152	Modular Campuses Close Outs (RSD)	
153	Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)	05/22/2013
154	Modular Structures at Langston Hughes Elementary School (RSD)	04/05/2010
155	Morris F.X. Jeff Elementary School Demolition (RSD)	
156	Morris F.X. Jeff Elementary School Mothball (RSD)	01/15/2013
157	Murray G. Henderson Elementary School Roof (RSD)	06/23/2012
158	Nelson Elementary School Refurbishment (OPSB)	04/18/2016
159	New Andrew H. Wilson Elementary School (RSD)	10/11/2009
160		09/14/2012
161	New Fannie C. Williams School (RSD)	08/24/2012
162	New Joseph A. Craig Elementary School (RSD)	12/09/2009
163	New L.B. Landry High School (RSD)	06/30/2010
164	New Lake Area High School (RSD)	12/28/2009
	New Lawrence D. Crocker School (RSD)	04/29/2013
166	New PK-8 School at North Kenilworth Park at Curran Site (OPSB)	01/29/2016
167	New Parkview School (RSD)	10/12/2012
168	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD)	
169	New William Frantz Elementary School (RSD)	
170	New Orleans High School Signature Center Study (RSD)	
171	Oretha C. Haley Demo (RSD)	05/07/2012
172	Oretha C. Haley Elementary School Mothball (RSD)	09/17/2012
173		08/06/2009
174		06/16/2010
175		06/02/2015
176		06/30/2016
177	Paul B. Habans Elementary School Roof Repairs (RSD)	07/27/2012
178	Phillis Wheatley Elementary School Demolition (RSD)	09/26/2011
179	Phillis Wheatley Elementary School (RSD)	07/10/2014

180	Down Allerson Element (SSD)	03/17/2017
181	Ray Abrams Elementary School <sup>(RSD)</sup> Rosenwald Elementary School Refurbishment <sup>(RSD)</sup>	04/07/2016
		07/14/2011
	Robert M. Lusher Elementary Roof Removal & Replacement (OPSB) Samuel J. Green Elementary School Refurbishment (RSD)	02/15/2016
	•	02/15/2016
	Samuel J. Green Elementary School Refurbishment Phase 2 (RSD)	
185	Sarah T. Reed High School Bleachers (RSD)	01/11/2012
186	Sarah T. Reed High School Auditorium Wall (RSD)	03/29/2010 02/18/2016
187		
188	Sarah T. Reed High School Refurbishment (RSD)	12/01/2015
189	Seabrook Computer Training Center Demolition (OPSB)	06/25/2010
190	onium and on more	11/14/2008
	Schaumburg Elementary School Roof Repairs (RSD)	05/09/2019
	Schwarz Alternative Repairs (RSD)	07/14/2009
	Schwarz Alternative Modulars Demolition (RSD)	04/02/2015
	Schwarz Modular Building Demolition (RSD)	04/02/2015
	Sherwood Forest Elementary School Demolition (RSD)	10/28/2010
196	Sherwood Forest Elementary School (RSD)	06/30/2016
	Small New Orleans East High School at Abramson (RSD)	09/24/2015
198	Sophie B. Wright School Renovation (RSD)	06/08/2016
199	Sophie B. Wright School Selective Demolition (RSD)	01/31/2014
200	Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)	07/26/2011
201	Stuart R. Bradley Elementary School Demolition (RSD)	01/27/2010
202	Stuart R. Bradley Elementary School (RSD)	06/26/2015
203	Sylvanie Williams Elementary School AHU Replacement (RSD)	07/30/2013
204	Sylvanie Williams Elementary School Play Yard <sup>(RSD)</sup>	09/23/2010
	Sylvanie Williams Elementary School Roof Repairs (RSD)	07/27/2012
206	Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)	04/13/2012
207	Sylvanie Williams Elementary School Refurbishment (RSD)	02/18/2016
208	Temporary Campus for McDonogh #11 Expropriation (OPSB)	
209	Thomas A. Edison Elementary School Demolition (RSD)	03/25/2010
210	Thomy Lafon Elementary School Demolition (RSD)	11/27/2011
211	Thomy Lafon School Interpretative Display (RSD)	10/15/2013
212	Thurgood Marshall Elementary School Refurbishment (RSD)	08/10/2018
213	Timbers Park Office Building #1 & #2 Demolition (OPSB)	09/18/2011
214	Timbers HVAC (OPSB)	09/11/2013
215	Timbers III - IT Room Relocation (OPSB)	02/11/2015
216	Village de L'est Elementary School Subsidence (RSD)	06/18/2012
217	Village de L'est Elementary School Refurbishment (RSD)	10/12/2106
218	Village de L'est Elementary School Roof and Modular Demolition (RSD)	06/16/2013
	Vorice J. Waters Elementary School Demolition (RSD)	01/14/2010
	Valena C. Jones Elementary School (RSD)	01/10/2013
221	Walter L. Cohen High School HVAC (RSD)	04/04/2014
222	Warren Easton High School Renovation (OPSB)	12/15/2015
	Warren Easton School Courtyard Waterproofing (OPSB)	11/24/2017
	Warren Easton High School Window Replacement (OPSB)	09/07/2012
	West Bank Swing Space for Alice Harte Elementary School (OPSB)	07/11/1931
	3	

226 New William J. Guste Elementary School (RSD)	10/06/2008
227 William J. Guste Elementary School Science Lab (RSD)	08/04/2009
228 William Frantz Elementary School Environmental Remediation & Selective Demolition (RSI	O4/15/2010
229 William Frantz Elementary School Roof (RSD)	08/12/2010



### BESE MONTHLY REPORT OPEN CONTRACTS as of 10/31/2022

Project	Contractor/Architect	Funding Source	Original Contract Amounts	Change Orders/Amendments	Contract Amounts
DEMOLITIONS					
DEMOLITIONS					
PHASE 1 SCHOOLS					
Crocker ES Construction	Mathes Brierre Architects	FEMA	\$ 50,000.00	\$ -	\$ 50,000.00
Crocker ES Construction Total			\$ 50,000.00	\$ -	\$ 50,000.00
PHASE 2 SCHOOLS					
Behrman ES Construction Gym Demo	Waggonner & Ball Architects, APC	FEMA	\$ -	\$ 47,338.00	\$ 47,338.00
Behrman ES Construction Gym Demo Total			\$ -	\$ 47,338.00	\$ 47,338.00
Behrman ES Construction New Gym	Waggonner & Ball Architects, APC	FEMA	\$ -	\$ 244,351.00	\$ 244,351.00
Behrman ES Construction New Gym Total			\$ -	\$ 244,351.00	\$ 244,351.00
Behrman ES Construction Selective Demo	Waggonner & Ball Architects, APC	FEMA	\$ -	\$ 64,837.00	\$ 64,837.00
Behrman ES Construction Selective Demo Total			\$ -	\$ 64,837.00	\$ 64,837.00
Behrman ES Construction Selective Demo/Gym Demo	Landis Construction Co., LLC	FEMA	\$ 1,214,934.00	\$ -	\$ 1,214,934.00
Behrman ES Construction Selective Demo/Gym Demo Total			\$ 1,214,934.00	\$ -	\$ 1,214,934.00
Behrman ES Construction	Landis Construction Co., LLC	Tax Credit	\$ 2,945,127.71	\$ -	\$ 2,945,127.71
Behrman ES Construction Total			\$ 2,945,127.71	\$ -	\$ 2,945,127.71
Behrman ES Construction(CMAR)	Waggonner & Ball Architects, APC	FEMA	\$ 2,345,881.00	\$ 414,344.69	\$ 2,760,225.69
	SSRCx, LLC	FEMA	\$ 135,710.88	\$ -	\$ 135,710.88
		Tax Credit	\$ 189,345.12	\$ -	\$ 189,345.12
	Landis Construction Co., LLC	Developer's Fees	\$ 1,542,693.43		\$ 1,542,693.43
		FEMA	\$ 17,462,104.14	\$ 72,601.86	\$ 17,534,706.00
		OSFF	\$ 12,416,587.17		\$ 12,416,587.17
Behrman ES Construction(CMAR) Total			\$ 34,092,321.74	\$ 486,946.55	\$ 34,579,268.29
Behrman ES Construction(CMAR) PreConstruction	Landis Construction Co., LLC	FEMA	\$ 170,000.00	\$ -	\$ 170,000.00
Behrman ES Construction(CMAR) PreConstruction Total			\$ 170,000.00		\$ 170,000.00
New Booker T Washington Medium High School	Hewitt-Washington & Associates Architects and Planners	FEMA	\$ -	\$ 5,027,813.93	
New Booker T Washington Medium High School Total			\$ -	\$ 5,027,813.93	
New Cohen HS (CMAR)	Grace Hebert	FEMA		\$ 930,863.61	· ·
	HMS Architects, APC	FEMA	\$ 1,271,281.70	\$ 140,588.16	\$ 1,411,869.86
	Thompson Builders	FEMA	\$ 154,175.00	\$ -	\$ 154,175.00
	Lemoine Company, LLC	CDBG	\$ 17,909,094.46	\$ -	\$ 17,909,094.46
		Developer's Fees	\$ 1,267,644.20		\$ 1,267,644.20
		FEMA	\$ 9,815,843.38	•	\$ 9,815,843.38
New Cohen HS (CMAR) Total			\$ 30,418,038.74		
New Cohen HS (CMAR) PreConstruction	Lemoine Company, LLC	CDBG	\$ 140,000.00		\$ 140,000.00
New Cohen HS (CMAR) PreConstruction Total			\$ 140,000.00	•	\$ 140,000.00
New Cohen HS (CMAR) Selective Demo	Lemoine Company, LLC	CDBG	\$ 2,264,956.95	-	\$ 2,264,956.95
New Cohen HS (CMAR) Selective Demo Total			\$ 2,264,956.95	\$ -	\$ 2,264,956.95



## **BESE MONTHLY REPORT**

OPEN CONTRACTS as of 10/31/2022

Funding Source

Original Contract Amounts

**Grand Total** 

Change Orders/Amendments

Contract Amounts

152,570,580.22

\$

Contractor/Architect


Project

Kerlerec CTE Renovation(CMAR)	SCNZ Architects, LLC	FEMA	\$ 2,198,720.00	\$ 347,367.50	2,546,087.50
	SSRCx, LLC	FEMA	\$ 226,473.00	\$ - !	\$ 226,473.00
	Broadmoor, LLC	Developer's Fees	\$ 737,728.00	!	\$ 737,728.00
Kerlerec CTE Renovation(CMAR) Tota	İ		\$ 3,162,921.00	\$ 347,367.50	\$ 3,510,288.50
Kerlerec CTE Renovation(CMAR) Pre-Construction	Broadmoor, LLC	FEMA	\$ 125,000.00	\$ 41,751.30	\$ 166,751.30
Kerlerec CTE Renovation(CMAR) Pre-Construction Tota	l		\$ 125,000.00	\$ 41,751.30	\$ 166,751.30
Kerlerec CTE Renovation(CMAR)/Selective Demo	Broadmoor, LLC	CDBG	\$ 20,633,164.00	\$ 120,497.91	20,753,661.91
		FEMA	\$ 9,065,884.00	:	9,065,884.00
Kerlerec CTE Renovation(CMAR)/Selective Demo Tota	İ		\$ 29,699,048.00	\$ 120,497.91	\$ 29,819,545.91
Kerlerec CTE Renovation(CMAR)GMP 2	SCNZ Architects, LLC	FEMA	\$ -	\$ 523,205.20	523,205.20
	Broadmoor, LLC	OSFF	\$ 2,865,248.00	\$ - :	2,865,248.00
Kerlerec CTE Renovation(CMAR)GMP 2 Tota	l		\$ 2,865,248.00	\$ 523,205.20	\$ 3,388,453.20
Other Services					
E-Rate Documentation	Educational Professional Services, LLC	Insurance Proceeds	\$ 18,000.00	\$ - :	18,000.00
E-Rate Documentation Tota			\$ 18,000.00	\$ - :	\$ 18,000.00
Program Management/Construction Management	Jacobs Project Management Company/CSRS Consortium	FEMA	\$ 22,629,667.00	\$ 14,799,756.92	36,810,584.62
		Insurance Proceeds		\$ - :	618,839.30
Program Management/Construction Management Tota			\$ 22,629,667.00	\$ 14,799,756.92	37,429,423.92



# RSD Program Summary-Phase II



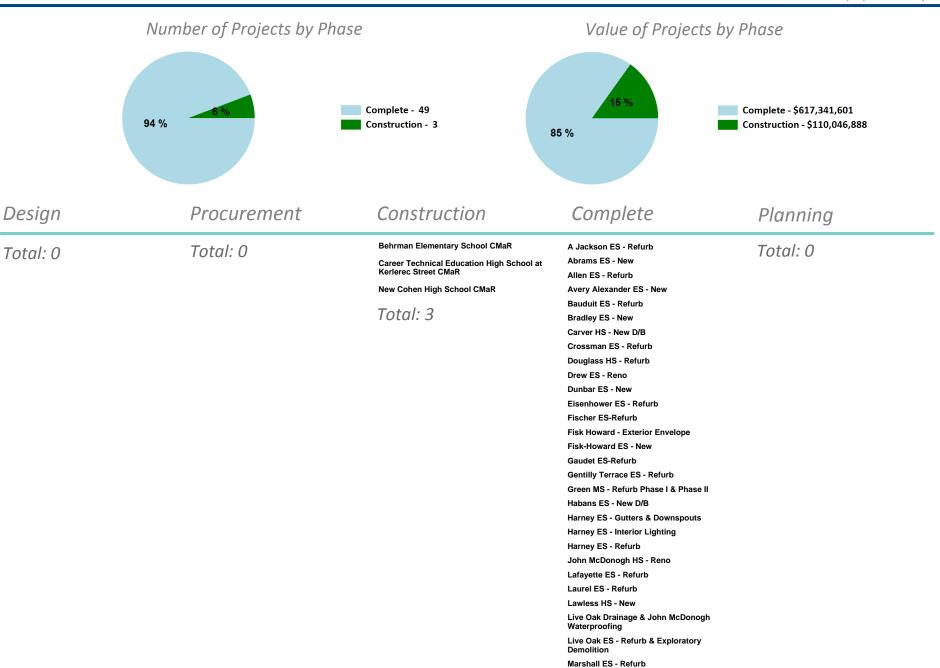



# RSD Program Summary-Phase II



Martin L King ES - Refurb

McDonogh 28 - Flooring Renovation Phase 2

McDonogh 28 ES - Refurb

McDonogh 32 ES - Refurb

McDonogh 42 ES - Reno

Morial ES - New

New Karr High School CMAR

NO East HS @Abramson - New

Reed HS - Refurb

Rosenwald ES - Refurb

Schaumburg ES - Refurb

Schaumburg Roof

Sherwood Forest ES - New D/B

Sophie B Wright HS - Phase 2 Interior Painting and Wood Floor Repairs

Sophie B Wright HS - Reno

Sylvanie Williams - Refurb

Tubman ES - Reno

Village de L'Est ES - Environmental

Village de L'Est ES - Refurb

Wicker ES - Refurb

Total: 49
