
Superintendent's Report May 2023







Dr. Cade BrumleyLouisiana Department
of Education





Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
FUTURE COMMUNITY MEETINGS	3
BID OPENINGS	3
DBE OVERVIEW MONTHLY SUMMARY	4
NEW & MAJOR RENOVATION	8
Behrman Elementary School CMaR (RSD)	8
Career Technical Education High School at Kerlerec Street CMaR (RSD)	8
New Cohen High School CMaR (RSD)	8
COMPLETED PROJECTS	9

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$114,000,000 in open contracts for the capital program after issuing no new contracts, change orders and amendments in May. In addition, the total change orders to date, \$478,000, accounting for less than one percent (0.46%) of the total open construction contracts. RSD anticipates issuing no new contracts in construction contracts/change orders, and \$478,000 in professional service contracts/amendments in June.

Future Community Meetings

None Scheduled

Bid Openings

None Scheduled



Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 27 projects as of May 31, 2023. The DBE subcontracts value is \$84,866,010 of the \$372,937,728 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 65 projects as of May 31, 2023. The DBE subcontracts value is \$24,723,075 of the \$78,177,771 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of May 31, 2023. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.


CMAR New:

DBE Contractors secured subcontracts on 6 projects as of May 31, 2023. The DBE subcontracts value is \$85,086,724 of the \$241,997,237 total of awarded contracts.

Total Amount of Contracts: \$802,250,293

4 Status Date: May 31, 2023


^{*} DBE provisions were included in projects bid after June 30, 2012

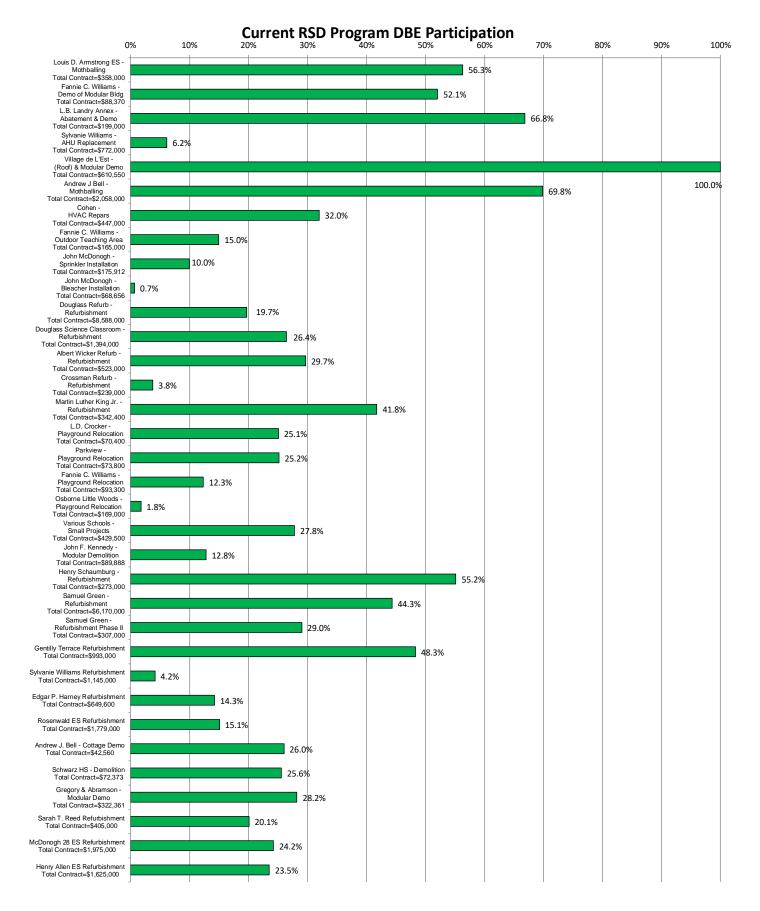

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

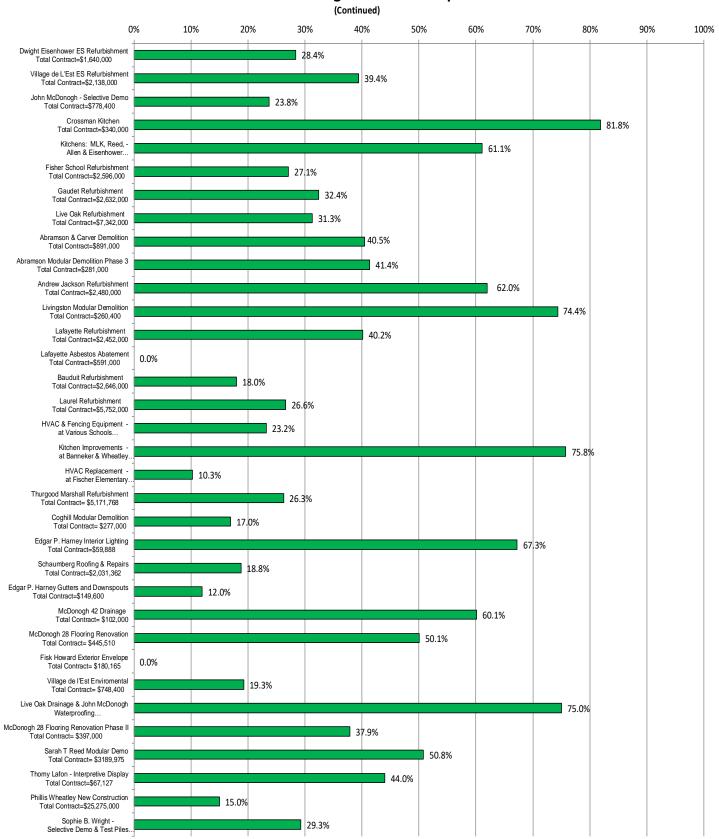

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.

RSD DBE Participation Target = 25% of Total Contract Amount

Current RSD Program DBE Participation

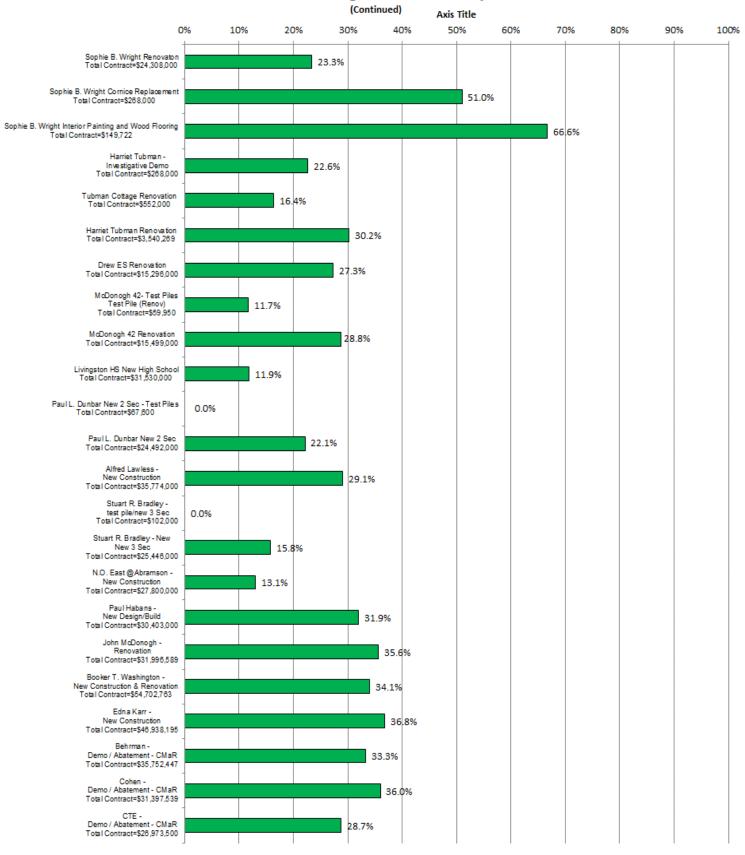

New & Major Renovation - Project Status

(Forecasted dates only include the next project phase)

Behrman Elementary School CMaR (RSD)

3819 Hershel Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school

Funding Source - FEMA

Architect – Waggonner & Ball Architects Contractor - Landis Construction

Construction Phase

- · Contractor addressing warranty items
- · Installation of library shelving in progress
- · Fielding proposals for installation of attic stair guardrail



Career Technical Education High School at Kerlerec Street CMAR (RSD)

1331 Kerlerec Street, New Orleans, LA 70116 District D Ward 7

Scope of work: Renovation of existing high school

Funding Source – CDBG Architect – SCNZ Architects

Contractor - Broadmoor Construction

Construction Phase

- · User training in progress
- · Warranty tickets being issued
- · Commissioning agents to revisit after adjustments



New Cohen High School CMAR (RSD)

3520 Dryades Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Construction of new high school

Funding Source - FEMA / CDBG

Architect - HMS Architects

Contractor - The Lemoine Company

Construction Phase

- · Contractor addressing warranty items
- · Installation of library shelving in progress
- · Working to procure stormwater bond



Status Date: May 31, 2023

Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition (RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation (RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School (RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment (RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment (RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs (RSD)	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment (RSD)	10/31/2017
8	Agnes Bauduit Elementary School Boiler (RSD)	12/07/2009
9	Albert Wicker Elementary School Refurbishment (RSD)	03/27/2014
10	Albert Wicker Elementary School Roof Repairs (RSD)	06/13/2013
11	Alfred Lawless Senior (RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing (RSD)	06/15/2011
13	Alice M. Harte Elementary School (OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition (OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement (RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball (RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs (RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels (RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage (RSD)	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation (OPSB)	
21	Augustine Elementary School Roof (RSD)	04/13/2012
22	Avery-Alexander Elementary School (RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition (RSD)	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad (RSD)	10/30/2017
25	Barbara C. Jordan Elementary School Demolition (RSD)	05/30/2011
26	Bell JH Shoring (RSD)	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation (RSD)	
28	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
29	Bienville Elementary School Demolition (RSD)	05/04/2009
30	Booker T. Washington High School Environmental Remediation (RSD)	12/13/2015
31	Booker T. Washington High School Partial Demolition (RSD)	04/07/2013
32	Carter G. Woodson Middle School Demolition (RSD)	02/09/2010
33	Central Services Warehouse Demolition (OPSB)	01/05/2012
34	Charles J. Colton Elementary Selective Demolition (RSD)	07/26/2010
35	Charles J. Colton Elementary School (RSD)	05/23/2013
36	Charles R. Drew Elementary School (RSD)	04/17/2015
37	Charles R. Drew Elementary Roof & Installation of Kitchen Hood (RSD)	06/08/2011
38	Cohen High School Health Clinic (RSD)	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School (RSD)	
40	Demolition of Modular Buildings at Coghill (RSD)	12/26/2018
41	Demolition of Modular Buildings at Gregory and Abramson (RSD)	06/23/2015
42	Demolition of Modular Buildings at Abramson and Carver ^(RSD)	01/18/2017

9

Status Date: May 31, 2023

43	B W (RSD)	01/18/2017
	Demolition of Modular Buildings at Livingston (RSD)	01/10/2017
44 45	Douglass High School Under Floor Utilities (RSD)	06/13/2012
46	Dr. Martin Luther King School Roof Repairs (RSD)	12/15/2014
47	Dr. Martin Luther King Jr. School Renovation (RSD)	02/18/2016
48	Dwight D. Eisenhower Elementary School Kitchen Refurbishment (RSD)	
_	Dwight D. Eisenhower Elementary School Roof Repairs (RSD)	07/27/2012 12/23/2015
49	Dwight D. Eisenhower Elementary School Refurbishment (RSD)	
50 54	East Bank Swing Space for Audubon Charter School (OPSB)	12/30/2011
51	Edgar P. Harney Elementary School Refurbishment (RSD)	00/40/0040
52	Edgar P. Harney Elementary School Roof Repairs (RSD)	06/13/2012
53	Edgar P. Harney Elementary School Downspouts and Gutters (RSD)	01/09/2019
54	Edgar P. Harney Elementary School Lighting Repairs (RSD)	08/08/2018
55	Edna Karr High School - Gymnasium Repair (OPSB)	12/23/2013
56	Edna Karr High School - Assessment (OPSB)	00/00/00/0
57	Edward Livingston Middle School Demolition (RSD)	09/28/2010
58	Edward Henry Phillips Junior High School Demolition (OPSB)	11/19/2010
59	New Edward Hynes School (OPSB)	02/06/2012
60	Edwards Hardin Lockett Lawless Demolition (RSD)	11/03/2008
61	Edward Livingston High School (RSD)	01/05/2015
62	Eleanor L. McMain School Replacement of Existing Chillers (OPSB)	08/30/2011
63	Eleanor L. McMain School Clinic (OPSB)	07/24/2013
64	Eleanor L. McMain School Maintenance Upgrades (OPSB)	12/12/2016
65	Eleanor L. McMain School Roof Replacement (OPSB)	05/13/2016
66	Ernest "Dutch" Morial Elementary ^(RSD)	03/17/2017
67	Ernest N. Morial Elementary Security Fencing (RSD)	05/10/2011
68	Fannie C. Williams Elementary School Demolition (RSD)	03/10/2009
69	Fisk-Howard Elementary School Demolition (RSD)	10/04/2011
70	Florence J. Chester Elementary School Demolition (RSD)	06/05/2011
71	Fortier (Lusher) High School Refurbishment (OPSB)	02/05/2016
72	Francis W. Gregory Demolition (RSD)	12/21/2011
73	Frederick A. Douglass High Refurbishment (RSD)	10/28/2014
74	Frederick A. Douglass High School Science Lab (RSD)	07/05/2016
75	Frederick A. Douglass High Switchgear (RSD)	08/04/2009
76	Frederick A. Douglass High Emergency Boiler Roof Repairs (RSD)	
77	Gaudet Elementary School Refurbishment (RSD)	12/20/2016
78	Gentilly Terrace Elementary School Refurbishment (RSD)	09/22/2015
79	George Mondy Elementary School Mothball (RSD)	
80	George Washington Carver School (RSD)	03/07/2016
81	George Washington Carver High School Demolition (RSD)	08/24/2011
82	Greater St. Stephens School (OPSB)	03/18/2013
83	Harriet R. Tubman Elementary School Selective Demolition (RSD)	12/14/2014
84	Harriet R. Tubman Elementary School Renovation (RSD)	08/01/2018
85	Harriet R. Tubman Cottage Renovation (RSD)	08/02/2018
86	Henry Allen Elementary School Refurbishment (RSD)	03/08/2016
87	Henry Allen Elementary School Kitchen Refurbishment (RSD)	02/18/2016
88	Henry Allen Elementary School Roof (RSD)	05/24/2010

	(200)	
89	Henry C. Schaumburg School Refurbishment (RSD)	06/26/2015
90	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation (RSD)	12/16/2011
91	Holy Cross Modular Relocation (RSD)	12/14/2010
92	Israel M. Augustine Middle School Roof Replacement (RSD)	04/13/2012
93	Israel M. Augustine Middle School Mothball (RSD)	01/18/2013
94	James Derham Demolition (RSD)	02/23/2012
95	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
96	New Jean Batiste de Bienville School (RSD)	06/15/2012
97	Jean Gordon Elementary School Demolition (RSD)	08/16/2010
98	JoEllen Smith Medical Center Demolition (OPSB)	
99	John Dibert Elementary School Roof (RSD)	08/20/2010
100	John W. Hoffman Elementary School Demolition (RSD)	05/25/2010
101	John F. Kennedy Modular Relocation (Schwarz Campus) (RSD)	11/05/2010
102	John F. Kennedy Modular Relocation (Coghill Modular Campus) (RSD)	08/05/2011
103	John F. Kennedy Modular Demolition (RSD)	09/16/2014
104	John F. Kennedy High School Demolition (RSD)	01/12/2012
105	John McDonogh Senior High School Bleachers and Sprinklers (RSD)	03/27/2014
106	John McDonogh Senior High School Roof (RSD)	05/04/2010
107	John A. Shaw Elementary School Mothball (RSD)	12/12/2012
108	Joseph S. Clark Senior High School Roof Repairs (RSD)	07/27/2012
109	Joseph A. Craig Elementary Canopies (RSD)	06/06/2011
110	Joseph A. Craig Elementary Elevator Installation (RSD)	01/20/2012
111	Joseph A. Hardin Elementary Security Fencing (RSD)	05/10/2011
112	Lafayette Elementary School Roof and Masonry (RSD)	06/22/2012
	Lake Area Landry Demolition (RSD)	05/01/2008
	Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)	11/13/2015
115	Langston Hughes Elementary School (Phase I) (RSD)	08/11/2009
116		11/10/2010
117	Langston Hughes Elementary School - Dumpster Pad (RSD)	10/12/2012
	Lawrence D. Crocker Elementary School Demolition (RSD)	04/02/2010
	Laurel Elementary School Refurbishment (RSD)	01/03/2018
120	L.B. Landry Annex Demolition (RSD)	05/02/2013
121	Little Woods Elementary School Demolition (RSD)	08/09/2010
122	Little Woods School (Dolores T. Aaron Elementary School) (RSD)	08/01/2013
123	Live Oak Elementary School Refurbishment (RSD)	01/06/2017
124	Live Oak Elementary School Roof (RSD)	08/04/2011
125	-	08/26/2011
126	Lorraine Hansberry Elementary School Mothball (RSD)	12/27/2012
127		02/18/2013
128	Lusher Elementary School Refurbishment (OPSB)	10/31/2016
129	Mahalia Jackson Elementary School (OPSB)	05/11/2010
130	Mahalia Jackson Elementary School Dumpster / Other Improvements (OPSB)	03/06/2012
131	Mahalia Jackson Elementary School Office Renovation (OPSB)	04/30/2013
132	Martin Behrman Elementary School Roof (RSD)	02/23/2010
133	Martin Luther King Jr. Elementary Canopy System (RSD)	11/05/2011
134	Martin Luther King Jr. School Modular Building, Deck, Canopy (RSD)	07/31/2012
	maran Edulor rang on concor modular building, been, canopy	5.75 .720 1Z

11

Status Date: May 31, 2023

135	Martin Luther King Jr. School Kitchen Refurbishment (RSD)	02/18/2016
136	Mary Church Terrell Elementary School Demolition (RSD)	04/17/2013
137	Mary M. Bethune Elementary School Refurbishment (OPSB)	10/26/2017
138	Mary M. Bethune Elementary 1st Floor Replacement (OPSB)	01/24/2011
139	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)	01/21/2011
140	McDonogh #7 High School Repairs (OPSB)	
141	McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)	06/11/2012
142	McDonogh #28 School Refurbishment (RSD)	03/15/2016
143	McDonogh #28 Elementary School Roof (RSD)	11/19/2011
144	McDonogh #32 Roof Replacement (RSD)	02/24/2012
	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior	0.444=100.44
145	Ramp & Handicap Seating in the Auditorium (OPSB)	01/17/2014
146	McDonogh #35 School at the Phillip/ Waters Site (OPSB)	09/23/2015
147	McDonogh #42 Elementary School Renovation (RSD)	05/28/2015
148	McDonogh #42 Elementary School Roof (RSD)	12/21/2011
149	McDonogh #42 Elementary School HVAC Replacement (RSD)	08/09/2010
150	Mildred C. Osborne Elementary School Demolition (RSD)	02/18/2010
151	Mildred C. Osborne Elementary School (RSD)	12/03/2012
152	Modular Campuses Close Outs (RSD)	
153	Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)	05/22/2013
154	Modular Structures at Langston Hughes Elementary School (RSD)	04/05/2010
155	Morris F.X. Jeff Elementary School Demolition (RSD)	
156	Morris F.X. Jeff Elementary School Mothball (RSD)	01/15/2013
157	Murray G. Henderson Elementary School Roof (RSD)	06/23/2012
158	Nelson Elementary School Refurbishment (OPSB)	04/18/2016
159	New Andrew H. Wilson Elementary School (RSD)	10/11/2009
160	New Carter G. Woodson School (RSD)	09/14/2012
161	New Fannie C. Williams School (RSD)	08/24/2012
	New Joseph A. Craig Elementary School (RSD)	12/09/2009
	New L.B. Landry High School (RSD)	06/30/2010
	New Lake Area High School (RSD)	12/28/2009
	New Lawrence D. Crocker School (RSD)	04/29/2013
	New PK-8 School at North Kenilworth Park at Curran Site (OPSB)	01/29/2016
167	New Parkview School (RSD)	10/12/2012
168	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD)	10/12/2012
169	New William Frantz Elementary School (RSD)	
170		
171	New Orleans High School Signature Center Study (RSD)	05/07/2012
	Oretha C. Haley Demo ^(RSD) Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
173 174	Parkview Elementary School Demolition (RSD)	08/06/2009 06/16/2010
	. da. i. banbar ilomontary concor bomonton	06/02/2015
175	Paul L. Dunbar Elementary School (RSD)	
176	· · · · · · · · · · · · · · · · · · ·	06/30/2016
177	Paul B. Habans Elementary School Roof Repairs (RSD)	07/27/2012
178	Phillis Wheatley Elementary School Demolition (RSD)	09/26/2011
179	Phillis Wheatley Elementary School (RSD)	07/10/2014

	(DCD)	
	Ray Abrams Elementary School (RSD)	03/17/2017
181	Resembled French and Section Results in the Control of the Control	04/07/2016
	Robert M. Lusher Elementary Roof Removal & Replacement (OPSB)	07/14/2011
183	Camaci C. Green Elementary Concer Retarblement	02/15/2016
184		02/15/2016
185	Sarah T. Reed High School Bleachers (RSD)	01/11/2012
186		03/29/2010
187		02/18/2016
188	out at 1. Rood Fight Control Relationships	12/01/2015
189	Seabrook Computer Training Center Demolition (OPSB)	06/25/2010
190	Schaumburg Chillers (RSD)	11/14/2008
191	Schaumburg Elementary School Roof Repairs (RSD)	05/09/2019
192	Schwarz Alternative Repairs (RSD)	07/14/2009
193	Schwarz Alternative Modulars Demolition (RSD)	04/02/2015
194	Schwarz Modular Building Demolition (RSD)	04/02/2015
195	Sherwood Forest Elementary School Demolition (RSD)	10/28/2010
196	Sherwood Forest Elementary School (RSD)	06/30/2016
197	Small New Orleans East High School at Abramson (RSD)	09/24/2015
198	Sophie B. Wright School Renovation (RSD)	06/08/2016
199	Sophie B. Wright School Selective Demolition (RSD)	01/31/2014
200	Sophie B. Wright Various Repairs/Restroom Renovations (OPSB)	07/26/2011
201	Stuart R. Bradley Elementary School Demolition (RSD)	01/27/2010
202	Stuart R. Bradley Elementary School (RSD)	06/26/2015
203	Sylvanie Williams Elementary School AHU Replacement (RSD)	07/30/2013
204	Sylvanie Williams Elementary School Play Yard (RSD)	09/23/2010
205	Sylvanie Williams Elementary School Roof Repairs (RSD)	07/27/2012
206	Sylvanie Williams Elementary School HVAC/Chiller Replacement (RSD)	04/13/2012
207	(DCD)	02/18/2016
208	Temporary Campus for McDonogh #11 Expropriation (OPSB)	
209	Thomas A. Edison Elementary School Demolition (RSD)	03/25/2010
210	Thomy Lafon Elementary School Demolition (RSD)	11/27/2011
211	Thomy Lafon School Interpretative Display (RSD)	10/15/2013
	Thurgood Marshall Elementary School Refurbishment (RSD)	08/10/2018
	Timbers Park Office Building #1 & #2 Demolition (OPSB)	09/18/2011
214	(09/11/2013
215	Timbers III - IT Room Relocation (OPSB)	02/11/2015
	Village de L'est Elementary School Subsidence (RSD)	06/18/2012
	Village de L'est Elementary School Refurbishment (RSD)	10/12/2106
	Village de L'est Elementary School Roof and Modular Demolition (RSD)	06/16/2013
	Vorice J. Waters Elementary School Demolition (RSD)	01/14/2010
	Valena C. Jones Elementary School (RSD)	01/10/2013
	Walter L. Cohen High School HVAC (RSD)	04/04/2014
	Warren Easton High School Renovation (OPSB)	12/15/2015
	Warren Easton School Courtyard Waterproofing (OPSB)	11/24/2017
	Warren Easton High School Window Replacement (OPSB)	09/07/2012
	West Bank Swing Space for Alice Harte Elementary School (OPSB)	07/11/1931
-	g -pare io. , insertial	

226 New William J. Guste Elementary School (RSD)	10/06/2008
227 William J. Guste Elementary School Science Lab (RSD)	08/04/2009
228 William Frantz Elementary School Environmental Remediation & Selective Demolition (RSD)	04/15/2010
229 William Frantz Elementary School Roof (RSD)	08/12/2010



BESE MONTHLY REPORT

OPEN CONTRACTS as of 05/31/2023

Project	Contractor/Architect	Funding Source	Original Contract Amounts	Change Orders/Amendments	Contract Amounts
HASE 1 SCHOOLS					
Crocker ES Construction	Mathes Brierre Architects	FEMA	\$ 50,000.00 \$	- \$	50,000.0
Crocker ES Constru	ction Total		\$ 50,000.00 \$	- \$	50,000.0
HASE 2 SCHOOLS					
Behrman ES Construction Gym Demo	Waggonner & Ball Architects, APC	FEMA	\$ - \$		-
Behrman ES Construction Gym D			\$ - \$	- \$	-
Behrman ES Construction New Gym	Waggonner & Ball Architects, APC	Developer's Fees	\$ - \$	- \$	(244,350.6
		FEMA	\$ <u> </u>	- \$	244,350.6
Behrman ES Construction New			\$ - \$	· · · · · · · · · · · · · · · · · · ·	-
Behrman ES Construction Selective Demo	Waggonner & Ball Architects, APC	FEMA	\$ - \$	64,837.00 \$	64,837.0
Behrman ES Construction Selective D	Demo Total		\$ - \$	64,837.00 \$	64,837.0
Behrman ES Construction Selective Demo/Gym Demo	Landis Construction Co., LLC	FEMA	\$ 1,214,934.00	- \$	1,214,934.0
Behrman ES Construction Selective Demo/Gym D	Demo Total		\$ 1,214,934.00	- \$	1,214,934.0
Behrman ES Construction(CMAR)	Waggonner & Ball Architects, APC	FEMA	\$ 2,345,881.00	312,486.55 \$	2,475,897.5
		Tax Credit	Ş	- \$	182,470.0
	SSRCx, LLC	FEMA	\$ 325,056.00	- \$	135,710.8
		Tax Credit	\$ - \$	- \$	189,345.
	Landis Construction Co., LLC	Developer's Fees	\$ 2,398,150.00	\$	2,398,150.
		FEMA	\$ 18,672,286.23	139,444.06 \$	18,746,667.
		OSFF	\$ 10,350,949.00	\$	10,350,949.0
		Tax Credit	\$ 2,945,127.71 \$	- \$	3,010,191.0
Behrman ES Construction(CN	MAR) Total		\$ 37,037,449.94	\$ 451,930.61 \$	37,489,380.5
Behrman ES Construction(CMAR) PreConstruction	Landis Construction Co., LLC	FEMA	\$ 170,000.00 \$	- \$	170,000.0
Behrman ES Construction(CMAR) PreConstruction	ction Total		\$ 170,000.00 \$	- \$	170,000.0
New Cohen HS (CMAR)	Grace Hebert	FEMA	Ş	930,863.61 \$	930,863.6
	HMS Architects, APC	FEMA	\$ 1,271,281.70	140,588.16 \$	1,411,869.8
	Thompson Builders	FEMA	\$ 154,175.00 \$	- \$	154,175.0
	Lemoine Company, LLC	CDBG	\$ 17,909,094.46	- \$	18,312,794.9
	• •	Developer's Fees	\$ 1,267,644.20	\$	1,267,644.
		FEMA	\$ 9,815,843.38	- \$	9,412,142.9
New Cohen HS (CN	MAR) Total		\$ 30,418,038.74	1,071,451.77 \$	31,489,490.
New Cohen HS (CMAR) PreConstruction	Lemoine Company, LLC	CDBG	\$ 140,000.00	- \$	140,000.0
New Cohen HS (CMAR) PreConstru	ction Total		\$ 140,000.00 \$	- \$	140,000.0



BESE MONTHLY REPORT

OPEN CONTRACTS as of 05/31/2023

Project	Contractor/Architect	Funding Source	Original Contract Amounts	Change Orders/Amendments	Contract Amounts
New Cohen HS (CMAR) Selective Demo	Lemoine Company, LLC	CDBG	\$ 2,264,956.95	\$ - \$	2,264,956.95
New Cohen HS (CMAR) Selective Demo Total			\$ 2,264,956.95	\$ - !	\$ 2,264,956.95
Kerlerec CTE Renovation(CMAR)	SCNZ Architects, LLC	FEMA	\$ 2,198,720.00	\$ 387,728.50	2,586,448.50
	SSRCx, LLC	FEMA	\$ 226,473.00	\$ - \$	226,473.00
Kerlerec CTE Renovation(CMAR) Total			\$ 2,425,193.00	\$ 387,728.50	\$ 2,812,921.50
Kerlerec CTE Renovation(CMAR) Pre-Construction	Broadmoor, LLC	FEMA	\$ 125,000.00	\$ 41,751.30 \$	166,751.30
Kerlerec CTE Renovation(CMAR) Pre-Construction Total			\$ 125,000.00	\$ 41,751.30	\$ 166,751.30
Kerlerec CTE Renovation(CMAR)/Selective Demo	Broadmoor, LLC	CDBG	\$ 20,633,164.00	\$ 253,626.31	20,886,790.31
		Developer's Fees	\$ 737,728.00	Ş	737,728.00
		FEMA	\$ 9,100,584.09	Ş	9,100,584.09
Kerlerec CTE Renovation(CMAR)/Selective Demo Total			\$ 30,471,476.09	\$ 253,626.31	\$ 30,725,102.40
Kerlerec CTE Renovation(CMAR)GMP 2	SCNZ Architects, LLC	FEMA	\$ -	\$ 523,205.20 \$	523,205.20
	Broadmoor, LLC	OSFF	\$ 2,830,548.00	\$ 26,076.57	2,856,624.57
Kerlerec CTE Renovation(CMAR)GMP 2 Total			\$ 2,830,548.00	\$ 549,281.77	\$ 3,379,829.77
Other Services					
E-Rate Documentation	Educational Professional Services, LLC	Insurance Proceeds	\$ 18,000.00	\$ - 5	18,000.00
E-Rate Documentation Total			\$ 18,000.00	\$ - 5	18,000.00
Program Management/Construction Management	Jacobs Project Management Company/CSRS Consortium	Developer's Fees	\$ 4,855,172.50	\$ - \$	4,855,172.50
Program Management/Construction Management Total			\$ 4,855,172.50	\$ - !	\$ 4,855,172.50
			Grand Total	•	114,841,376.48
