


# Superintendent's Report April, 2017



**Dr. Henderson Lewis Jr.**  
Orleans Parish School Board



**Mr. John White**  
Louisiana Department of Education  
**Mrs. Kunjan Narehania**  
Recovery School District

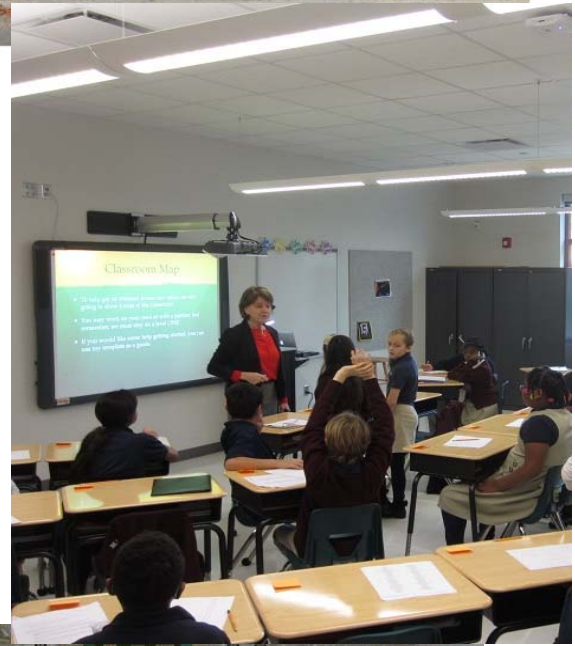

Prepared By





# Table of Contents

Right-Click on the school name to proceed to that page

|   |    |
|---|----|
| <b>TABLE OF CONTENTS</b>  | 1  |
| <b>FINANCIAL OVERVIEW</b>   | 2  |
| <b>COMMUNITY MEETINGS</b>   | 3  |
| <b>BID OPENINGS</b>   | 4  |
| <b>DBE OVERVIEW MONTHLY SUMMARY</b>   | 5  |
| <b>NEW &amp; MAJOR RENOVATION</b>   | 10 |
| Avery Alexander Elementary School <sup>(RSD)</sup>                                      | 10 |
| Benjamin Franklin Elementary School Renovation <sup>(OPSB)</sup>                        | 10 |
| New Karr High School, CMAR <sup>(RSD)</sup>   | 10 |
| John McDonogh High School Renovation CMAR <sup>(RSD)</sup>                              | 11 |
| Harriet R. Tubman Elementary School Renovation <sup>(RSD)</sup>                         | 11 |
| Booker T. Washington School CMAR <sup>(RSD)</sup>                                       | 11 |
| <b>REFURBISHMENTS</b>   | 12 |
| Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad <sup>(RSD)</sup>        | 12 |
| Agnes L. Bauduit Elementary School Refurbishment <sup>(RSD)</sup>                       | 12 |
| Mary M. Bethune Elementary School Refurbishment <sup>(OPSB)</sup>                       | 12 |
| Warren Easton Courtyard Waterproofing <sup>(OPSB)</sup>                                 | 13 |
| William J. Fischer Elementary Refurbishment <sup>(RSD)</sup>                            | 13 |
| William J. Fischer Elementary School HVAC Replacement <sup>(RSD)</sup>                  | 13 |
| Samuel J. Green Elementary School Refurbishment <sup>(RSD)</sup>                        | 14 |
| Andrew Jackson School Refurbishment <sup>(RSD)</sup>                                    | 14 |
| Lafayette Elementary School Refurbishment <sup>(RSD)</sup>                              | 14 |
| Laurel Elementary School Refurbishment <sup>(RSD)</sup>                                 | 15 |
| Thurgood Marshall Elementary School Refurbishment <sup>(RSD)</sup>                      | 15 |
| McDonogh #28 School Flooring Refurbishment <sup>(RSD)</sup>                             | 15 |
| McDonogh #32 School Refurbishment <sup>(RSD)</sup>                                      | 16 |
| Schaumburg Roof & Harney Gutters & Downspouts <sup>(RSD)</sup>                          | 16 |
| Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing <sup>(RSD)</sup> | 16 |
| <b>DEMOLITIONS</b>  | 17 |
| Demolition of Modulars at Abramson 3 <sup>(RSD)</sup>                                   | 17 |
| <b>COMPLETED PROJECTS</b>   | 17 |

# Overview

## FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$561 million in open contracts for the capital program after issuing \$752 thousand in new contracts, change orders and amendments in April. In addition, the total change orders to date, \$10 million, account for one percent (1.91%) of the total open construction contracts. RSD anticipates issuing approximately \$748 thousand in construction contracts/change orders, and \$1.5 million in professional service contracts/amendments in May.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 million in new contracts, change orders and amendments in April. In addition, the total change orders to date, \$9.5 million, account for approximately four percent (4.78%) of the total open construction contracts. OPSB anticipates issuing approximately \$467 thousand in construction contracts/change orders and \$96 thousand in professional service contracts and amendments in May.

# Community Meetings



## Future Community Meetings

# Bid Openings

**Projects which are scheduled to bid in the next 60 days**

**June 7, 2017**

Abramson Modular Demolition Phase 3 Bid Opening

**June 14, 2017**

Benjamin Franklin Elementary School Renovation Bid Opening

**July 6, 2017**

Thurgood Marshall School Refurbishment Bid Opening

## Disadvantaged Business Enterprises (DBE) Monthly Summary



### Recovery School District

#### New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of April 30, 2017. The DBE subcontracts value is \$81,171,162 of the \$363,307,364 total of awarded contracts.

#### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 51 projects as of April 30, 2017. The DBE subcontracts value is \$21,233,215 of the \$67,382,535 total of awarded contracts.

#### Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of April 30, 2017. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

#### CMAR New:

DBE Contractors secured subcontracts on 2 projects as of April 30, 2017. The DBE subcontracts value is \$32,624,001 of the \$86,699,352 total of awarded contracts.

Total Amount of Contracts: \$ 626,526,808

### Orleans Parish School Board



#### New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of April 30, 2017. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.


#### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of April 30, 2017. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$231,354,830

\* DBE provisions were included in projects bid after June 30, 2012

## Current RSD Program DBE Participation

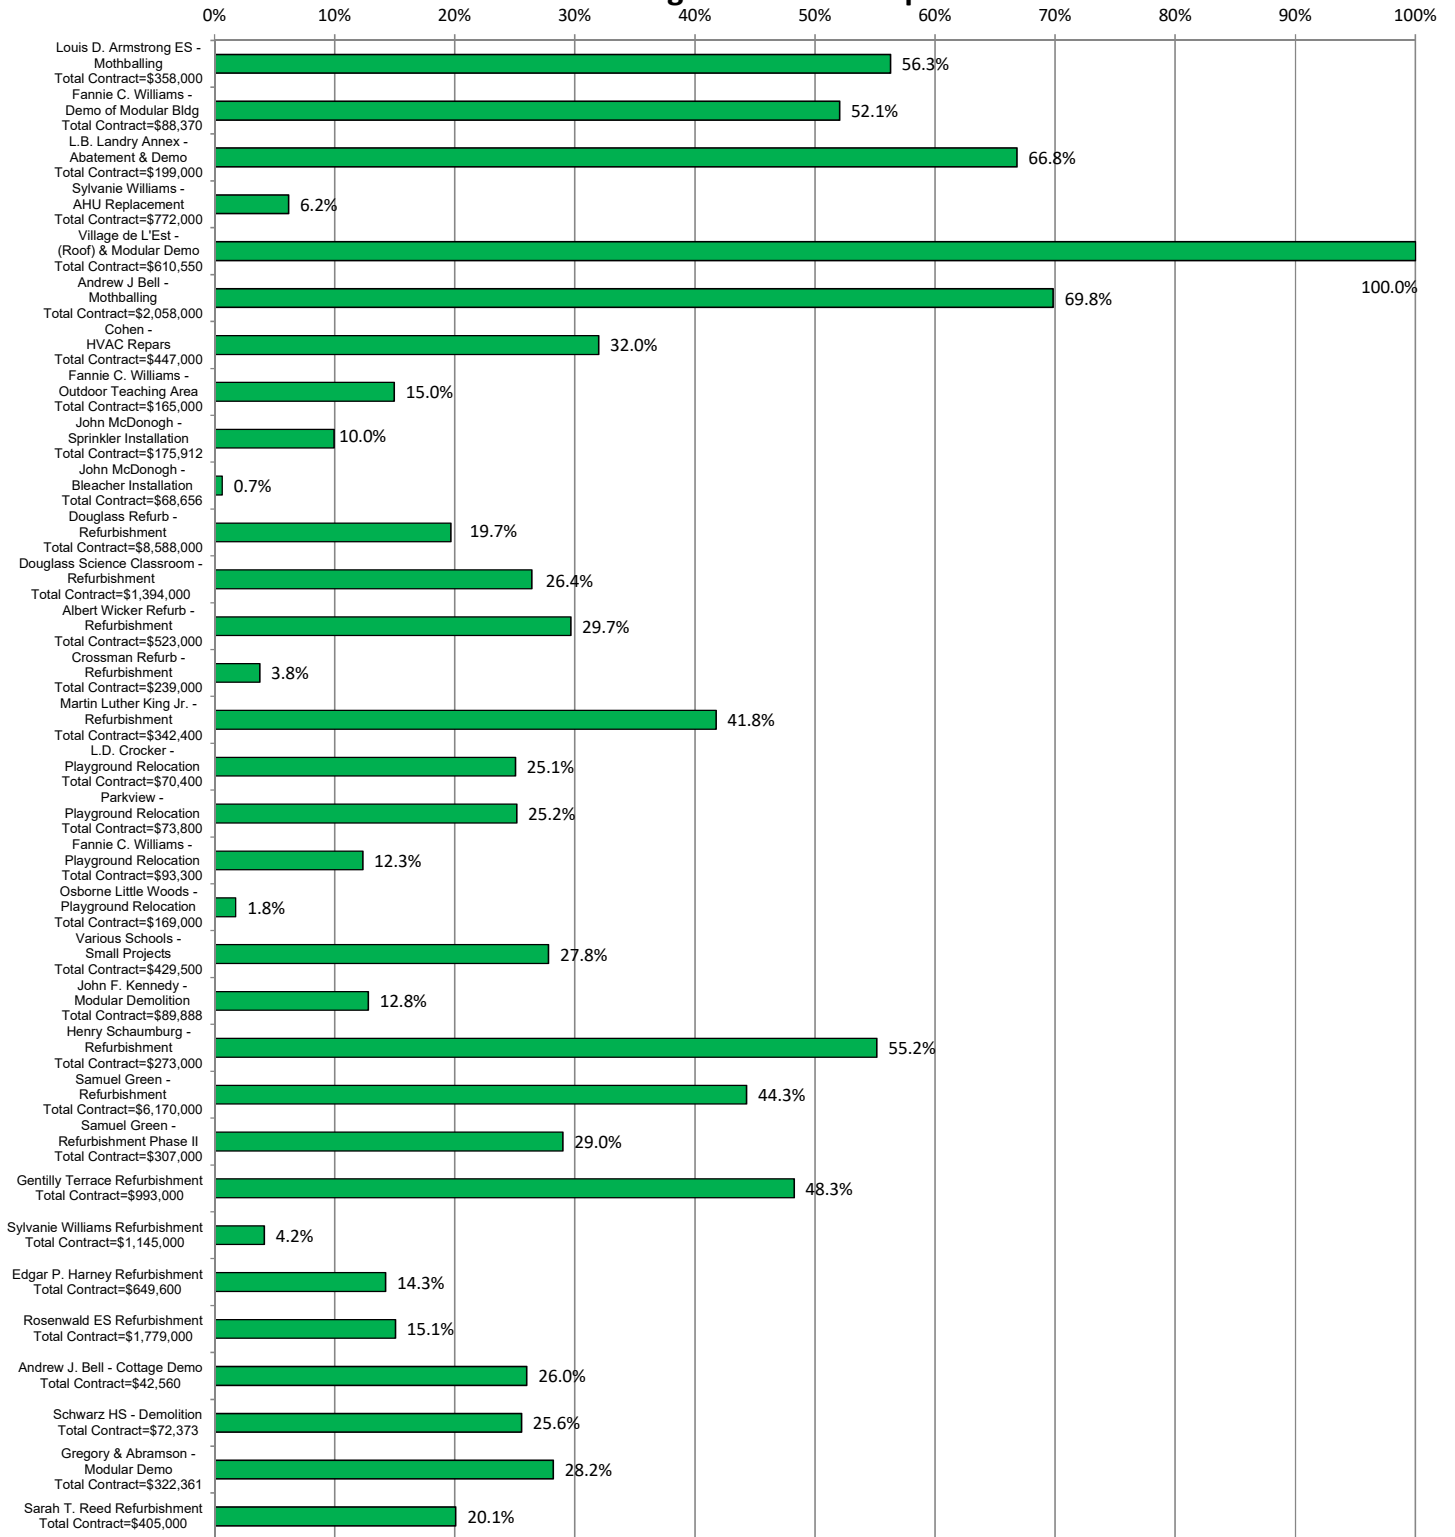


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

Status Date: 30 April 2017



## Current RSD Program DBE Participation


(Continued)

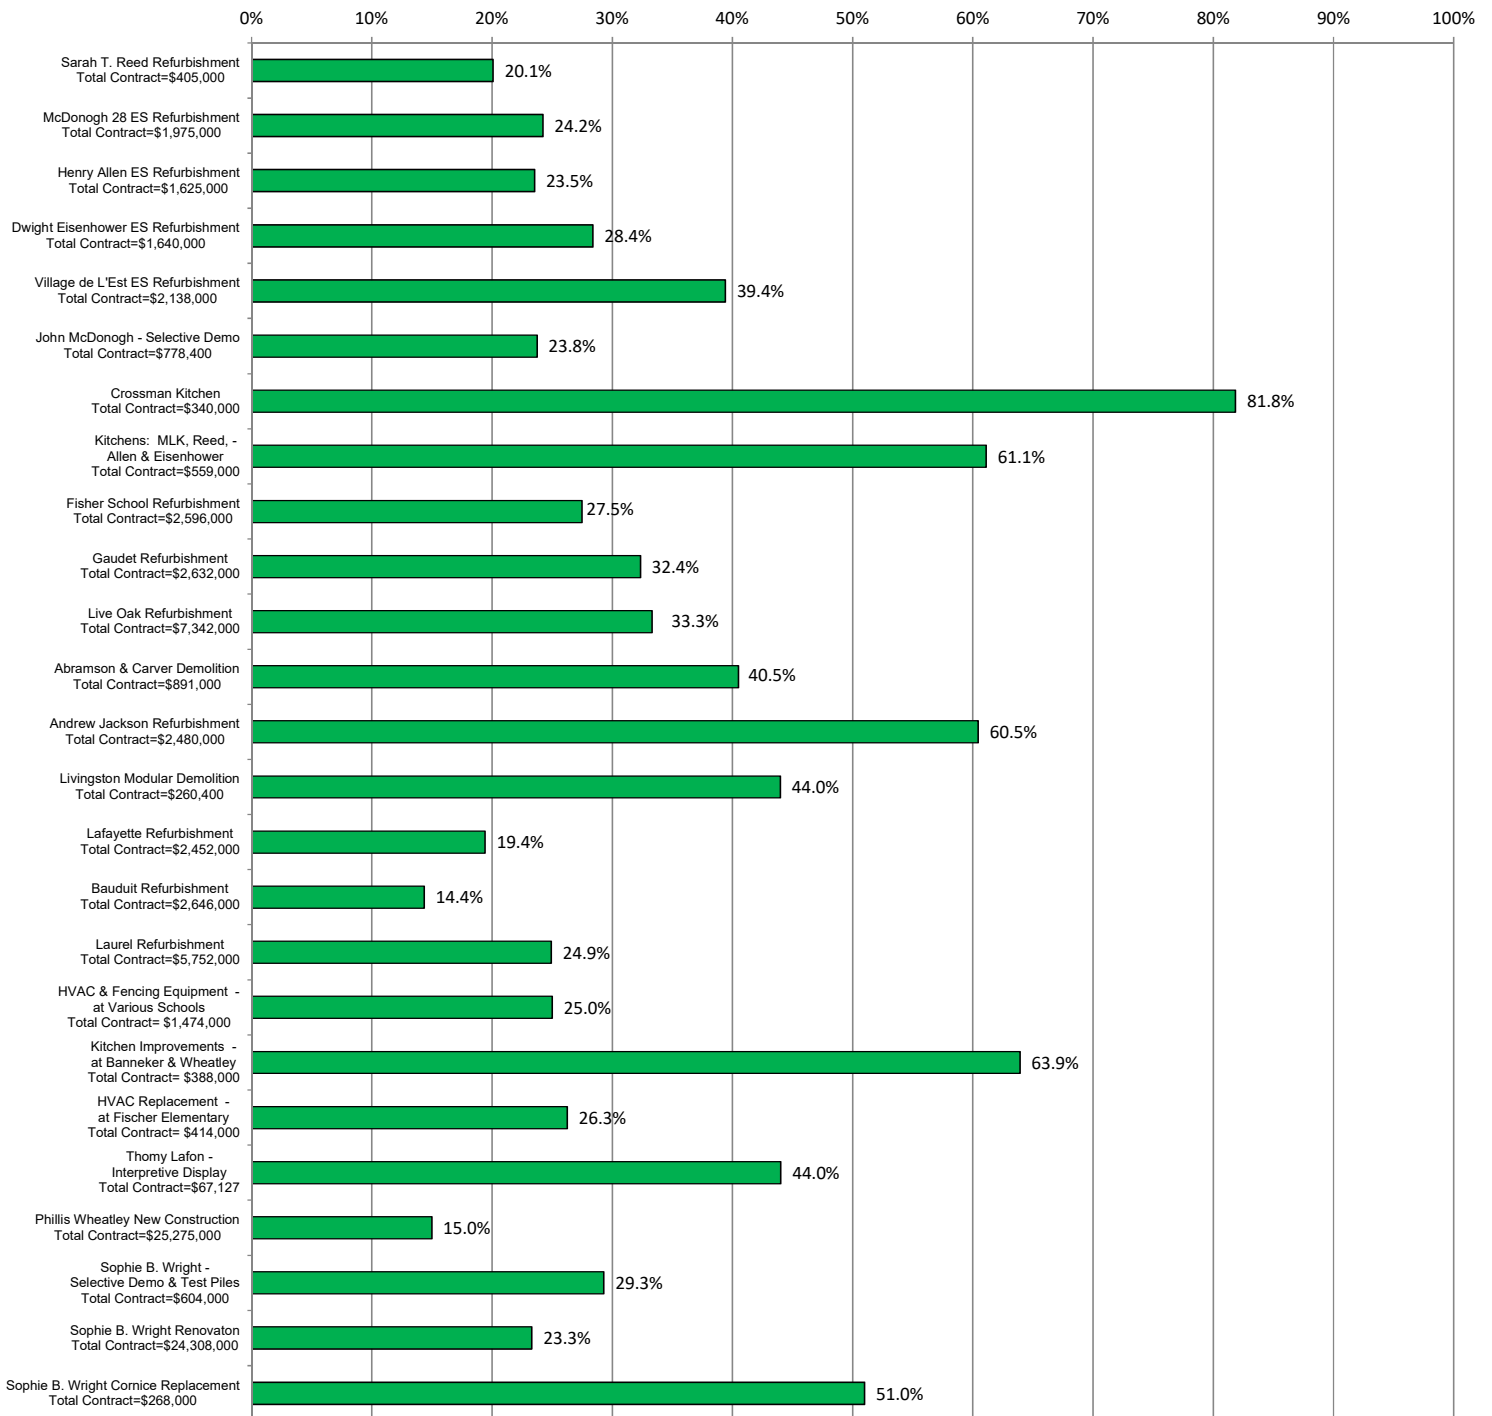

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount


## Current RSD Program DBE Participation

(Continued)

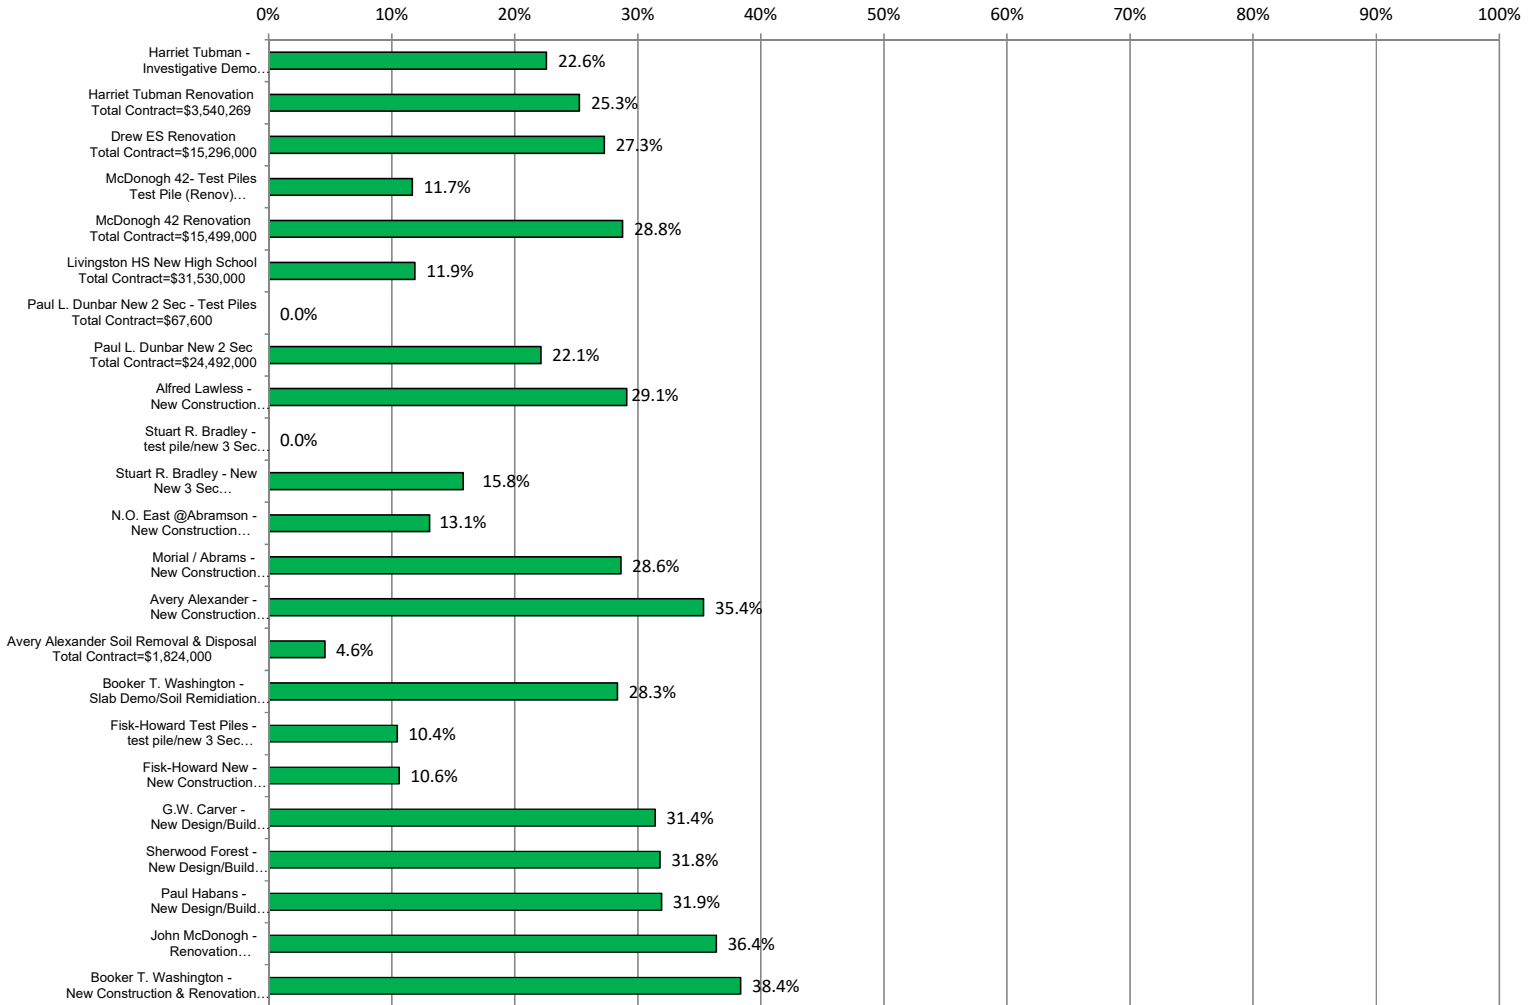

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

### Current OPSB Program DBE Participation

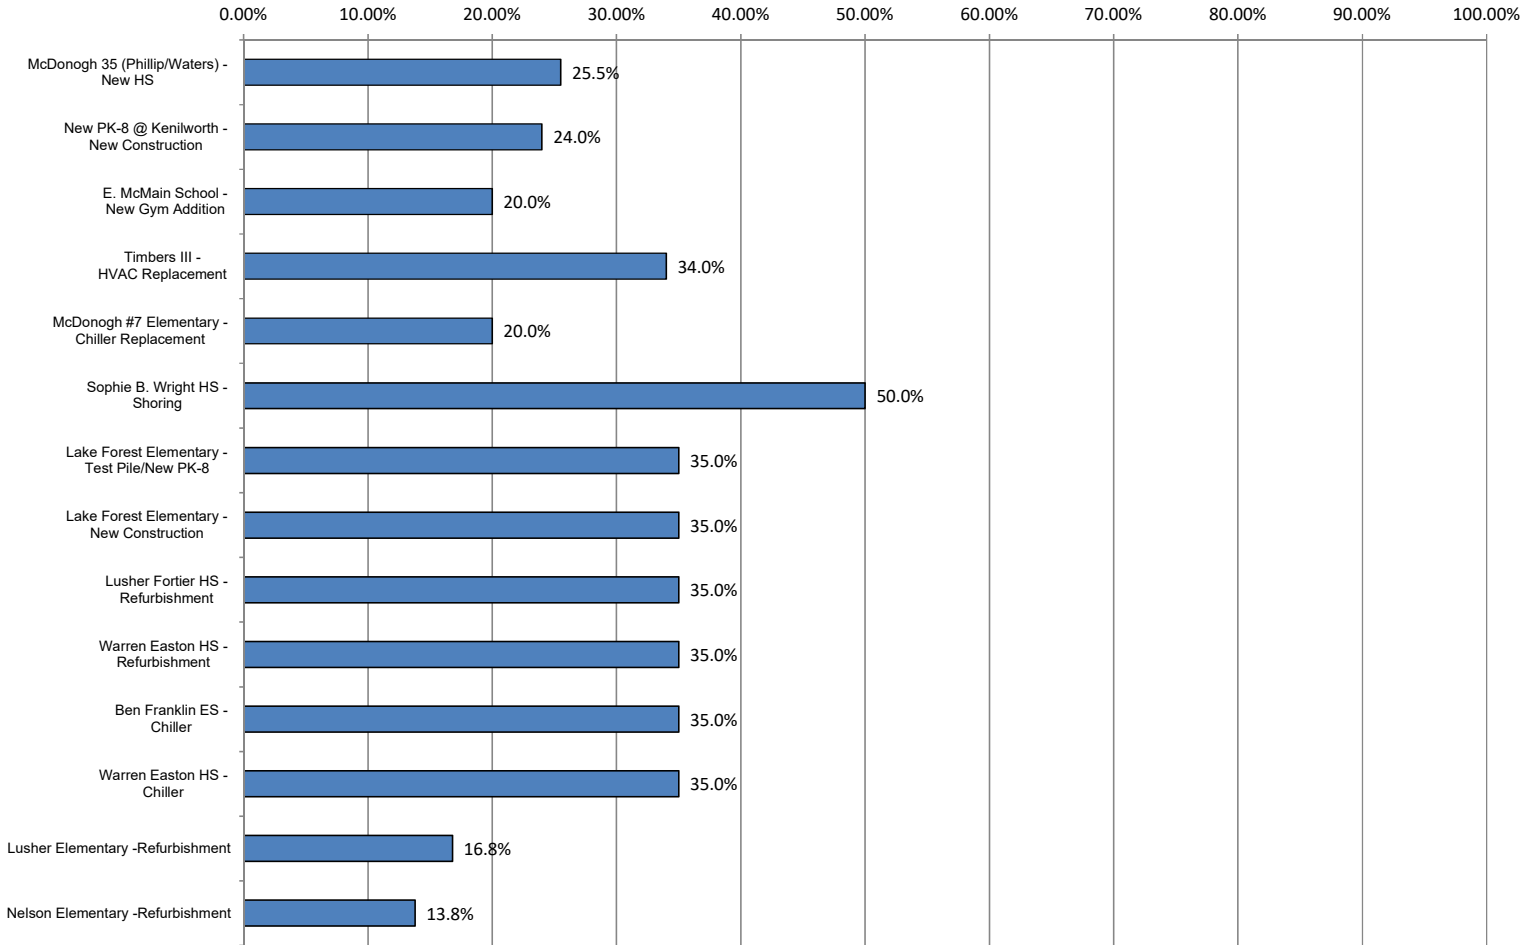

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
 OPSB DBE Participation Target = 35% of Total Contract Amount

## New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

### Avery Alexander Elementary School <sup>(RSD)</sup>

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

#### Construction Phase

- Installation of landscaping and fencing continues
- A&E is developing the punch list
- Commissioning to start the beginning of June

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



### Benjamin Franklin Elementary School Renovation <sup>(OPSB)</sup>

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

#### Procurement Phase

- 1st Advertisement - May 10th
- 2nd Advertisement - May 17th
- 3rd Advertisement - May 24th
- Pre-Bid Conference - May 25th
- Bid Opening - June 14th



### New Karr High School CMAR <sup>(RSD)</sup>

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - TBD

#### Design Phase

- 90% Construction Documents are due May 10th
- 100% Construction Documents are due June 14th

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



## John McDonogh High School Renovation CMAR <sup>(RSD)</sup>

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

### Construction Phase

- Pile driving on Gymnasium has started
- Masonry tuckpointing continues
- Mechanical and electrical rough-in work is ongoing
- interior wall framing continues on main building

Contractual Substantial Completion – October 2018

Forecasted Substantial Completion – October 2018



## Harriet R. Tubman Elementary School Renovation <sup>(RSD)</sup>

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV


Contractor - Construction Masters Inc

### Construction Phase

- Repairs to sidewalks continue
- Refurbishment of windows continue
- Damaged existing framing repair ongoing
- MEP installation continues
- Exterior plaster repairs ongoing

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018

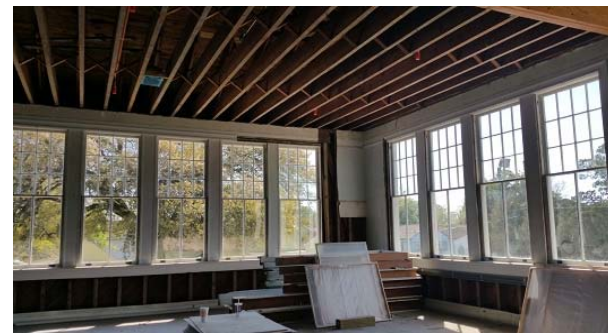

## Booker T. Washington School CMAR <sup>(RSD)</sup>

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

### Construction Phase

- Slab on grade pours continue
- Underground utility rough-in work continues
- Excavation and forming of pile caps continue

Contractual Substantial Completion – 2019

Forecasted Substantial Completion – 2019



## REFURBISHMENTS

### Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad <sup>(RSD)</sup>

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

2300 Dumaine Street, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen at Banneker and addition of grease trap at Wheatley

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Commander Corp

#### Construction Phase

- Contractor to mobilize at Banneker May 29th



### Agnes L. Bauduit Elementary School Refurbishment <sup>(RSD)</sup>

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor – One Construction

#### Construction Phase

- Window refurbishment continues
- HVAC work continues
- Parapet flashing is 50% complete
- Stucco repairs are ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – July 2017



### Mary M. Bethune Elementary School Refurbishment <sup>(OPSB)</sup>

4040 Eagle Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects

Contractor – Construction Masters Inc.

#### Construction Phase

- Contractor is mobilizing



## Warren Easton School Courtyard Waterproofing <sup>(OPSB)</sup>

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Repairs to courtyard waterproofing

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - TBD

### Construction Phase

- Contractor has mobilized
- Brick and mortar repairs have started



## William J. Fischer Elementary School Refurbishment <sup>(RSD)</sup>

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Perez

### Construction Phase

- Project is in warranty period
- Contractor to fix rear gate and fencing issues

Contractual Substantial Completion – January 2017

Actual Substantial Completion – January 2017



## William J. Fischer Elementary School HVAC Replacement <sup>(RSD)</sup>

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Replacement of existing HVAC

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Blanchard Mechanical

### Procurement Phase

- Contracts are being reviewed



## Samuel J. Green Elementary School Refurbishment Phase 2 <sup>(RSD)</sup>

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Crescent Commercial

### Close Out Phase

- Project is Substantially Complete

Contractual Substantial Completion – March 2017

Actual Substantial Completion – March 2017



## Andrew Jackson School Refurbishment <sup>(RSD)</sup>

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

### Construction Phase

- 2nd floor window refurbishment is ongoing
- Kitchen work is complete
- Work on the dumpster pad continues

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



## Lafayette Elementary School Refurbishment <sup>(RSD)</sup>

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Tuna Construction

### Construction Phase

- Window refurbishment is ongoing
- Painting has started in 2nd floor classrooms
- Modulares will be removed the end of May
- 3rd floor abatement is underway

Contractual Substantial Completion – July 2017

Forecasted Substantial Completion – July 2017





## Laurel Elementary School Refurbishment <sup>(RSD)</sup>

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

### Construction Phase

- Installation of VCT has started
- Installation of ceiling grid and lights is complete on the 2nd floor
- Window replacement continues
- Brick and mortar repairs continue

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017



## Thurgood Marshall Elementary School Refurbishment <sup>(RSD)</sup>

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

### Procurement Phase

- 1st Advertisement - May 131st
- 2nd Advertisement - June 7th
- 3rd Advertisement - June 14th
- Pre-Bid Conference - June 15th
- Bid Opening - July 6th



## McDonogh #28 School Flooring Refurbishment <sup>(RSD)</sup>

2733 Esplanade Boulevard, New Orleans, LA 70114 District A Ward 7

Scope of work: Refurbishment of existing elementary school flooring

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Hamp's Construction

### Procurement Phase

- Contract execution is underway



### McDonogh #32 School Refurbishment <sup>(RSD)</sup>

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Project place "On Hold"



### Schaumburg Roof & Harney Gutters & Downspouts <sup>(RSD)</sup>

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of roof at Schaumberg and gutters at Harney

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - TBD

Design Phase

- 50% Construction Documents are due June 30th
- 100% Construction Documents are due August 7th

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



### Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing <sup>(RSD)</sup>

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - Industrial and Mechanical Contractors, Inc

Procurement Phase

- Contract execution is underway



## DEMOLITIONS

### Demolition of Modular Buildings at Abramson 3 <sup>(RSD)</sup>

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – TBD

#### Procurement Phase

- 1st Advertisement - May 3rd
- 2nd Advertisement - May 10th
- 3rd Advertisement - May 17th
- Pre-Bid Conference - May 18th
- Bid Opening - June 7th



## Comprehensive List - Completed Projects

|    |   |            |
|----|---|------------|
| 1  | Abrams   Morial   Abramson   Coghill Demolition <sup>(RSD)</sup>                                | 11/17/2008 |
| 2  | A. D. Cross Elementary School Energy Conservation <sup>(RSD)</sup>                              |            |
| 3  | A. D. Crossman Elementary School and Benjamin Banneker Elementary School <sup>(RSD)</sup>       | 06/12/2012 |
| 4  | A. D. Crossman Elementary School Refurbishment <sup>(RSD)</sup>                                 | 06/04/2014 |
| 5  | A. D. Crossman School Kitchen Refurbishment <sup>(RSD)</sup>                                    | 01/15/2017 |
| 6  | A. P. Tureaud Elementary School Roof Repairs <sup>(RSD)</sup>                                   | 06/13/2013 |
| 7  | Agnes Bauduit Elementary School Boiler <sup>(RSD)</sup>   | 12/07/2009 |
| 8  | Albert Wicker Elementary School Refurbishment <sup>(RSD)</sup>                                  | 03/27/2014 |
| 9  | Albert Wicker Elementary School Roof Repairs <sup>(RSD)</sup>                                   | 06/13/2013 |
| 10 | Alfred Lawless Senior <sup>(RSD)</sup>  | 12/18/2015 |
| 11 | Alfred Lawless Senior High Security Fencing <sup>(RSD)</sup>                                    | 06/15/2011 |
| 12 | Alice M. Harte Elementary School <sup>(OPSB)</sup>  | 11/19/2014 |
| 13 | Alice M. Harte Elementary School Demolition <sup>(OPSB)</sup>                                   | 12/14/2011 |
| 14 | Andrew J. Bell Junior High School Roof Replacement <sup>(RSD)</sup>                             | 02/08/2014 |
| 15 | Andrew J. Bell Junior High School Mothball <sup>(RSD)</sup>                                     | 06/28/2011 |
| 16 | Andrew Jackson Elementary School Roof Repairs <sup>(RSD)</sup>                                  | 07/27/2012 |
| 17 | Andrew Jackson Elementary School Solar Panels <sup>(RSD)</sup>                                  | 01/14/2013 |
| 18 | Andrew H. Wilson Elementary School Cottage <sup>(RSD)</sup>                                     | 10/11/2010 |
| 19 | Arthur Ashe Elementary School Kitchen Renovation <sup>(OPSB)</sup>                              |            |
| 20 | Augustine Elementary School Roof <sup>(RSD)</sup>   | 04/13/2012 |
| 21 | Avery-Alexander Elementary School Demolition <sup>(RSD)</sup>                                   | 06/15/2012 |
| 22 | Barbara C. Jordan Elementary School Demolition <sup>(RSD)</sup>                                 | 05/30/2011 |
| 23 | Bell JH Shoring <sup>(RSD)</sup>  | 06/28/2011 |
| 24 | Benjamin Banneker Elementary School Energy Conservation <sup>(RSD)</sup>                        |            |
| 25 | Benjamin Franklin Senior High School <sup>(OPSB)</sup>  | 08/23/2013 |
| 26 | Bienville Elementary School Demolition <sup>(RSD)</sup>   | 05/04/2009 |
| 27 | Booker T. Washington High School Environmental Remediation <sup>(RSD)</sup>                     | 12/13/2015 |
| 28 | Booker T. Washington High School Partial Demolition <sup>(RSD)</sup>                            | 04/07/2013 |
| 29 | Carter G. Woodson Middle School Demolition <sup>(RSD)</sup>                                     | 02/09/2010 |
| 30 | Central Services Warehouse Demolition <sup>(OPSB)</sup>   | 01/05/2012 |
| 31 | Charles J. Colton Elementary Selective Demolition <sup>(RSD)</sup>                              | 07/26/2010 |
| 32 | Charles J. Colton Elementary School <sup>(RSD)</sup>  | 05/23/2013 |
| 33 | Charles R. Drew Elementary School <sup>(RSD)</sup>  | 04/17/2015 |
| 34 | Charles R. Drew Elementary Roof & Installation of Kitchen Hood <sup>(RSD)</sup>                 | 06/08/2011 |
| 35 | Cohen High School Health Clinic <sup>(RSD)</sup>  | 12/24/2008 |
| 36 | Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School <sup>(RSD)</sup> |            |
| 37 | Demolition of Modular Buildings at Gregory and Abramson <sup>(RSD)</sup>                        | 06/23/2015 |
| 38 | Demolition of Modular Buildings at Abramson and Carver <sup>(RSD)</sup>                         | 01/18/2017 |
| 39 | Demolition of Modular Buildings at Livingston <sup>(RSD)</sup>                                  | 01/18/2017 |
| 40 | Douglass High School Under Floor Utilities <sup>(RSD)</sup>                                     |            |
| 41 | Dr. Martin Luther King School Roof Repairs <sup>(RSD)</sup>                                     | 06/13/2012 |
| 42 | Dr. Martin Luther King Jr. School Renovation <sup>(RSD)</sup>                                   | 12/15/2014 |
| 43 | Dwight D. Eisenhower Elementary School Kitchen Refurbishment <sup>(RSD)</sup>                   | 02/18/2016 |

|    |   |            |
|----|---|------------|
| 44 | Dwight D. Eisenhower Elementary School Roof Repairs <sup>(RSD)</sup>                                | 07/27/2012 |
| 45 | Dwight D. Eisenhower Elementary School Refurbishment <sup>(RSD)</sup>                               | 12/23/2015 |
| 46 | East Bank Swing Space for Audubon Charter School <sup>(OPSB)</sup>                                  | 12/30/2011 |
| 47 | Edgar P. Harney Elementary School Refurbishment <sup>(RSD)</sup>                                    |            |
| 48 | Edgar P. Harney Elementary School Roof Repairs <sup>(RSD)</sup>                                     | 06/13/2012 |
| 49 | Edna Karr High School - Gymnasium Repair <sup>(OPSB)</sup>  | 12/23/2013 |
| 50 | Edna Karr High School - Assessment <sup>(OPSB)</sup>  |            |
| 51 | Edward Livingston Middle School Demolition <sup>(RSD)</sup>   | 09/28/2010 |
| 52 | Edward Henry Phillips Junior High School Demolition <sup>(OPSB)</sup>                               | 11/19/2010 |
| 53 | New Edward Hynes School <sup>(OPSB)</sup>   | 02/06/2012 |
| 54 | Edwards   Hardin   Lockett   Lawless Demolition <sup>(RSD)</sup>                                    | 11/03/2008 |
| 55 | Edward Livingston High School <sup>(RSD)</sup>  | 01/05/2015 |
| 56 | Eleanor L. McMMain School Replacement of Existing Chillers <sup>(OPSB)</sup>                        | 08/30/2011 |
| 57 | Eleanor L. McMMain School Clinic <sup>(OPSB)</sup>  | 07/24/2013 |
| 58 | Eleanor L. McMMain School Maintenance Upgrades <sup>(OPSB)</sup>                                    | 12/12/2016 |
| 59 | Eleanor L. McMMain School Roof Replacement <sup>(OPSB)</sup>  | 05/13/2016 |
| 60 | Ernest "Dutch" Morial Elementary <sup>(RSD)</sup>   | 03/17/2017 |
| 61 | Ernest N. Morial Elementary Security Fencing <sup>(RSD)</sup>                                       | 05/10/2011 |
| 62 | Fannie C. Williams Elementary School Demolition <sup>(RSD)</sup>                                    | 03/10/2009 |
| 63 | Fisk-Howard Elementary School Demolition <sup>(RSD)</sup>   | 10/04/2011 |
| 64 | Florence J. Chester Elementary School Demolition <sup>(RSD)</sup>                                   | 06/05/2011 |
| 65 | Fortier (Lusher) High School Refurbishment <sup>(OPSB)</sup>  | 02/05/2016 |
| 66 | Francis W. Gregory Demolition <sup>(RSD)</sup>  | 12/21/2011 |
| 67 | Frederick A. Douglass High Refurbishment <sup>(RSD)</sup>   | 10/28/2014 |
| 68 | Frederick A. Douglass High School Science Lab <sup>(RSD)</sup>                                      | 07/05/2016 |
| 69 | Frederick A. Douglass High Switchgear <sup>(RSD)</sup>  | 08/04/2009 |
| 70 | Frederick A. Douglass High Emergency Boiler Roof Repairs <sup>(RSD)</sup>                           |            |
| 71 | Gaudet Elementary School Refurbishment <sup>(RSD)</sup>   | 12/20/2016 |
| 72 | Gentilly Terrace Elementary School Refurbishment <sup>(RSD)</sup>                                   | 09/22/2015 |
| 73 | George Mondy Elementary School Mothball <sup>(RSD)</sup>  |            |
| 74 | George Washington Carver School <sup>(RSD)</sup>  | 03/07/2016 |
| 75 | George Washington Carver High School Demolition <sup>(RSD)</sup>                                    | 08/24/2011 |
| 76 | Greater St. Stephens School <sup>(OPSB)</sup>   | 03/18/2013 |
| 77 | Harriet R. Tubman Elementary School Selective Demolition <sup>(RSD)</sup>                           | 12/14/2014 |
| 78 | Henry Allen Elementary School Refurbishment <sup>(RSD)</sup>  | 03/08/2016 |
| 79 | Henry Allen Elementary School Kitchen Refurbishment <sup>(RSD)</sup>                                | 02/18/2016 |
| 80 | Henry Allen Elementary School Roof <sup>(RSD)</sup>   | 05/24/2010 |
| 81 | Henry C. Schaumburg School Refurbishment <sup>(RSD)</sup>   | 06/26/2015 |
| 82 | Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation <sup>(RSD)</sup> | 12/16/2011 |
| 83 | Holy Cross Modular Relocation <sup>(RSD)</sup>  | 12/14/2010 |
| 84 | Israel M. Augustine Middle School Roof Replacement <sup>(RSD)</sup>                                 | 04/13/2012 |
| 85 | Israel M. Augustine Middle School Mothball <sup>(RSD)</sup>   | 01/18/2013 |
| 86 | James Derham Demolition <sup>(RSD)</sup>  | 02/23/2012 |
| 87 | James W. Johnson Elementary School Roof <sup>(RSD)</sup>  | 07/31/2010 |
| 88 | New Jean Batiste de Bienville School <sup>(RSD)</sup>   | 06/15/2012 |
| 89 | Jean Gordon Elementary School Demolition <sup>(RSD)</sup>   | 08/16/2010 |

|     |   |            |
|-----|---|------------|
| 90  | JoEllen Smith Medical Center Demolition <sup>(OPSB)</sup>                         |            |
| 91  | John Dibert Elementary School Roof <sup>(RSD)</sup>                               | 08/20/2010 |
| 92  | John W. Hoffman Elementary School Demolition <sup>(RSD)</sup>                     | 05/25/2010 |
| 93  | John F. Kennedy Modular Relocation (Schwarz Campus) <sup>(RSD)</sup>              | 11/05/2010 |
| 94  | John F. Kennedy Modular Relocation (Coghill Modular Campus) <sup>(RSD)</sup>      | 08/05/2011 |
| 95  | John F. Kennedy Modular Demolition <sup>(RSD)</sup>                               | 09/16/2014 |
| 96  | John F. Kennedy High School Demolition <sup>(RSD)</sup>                           | 01/12/2012 |
| 97  | John McDonogh Senior High School Bleachers and Sprinklers <sup>(RSD)</sup>        | 03/27/2014 |
| 98  | John McDonogh Senior High School Roof <sup>(RSD)</sup>                            | 05/04/2010 |
| 99  | John A. Shaw Elementary School Mothball <sup>(RSD)</sup>                          | 12/12/2012 |
| 100 | Joseph S. Clark Senior High School Roof Repairs <sup>(RSD)</sup>                  | 07/27/2012 |
| 101 | Joseph A. Craig Elementary Canopies <sup>(RSD)</sup>                              | 06/06/2011 |
| 102 | Joseph A. Craig Elementary Elevator Installation <sup>(RSD)</sup>                 | 01/20/2012 |
| 103 | Joseph A. Hardin Elementary Security Fencing <sup>(RSD)</sup>                     | 05/10/2011 |
| 104 | Lafayette Elementary School Roof and Masonry <sup>(RSD)</sup>                     | 06/22/2012 |
| 105 | Lake Area   Landry Demolition <sup>(RSD)</sup>                                    | 05/01/2008 |
| 106 | Lake Forest PK-8 at the Greater St. Stephens Site <sup>(OPSB)</sup>               | 11/13/2015 |
| 107 | Langston Hughes Elementary School (Phase I) <sup>(RSD)</sup>                      | 08/11/2009 |
| 108 | Langston Hughes Elementary School - New Gymnasium (Phase II) <sup>(RSD)</sup>     | 11/10/2010 |
| 109 | Langston Hughes Elementary School - Dumpster Pad <sup>(RSD)</sup>                 | 10/12/2012 |
| 110 | Lawrence D. Crocker Elementary School Demolition <sup>(RSD)</sup>                 | 04/02/2010 |
| 111 | L.B. Landry Annex Demolition <sup>(RSD)</sup>                                     | 05/02/2013 |
| 112 | Little Woods Elementary School Demolition <sup>(RSD)</sup>                        | 08/09/2010 |
| 113 | Little Woods School (Dolores T. Aaron Elementary School) <sup>(RSD)</sup>         | 08/01/2013 |
| 114 | Live Oak Elementary School Refurbishment <sup>(RSD)</sup>                         | 01/06/2017 |
| 115 | Live Oak Elementary School Roof <sup>(RSD)</sup>                                  | 08/04/2011 |
| 116 | Live Oak Elementary School Exterior Door Replacement <sup>(RSD)</sup>             | 08/26/2011 |
| 117 | Lorraine Hansberry Elementary School Mothball <sup>(RSD)</sup>                    | 12/27/2012 |
| 118 | Louis D. Armstrong Elementary School <sup>(RSD)</sup>                             | 02/18/2013 |
| 119 | Lusher Elementary School Refurbishment <sup>(OPSB)</sup>                          | 10/31/2016 |
| 120 | Mahalia Jackson Elementary School <sup>(OPSB)</sup>                               | 05/11/2010 |
| 121 | Mahalia Jackson Elementary School Dumpster / Other Improvements <sup>(OPSB)</sup> | 03/06/2012 |
| 122 | Mahalia Jackson Elementary School Office Renovation <sup>(OPSB)</sup>             | 04/30/2013 |
| 123 | Martin Behrman Elementary School Roof <sup>(RSD)</sup>                            | 02/23/2010 |
| 124 | Martin Luther King Jr. Elementary Canopy System <sup>(RSD)</sup>                  | 11/05/2011 |
| 125 | Martin Luther King Jr. School Modular Building, Deck, Canopy <sup>(RSD)</sup>     | 07/31/2012 |
| 126 | Martin Luther King Jr. School Kitchen Refurbishment <sup>(RSD)</sup>              | 02/18/2016 |
| 127 | Mary Church Terrell Elementary School Demolition <sup>(RSD)</sup>                 | 04/17/2013 |
| 128 | Mary M. Bethune Elementary 1st Floor Replacement <sup>(OPSB)</sup>                | 01/24/2011 |
| 129 | Mary M. Bethune Elementary Rear Yard Repair/Resurfacing <sup>(OPSB)</sup>         | 01/21/2011 |
| 130 | McDonogh #7 High School Repairs <sup>(OPSB)</sup>                                 |            |
| 131 | McDonogh #15 Elementary Exterior Masonry to SOI Standards <sup>(RSD)</sup>        | 06/11/2012 |
| 132 | McDonogh #28 School Refurbishment <sup>(RSD)</sup>                                | 03/15/2016 |
| 133 | McDonogh #28 Elementary School Roof <sup>(RSD)</sup>                              | 11/19/2011 |
| 134 | McDonogh #32 Roof Replacement <sup>(RSD)</sup>                                    | 02/24/2012 |

|     |   |            |
|-----|---|------------|
| 135 | McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium <sup>(OPSB)</sup> | 01/17/2014 |
| 136 | McDonogh #35 School at the Phillip/ Waters Site <sup>(OPSB)</sup>   | 09/23/2015 |
| 137 | McDonogh #42 Elementary School Renovation <sup>(RSD)</sup>  | 05/28/2015 |
| 138 | McDonogh #42 Elementary School Roof <sup>(RSD)</sup>  | 12/21/2011 |
| 139 | McDonogh #42 Elementary School HVAC Replacement <sup>(RSD)</sup>  | 08/09/2010 |
| 140 | Mildred C. Osborne Elementary School Demolition <sup>(RSD)</sup>  | 02/18/2010 |
| 141 | Mildred C. Osborne Elementary School <sup>(RSD)</sup>   | 12/03/2012 |
| 142 | Modular Campuses Close Outs <sup>(RSD)</sup>  |            |
| 143 | Modular Classroom Demolition at Fannie C. Williams Elementary School <sup>(RSD)</sup>                               | 05/22/2013 |
| 144 | Modular Structures at Langston Hughes Elementary School <sup>(RSD)</sup>  | 04/05/2010 |
| 145 | Morris F.X. Jeff Elementary School Demolition <sup>(RSD)</sup>  |            |
| 146 | Morris F.X. Jeff Elementary School Mothball <sup>(RSD)</sup>  | 01/15/2013 |
| 147 | Murray G. Henderson Elementary School Roof <sup>(RSD)</sup>   | 06/23/2012 |
| 148 | Nelson Elementary School Refurbishment <sup>(OPSB)</sup>  | 04/18/2016 |
| 149 | New Andrew H. Wilson Elementary School <sup>(RSD)</sup>   | 10/11/2009 |
| 150 | New Carter G. Woodson School <sup>(RSD)</sup>   | 09/14/2012 |
| 151 | New Fannie C. Williams School <sup>(RSD)</sup>  | 08/24/2012 |
| 152 | New Joseph A. Craig Elementary School <sup>(RSD)</sup>  | 12/09/2009 |
| 153 | New L.B. Landry High School <sup>(RSD)</sup>  | 06/30/2010 |
| 154 | New Lake Area High School <sup>(RSD)</sup>  | 12/28/2009 |
| 155 | New Lawrence D. Crocker School <sup>(RSD)</sup>   | 04/29/2013 |
| 156 | New PK-8 School at North Kenilworth Park at Curran Site <sup>(OPSB)</sup>   | 01/29/2016 |
| 157 | New Parkview School <sup>(RSD)</sup>  | 10/12/2012 |
| 158 | New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens <sup>(RSD)</sup>                                      |            |
| 159 | New William Frantz Elementary School <sup>(RSD)</sup>   |            |
| 160 | New Orleans High School Signature Center Study <sup>(RSD)</sup>   |            |
| 161 | Oretha C. Haley Demo <sup>(RSD)</sup>   | 05/07/2012 |
| 162 | Oretha C. Haley Elementary School Mothball <sup>(RSD)</sup>   | 09/17/2012 |
| 163 | Parkview Elementary School Demolition <sup>(RSD)</sup>  | 08/06/2009 |
| 164 | Paul L. Dunbar Elementary School Demolition <sup>(RSD)</sup>  | 06/16/2010 |
| 165 | Paul L. Dunbar Elementary School <sup>(RSD)</sup>   | 06/02/2015 |
| 166 | Paul B. Habans Elementary School <sup>(RSD)</sup>   | 06/30/2016 |
| 167 | Paul B. Habans Elementary School Roof Repairs <sup>(RSD)</sup>  | 07/27/2012 |
| 168 | Phillis Wheatley Elementary School Demolition <sup>(RSD)</sup>  | 09/26/2011 |
| 169 | Phillis Wheatley Elementary School <sup>(RSD)</sup>   | 07/10/2014 |
| 170 | Ray Abrams Elementary School <sup>(RSD)</sup>   | 03/17/2017 |
| 171 | Rosenwald Elementary School Refurbishment <sup>(RSD)</sup>  | 04/07/2016 |
| 172 | Robert M. Lusher Elementary Roof Removal & Replacement <sup>(OPSB)</sup>  | 07/14/2011 |
| 173 | Samuel J. Green Elementary School Refurbishment <sup>(RSD)</sup>  | 02/15/2016 |
| 174 | Sarah T. Reed High School Bleachers <sup>(RSD)</sup>  | 01/11/2012 |
| 175 | Sarah T. Reed High School Auditorium Wall <sup>(RSD)</sup>  | 03/29/2010 |
| 176 | Sarah T. Reed High School Kitchen Refurbishment <sup>(RSD)</sup>  | 02/18/2016 |
| 177 | Sarah T. Reed High School Refurbishment <sup>(RSD)</sup>  | 12/01/2015 |
| 178 | Seabrook Computer Training Center Demolition <sup>(OPSB)</sup>  | 06/25/2010 |
| 179 | Schaumburg Chillers <sup>(RSD)</sup>  | 11/14/2008 |

|     |  |            |
|-----|--|------------|
| 180 | Schwarz Alternative Repairs <sup>(RSD)</sup>   | 07/14/2009 |
| 181 | Schwarz Alternative Modulars Demolition <sup>(RSD)</sup>   | 04/02/2015 |
| 182 | Schwarz Modular Building Demolition <sup>(RSD)</sup>   | 04/02/2015 |
| 183 | Sherwood Forest Elementary School Demolition <sup>(RSD)</sup>                                      | 10/28/2010 |
| 184 | Sherwood Forest Elementary School <sup>(RSD)</sup>   | 06/30/2016 |
| 185 | Small New Orleans East High School at Abramson <sup>(RSD)</sup>                                    | 09/24/2015 |
| 186 | Sophie B. Wright School Renovation <sup>(RSD)</sup>  | 06/08/2016 |
| 187 | Sophie B. Wright School Selective Demolition <sup>(RSD)</sup>                                      | 01/31/2014 |
| 188 | Sophie B. Wright Various Repairs/Restroom Renovations <sup>(OPSB)</sup>                            | 07/26/2011 |
| 189 | Stuart R. Bradley Elementary School Demolition <sup>(RSD)</sup>                                    | 01/27/2010 |
| 190 | Stuart R. Bradley Elementary School <sup>(RSD)</sup>   | 06/26/2015 |
| 191 | Sylvanie Williams Elementary School AHU Replacement <sup>(RSD)</sup>                               | 07/30/2013 |
| 192 | Sylvanie Williams Elementary School Play Yard <sup>(RSD)</sup>                                     | 09/23/2010 |
| 193 | Sylvanie Williams Elementary School Roof Repairs <sup>(RSD)</sup>                                  | 07/27/2012 |
| 194 | Sylvanie Williams Elementary School HVAC/Chiller Replacement <sup>(RSD)</sup>                      | 04/13/2012 |
| 195 | Sylvanie Williams Elementary School Refurbishment <sup>(RSD)</sup>                                 | 02/18/2016 |
| 196 | Temporary Campus for McDonogh #11 Expropriation <sup>(OPSB)</sup>                                  |            |
| 197 | Thomas A. Edison Elementary School Demolition <sup>(RSD)</sup>                                     | 03/25/2010 |
| 198 | Thomy Lafon Elementary School Demolition <sup>(RSD)</sup>  | 11/27/2011 |
| 199 | Thomy Lafon School Interpretative Display <sup>(RSD)</sup>   | 10/15/2013 |
| 200 | Timbers Park Office Building #1 & #2 Demolition <sup>(OPSB)</sup>                                  | 09/18/2011 |
| 201 | Timbers HVAC <sup>(OPSB)</sup>   | 09/11/2013 |
| 202 | Timbers III - IT Room Relocation <sup>(OPSB)</sup>   | 02/11/2015 |
| 203 | Village de L'est Elementary School Subsidence <sup>(RSD)</sup>                                     | 06/18/2012 |
| 204 | Village de L'est Elementary School Refurbishment <sup>(RSD)</sup>                                  | 10/12/2106 |
| 205 | Village de L'est Elementary School Roof and Modular Demolition <sup>(RSD)</sup>                    | 06/16/2013 |
| 206 | Vorice J. Waters Elementary School Demolition <sup>(RSD)</sup>                                     | 01/14/2010 |
| 207 | Valena C. Jones Elementary School <sup>(RSD)</sup>   | 01/10/2013 |
| 208 | Walter L. Cohen High School HVAC <sup>(RSD)</sup>  | 04/04/2014 |
| 209 | Warren Easton High School Renovation <sup>(OPSB)</sup>   | 12/15/2015 |
| 210 | Warren Easton High School Window Replacement <sup>(OPSB)</sup>                                     | 09/07/2012 |
| 211 | West Bank Swing Space for Alice Harte Elementary School <sup>(OPSB)</sup>                          | 07/11/1931 |
| 212 | New William J. Guste Elementary School <sup>(RSD)</sup>  | 10/06/2008 |
| 213 | William J. Guste Elementary School Science Lab <sup>(RSD)</sup>                                    | 08/04/2009 |
| 214 | William Frantz Elementary School Environmental Remediation & Selective Demolition <sup>(RSD)</sup> | 04/15/2010 |
| 215 | William Frantz Elementary School Roof <sup>(RSD)</sup>   | 08/12/2010 |
