


Superintendent's Report November 2017



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Ms. Kunjan Narechania
Recovery School District

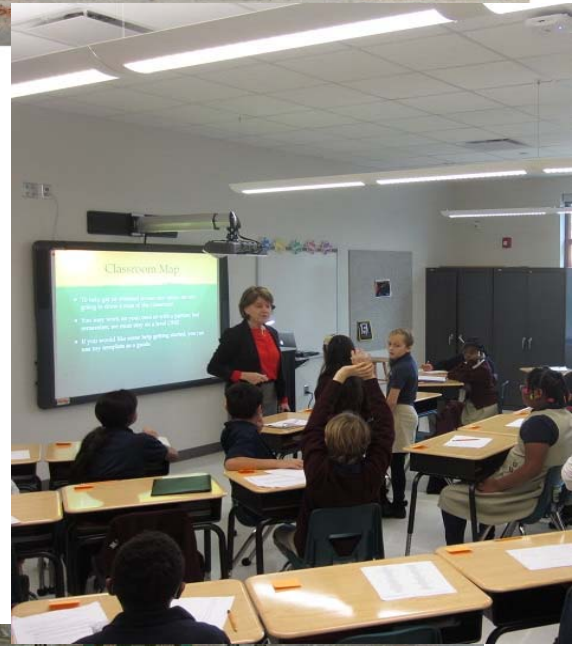

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	10
Benjamin Franklin Elementary School Renovation ^(OPSB)	10
New Karr High School, CMAR ^(RSD)	10
New Orleans Charter Science and Mathematics High School ^(OPSB)	10
John McDonogh High School Renovation CMAR ^(RSD)	11
Harriet R. Tubman Elementary School Renovation ^(RSD)	11
Booker T. Washington School CMAR ^(RSD)	11
REFURBISHMENTS	12
Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)	12
Mary M. Bethune Elementary School Refurbishment ^(OPSB)	12
Warren Easton Courtyard Waterproofing ^(OPSB)	12
Harney Elementary School Downspout and Gutter Repairs ^(RSD)	13
Lafayette Elementary School Refurbishment ^(RSD)	13
Laurel Elementary School Refurbishment ^(RSD)	13
Thurgood Marshall Elementary School Refurbishment ^(RSD)	14
McDonogh #28 School Flooring Refurbishment ^(RSD)	14
McDonogh #32 School Refurbishment ^(RSD)	14
Eleanor McMain School Envelope Repairs ^(OPSB)	15
Harriet R. Tubman Elementary School Cottage Renovation ^(RSD)	15
Schaumburg Elementary School Roof Repairs ^(RSD)	15
Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing ^(RSD)	16
DEMOLITIONS	17
Demolition of Modulars at Abramson 3 ^(RSD)	17
Demolition of Modulars at Coghill ^(RSD)	17
COMPLETED PROJECTS	18

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$469 million in open contracts for the capital program after issuing \$2.8 million in new contracts, change orders and amendments in November. In addition, the total change orders to date, \$7.3 million, account for one percent (1.75%) of the total open construction contracts. RSD anticipates issuing \$309 thousand in construction contracts/change orders, and \$1.6 million in professional service contracts/amendments in December.



The OPSB has \$233 million in open contracts for the capital program after issuing \$0 thousand in new contracts, change orders and amendments in November. In addition, the total change orders to date, \$9.3 million, account for approximately four percent (4.74%) of the total open construction contracts. OPSB anticipates issuing approximately \$1.9 million in construction contracts/change orders and \$113 thousand in professional service contracts and amendments in December.

Community Meetings



Future Community Meetings

No Community Meeting are Scheduled

Bid Openings

Projects which are scheduled to bid in the next 60 days

February 7, 2018

McDonogh 28 Flooring Renovation Phase 2 bid Opening

February 28, 2018

Lafayette School Refurbishment Renovation Phase 2 bid Opening

Disadvantaged Business Enterprises (DBE) Monthly Summary



Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of November 30, 2017. The DBE subcontracts value is \$81,532,322 of the \$362,866,202 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 54 projects as of November 30, 2017. The DBE subcontracts value is \$23,188,080 of the \$73,075,270 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of November 30, 2017. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 2 projects as of November 30, 2017. The DBE subcontracts value is \$29,764,319 of the \$86,699,352 total of awarded contracts.

Total Amount of Contracts: \$ 631,778,381

Orleans Parish School Board



New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of November 30, 2017. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of November 30, 2017. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$231,354,830


* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

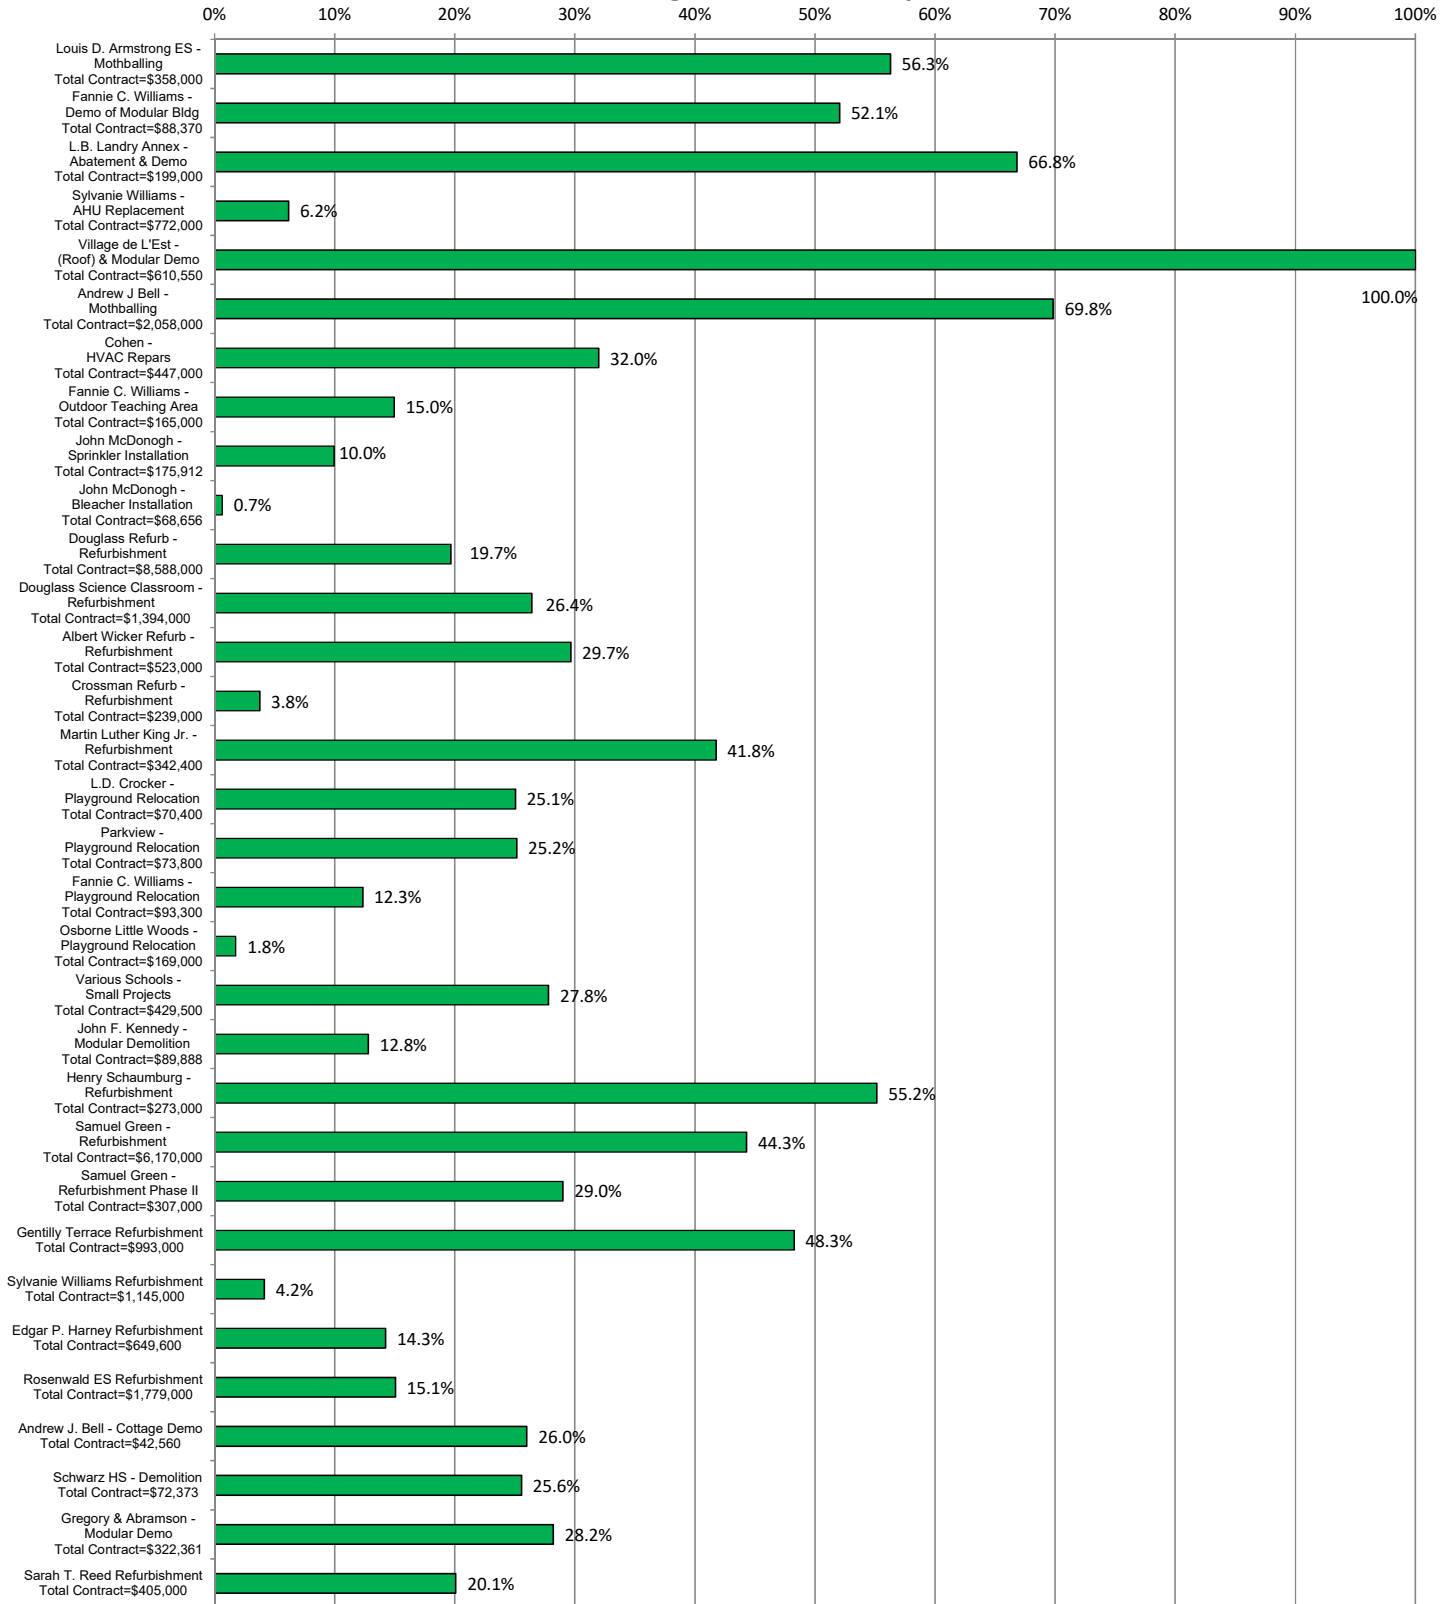

Current RSD Program DBE Participation


(Continued)

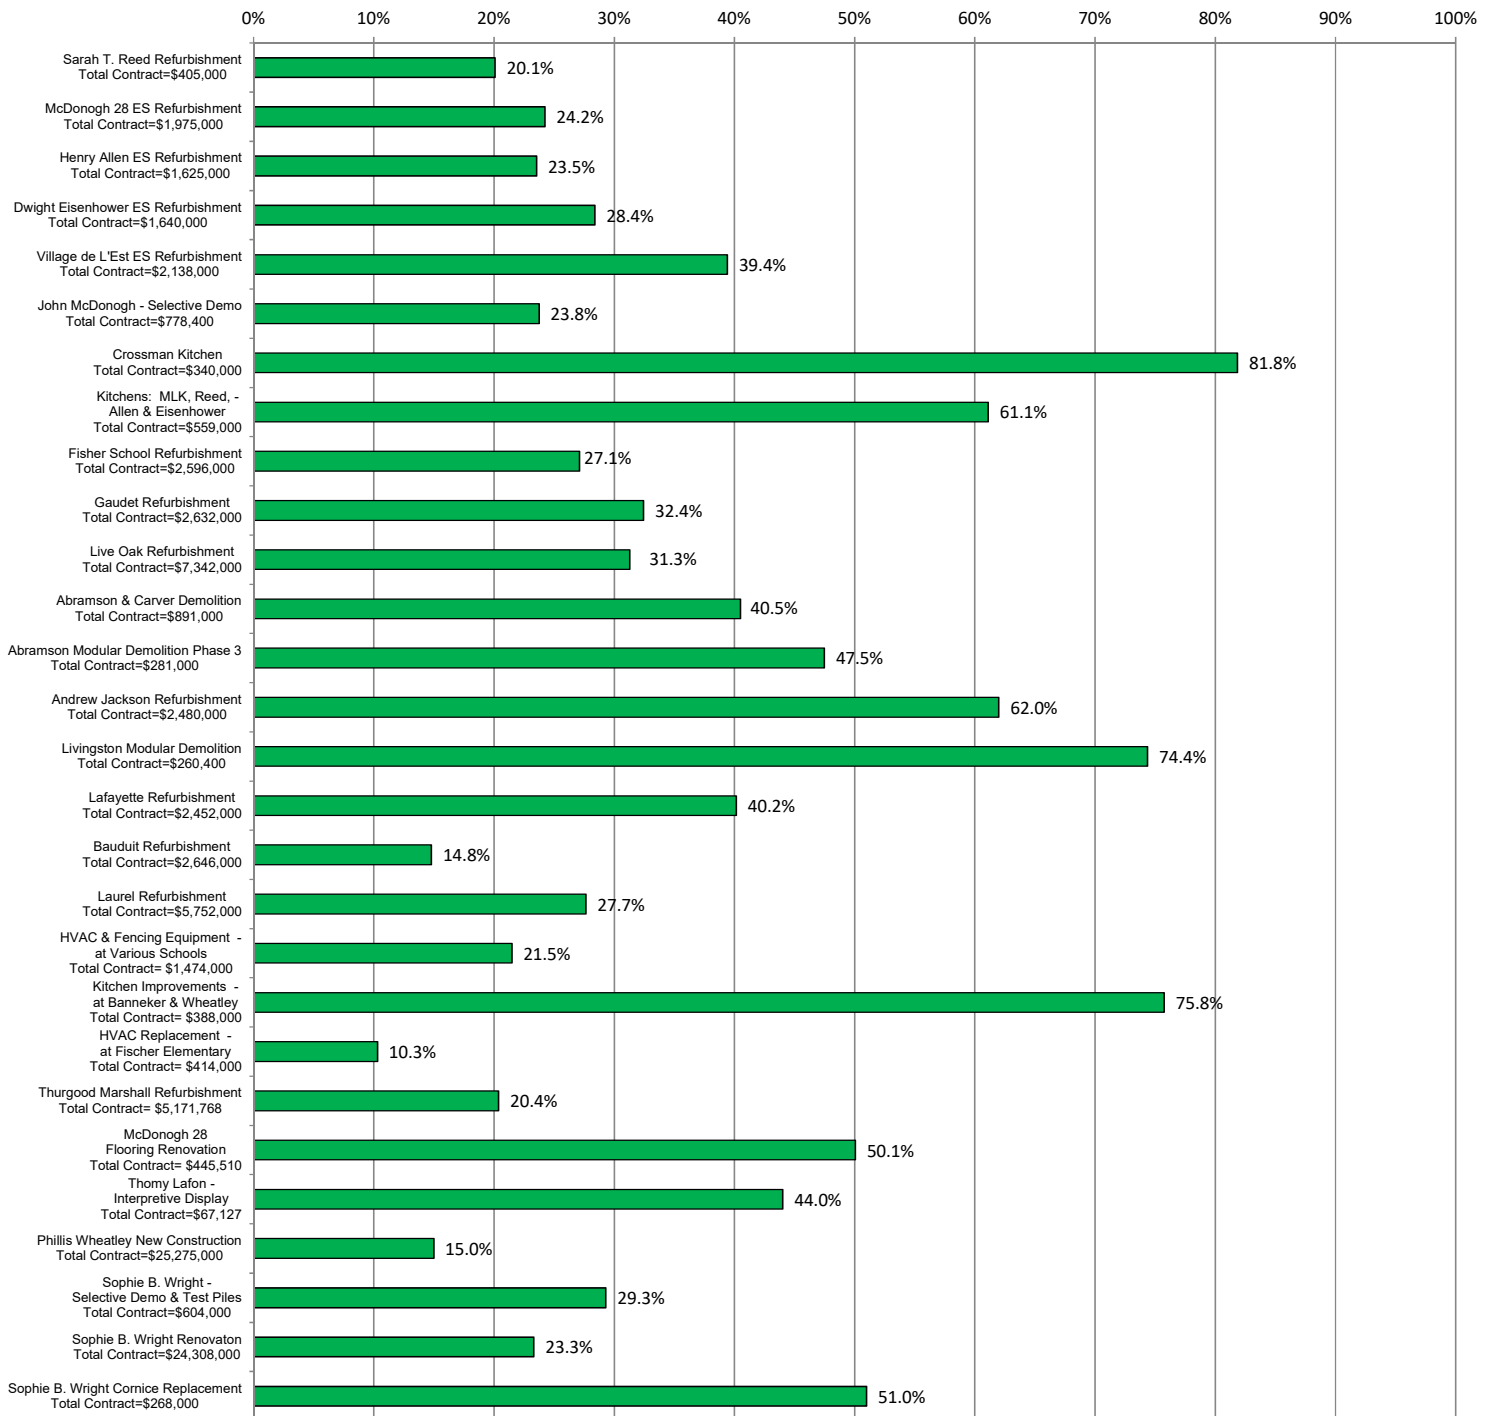

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

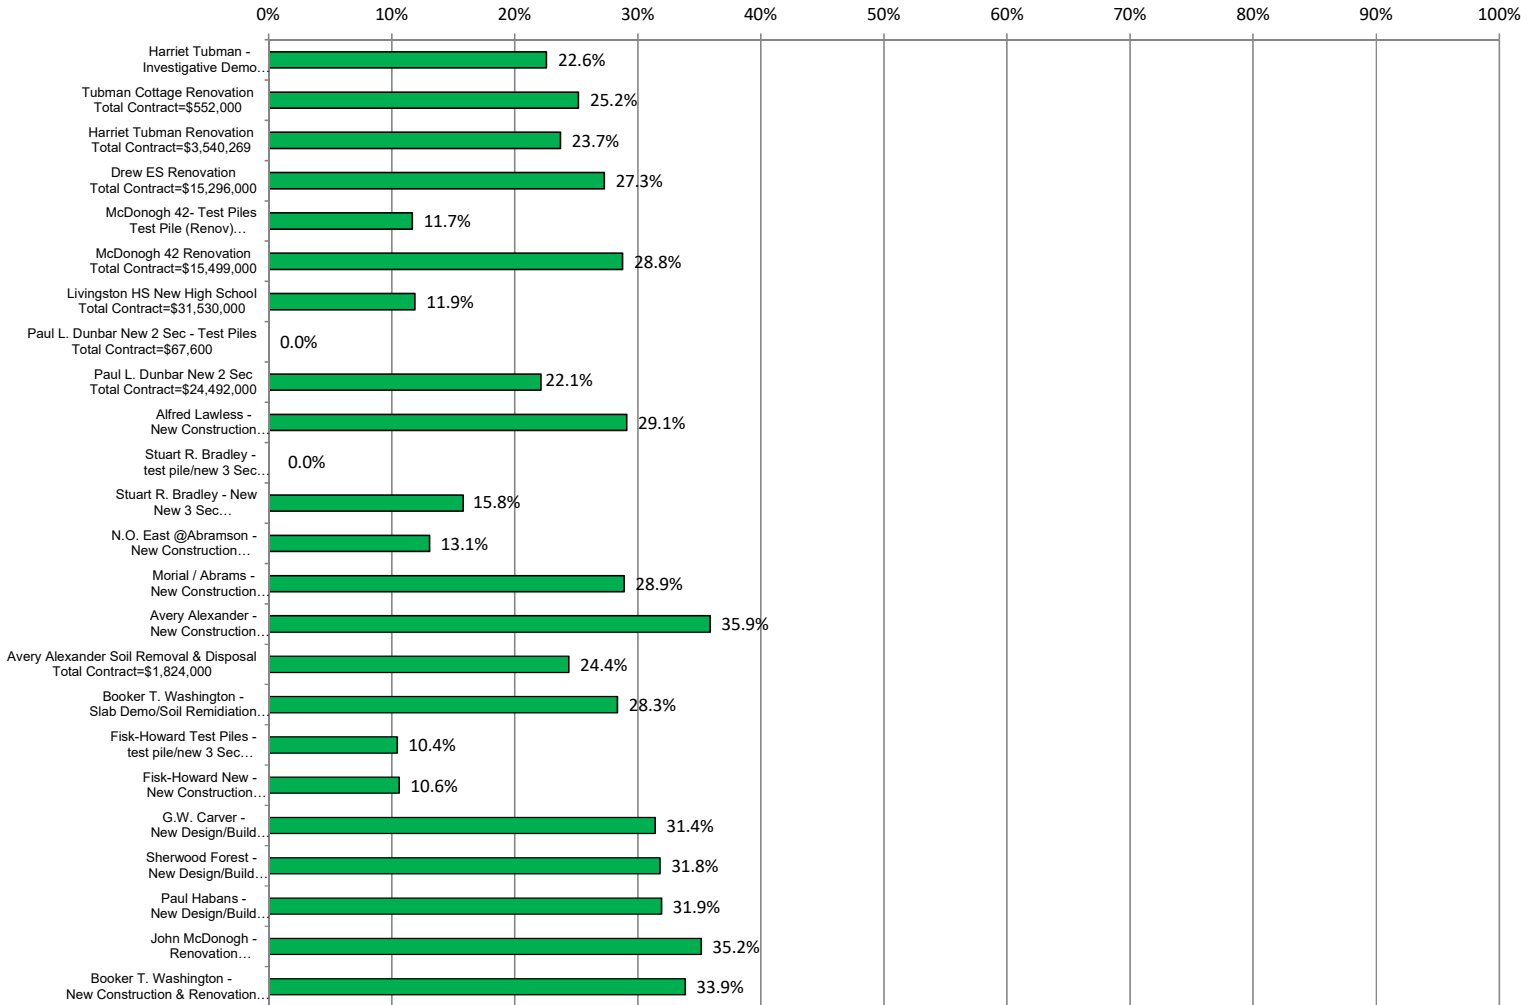

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

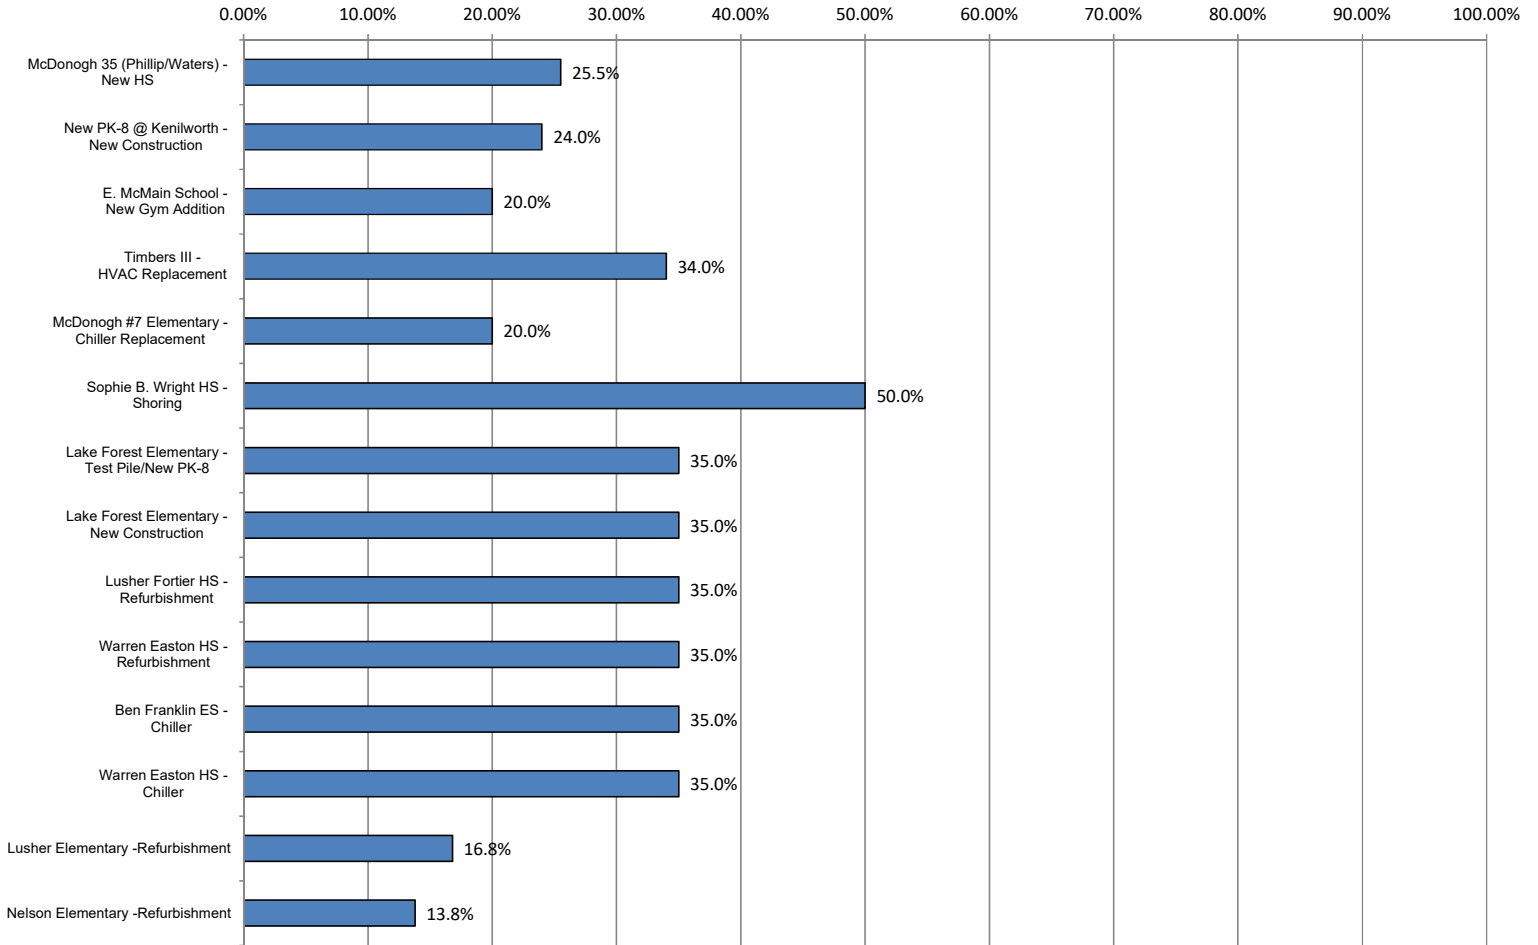

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Construction Masters

Construction Phase

- Contracts are signed
- Notice to Proceed November 28th



New Karr High School CMAR ^(RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - TBD

Design Phase

- 100% Construction documents were received November 20th
- GMP is being reviewed

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



New Orleans Charter Science and Mathematics High School ^(OPSB)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - TBD

Design Phase

- 90% Construction documents are being developed

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



John McDonogh High School Renovation CMAR ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- Interior painting has started in Main building
- Installation of doors has started
- Connections to exterior mechanical units is ongoing
- Plaster repairs and window painting continues on the exterior
- Gymnasium steel erection is ongoing

Contractual Substantial Completion – October 2018

Forecasted Substantial Completion – October 2018



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

Construction Phase

- Floor replacement continues on second floor
- MEP system installation ongoing
- Exterior plaster repair and painting continues
- New fence installation is ongoing

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates


Contractor – Core Construction

Construction Phase

- Erection of steel continues in Area E
- Roofing work is ongoing at the kitchen and performance wing
- CMU walls construction at the gymnasium continues
- Spray on fire proofing has started

Contractual Substantial Completion – January 2019

Forecasted Substantial Completion – January 2019

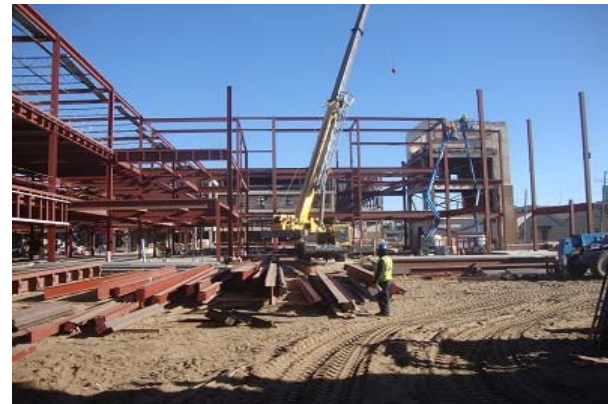

REFURBISHMENTS

Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

2300 Dumaine Street, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen at Banneker and addition of grease trap at Wheatley

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Commander Corp

Closeout Phase

- Substantial Completion October 2017
- GC working on warranty items

Contractual Substantial Completion – September 2017

Actual Substantial Completion – October 2017



Mary M. Bethune Elementary School Refurbishment ^(OPSB)

4040 Eagle Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects

Contractor – Construction Masters Inc.

Closeout Phase

- Substantial Complete October 26th
- GC working on warranty items

Contractual Substantial Completion – October 2017

Actual Substantial Completion – October 2017



Warren Easton School Courtyard Waterproofing ^(OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Repairs to courtyard waterproofing

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - Thigpen Construction Company

Construction Phase

- Substantial Complete November 24th
- GC working on warranty items

Contractual Substantial Completion – November 2017

Forecasted Substantial Completion – November 2017



Harney Elementary School Downspout and Gutter Repairs ^(RSD)

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of downspouts and gutters

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - TBD

Procurement Phase

- Project to be rebid



Lafayette Elementary School Refurbishment Phase 2 ^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to floor replacement

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- 1st Advertisement - January 24th
- 2nd Advertisement - January 31st
- 3rd Advertisement - February 7th
- Pre-Bid Conference - February 8th
- Bid Opening - February 28th



Laurel Elementary School Refurbishment ^(RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Dumpster pad work continues
- Parking lot work is ongoing
- HVAC work at IT room has started

Contractual Substantial Completion – November 2017

Forecasted Substantial Completion – December 2017



Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Blanchard Mechanical Contractors

Construction Phase

- Window work continues
- Duct work rough-in continues
- Electrical rough in continues
- Exterior cleaning and tuck point has started

Contractual Substantial Completion – June 2018

Forecasted Substantial Completion – June 2018



McDonogh #28 School Flooring Refurbishment Phase 2 ^(RSD)

2733 Esplanade Boulevard, New Orleans, LA 70114 District A Ward 7

Scope of work: Refurbishment of existing elementary school flooring

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement - January 3rd
- 2nd Advertisement - January 10th
- 3rd Advertisement - January 17th
- Pre-Bid Conference - January 18th
- Bid Opening - February 7th



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – HMS Architects

Contractor - TBD

Design Phase

- On hold by Owner



Eleanor McMain School Envelope Repairs ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Exterior stucco and window repairs

Funding Source – General Fund & Harrah's

Architect – Concordia, LLC

Contractor – TBD

Design Phase

- A&E is working on Schematic Design drawings



Harriet R. Tubman Elementary School Cottage Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing cottage to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Framing repairs continue
- Exterior siding removal is complete
- Repairs to roof structure has started

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Schaumburg Elementary School Roof Repairs ^(RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - TBD

Procurement Phase

- Bids are under advisement



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

6501 Berkley Drive, New Orleans, LA 70131 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - Industrial and Mechanical Contractors, Inc

Construction Phase

- Village - Control work to begin in December
- Village - Ductwork installation is ongoing
- Reed - Gate work is ongoing
- Reed - Window installation at Gymnasium has started
- Rosenwald - Contractor is installing the fan coils units
- Rosenwald - Public address system work is nearing completion

Contractual Substantial Completion – December 2017

Forecasted Substantial Completion – December 2017



DEMOLITIONS

Demolition of Modular Buildings at Abramson 3 ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – Ashley Savarino Unlimited Construction

Construction Phase

- Excavation of limestone continues
- Hauling of debris continues

Contractual Substantial Completion – February 2018

Forecasted Substantial Completion – February 2018



Demolition of Modular Buildings at Coghill ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – TBD

Procurement Phase

- Bids are under advisement



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment ^(RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment ^(RSD)	10/31/2017
8	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
9	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
10	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
11	Alfred Lawless Senior ^(RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
13	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
21	Augustine Elementary School Roof ^(RSD)	04/13/2012
22	Avery-Alexander Elementary School ^(RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
24	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
25	Bell JH Shoring ^(RSD)	06/28/2011
26	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
27	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
28	Bienville Elementary School Demolition ^(RSD)	05/04/2009
29	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
30	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
31	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
32	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
33	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
34	Charles J. Colton Elementary School ^(RSD)	05/23/2013
35	Charles R. Drew Elementary School ^(RSD)	04/17/2015
36	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
37	Cohen High School Health Clinic ^(RSD)	12/24/2008
38	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
39	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
40	Demolition of Modular Buildings at Abramson and Carver ^(RSD)	01/18/2017
41	Demolition of Modular Buildings at Livingston ^(RSD)	01/18/2017
42	Douglass High School Under Floor Utilities ^(RSD)	
43	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012

44	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
45	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
46	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
47	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
48	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011
49	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
50	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
51	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
52	Edna Karr High School - Assessment ^(OPSB)	
53	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
54	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
55	New Edward Hynes School ^(OPSB)	02/06/2012
56	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
57	Edward Livingston High School ^(RSD)	01/05/2015
58	Eleanor L. McMMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
59	Eleanor L. McMMain School Clinic ^(OPSB)	07/24/2013
60	Eleanor L. McMMain School Maintenance Upgrades ^(OPSB)	12/12/2016
61	Eleanor L. McMMain School Roof Replacement ^(OPSB)	05/13/2016
62	Ernest "Dutch" Morial Elementary ^(RSD)	03/17/2017
63	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
64	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
65	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
66	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
67	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
68	Francis W. Gregory Demolition ^(RSD)	12/21/2011
69	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
70	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
71	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
72	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
73	Gaudet Elementary School Refurbishment ^(RSD)	12/20/2016
74	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
75	George Mondy Elementary School Mothball ^(RSD)	
76	George Washington Carver School ^(RSD)	03/07/2016
77	George Washington Carver High School Demolition ^(RSD)	08/24/2011
78	Greater St. Stephens School ^(OPSB)	03/18/2013
79	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
80	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
81	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
82	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
83	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
84	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
85	Holy Cross Modular Relocation ^(RSD)	12/14/2010
86	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
87	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
88	James Derham Demolition ^(RSD)	02/23/2012
89	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010

90	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
91	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
92	JoEllen Smith Medical Center Demolition ^(OPSB)	
93	John Dibert Elementary School Roof ^(RSD)	08/20/2010
94	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
95	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
96	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
97	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
98	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
99	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
100	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
101	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
102	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
103	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
104	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
105	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
106	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
107	Lake Area Landry Demolition ^(RSD)	05/01/2008
108	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
109	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
110	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
111	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
112	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
113	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
114	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
115	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
116	Live Oak Elementary School Refurbishment ^(RSD)	01/06/2017
117	Live Oak Elementary School Roof ^(RSD)	08/04/2011
118	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
119	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
120	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
121	Lusher Elementary School Refurbishment ^(OPSB)	10/31/2016
122	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
123	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
124	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
125	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
126	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
127	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
128	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
129	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
130	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
131	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
132	McDonogh #7 High School Repairs ^(OPSB)	
133	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
134	McDonogh #28 School Refurbishment ^(RSD)	03/15/2016
135	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011

136	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
137	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
138	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
139	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
140	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
141	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
142	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
143	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
144	Modular Campuses Close Outs ^(RSD)	
145	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
146	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010
147	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
148	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
149	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
150	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
151	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
152	New Carter G. Woodson School ^(RSD)	09/14/2012
153	New Fannie C. Williams School ^(RSD)	08/24/2012
154	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
155	New L.B. Landry High School ^(RSD)	06/30/2010
156	New Lake Area High School ^(RSD)	12/28/2009
157	New Lawrence D. Crocker School ^(RSD)	04/29/2013
158	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
159	New Parkview School ^(RSD)	10/12/2012
160	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
161	New William Frantz Elementary School ^(RSD)	
162	New Orleans High School Signature Center Study ^(RSD)	
163	Oretha C. Haley Demo ^(RSD)	05/07/2012
164	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
165	Parkview Elementary School Demolition ^(RSD)	08/06/2009
166	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
167	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
168	Paul B. Habans Elementary School ^(RSD)	06/30/2016
169	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
170	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
171	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
172	Ray Abrams Elementary School ^(RSD)	03/17/2017
173	Rosenwald Elementary School Refurbishment ^(RSD)	04/07/2016
174	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
175	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
176	Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD)	02/15/2016
177	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
178	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
179	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
180	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015

181	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
182	Schaumburg Chillers ^(RSD)	11/14/2008
183	Schwarz Alternative Repairs ^(RSD)	07/14/2009
184	Schwarz Alternative Modulares Demolition ^(RSD)	04/02/2015
185	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
186	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
187	Sherwood Forest Elementary School ^(RSD)	06/30/2016
188	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
189	Sophie B. Wright School Renovation ^(RSD)	06/08/2016
190	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
191	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
192	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
193	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
194	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
195	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
196	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
197	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
198	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
199	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
200	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
201	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
202	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
203	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
204	Timbers HVAC ^(OPSB)	09/11/2013
205	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
206	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
207	Village de L'est Elementary School Refurbishment ^(RSD)	10/12/2016
208	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
209	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
210	Valena C. Jones Elementary School ^(RSD)	01/10/2013
211	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
212	Warren Easton High School Renovation ^(OPSB)	12/15/2015
213	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
214	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
215	New William J. Guste Elementary School ^(RSD)	10/06/2008
216	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
217	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
218	William Frantz Elementary School Roof ^(RSD)	08/12/2010
