


Superintendent's Report April, 2015



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District

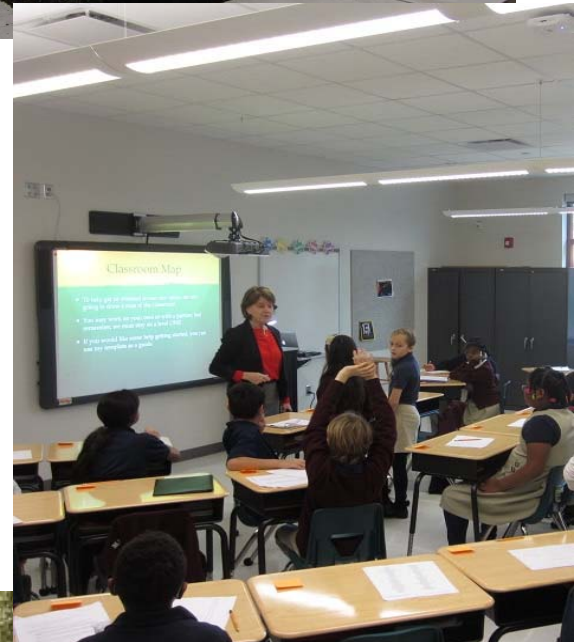

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	4
COMMUNITY MEETINGS	5
BID OPENINGS	6
DBE OVERVIEW MONTHLY SUMMARY	7
NEW & MAJOR RENOVATION	13
Ray Abrams Elementary School ^(RSD)	13
Avery Alexander Elementary School ^(RSD)	13
James Audubon School ^(OPSB)	13
Stuart R. Bradley School ^(RSD)	14
George Washington Carver School ^(RSD)	14
Charles R. Drew Elementary School ^(RSD)	14
Paul L. Dunbar School ^(RSD)	15
Benjamin Franklin Elementary School Renovation ^(OPSB)	15
Paul B. Habans School ^(RSD)	15
New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	16
Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	16
Alfred Lawless School ^(RSD)	16
John McDonogh High School Selective Demolition ^(RSD)	17
John McDonogh High School Renovation ^(RSD)	17
McDonogh #35 School (Phillip/Waters Site) ^(OPSB)	17
McDonogh #42 Elementary School ^(RSD)	18
Eleanor L. McMain School Gymnasium ^(OPSB)	18
Ernest "Dutch" Morial Elementary School ^(RSD)	18
Small New Orleans East High School at Abramson ^(RSD)	19
Sherwood Forest School ^(RSD)	19
Harriet R. Tubman Elementary School Renovation ^(RSD)	19
Booker T. Washington School Environmental Remediation ^(RSD)	20
Booker T. Washington School ^(RSD)	20
Sophie B. Wright School ^(RSD)	20

REFURBISHMENTS	21
Henry Allen Elementary School Refurbishment ^(RSD)	21
Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	21
Benjamin Banneker Elementary Kitchen School Refurbishment ^(RSD)	21
Bethune and Tureaud Elementary School Refurbishment ^(OPSB)	22
Agnes L. Bauduit Elementary School Refurbishment ^(RSD)	22
Walter L. Cohen High School Kitchen Refurbishment ^(RSD)	22
A. D. Crossman School Kitchen Refurbishment ^(RSD)	23
Frederick A. Douglass High School Science Lab ^(RSD)	23
Warren Easton School Refurbishment ^(OPSB)	23
Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	24
Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	24
William J. Fischer Elementary Refurbishment ^(RSD)	24
Fortier (Lusher) High School Refurbishment ^(OPSB)	25
Gaudet Elementary School Refurbishment ^(RSD)	25
Gentilly Terrace School Refurbishment ^(RSD)	25
Gentilly Terrace School Kitchen Refurbishment ^(RSD)	26
Samuel J. Green Elementary School Refurbishment ^(RSD)	26
Edgar P. Harney Elementary School Refurbishment ^(RSD)	26
Andrew Jackson School Refurbishment ^(RSD)	27
Andrew Jackson School Kitchen Refurbishment ^(RSD)	27
J. W. Johnson Elementary School Refurbishment ^(RSD)	27
Dr. Martin L. King Elementary School Kitchen Refurbishment ^(RSD)	28
Lafayette Elementary School Refurbishment ^(RSD)	28
Laurel Elementary School Refurbishment ^(RSD)	28
Live Oak Elementary School Refurbishment ^(RSD)	29
Lusher Elementary School Refurbishment ^(OPSB)	29
Thurgood Marshall Elementary School Refurbishment ^(RSD)	29
McDonogh #28 School Refurbishment ^(RSD)	30
McDonogh #28 School Kitchen Refurbishment ^(RSD)	30
McDonogh #32 School Refurbishment ^(RSD)	30
Nelson Elementary School Refurbishment ^(OPSB)	31
Sarah T. Reed School Refurbishment ^(RSD)	31
Sarah T. Reed School Kitchen Refurbishment ^(RSD)	31
Rosenwald Elementary School Refurbishment ^(RSD)	32
Henry C. Schaumburg Elementary School Refurbishment ^(RSD)	32
Village de l'Est Elementary School Refurbishment ^(RSD)	32
Albert Wicker School Kitchen Refurbishment ^(RSD)	33
Sylvanie F. Williams School Refurbishment ^(RSD)	33

OTHER PROJECTS	34
Eleanor L. McMain School Roof Replacement ^(OPSB)	34
Eleanor L. McMain School Maintenance Upgrades ^(OPSB)	34
Timbers III - Building Controls ^(OPSB)	34
Building Automation System Integration At Recovery School District Central And Remote Offices ^(RSD)	35
 MOTHBALL OR SAFE & SECURE OF SELECTED SCHOOLS	36
Andrew J. Bell Junior High School Shoring and Mothball ^(RSD)	36
Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School ^(RSD)	36
Demolition of Modular Buildings Gregory and Abramson ^(RSD)	35
JoEllen Smith Medical Center Demolition ^(OPSB)	37
Demolition of Modulars at Livingston ^(RSD)	37
 COMPLETED PROJECTS	38

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$582 million in open contracts for the capital program after issuing \$98 million in new contracts and \$412 thousand in change orders and amendments in April. In addition, the total change orders to date, \$5.4 million, account for approximately one percent (1.04%) of the total open construction contracts. RSD anticipates issuing approximately \$10 million in construction contracts/change orders, and \$1 million in professional service contracts/amendments in May.



The OPSB has \$210 million in open contracts for the capital program after issuing no new contracts and \$696 thousand in change orders and amendments in April. In addition, the total change orders to date, \$3.6 million, account for approximately two percent (2.00%) of the total open construction contracts. OPSB anticipates issuing approximately \$5.5 million in construction contracts/change orders and \$877 thousand in professional service contracts/amendments in May.

Community Meetings



Future Community Meetings

May 7, 2015

Avery Alexander School Community Meeting
5141 Franklin Avenue New Orleans, LA 70122

Bid Openings

Bids that were opened in March, 2015

April 1, 2015

- Frederick A. Douglass High School Science Classroom Renovation

The following projects are scheduled to bid in the next 60 days:

June 10, 2015

- McMain High School New Roof & Maintenance Upgrades

Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District



New & Renovations:

DBE Contractors secured subcontracts on 17 projects as of April 30, 2015. The DBE subcontracts value is \$48,968,584 of the \$252,253,077 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 33 projects as of April 30, 2015. The DBE subcontracts value is \$9,927,989 of the \$33,011,670 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of April 30, 2015. The DBE subcontracts value is \$35,025,777 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$ 394,402,304

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 12 projects as of April 30, 2015. The DBE subcontracts value is \$54,086,557 of the \$199,371,360 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of April 30, 2015. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$200,274,359

* DBE provisions were included in projects bid after June 30, 2012


Current RSD Program DBE Participation

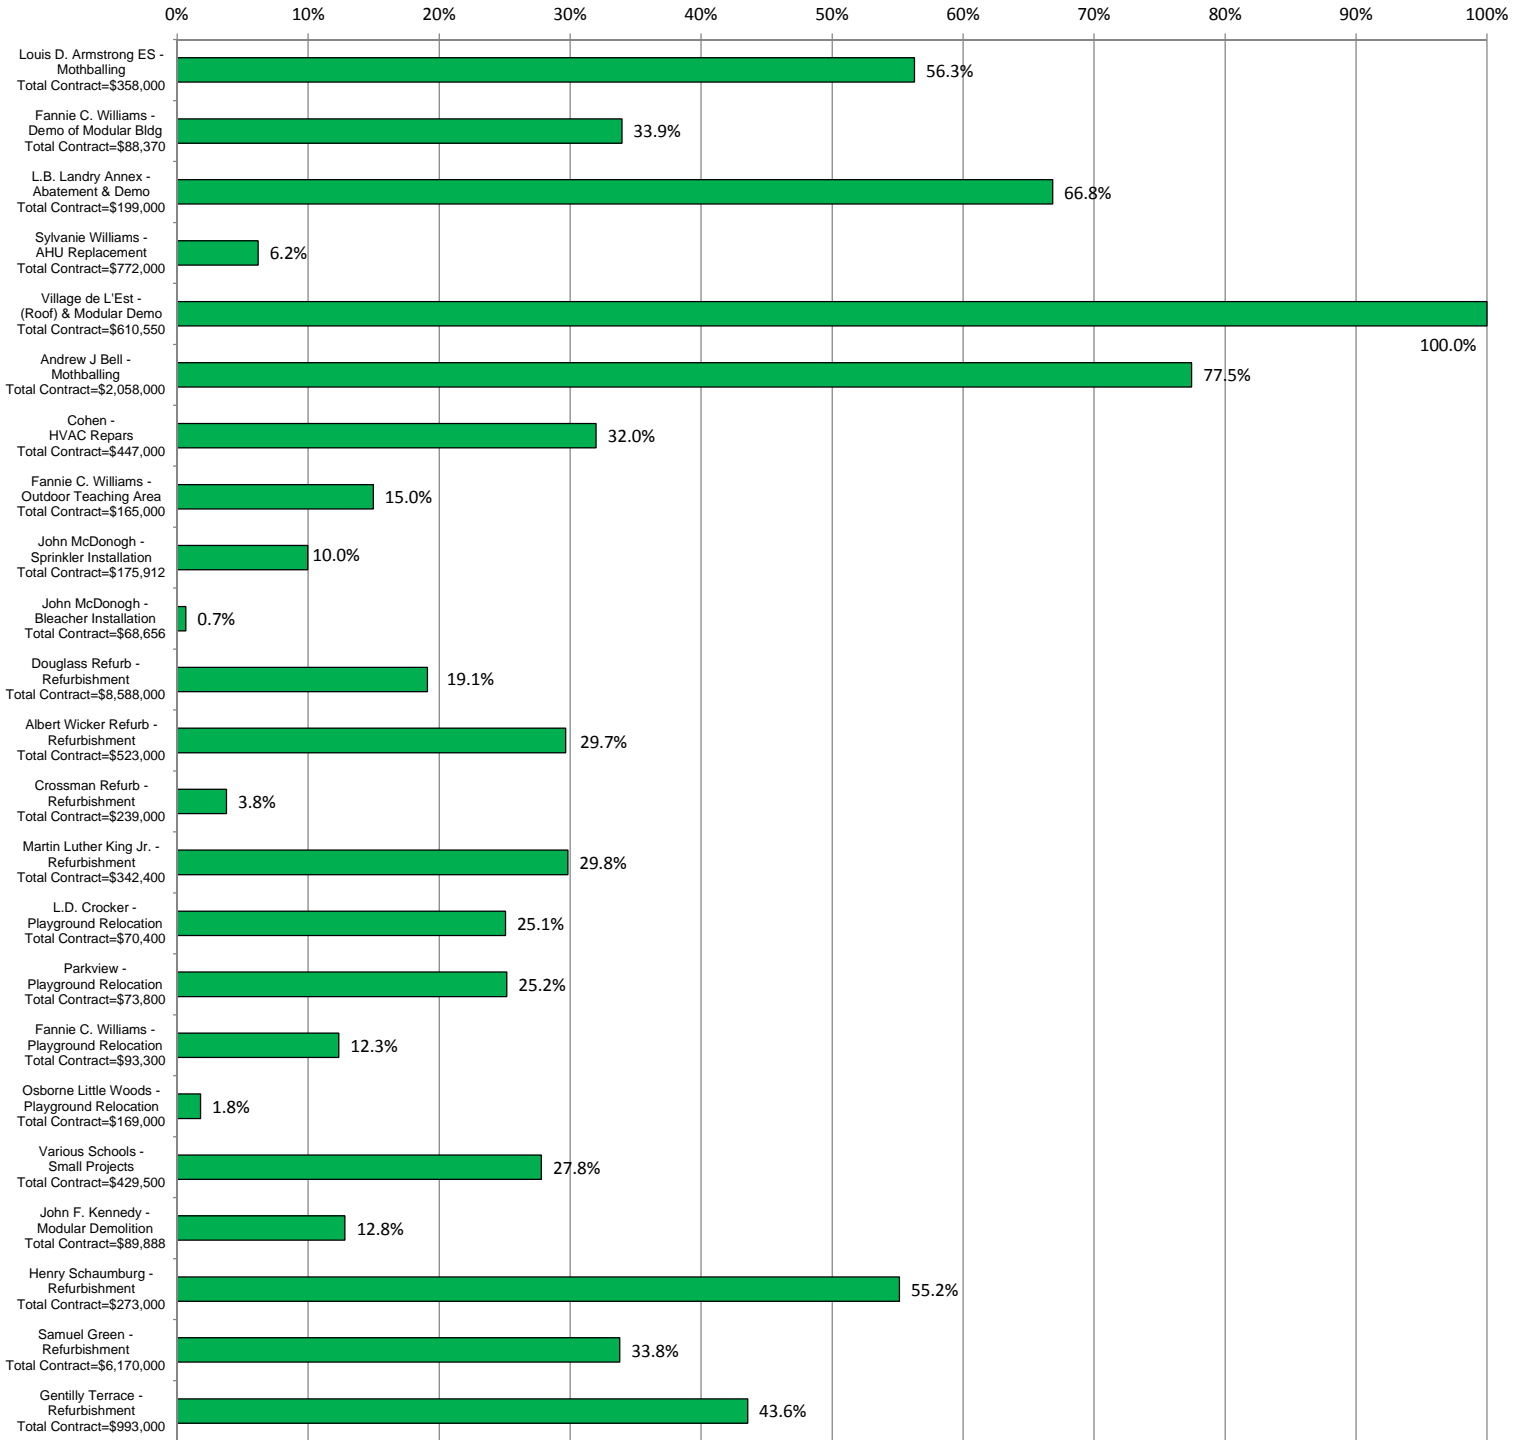

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current RSD Program DBE Participation


(Continued)

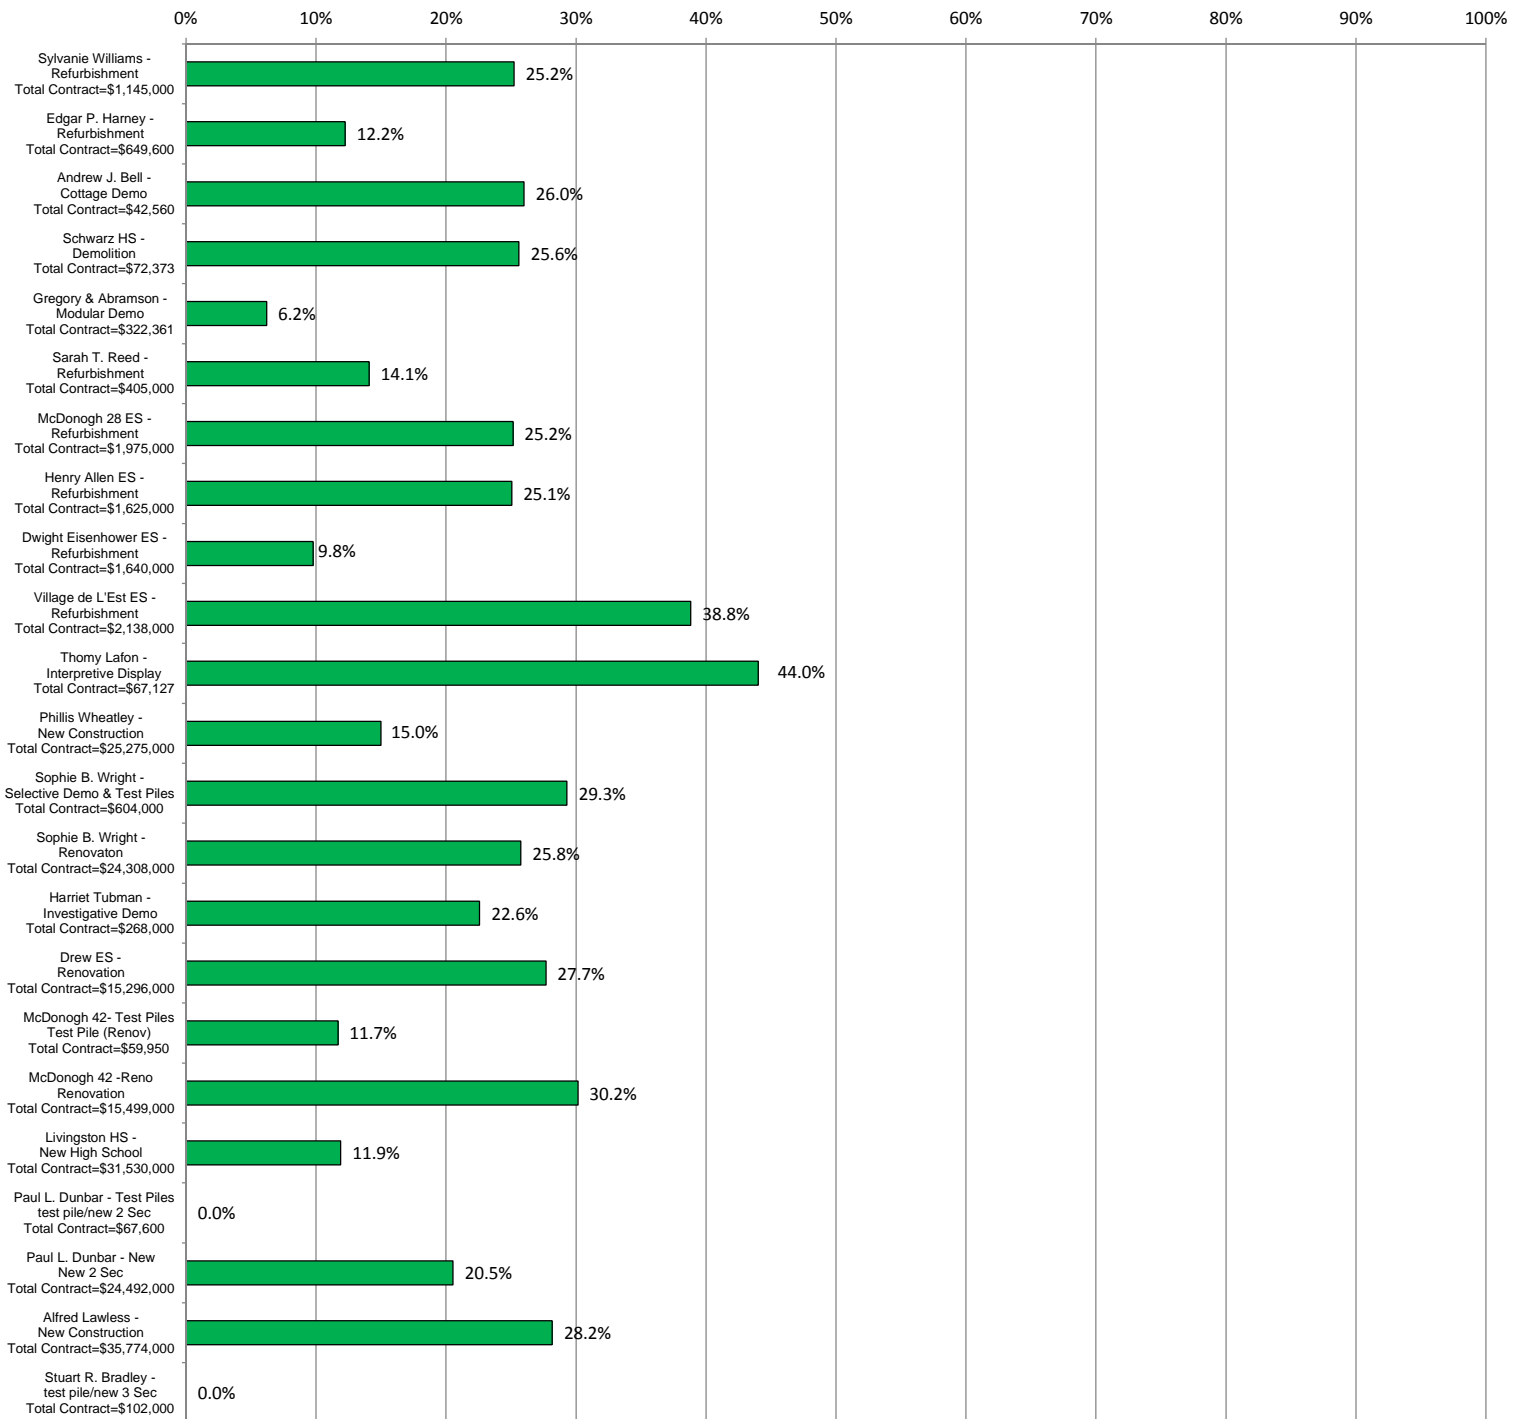

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

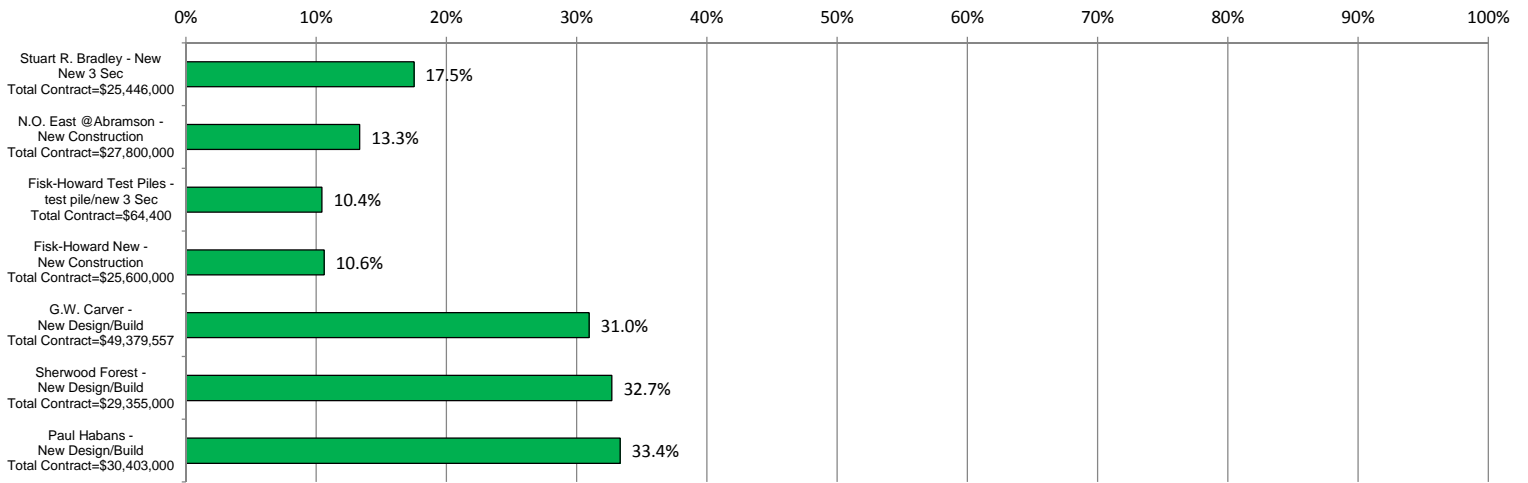

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

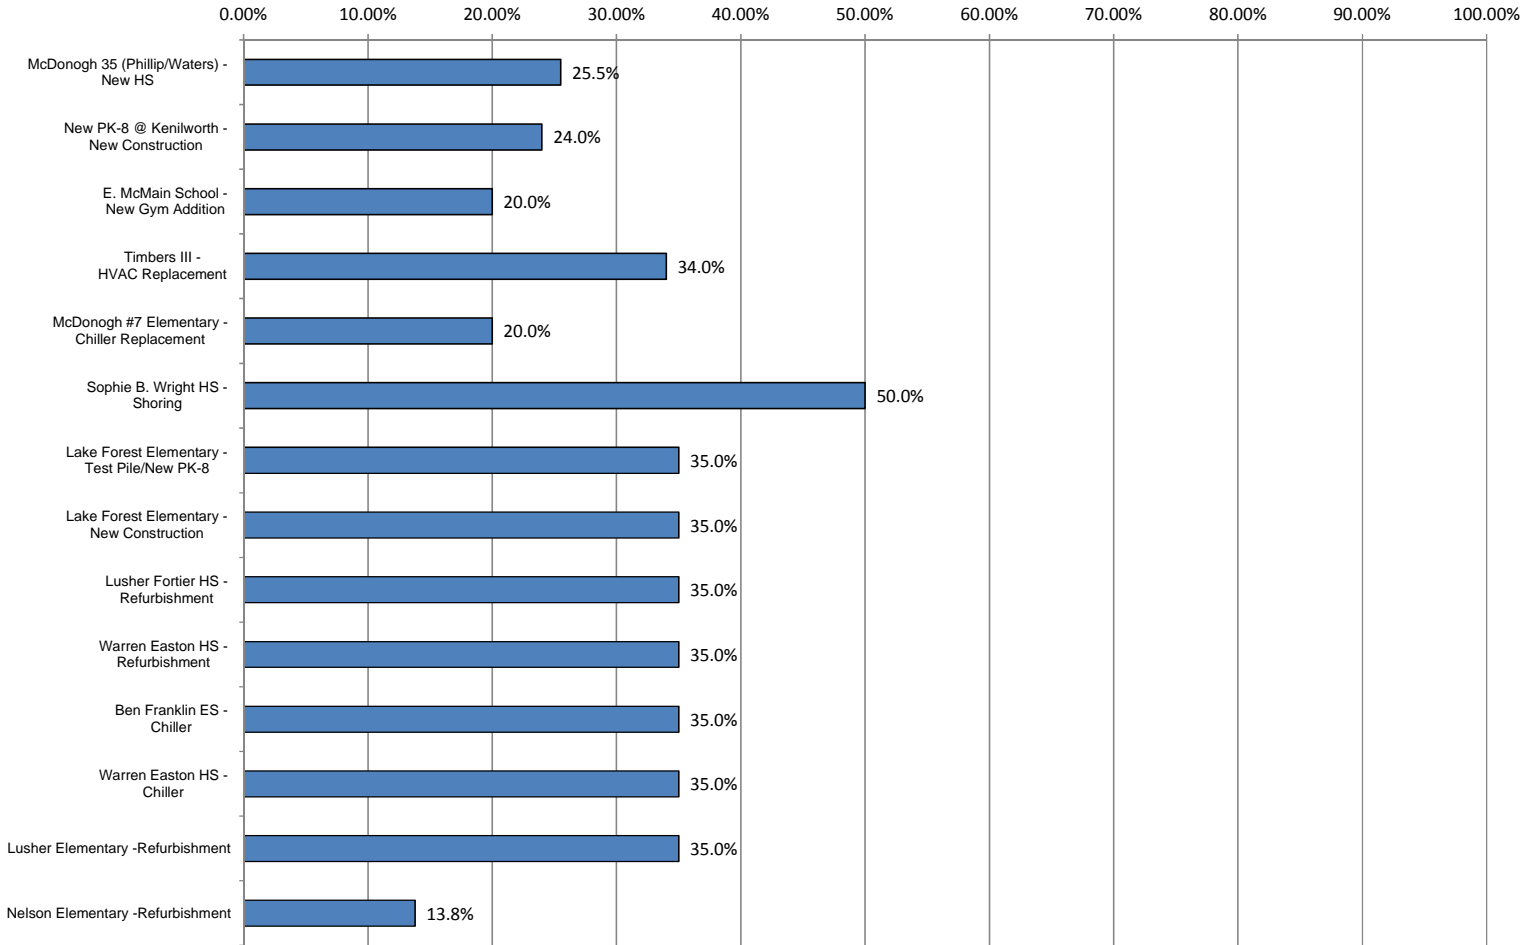

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School ^(RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Notice to Proceed - May 5th
- Contractor is mobilizing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



Avery Alexander Elementary School ^(RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- Notice to Proceed - May 15th

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



James Audubon School ^(OPSB)

428 Broadway Avenue, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation of existing elementary school and new addition

Funding Source – FEMA

Architect – Blitch/Knevel Architects

Contractor – FHP Tectonics Corporation

Construction Phase

- Reinstall of exterior curtain wall continues
- Installation of ceiling grid is ongoing
- Floor tile installation is ongoing in the existing building

Contractual Substantial Completion – September 2013

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – June 2015



Stuart R. Bradley School ^(RSD)

2401 Humanity Street, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Landis Construction Co.

Construction Phase

- Window installation is complete
- Painting of gypsum board is complete
- Installation of lighting and ceiling grid is nearly complete
- Punch list is anticipate beginning of June

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – August 2015



George Washington Carver School ^(RSD)

3059 Higgins Blvd., New Orleans, LA 70126 District E Ward 9

Scope of work: New High School, Design Build

Funding Source – FEMA

Contractor – Broadmoor LLC

Construction Phase

- Metal stud framing is ongoing
- MEP above ceilings has started
- Installation of door and window frames in ongoing
- Precast panels installation continues
- Roofing installation to start mid of May

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



Charles R. Drew Elementary School ^(RSD)

3819 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Blich / Knevel Architects, Inc.

Contractor – Core Construction

Close Out Phase

- Substantial Completion April 17th
- Punch list work continues

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015

School Ready for Occupancy – June 2015



Paul L. Dunbar School ^(RSD)

9330 Forshey Street, New Orleans, LA 70125 District A Ward 17

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor – McDonnell Group, LLC

Construction Phase

- Site work continues
- Flooring and ceiling grid installation continues
- Metal panel and cast stone installation is ongoing
- Window installation is ongoing
- Roof installation is ongoing

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – August 2015



Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- 100% Construction Documents were received April 17th
- The Owner is evaluating the refurbishment or replacement of the windows

Procurement Phase

- Anticipated 1st Advertisement – May 2015
- Anticipated Bid Opening – June 2015



Paul B. Habans School ^(RSD)

3501 Siene Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

Construction Phase

- Grade beam pours are ongoing
- Underground MEP work is ongoing
- Storm drainage is 90% complete
- Steel is being delivered to site

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)

8500 Curran Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Mathes Brierre Architects

Contractor – Woodrow Wilson Construction Company, Inc.

Construction Phase

- MEP work is ongoing
- Gypsum board and metal stud installation is 890% complete
- Installation of ceiling grid is ongoing
- Installation of windows continues

Contractual Substantial Completion – September 2014

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – July 2015



Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)

11110 Lake Forest Boulevard 70128 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Imre Hegedus & Associates Architects

Contractor – The McDonnel Group

Construction Phase

- MEP rough-in continues
- Installation of gypsum board is ongoing
- Window installation continues
- Installation of masonry brick is 67% complete
- Site work is 20% complete, pouring of parking beginning of May

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015

School Ready for Occupancy – August 2015



Alfred Lawless School ^(RSD)

5300 Law Street, New Orleans, LA 70117 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- Permanent power to be connected in May
- Roof installation is 98% complete
- Installation of windows 95% complete
- Exterior brick work is 95% complete
- Electric and HVAC main distribution continues

Contractual Substantial Completion – November 2015

Forecasted Substantial Completion – November 2015

School Ready for Occupancy – January 2016



John McDonogh High School Selective Demolition ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Zimmer-Eschette Services

Construction Phase

- Notice to Proceed - May 11th
- Contractor is mobilizing

Contractual Substantial Completion – October 2015

Forecasted Substantial Completion – October 2015



John McDonogh High School Renovation ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

Design Phase - SD

- Short list to be announced May 1st
- Interviews will be May 4th
- Successful Proposal will be announced June 2015



McDonogh #35 School (Phillip/Waters Site) ^(OPSB)

1200 Senate Street, New Orleans, LA 70122 District D Ward 7

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler, Thompson, Brown Architects

Contractor – Citadel Builders, LLC

Construction Phase

- Installation of MEP nearly complete
- Brick masonry and window installation is 95% complete
- Drywall installation is finished
- Metal panel installation is 95% complete

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – July 2015

School Ready for Occupancy – July 2015



McDonogh #42 Elementary School ^(RSD)

1651 North Tonti Street, New Orleans, LA 70119 District A Ward 7

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA, QSCB, NMTC, Insurance Proceeds

Architect – Eskew+Dumez+Ripple

Contractor – Core Construction

Construction Phase

- Contractor has started work on punch list
- State Fire Marshal has granted temporary occupancy
- Substantial completion is anticipated May 13th

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – May 2015

School Ready for Occupancy – June 2015



Eleanor L. McMain School Gymnasium ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source – FEMA

Architect – Jahncke & Burns Architects

Contractor – Gibbs Construction

Construction Phase

- Installation of roofing is ongoing

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – June 2015



Ernest "Dutch" Morial Elementary School ^(RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Notice to Proceed - May 5th
- Contractor is mobilizing

Contractual Substantial Completion – January 2017

Forecasted Substantial Completion – January 2017



Small New Orleans East High School at Abramson^(RSD)

5552 Read Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

Construction Phase

- Exterior masonry installation continues
- MEP distribution lines are being installed
- Door and window installation is ongoing
- Installation of interior finishes continues

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – October 2015

School Ready for Occupancy – November 2015



Sherwood Forest School^(RSD)

4801 Maid Marion Drive, New Orleans, LA 70128 District E Ward 9

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

Construction Phase

- Ground Breaking - April 29th
- Underground MEP work is ongoing
- Pouring of slab on grade to start beginning of May
- Delivery of structural steel has started

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



Harriet R. Tubman Elementary School Renovation^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- 50% Construction Documents were received April 9th
- Plan modifications will extend the completion of 100% Construction Documents until June

Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



Booker T. Washington School Environmental Remediation ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The remediation of the site

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – SEMS, Inc

Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - July 2015



Booker T. Washington School ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – TBD

Design Phase - SD

- Short list was announced April 23rd
- Interviews were held April 27th
- Successful Proposal will be announced June 2015



Sophie B. Wright High School Renovation ^(RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Renovation of existing school and gymnasium addition

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – Core Construction

Construction Phase

- Termite damage repairs are ongoing
- Removal and refurbishment of windows continues
- Grade beams are being poured
- 1st floor plumbing rough in continues

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



REFURBISHMENTS

Henry Allen Elementary School Refurbishment ^(RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Tuna Construction

Construction Phase

- Notice to Proceed - April 27th

Contractual Substantial Completion – February 2016

Forecasted Substantial Completion – February 2016



Henry Allen Elementary School Kitchen Refurbishment ^(RSD)

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - June 2015



Benjamin Banneker Elementary School Kitchen Refurbishment ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – January 2016
- Anticipated Bid Opening – March 2016



Agnes L. Bauduit Elementary School Refurbishment (RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor - TBD

Design Phase - CD

- Bid Documents are due June 2015
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – July 2015
- Anticipated Bid Opening – August 2015



Bethune and Tureaud Elementary School Refurbishment (OPSB)

4040 Eagle Street & 2021 Pauger Street, New Orleans, LA District A Ward 3 & District D Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - TBD

Design Phase - CD

- 50% Construction Documents were received April 17th
- 100% Construction Documents are due May 26th

Procurement Phase

- Anticipated 1st Advertisement – July 2015
- Anticipated Bid Opening – August 2015



Walter L. Cohen High School Kitchen Refurbishment (RSD)

3520 Dryades, New Orleans Street, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – January 2016
- Anticipated Bid Opening – March 2016



A. D. Crossman School Kitchen Refurbishment ^(RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Procurement Phase

- Bids were over the AFC
- Project to be re-bid as a single project



Frederick A. Douglass High School Science Lab ^(RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovations to science lab

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – One Construction

Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - May 2015

Warren Easton School ^(OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Refurbishment of existing high school, including but not limited to structure, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - Tuna Construction

Construction Phase

- Work is ongoing on the first floor and band room area
- Restroom renovations continues
- Ceiling work has been completed
- Sprinkler work at the Gymnasium will continue during summer break

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Harry Baker Smith Architects II, PLLC

Contractor - CDW Construction

Construction Phase

- Notice to Proceed - April 16th
- Contractor is mobilizing

Contractual Substantial Completion – January 2016

Forecasted Substantial Completion – January 2016



Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - June 2015



William J. Fischer Elementary School Refurbishment ^(RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



Fortier (Lusher) High School Refurbishment ^(OPSB)

5624 Freret Street, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation and repairs to the roof, masonry, plaster, windows, exterior doors, canopies, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Core Construction

Construction Phase

- Installation of gypsums ongoing
- Plaster repair is complete
- Painting of walls and doors continues
- Installation of new door and hardware continues
- Repairs to exterior brick work is ongoing

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



Gaudet Elementary School Refurbishment ^(RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 100% Construction Documents were received April 1st
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



Gentilly Terrace School Refurbishment ^(RSD)

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - One Construction

Construction Phase

- Construction is 93% complete
- Punch List work is proceeding
- The contract will be extended due to added kitchen scope

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



Gentilly Terrace School Kitchen Refurbishment ^(RSD)

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - One Construction

Procurement Phase

- Project will be canceled and the kitchen scope will be incorporated with school refurbishment



Samuel J. Green Elementary School Refurbishment ^(RSD)

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Hernandez Consulting, LLC

Construction Phase

- Installation of gypsum board at restrooms continues
- Rough in of fire suppression is nearly complete
- Electrical and plumbing renovations is ongoing
- Stripping and staining of wood floors continues
- Exterior brick repairs is ongoing
- Roof repairs continues

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015



Edgar P. Harney Elementary School Refurbishment ^(RSD)

2503 Willow Street, New Orleans, LA 70113 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Hamp's Construction, LLC

Procurement Phase

- Construction will resume at beginning of summer break

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – September 2015



Andrew Jackson School Refurbishment ^(RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- Kitchen scope was added to the refurbishment project
- Project to be rebid
- Anticipated 1st Advertisement – August 2015
- Anticipated Bid Opening – September 2015



Andrew Jackson School Kitchen Refurbishment ^(RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- Project will be canceled and the kitchen scope will be incorporated with school refurbishment



J. W. Johnson Elementary School Refurbishment ^(RSD)

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



Dr. Martin L. King Elementary School Kitchen Refurbishment ^(RSD)

1617 Caffin Avenue, New Orleans, LA 70117 District E Ward 9

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - June 2015



Lafayette Elementary School Refurbishment ^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – June 2015
- Anticipated Bid Opening – August 2015



Laurel Elementary School Refurbishment ^(RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – June 2015
- Anticipated Bid Opening – August 2015



Live Oak Elementary School Refurbishment ^(RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – July 2015
- Anticipated Bid Opening – August 2015



Lusher Elementary School Refurbishment ^(OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source – FEMA

Architect – Meyer Engineers, LTD.


Contractor - Hamps

Construction Phase

- Notice to Proceed - May 4th

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – November 2016

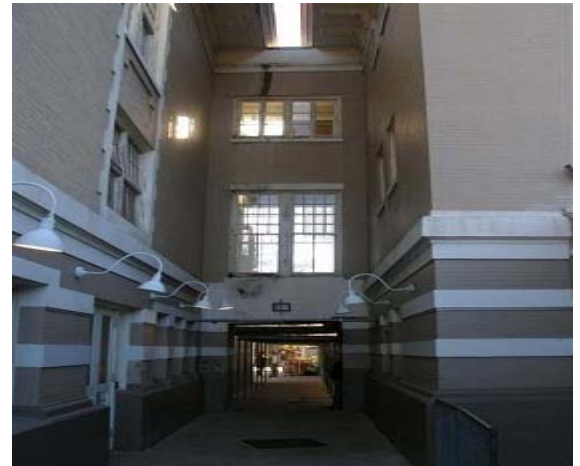

Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- 50% Construction Documents were received April 21st
- 100% Construction Documents are due June 9th

Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



McDonogh #28 School Refurbishment (RSD)

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – SCNZ Architects, LLC

Contractor - Tuna Construction

Construction Phase

- Notice to Proceed - May 10th

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



McDonogh #28 School Kitchen Refurbishment (RSD)

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Tuna Construction

Construction Phase

- Project will be canceled and the kitchen scope will be incorporated with school refurbishment



McDonogh #32 School Refurbishment (RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- Bid Documents are due August 18th
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



Nelson Elementary School Refurbishment ^(OPSB)

3121 St. Bernard Avenue, New Orleans, LA 70119 District D Ward 7

Scope of work: Renovation and repairs to the roof, masonry, windows, exterior doors, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – Harry Baker Smith Architects

Contractor - Blanchard Mechanical Contractor

Construction Phase

- Notice to Proceed - May 6th
- Contractor is mobilizing



Sarah T. Reed School Refurbishment ^(RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - Tuna Construction

Construction Phase

- Sidewalk work is complete
- Courtyard drainage work is complete
- Exterior improvements are ongoing

Contractual Substantial Completion – December 2015

Forecasted Substantial Completion – December 2015



Sarah T. Reed School Kitchen Refurbishment ^(RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - June 2015



Rosenwald Elementary School Refurbishment ^(RSD)

6501 Berkley Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - One Construction

Construction Phase

- Notice to Proceed - May 11th

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015



Henry C. Schaumburg Elementary School ^(RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc

Contractor - Hernandez Consulting, LLC

Construction Phase

- Dumpster pad work is complete
- Roof repairs are ongoing

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



Village de l'Est Elementary School Refurbishment ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CBDG

Architect – Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

Construction Phase

- Notice to Proceed - April 20th

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – April 2016



Albert Wicker School Kitchen Refurbishment ^(RSD)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – January 2016
- Anticipated Bid Opening – March 2016



Sylvanie F. Williams School Refurbishment ^(RSD)

3127 Martin Luther King Jr. Boulevard, New Orleans, LA 70125 District B Ward 2

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Hamps

Construction Phase

- Roof work is ongoing
- Plumbing work is 95% complete
- Stucco repairs continues

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015



OTHER PROJECTS

Eleanor L. McMain School Roof Replacement (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Roof replacement

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – TBD

Procurement Phase

- 1st Advertisement - May 6th
- 2nd Advertisement - May 13th
- 3rd Advertisement - May 20th
- Pre-Bid Conference - May 21st
- Bid Opening - June 10th

Eleanor L. McMain School Maintenance Upgrades (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work.

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – TBD

Design Phase - CD

- Owner has placed project on hold

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD

Timbers III - Building Controls (OPSB)

3520 General DeGaulle Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: Design and installation of new building controls

Funding Source – OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - PC

- Owner has placed project on hold

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



Building Automation System Integration At Recovery School

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview ES

Funding Source – FEMA

Architect – Moses Engineers

Contractor – Synergy Building Solutions, Inc.

Construction Phase

- The five Quick Start Schools are complete, the Energy Dash Board is being implemented
- Sylvania Williams Elementary School, Sarah T. Reed Elementary School, Fannie C. Williams Elementary School, Bienville Elementary School, Charles L. Colton Elementary School, William Frantz Elementary School, Parkview Elementary School, Osborne Elementary School, Carter G. Woodson Elementary School, Walter Cohen High School, Dolores T Aaron Elementary School, A. D. Crossman Elementary School, and Albert Wicker Elementary School are complete
- New integration work is ongoing at Benjamin Banneker Elementary School
- Integrations 75% complete at Lawrence D. Crocker Elementary School

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – May 2015



MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

Andrew J. Bell Junior High School Mothball ^(RSD)

1010 N. Galvez St., New Orleans, LA 70119 District D Ward 6

Scope of work: Design Services to assist in determining the condition of the facilities both interior and exterior, make recommendations to stabilize the facilities and provide drawings required to provide a water barrier, ventilation, and rudimentary fire detection and to secure openings and entryways. Construction Services to stabilize the facility according to the designer's drawings and specifications.

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – CDW Services, LLC

Mothballing of Closed Schools - Safe & Secure

- Mothballing of the Gymnasium, Administration Building, Annex, Building "C", Building "D", Chapel, & E.A.Christy Building

Close Out Phase

- Substantial Completion - April 30th
- Punch list anticipated to be completed by June 30th

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015



Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School ^(RSD)

1010 N. Galvez St. & 2327 St. Philip Street, New Orleans, LA 70119 District D Ward 6

Scope of work: Demolition of existing caretakers cottages

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – Concrete Busters

Close Out Phase

- Substantial Completion - April 1st
- Punch list anticipated to be completed by June 19th

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015



Demolition of Modular Buildings at Gregory and Abramson ^(RSD)

1700 Pratt Drive & 5552 Read Boulevard, New Orleans, LA District D Ward 7 & District E Ward 9

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Holly & Smith Architects

Contractor – Ashley Savarino Unlimited Construction

Construction Phase

- Gregory - Modular building are being removed
- Gregory - Site work has started
- Abramson - Final grading and Hydro seeding has started

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – June 2015



JoEllen Smith Medical Center Demolition (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

Design Phase - CD

- RFQ Package is being developed
- Anticipated 1st Advertisement of RFQ – April



Demolition of Modular Buildings at Livingston (RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – TBD

Procurement Phase

- Anticipated 1st Advertisement – November 2015
- Anticipated Bid Opening – December 2015



Comprehensive List - Completed Projects

- 1 Abrams | Morial | Abramson | Coghill Demolition ^(RSD)
- 2 A. D. Cross Elementary School Energy Conservation ^(RSD)
- 3 A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)
- 4 A. D. Crossman Elementary School Refurbishment ^(RSD)
- 5 A. P. Tureaud Elementary School Roof Repairs ^(RSD)
- 6 Agnes Bauduit Elementary School Boiler ^(RSD)
- 7 Albert Wicker Elementary School Refurbishment ^(RSD)
- 8 Albert Wicker Elementary School Roof Repairs ^(RSD)
- 9 Alfred Lawless Senior High Security Fencing ^(RSD)
- 10 Alice M. Harte Elementary School ^(OPSB)
- 11 Alice M. Harte Elementary School Demolition ^(OPSB)
- 12 Andrew J. Bell Junior High School Roof Replacement ^(RSD)
- 13 Andrew Jackson Elementary School Roof Repairs ^(RSD)
- 14 Andrew Jackson Elementary School Solar Panels ^(RSD)
- 15 Andrew H. Wilson Elementary School Cottage ^(RSD)
- 16 Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)
- 17 Augustine Elementary School Roof ^(RSD)
- 18 Avery-Alexander Elementary School Demolition ^(RSD)
- 19 Barbara C. Jordan Elementary School Demolition ^(RSD)
- 20 Bell JH Shoring ^(RSD)
- 21 Benjamin Banneker Elementary School Energy Conservation ^(RSD)
- 22 Benjamin Franklin Senior High School ^(OPSB)
- 23 Bienville Elementary School Demolition ^(RSD)
- 24 Booker T. Washington High School Partial Demolition ^(RSD)
- 25 Carter G. Woodson Middle School Demolition ^(RSD)
- 26 Central Services Warehouse Demolition ^(OPSB)
- 27 Charles J. Colton Elementary Selective Demolition ^(RSD)
- 28 Charles J. Colton Elementary School ^(RSD)
- 29 Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)
- 30 Cohen High School Health Clinic ^(RSD)
- 31 Douglass High School Under Floor Utilities ^(RSD)
- 32 Dr. Martin Luther King School Roof Repairs ^(RSD)
- 33 Dr. Martin Luther King Jr. School Renovation ^(RSD)
- 34 Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)
- 35 East Bank Swing Space for Audubon Charter School ^(OPSB)
- 36 Edgar P. Harney Elementary School Roof Repairs ^(RSD)
- 37 Edna Karr High School - Gymnasium Repair ^(OPSB)
- 38 Edna Karr High School - Assessment ^(OPSB)
- 39 Edward Livingston Middle School Demolition ^(RSD)
- 40 Edward Henry Phillips Junior High School Demolition ^(OPSB)
- 41 New Edward Hynes School ^(OPSB)
- 42 Edwards | Hardin | Lockett | Lawless Demolition ^(RSD)

- 43 Edward Livingston High School ^(RSD)
- 44 Eleanor L. McMain School Replacement of Existing Chillers ^(OPSB)
- 45 Eleanor L. McMain School Clinic ^(OPSB)
- 46 Ernest N. Morial Elementary Security Fencing ^(RSD)
- 47 Fannie C. Williams Elementary School Demolition ^(RSD)
- 48 Fisk-Howard Elementary School Demolition ^(RSD)
- 49 Florence J. Chester Elementary School Demolition ^(RSD)
- 50 Francis W. Gregory Demolition ^(RSD)
- 51 Frederick A. Douglass High Refurbishment ^(RSD)
- 52 Frederick A. Douglass High Switchgear ^(RSD)
- 53 Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)
- 54 George Mondy Elementary School Mothball ^(RSD)
- 55 George Washington Carver High School Demolition ^(RSD)
- 56 Greater St. Stephens School ^(OPSB)
- 57 Harriet R. Tubman Elementary School Selective Demolition ^(RSD)
- 58 Henry Allen Elementary School Roof ^(RSD)
- 59 Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)
- 60 Holy Cross Modular Relocation ^(RSD)
- 61 Israel M. Augustine Middle School Roof Replacement ^(RSD)
- 62 Israel M. Augustine Middle School Mothball ^(RSD)
- 63 James Derham Demolition ^(RSD)
- 64 James W. Johnson Elementary School Roof ^(RSD)
- 65 New Jean Batiste de Bienville School ^(RSD)
- 66 Jean Gordon Elementary School Demolition ^(RSD)
- 67 John Dibert Elementary School Roof ^(RSD)
- 68 John W. Hoffman Elementary School Demolition ^(RSD)
- 69 John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)
- 70 John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)
- 71 John F. Kennedy Modular Demolition ^(RSD)
- 72 John F. Kennedy High School Demolition ^(RSD)
- 73 John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)
- 74 John McDonogh Senior High School Roof ^(RSD)
- 75 John A. Shaw Elementary School Mothball ^(RSD)
- 76 Joseph S. Clark Senior High School Roof Repairs ^(RSD)
- 77 Joseph A. Craig Elementary Canopies ^(RSD)
- 78 Joseph A. Craig Elementary Elevator Installation ^(RSD)
- 79 Joseph A. Hardin Elementary Security Fencing ^(RSD)
- 80 Lafayette Elementary School Roof and Masonry ^(RSD)
- 81 Lake Area | Landry Demolition ^(RSD)
- 82 Langston Hughes Elementary School (Phase I) ^(RSD)
- 83 Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)
- 84 Langston Hughes Elementary School - Dumpster Pad ^(RSD)
- 85 Lawrence D. Crocker Elementary School Demolition ^(RSD)
- 86 L.B. Landry Annex Demolition ^(RSD)
- 87 Little Woods Elementary School Demolition ^(RSD)

- 88 Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)
- 89 Live Oak Elementary School Roof ^(RSD)
- 90 Live Oak Elementary School Exterior Door Replacement ^(RSD)
- 91 Lorraine Hansberry Elementary School Mothball ^(RSD)
- 92 Louis D. Armstrong Elementary School ^(RSD)
- 93 Mahalia Jackson Elementary School ^(OPSB)
- 94 Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)
- 95 Mahalia Jackson Elementary School Office Renovation ^(OPSB)
- 96 Martin Behrman Elementary School Roof ^(RSD)
- 97 Martin Luther King Jr. Elementary Canopy System ^(RSD)
- 98 Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)
- 99 Mary Church Terrell Elementary School Demolition ^(RSD)
- 100 Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)
- 101 Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)
- 102 McDonogh #7 High School Repairs ^(OPSB)
- 103 McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)
- 104 McDonogh #28 Elementary School Roof ^(RSD)
- 105 McDonogh #32 Roof Replacement ^(RSD)
- 106 McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)
- 107 McDonogh #42 Elementary School Roof ^(RSD)
- 108 McDonogh #42 Elementary School HVAC Replacement ^(RSD)
- 109 Mildred C. Osborne Elementary School Demolition ^(RSD)
- 110 Mildred C. Osborne Elementary School ^(RSD)
- 111 Modular Campuses Close Outs ^(RSD)
- 112 Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)
- 113 Modular Structures at Langston Hughes Elementary School ^(RSD)
- 114 Morris F.X. Jeff Elementary School Demolition ^(RSD)
- 115 Morris F.X. Jeff Elementary School Mothball ^(RSD)
- 116 Murray G. Henderson Elementary School Roof ^(RSD)
- 117 New Andrew H. Wilson Elementary School ^(RSD)
- 118 New Carter G. Woodson School ^(RSD)
- 119 New Fannie C. Williams School ^(RSD)
- 120 New Joseph A. Craig Elementary School ^(RSD)
- 121 New L.B. Landry High School ^(RSD)
- 122 New Lake Area High School ^(RSD)
- 123 New Lawrence D. Crocker School ^(RSD)
- 124 New Parkview School ^(RSD)
- 125 New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)
- 126 New William Frantz Elementary School ^(RSD)
- 127 New Orleans High School Signature Center Study ^(RSD)
- 128 Oretha C. Haley Demo ^(RSD)
- 129 Oretha C. Haley Elementary School Mothball ^(RSD)
- 130 Parkview Elementary School Demolition ^(RSD)
- 131 Paul L. Dunbar Elementary School Demolition ^(RSD)

- 132 Paul B. Habans Elementary School Roof Repairs ^(RSD)
- 133 Phillis Wheatley Elementary School Demolition ^(RSD)
- 134 Phillis Wheatley Elementary School ^(RSD)
- 135 Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)
- 136 Sarah T. Reed High School Bleachers ^(RSD)
- 137 Sarah T. Reed High School Auditorium Wall ^(RSD)
- 138 Seabrook Computer Training Center Demolition ^(OPSB)
- 139 Schaumburg Chillers ^(RSD)
- 140 Schwarz Alternative Repairs ^(RSD)
- 141 Schwarz Alternative Modulars Demolition ^(RSD)
- 142 Schwarz Modular Building Demolition ^(RSD)
- 143 Sherwood Forest Elementary School Demolition ^(RSD)
- 144 Sophie B. Wright School Selective Demolition ^(RSD)
- 145 Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)
- 146 Stuart R. Bradley Elementary School Demolition ^(RSD)
- 147 Sylvanie Williams Elementary School AHU Replacement ^(RSD)
- 148 Sylvanie Williams Elementary School Play Yard ^(RSD)
- 149 Sylvanie Williams Elementary School Roof Repairs ^(RSD)
- 150 Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)
- 151 Temporary Campus for McDonogh #11 Expropriation ^(OPSB)
- 152 Thomas A. Edison Elementary School Demolition ^(RSD)
- 153 Thomy Lafon Elementary School Demolition ^(RSD)
- 154 Thomy Lafon School Interpretative Display ^(RSD)
- 155 Timbers Park Office Building #1 & #2 Demolition ^(OPSB)
- 156 Timbers HVAC ^(OPSB)
- 157 Timbers III - IT Room Relocation ^(OPSB)
- 158 Village de L'est Elementary School Subsidence ^(RSD)
- 159 Village de L'est Elementary School Roof and Modular Demolition ^(RSD)
- 160 Vorice J. Waters Elementary School Demolition ^(RSD)
- 161 Valena C. Jones Elementary School ^(RSD)
- 162 Walter L. Cohen High School HVAC ^(RSD)
- 163 Warren Easton High School Window Replacement ^(OPSB)
- 164 West Bank Swing Space for Alice Harte Elementary School ^(OPSB)
- 165 New William J. Guste Elementary School ^(RSD)
- 166 William J. Guste Elementary School Science Lab ^(RSD)
- 167 William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)
- 168 William Frantz Elementary School ^(RSD)
- 169 William Frantz Elementary School Roof ^(RSD)
