


Superintendent's Report July, 2016



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District

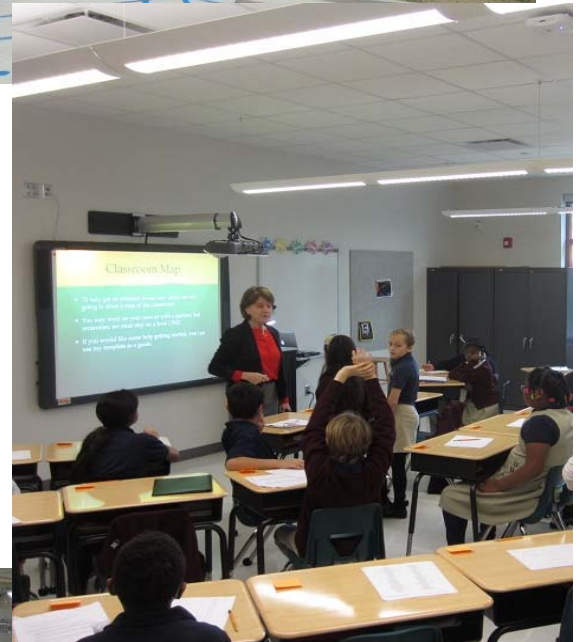

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	3
COMMUNITY MEETINGS	4
BID OPENINGS	5
DBE OVERVIEW MONTHLY SUMMARY	6
NEW & MAJOR RENOVATION	11
Ray Abrams Elementary School ^(RSD)	11
Avery Alexander Elementary School ^(RSD)	11
Benjamin Franklin Elementary School Renovation ^(OPSB)	11
JoEllen Smith Medical Center Demolition ^(OPSB)	12
New Karr High School, CMAR ^(OPSB)	12
John McDonogh High School Renovation CMAR ^(RSD)	12
Eleanor L. McMain School Gymnasium ^(OPSB)	13
Ernest "Dutch" Morial Elementary School ^(RSD)	13
Harriet R. Tubman Elementary School Renovation ^(RSD)	13
Booker T. Washington School CMAR ^(RSD)	14
Sophie B. Wright School ^(RSD)	14
REFURBISHMENTS	15
Benjamin Banneker Elementary Kitchen School Refurbishment ^(RSD)	15
Agnes L. Bauduit Elementary School Refurbishment ^(RSD)	15
A. D. Crossman School Kitchen Refurbishment ^(RSD)	15
Frederick A. Douglass High School Science Lab ^(RSD)	16
William J. Fischer Elementary Refurbishment ^(RSD)	16
Gaudet Elementary School Refurbishment ^(RSD)	16
Andrew Jackson School Refurbishment ^(RSD)	17
J. W. Johnson Elementary School Refurbishment ^(RSD)	17
Lafayette Elementary School Refurbishment ^(RSD)	17
Laurel Elementary School Refurbishment ^(RSD)	18
Live Oak Elementary School Refurbishment ^(RSD)	18
Lusher Elementary School Refurbishment ^(OPSB)	18
Thurgood Marshall Elementary School Refurbishment ^(RSD)	19
McDonogh #32 School Refurbishment ^(RSD)	19
Village de l'Est Elementary School Refurbishment ^(RSD)	19

OTHER PROJECTS	20
Eleanor L. McMain School Maintenance Upgrades ^(OPSB)	20
Building Automation System Integration At Recovery School District Central And Remote Offices ^(RSD)	20
DEMOLITIONS	21
Demolition of Modulares at Abramson and Carver ^(RSD)	21
Demolition of Modulares at Livingston ^(RSD)	21
COMPLETED PROJECTS	22

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$554 million in open contracts for the capital program after issuing \$558 thousand in new contracts, change orders and amendments in July. In addition, the total change orders to date, \$5.7 million, account for one percent (1.19%) of the total open construction contracts. RSD anticipates issuing approximately \$6.9 million in construction contracts/change orders, and \$514 thousand in professional service contracts/amendments in August.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 thousand in new contracts, change orders and amendments in July. In addition, the total change orders to date, \$8.1 million, account for approximately four percent (4.13%) of the total open construction contracts. OPSB anticipates issuing approximately \$343 thousand in construction contracts/change orders and -\$214 thousand in professional service contracts and amendments in August.

Community Meetings



Future Community Meetings

August 31, 2016

George Washington Carver High School Ribbon Cutting
3059 Higgins Boulevard New Orleans, LA 70126

September 16, 2016

Alfred Lawless High School Ribbon Cutting
5301 North Rocheblave Street New Orleans, LA 70117

September 30, 2016

Sherwood Forest Elementary School Ribbon Cutting
4801 Maid Marion Drive New Orleans, LA 70128

October 4, 2016

Sophie B. Wright High School Ribbon Cutting
1426 Napoleon Avenue New Orleans, LA 70115

October 18, 2016

Paul B. Habans Elementary School Ribbon Cutting
3501 Seine Drive New Orleans, LA 70114

Bid Openings

The following projects are scheduled to bid in the next 60 days

August 3, 2016

- Green School Refurbishment Phase II

Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District



New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of July 31, 2016. The DBE subcontracts value is \$79,963,9108 of the \$362,548,187 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 47 projects as of July 31, 2016. The DBE subcontracts value is \$19,665,249 of the \$64,799,535 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of July 31, 2016. The DBE subcontracts value is \$33,7454,5327 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$ 536,485,279

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of July 31, 2016. The DBE subcontracts value is \$54,086,557 of the \$199,371,360 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of July 31, 2016. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$200,274,359


* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

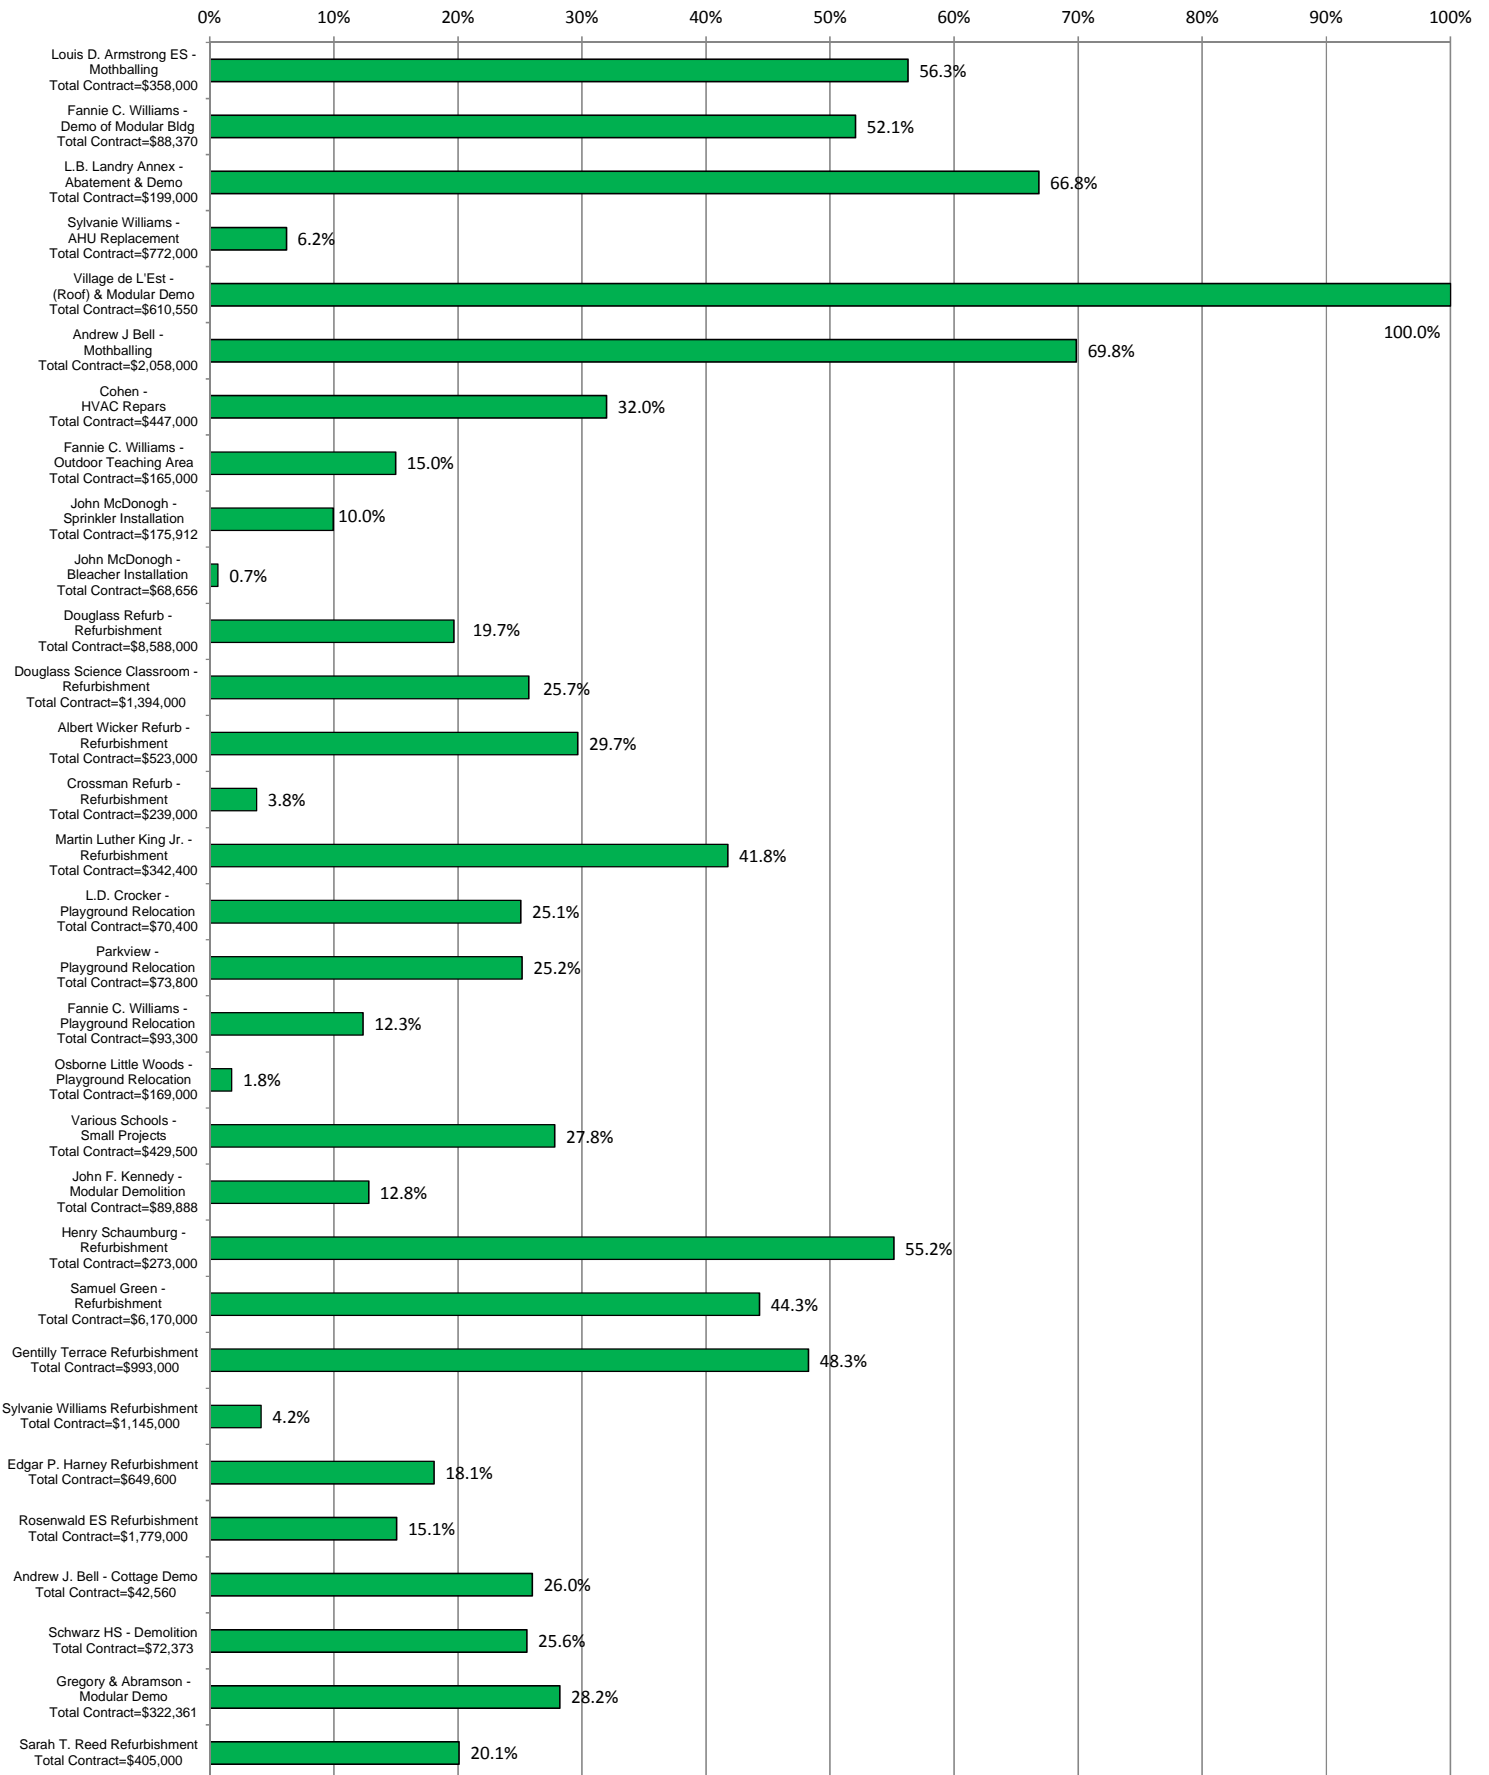

Current RSD Program DBE Participation


(Continued)

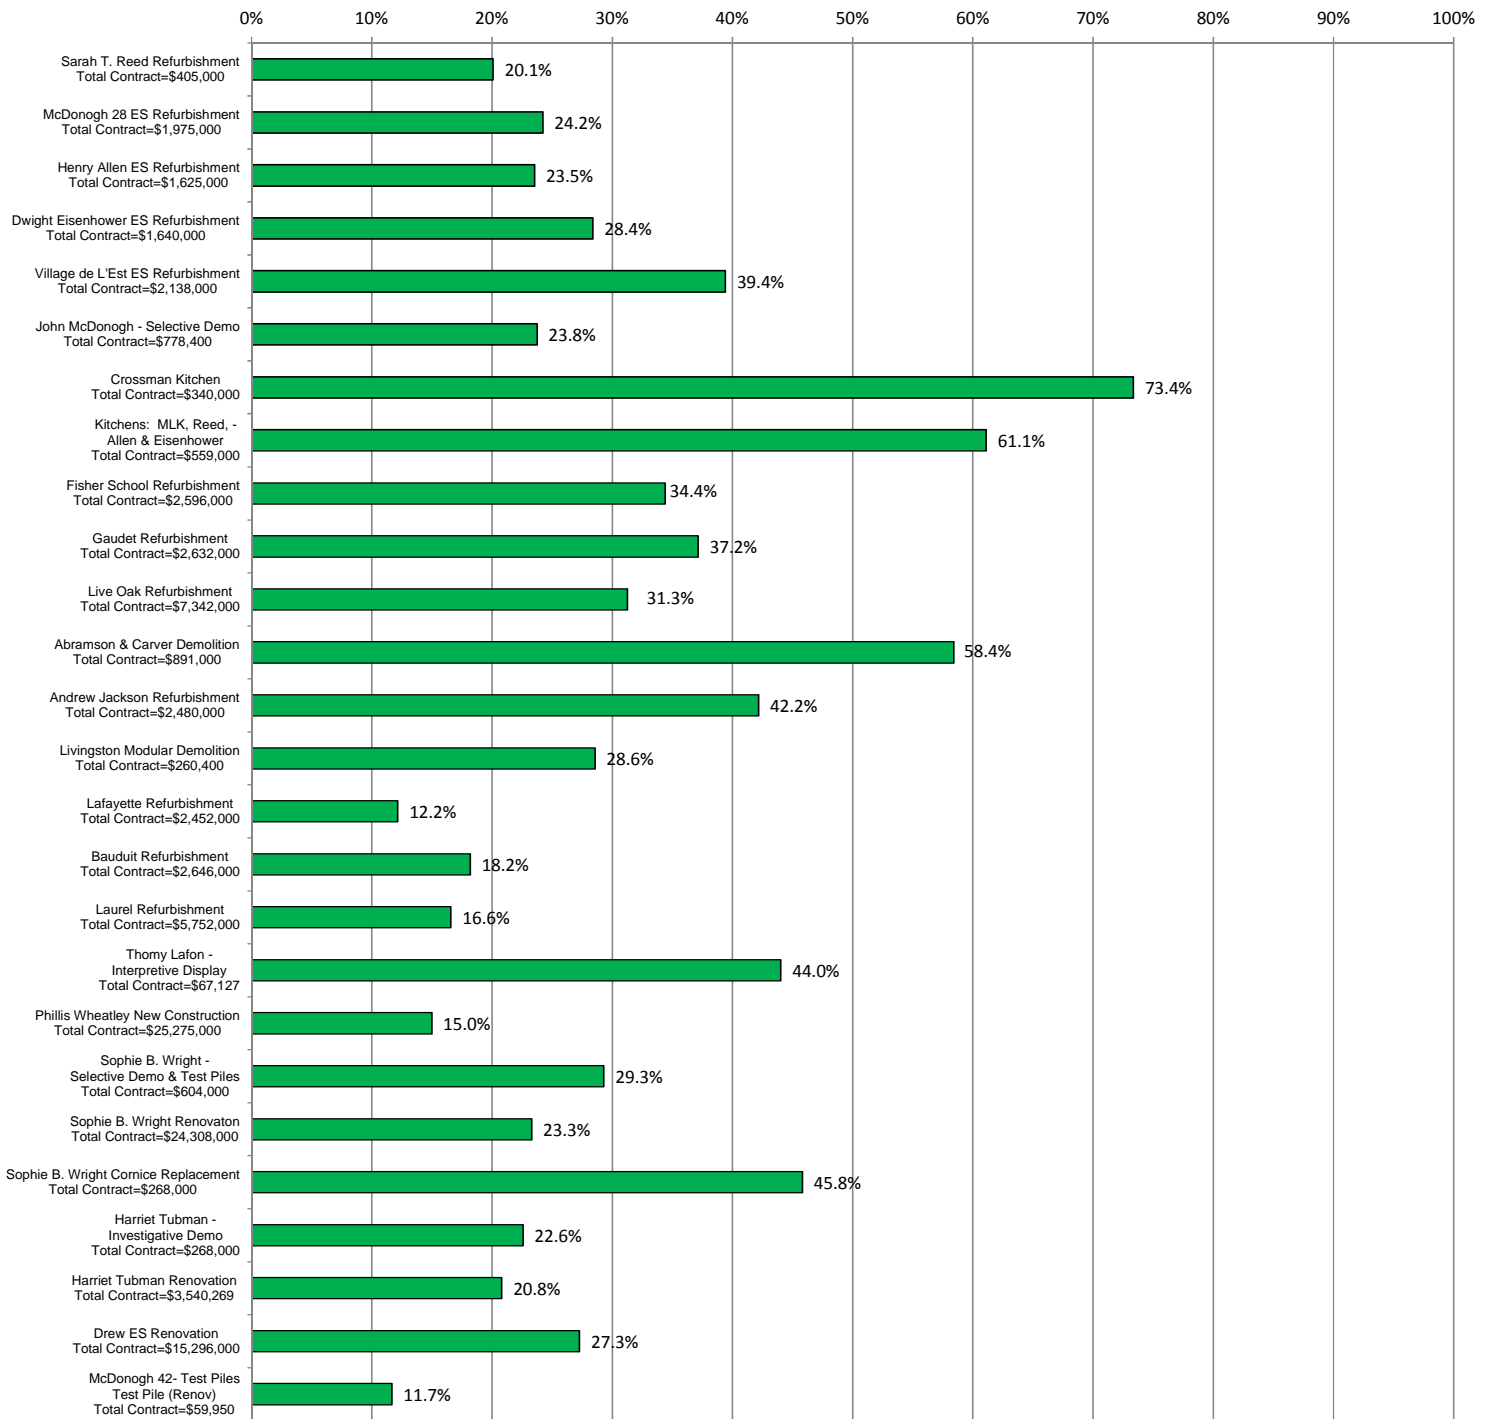

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

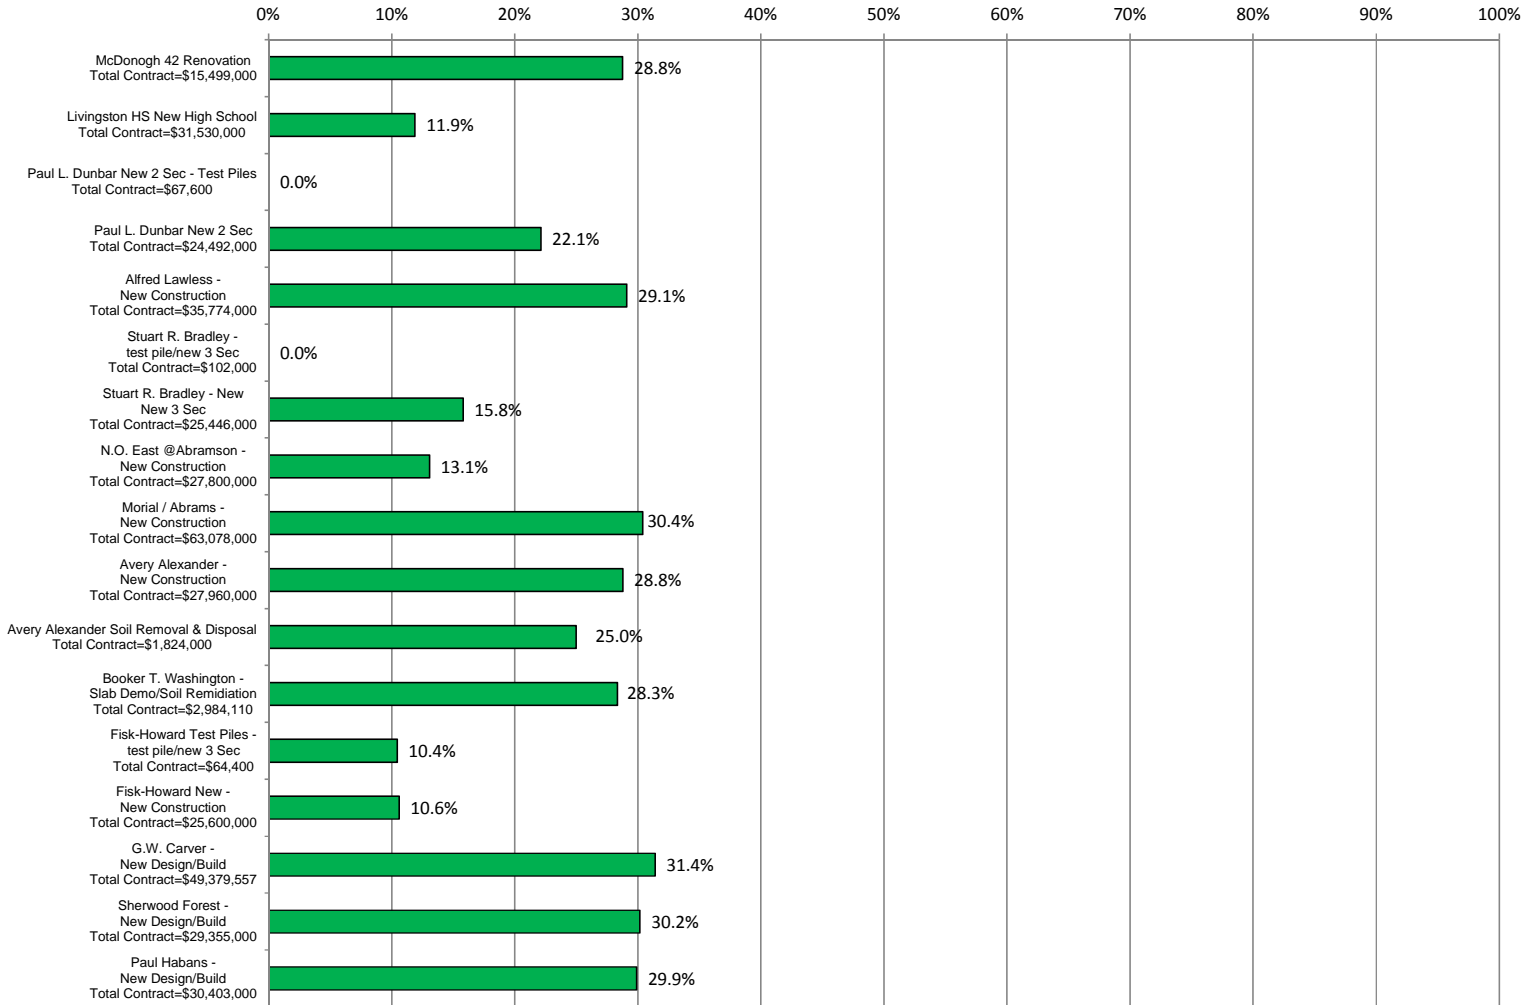

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

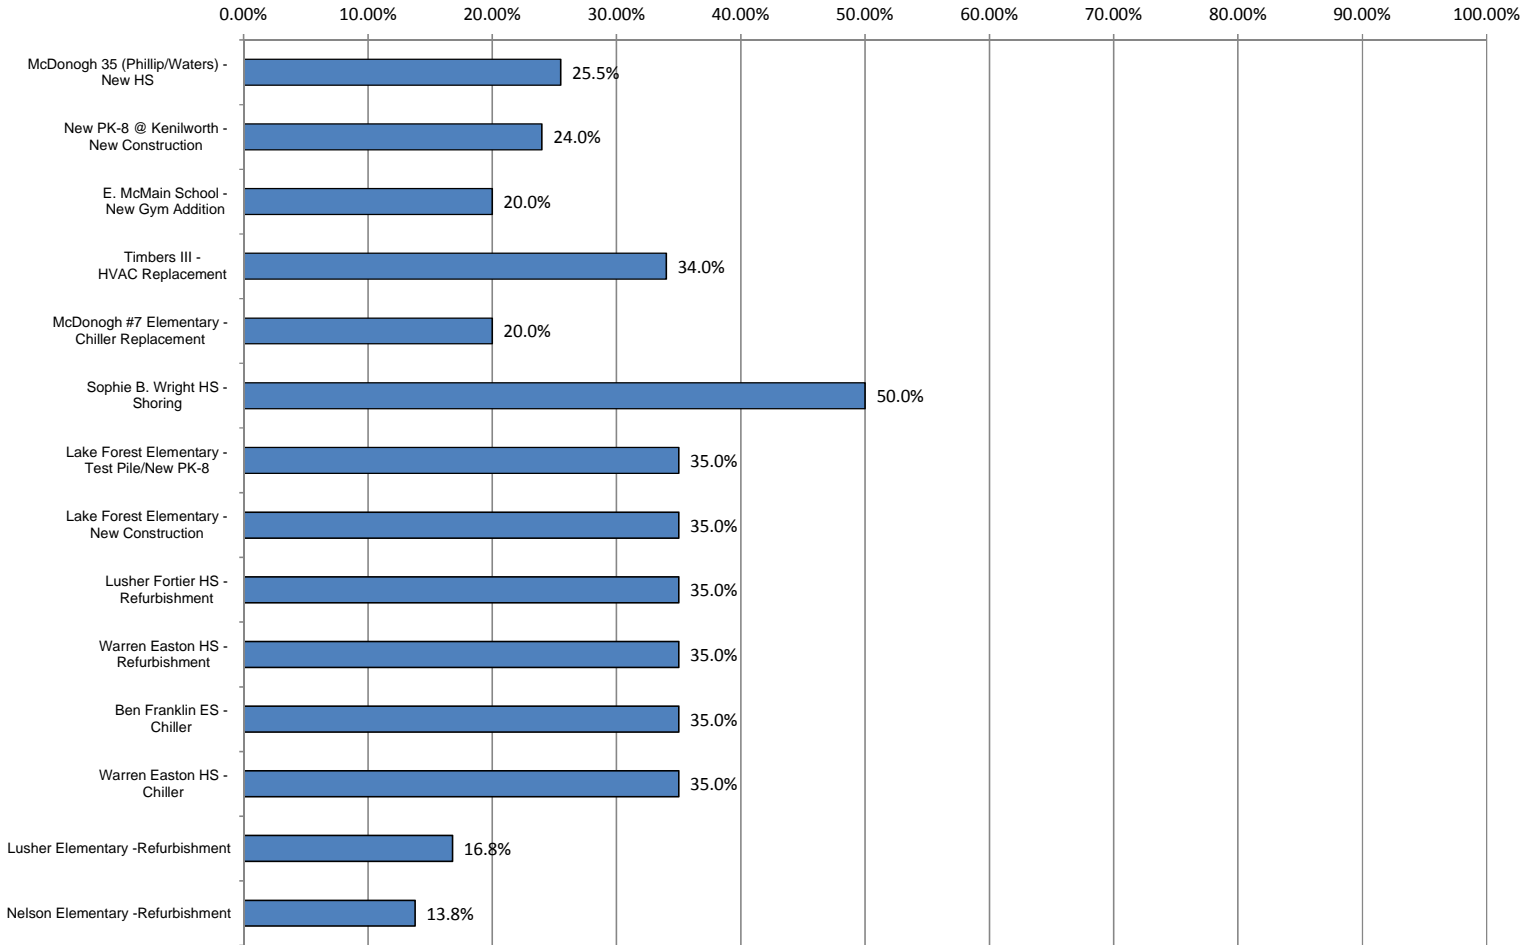

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School ^(RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Window installation continues
- Elevator installation is ongoing
- Installation of ceiling grid has started
- Interior gypsum board finishes are underway
- Site paving and grading continues

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



Avery Alexander Elementary School ^(RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- Installation of brick continues
- Stud wall framing and interior gypsum board has started
- Overhead mechanical rough is ongoing
- Window installation to start in August
- Permanent power is anticipated in September

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- Owner is review scope with A&E



JoEllen Smith Medical Center Demolition (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – Core Construction

Demolition Phase

- Demolition is 20% complete
- Remediation work is moving forward
- Buildings should be down to just slab in October

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – November 2016



New Karr High School CMAR (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – TBD

Contractor - TBD

Procurement Phase

- Attorney General to determine if OPSB is Eligible for CMAR Procurement

Contractual Substantial Completion – November 2018

Forecasted Substantial Completion – November 2018



John McDonogh High School Renovation CMAR (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Design Phase

- Work on Construction Documents continues
- Test pile program to start in September
- Bids for the Gymnasium Demolition were received and are being reviewed



Eleanor L. McMain School Gymnasium ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source – FEMA

Architect – Jahncke & Burns Architects

Contractor – Gibbs Construction

Construction Phase

- Contractor is working on the punch list
- Final Commissioning is ongoing
- Substantial Completion June 14th

Contractual Substantial Completion – June 2016

Forecasted Substantial Completion – June 2016



Ernest "Dutch" Morial Elementary School ^(RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Window installation is ongoing
- Gypsum board tape and float is ongoing
- Terrazzo installation has started
- Elevator installation has started

Contractual Substantial Completion – January 2017

Forecasted Substantial Completion – February 2017



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

Construction Phase

- Selective demolition is finishing
- Cafetorium foundation work is ongoing
- Window refurbishment has started

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Test pile installation is complete, pile load test & report due in September
- Submittal package sent to FEMA/Historical Preservation



Sophie B. Wright High School Renovation ^(RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Renovation of existing school and gymnasium addition

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – Core Construction

Construction Phase

- Punch list work continues
- Waterproofing of the cornice is complete
- Substantial Completion July 8th
- First day of school is August 15th
- Installation of replacement cornice is underway

Contractual Substantial Completion – July 2016

Forecasted Substantial Completion – July 2016



REFURBISHMENTS

Benjamin Banneker Elementary School Kitchen Refurbishment ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- A&E is revising the bid documents

Procurement Phase

- Anticipated 1st Advertisement – August 2016
- Anticipated Bid Opening – September 2016



Agnes L. Bauduit Elementary School Refurbishment ^(RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor – One Construction

Construction Phase

- Window stripping and repairs are ongoing
- Quarry tile installation has started
- Exterior pressure washing of the building is ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



A. D. Crossman School Kitchen Refurbishment ^(RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - CDW Services

Construction Phase

- Dumpster pad is formed and will be poured soon
- New grease trap and piping has been installed

Contractual Substantial Completion – July 2016

Forecasted Substantial Completion – July 2016



Frederick A. Douglass High School Science Lab ^(RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovations to science lab

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – One Construction

Construction Phase

- Substantial Completion July 5th
- Punch list work is nearly complete

Contractual Substantial Completion – July 2016

Forecasted Substantial Completion – July 2016



William J. Fischer Elementary School Refurbishment ^(RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Perez

Construction Phase

- HVAC repairs are 40% complete
- Sprinkler installation is 50% complete
- Window repairs are being coordinated with the school

Contractual Substantial Completion – February 2017

Forecasted Substantial Completion – February 2017



Gaudet Elementary School Refurbishment ^(RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - One Construction

Construction Phase

- Roofing work is 50% complete
- Electrical panel installation is complete, lighting work has started
- HVAC and doors to arrive onsite beginning of August
- Restroom repairs have started

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – November 2016



Andrew Jackson School Refurbishment ^(RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Construction Phase

- Windows were stripped, repaired and reset
- Sprinkler drops are being installed in restrooms
- Work continues after school hours and on weekends

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



J. W. Johnson Elementary School Refurbishment ^(RSD)

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Owner has placed this project on hold

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



Lafayette Elementary School Refurbishment ^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Tuna Construction

Construction Phase

- Exterior demolition has started for new dumpster pad
- Window work at the stairwells has started
- Installation of plumbing at the dumpster will begin shortly

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



Laurel Elementary School Refurbishment ^(RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Notice to Proceed August 31

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017



Live Oak Elementary School Refurbishment ^(RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- Restroom repairs are complete
- VCT installation is almost complete in the dining area
- Repairs on the existing AHU's continues
- Work continues after school hours and on weekends

Contractual Substantial Completion – July 2017

Forecasted Substantial Completion – July 2017



Lusher Elementary School Refurbishment ^(OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source – FEMA

Architect – Meyer Engineers, LTD.

Contractor - Dynamic

Construction Phase

- Interior finishes are ongoing
- Work in the elevator area is being preformed after school hours

Contractual Substantial Completion – August 2016

Forecasted Substantial Completion – September 2016



Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- Securing FEMA approval on elevator location
- A&E is incorporating additional scope

Procurement Phase

- Anticipated 1st Advertisement – September 2016
- Anticipated Bid Opening – November 2016



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- MEP drawings and Specifications are being reviewed

Procurement Phase

- Anticipated 1st Advertisement – September 2016
- Anticipated Bid Opening – November 2016



Village de l'Est Elementary School Refurbishment ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

Construction Phase

- HVAC controls and testing and balance are not complete
- Punch list work has started
- Substantial Completion is anticipated in August

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – August 2016



OTHER PROJECTS

Eleanor L. McMain School Maintenance Upgrades ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work.

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – Tuna Construction

Construction Phase

- Flooring repairs continues
- Restroom work is 90% complete
- Kitchen work is ongoing

Contractual Substantial Completion – June 2016

Forecasted Substantial Completion – August 2016



Building Automation System Integration At Recovery School

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview ES

Funding Source – FEMA

Architect – Moses Engineers

Contractor – Synergy Building Solutions, Inc.

Construction Phase

- Moses is reviewing training docs and O&M manuals

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – July 2016



DEMOLITIONS

Demolition of Modular Buildings at Abramson and Carver ^(RSD)

5552 Read Boulevard and 3059 Higgins Boulevard, New Orleans, LA

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters, Inc.

Construction Phase

- Abramson - ornamental fencing is complete
- Abramson - Gate installation is ongoing
- Carver - limestone removal work continues

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – September 2016



Demolition of Modular Buildings at Livingston ^(RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – Concrete Busters of Louisiana

Construction Phase

- Fire damaged trailer has been removed
- Trailers are scheduled to be moved in August

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – September 2016



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
6	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
7	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
8	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
9	Alfred Lawless Senior ^(RSD)	12/18/2015
10	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
11	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
12	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
13	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
14	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
15	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
16	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
17	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
18	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
19	Augustine Elementary School Roof ^(RSD)	04/13/2012
20	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
21	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
22	Bell JH Shoring ^(RSD)	06/28/2011
23	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
24	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
25	Bienville Elementary School Demolition ^(RSD)	05/04/2009
26	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
27	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
28	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
29	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
30	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
31	Charles J. Colton Elementary School ^(RSD)	05/23/2013
32	Charles R. Drew Elementary School ^(RSD)	04/17/2015
33	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
34	Cohen High School Health Clinic ^(RSD)	12/24/2008
35	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
36	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
37	Douglass High School Under Floor Utilities ^(RSD)	
38	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
39	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
40	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
41	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
42	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
43	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011

44	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
45	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
46	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
47	Edna Karr High School - Assessment ^(OPSB)	
48	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
49	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
50	New Edward Hynes School ^(OPSB)	02/06/2012
51	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
52	Edward Livingston High School ^(RSD)	01/05/2015
53	Eleanor L. McMains School Replacement of Existing Chillers ^(OPSB)	08/30/2011
54	Eleanor L. McMains School Clinic ^(OPSB)	07/24/2013
55	Eleanor L. McMains School Roof Replacement ^(OPSB)	05/13/2016
56	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
57	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
58	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
59	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
60	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
61	Francis W. Gregory Demolition ^(RSD)	12/21/2011
62	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
63	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
64	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
65	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
66	George Mondy Elementary School Mothball ^(RSD)	
67	George Washington Carver School ^(RSD)	03/07/2016
68	George Washington Carver High School Demolition ^(RSD)	08/24/2011
69	Greater St. Stephens School ^(OPSB)	03/18/2013
70	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
71	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
72	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
73	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
74	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
75	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
76	Holy Cross Modular Relocation ^(RSD)	12/14/2010
77	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
78	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
79	James Derham Demolition ^(RSD)	02/23/2012
80	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
81	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
82	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
83	John Dibert Elementary School Roof ^(RSD)	08/20/2010
84	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
85	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
86	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
87	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
88	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
89	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014

90	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
91	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
92	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
93	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
94	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
95	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
96	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
97	Lake Area Landry Demolition ^(RSD)	05/01/2008
98	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
99	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
100	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
101	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
102	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
103	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
104	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
105	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
106	Live Oak Elementary School Roof ^(RSD)	08/04/2011
107	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
108	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
109	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
110	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
111	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
112	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
113	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
114	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
115	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
116	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
117	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
118	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
119	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
120	McDonogh #7 High School Repairs ^(OPSB)	
121	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
122	McDonogh #28 School Refurbishment ^(RSD)	03/15/2016
123	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
124	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
125	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
126	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
127	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
128	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
129	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
130	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
131	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
132	Modular Campuses Close Outs ^(RSD)	
133	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
134	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010

135	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
136	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
137	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
138	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
139	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
140	New Carter G. Woodson School ^(RSD)	09/14/2012
141	New Fannie C. Williams School ^(RSD)	08/24/2012
142	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
143	New L.B. Landry High School ^(RSD)	06/30/2010
144	New Lake Area High School ^(RSD)	12/28/2009
145	New Lawrence D. Crocker School ^(RSD)	04/29/2013
146	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
147	New Parkview School ^(RSD)	10/12/2012
148	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
149	New William Frantz Elementary School ^(RSD)	
150	New Orleans High School Signature Center Study ^(RSD)	
151	Oretha C. Haley Demo ^(RSD)	05/07/2012
152	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
153	Parkview Elementary School Demolition ^(RSD)	08/06/2009
154	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
155	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
156	Paul B. Habans Elementary School ^(RSD)	06/30/2016
157	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
158	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
159	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
160	Rosenwald Elementary School Refurbishment ^(RSD)	04/07/2016
161	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
162	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
163	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
164	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
165	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
166	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
167	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
168	Schaumburg Chillers ^(RSD)	11/14/2008
169	Schwarz Alternative Repairs ^(RSD)	07/14/2009
170	Schwarz Alternative Modulares Demolition ^(RSD)	04/02/2015
171	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
172	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
173	Sherwood Forest Elementary School ^(RSD)	06/30/2016
174	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
175	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
176	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
177	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
178	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
179	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
180	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010

181	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
182	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
183	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
184	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
185	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
186	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
187	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
188	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
189	Timbers HVAC ^(OPSB)	09/11/2013
190	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
191	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
192	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
193	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
194	Valena C. Jones Elementary School ^(RSD)	01/10/2013
195	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
196	Warren Easton High School Renovation ^(OPSB)	12/15/2015
197	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
198	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
199	New William J. Guste Elementary School ^(RSD)	10/06/2008
200	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
201	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
202	William Frantz Elementary School Roof ^(RSD)	08/12/2010
