


# Superintendent's Report March, 2015



**Dr. Henderson Lewis Jr.**  
Orleans Parish School Board



**Mr. John White**  
Louisiana Department of Education  
**Mr. Patrick Dobard**  
Recovery School District

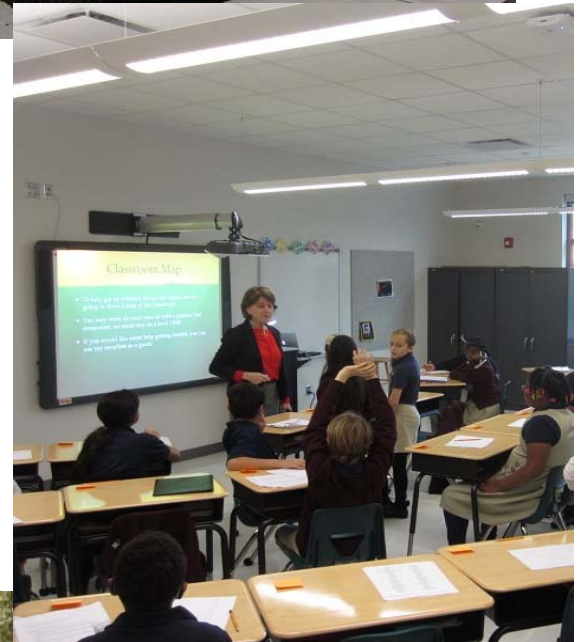

Prepared By





# Table of Contents

Right-Click on the school name to proceed to that page

<b>TABLE OF CONTENTS</b>	1
<b>FINANCIAL OVERVIEW</b>	4
<b>COMMUNITY MEETINGS</b>	5
<b>BID OPENINGS</b>	6
<b>DBE OVERVIEW MONTHLY SUMMARY</b>	7
<b>NEW &amp; MAJOR RENOVATION</b>	13
Ray Abrams Elementary School <sup>(RSD)</sup>	13
Avery Alexander Elementary School <sup>(RSD)</sup>	13
James Audubon School <sup>(OPSB)</sup>	13
Stuart R. Bradley School <sup>(RSD)</sup>	14
George Washington Carver School <sup>(RSD)</sup>	14
Charles R. Drew Elementary School <sup>(RSD)</sup>	14
Paul L. Dunbar School <sup>(RSD)</sup>	15
Benjamin Franklin Elementary School Renovation <sup>(OPSB)</sup>	15
Paul B. Habans School <sup>(RSD)</sup>	15
New PK-8 School at North Kenilworth Park at Curran Site <sup>(OPSB)</sup>	16
Lake Forest PK-8 at the Greater St. Stephens Site <sup>(OPSB)</sup>	16
Alfred Lawless School <sup>(RSD)</sup>	16
John McDonogh High School Selective Demolition <sup>(RSD)</sup>	17
John McDonogh High School Renovation <sup>(RSD)</sup>	17
McDonogh #35 School (Phillip/Waters Site) <sup>(OPSB)</sup>	17
McDonogh #42 Elementary School <sup>(RSD)</sup>	18
Eleanor L. McMain School Gymnasium <sup>(OPSB)</sup>	18
Ernest "Dutch" Morial Elementary School <sup>(RSD)</sup>	18
Small New Orleans East High School at Abramson <sup>(RSD)</sup>	19
Sherwood Forest School <sup>(RSD)</sup>	19
Harriet R. Tubman Elementary School Renovation <sup>(RSD)</sup>	19
Booker T. Washington School Environmental Remediation <sup>(RSD)</sup>	20
Booker T. Washington School <sup>(RSD)</sup>	20
Sophie B. Wright School <sup>(RSD)</sup>	20

<b>REFURBISHMENTS</b>	21
Henry Allen Elementary School Refurbishment <sup>(RSD)</sup>	21
Henry Allen Elementary School Kitchen Refurbishment <sup>(RSD)</sup>	21
Benjamin Banneker Elementary Kitchen School Refurbishment <sup>(RSD)</sup>	21
Bethune and Tureaud Elementary School Refurbishment <sup>(OPSB)</sup>	22
Agnes L. Bauduit Elementary School Refurbishment <sup>(RSD)</sup>	22
Walter L. Cohen High School Kitchen Refurbishment <sup>(RSD)</sup>	22
A. D. Crossman School Kitchen Refurbishment <sup>(RSD)</sup>	23
Frederick A. Douglass High School Science Lab <sup>(RSD)</sup>	23
Warren Easton School Refurbishment <sup>(OPSB)</sup>	23
Dwight D. Eisenhower Elementary School Refurbishment <sup>(RSD)</sup>	24
Dwight D. Eisenhower Elementary School Kitchen Refurbishment <sup>(RSD)</sup>	24
William J. Fischer Elementary Refurbishment <sup>(RSD)</sup>	24
Fortier (Lusher) High School Refurbishment <sup>(OPSB)</sup>	25
Gaudet Elementary School Refurbishment <sup>(RSD)</sup>	25
Gentilly Terrace School Refurbishment <sup>(RSD)</sup>	25
Gentilly Terrace School Kitchen Refurbishment <sup>(RSD)</sup>	26
Samuel J. Green Elementary School Refurbishment <sup>(RSD)</sup>	26
Edgar P. Harney Elementary School Refurbishment <sup>(RSD)</sup>	26
Andrew Jackson School Refurbishment <sup>(RSD)</sup>	27
Andrew Jackson School Kitchen Refurbishment <sup>(RSD)</sup>	27
J. W. Johnson Elementary School Refurbishment <sup>(RSD)</sup>	27
Dr. Martin L. King Elementary School Kitchen Refurbishment <sup>(RSD)</sup>	28
Lafayette Elementary School Refurbishment <sup>(RSD)</sup>	28
Laurel Elementary School Refurbishment <sup>(RSD)</sup>	28
Live Oak Elementary School Refurbishment <sup>(RSD)</sup>	29
Lusher Elementary School Refurbishment <sup>(OPSB)</sup>	29
Thurgood Marshall Elementary School Refurbishment <sup>(RSD)</sup>	29
McDonogh #28 School Refurbishment <sup>(RSD)</sup>	30
McDonogh #28 School Kitchen Refurbishment <sup>(RSD)</sup>	30
McDonogh #32 School Refurbishment <sup>(RSD)</sup>	30
Nelson Elementary School Refurbishment <sup>(OPSB)</sup>	31
Sarah T. Reed School Refurbishment <sup>(RSD)</sup>	31
Sarah T. Reed School Kitchen Refurbishment <sup>(RSD)</sup>	31
Rosenwald Elementary School Refurbishment <sup>(RSD)</sup>	32
Henry C. Schaumburg Elementary School Refurbishment <sup>(RSD)</sup>	32
Village de l'Est Elementary School Refurbishment <sup>(RSD)</sup>	32
Albert Wicker School Kitchen Refurbishment <sup>(RSD)</sup>	33
Sylvanie F. Williams School Refurbishment <sup>(RSD)</sup>	33

<b>OTHER PROJECTS</b>	34
Eleanor L. McMain School Roof Replacement <sup>(OPSB)</sup>	34
Eleanor L. McMain School Maintenance Upgrades <sup>(OPSB)</sup>	34
Timbers III - Building Controls <sup>(OPSB)</sup>	34
Building Automation System Integration At Recovery School District Central And Remote Offices <sup>(RSD)</sup>	35
 <b>MOTHBALL OR SAFE &amp; SECURE OF SELECTED SCHOOLS</b>	 36
Andrew J. Bell Junior High School Shoring and Mothball <sup>(RSD)</sup>	36
Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School <sup>(RSD)</sup>	36
Demolition of Modular Buildings Gregory and Abramson <sup>(RSD)</sup>	35
JoEllen Smith Medical Center Demolition <sup>(OPSB)</sup>	37
Demolition of Modulares at Livingston <sup>(RSD)</sup>	37
Demolition of Modulares at Schwarz <sup>(RSD)</sup>	37
 <b>COMPLETED PROJECTS</b>	 38

# Overview

## FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$488 million in open contracts for the capital program after issuing \$175 thousand in new contracts and \$386 thousand in change orders and amendments in March. In addition, the total change orders to date, \$5.2 million, account for approximately one percent (1.19%) of the total open construction contracts. RSD anticipates issuing approximately \$106 million in construction contracts/change orders, and \$207 thousand in professional service contracts/amendments in April.



The OPSB has \$210 million in open contracts for the capital program after issuing \$0 thousand in new contracts and \$132 thousand in change orders and amendments in March. In addition, the total change orders to date, \$3 million, account for approximately two percent (1.62%) of the total open construction contracts. OPSB anticipates issuing approximately \$1.5 million in construction contracts/change orders and \$482 thousand in professional service contracts/amendments in April.

# Community Meetings



## Future Community Meetings

### **April 14, 2015**

Ernest “Dutch” Morial Elementary School Community Meeting  
4807 Wilson Avenue New Orleans, LA 70126

### **April 16, 2015**

Ray Abrams Elementary School Community Meeting  
5919 Morrison Road New Orleans, LA 70126

### **April 29, 2015**

Ground Breaking for Sherwood Forest Elementary School  
4801 Maid Marion Drive New Orleans, LA 70128

# **Bid Openings**

## **Bids that were opened in March, 2015**

### **March 3, 2015**

- Rosenwald Elementary School Refurbishment

### **March 4, 2015**

- Kitchen Improvements at Crossman & Gentilly Terrace

### **March 11, 2015**

- Kitchen Improvements at Allen, Dr. Martin Luther King & Eisenhower

### **March 24, 2015**

- Statement of Qualifications CMAR New Booker T. Washington High School

### **March 31, 2015**

- Statement of Qualifications CMAR John McDonogh High School Renovation

## **The following projects are scheduled to bid in the next 60 days:**

### **April 1st, 2015**

- Frederick A. Douglass High School Science Classroom Renovation



# Disadvantaged Business Enterprises (DBE) Monthly Summary

## Recovery School District



### New & Renovations:

DBE Contractors secured subcontracts on 17 projects as of March 31, 2015. The DBE subcontracts value is \$48,882,578 of the \$252,253,077 total of awarded contracts.

### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 33 projects as of March 31, 2015. The DBE subcontracts value is \$9,473,975 of the \$33,011,670 total of awarded contracts.

### Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of March 31, 2015. The DBE subcontracts value is \$35,025,777 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$ 394,402,304

## Orleans Parish School Board

### New & Renovations:

DBE Contractors secured subcontracts on 8 projects as of March 31, 2015. The DBE subcontracts value is \$52,546,433 of the \$193,549,360 total of awarded contracts.


### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of March 31, 2015. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$194,452,359

\* DBE provisions were included in projects bid after June 30, 2012


## Current RSD Program DBE Participation

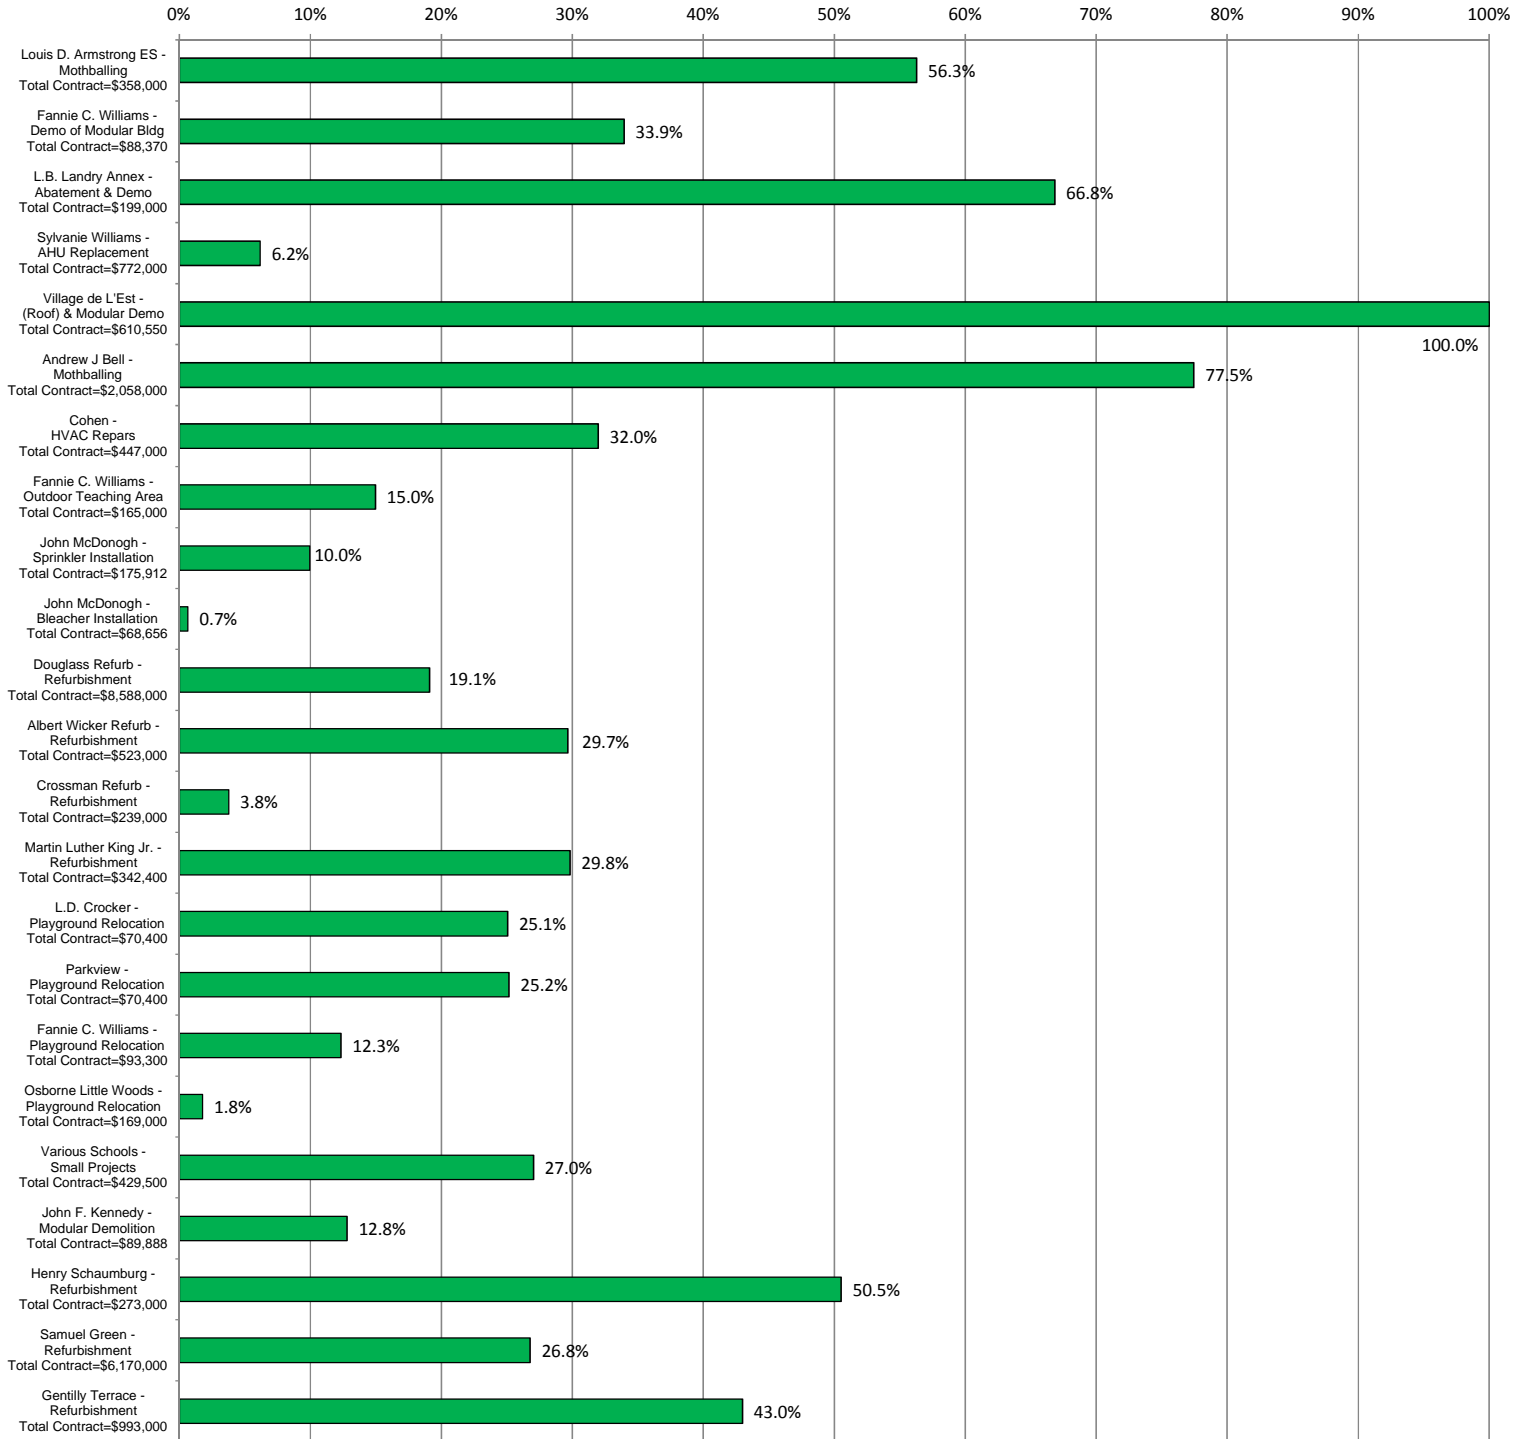

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount


## Current RSD Program DBE Participation

(Continued)

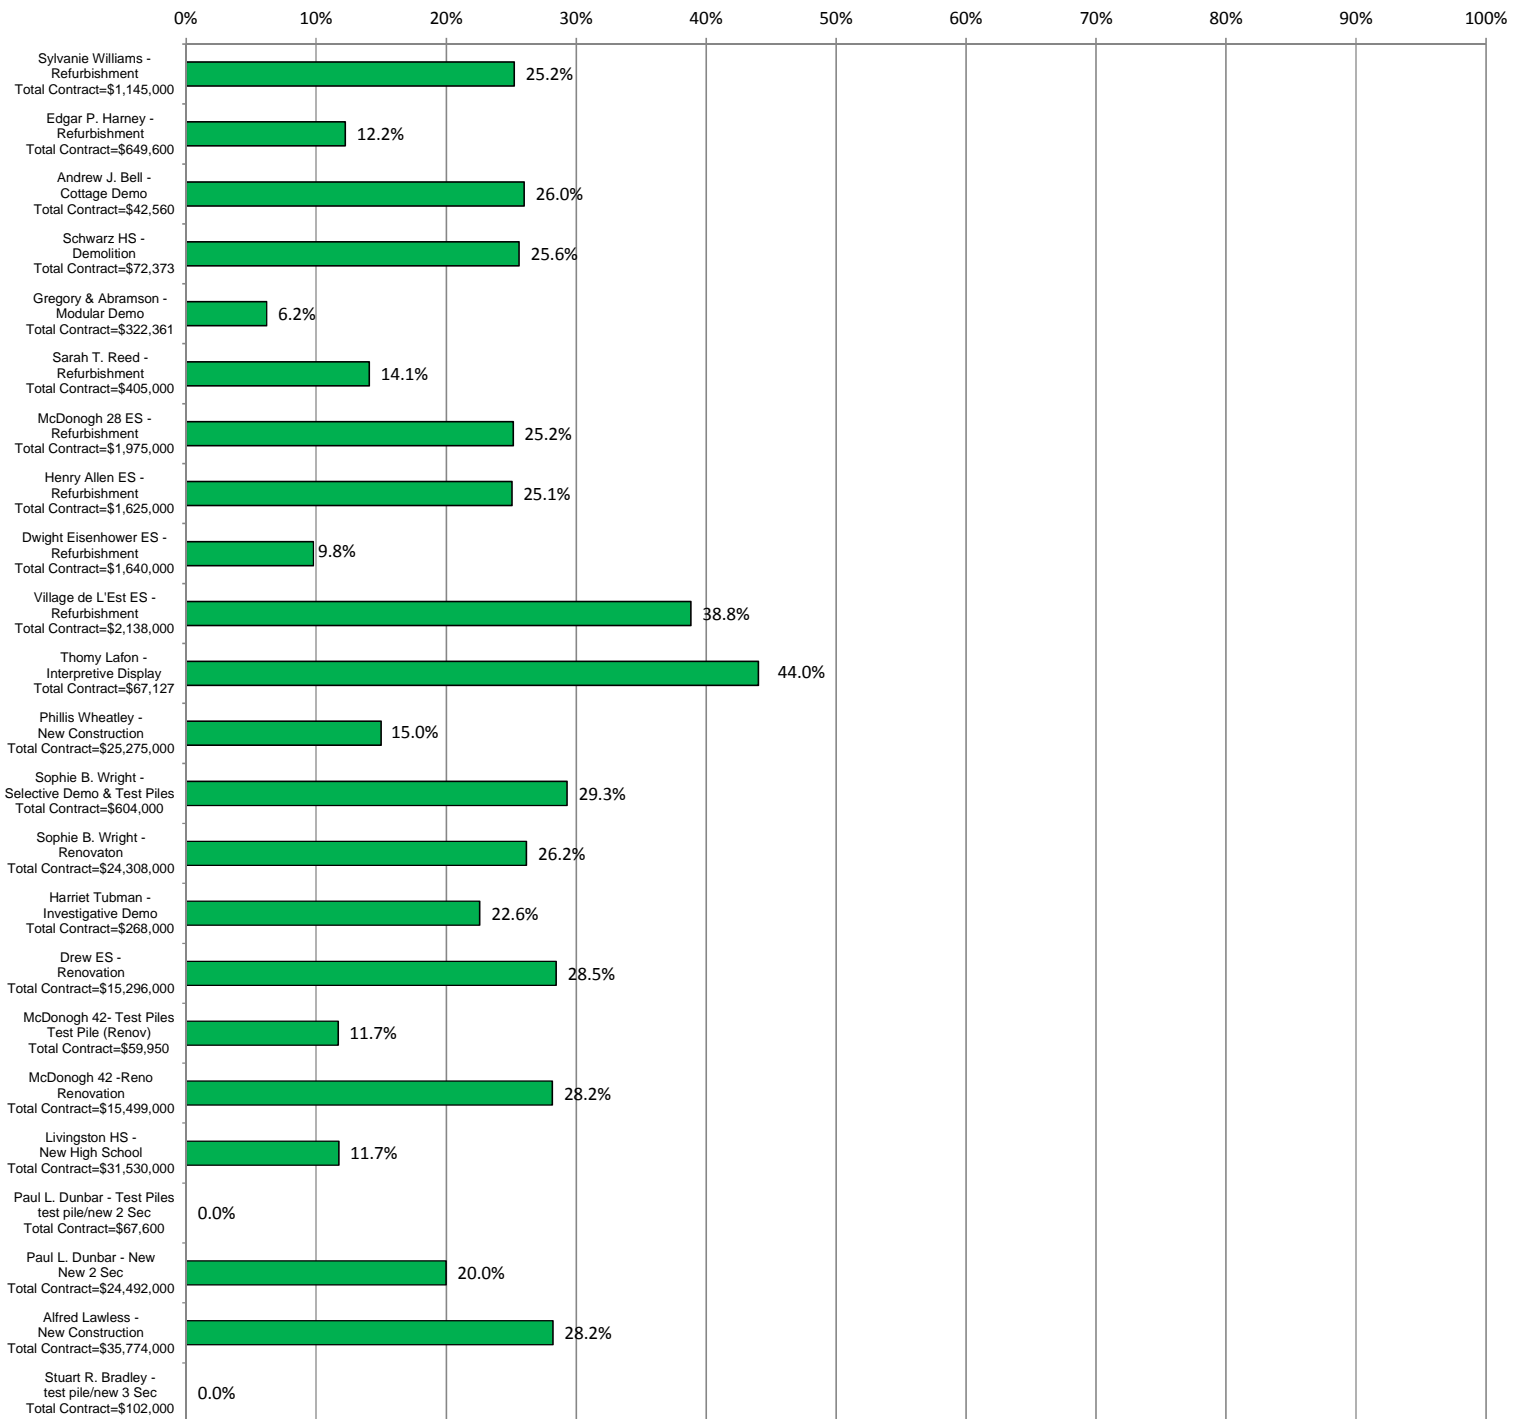


**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

### Current RSD Program DBE Participation (Continued)

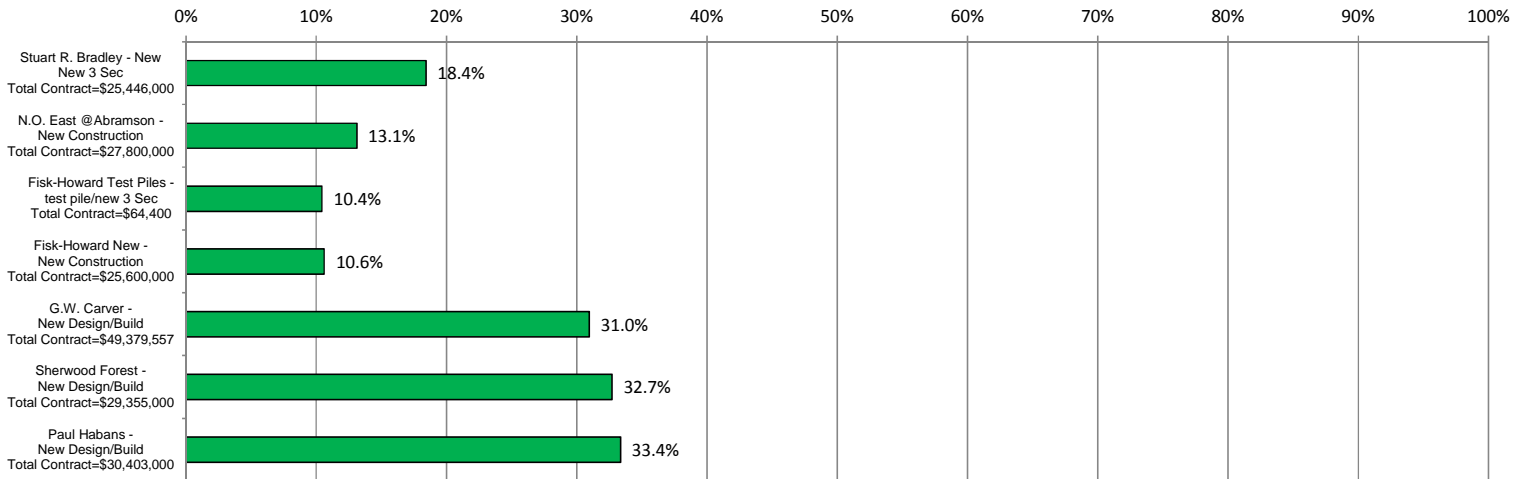

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

### Current OPSB Program DBE Participation

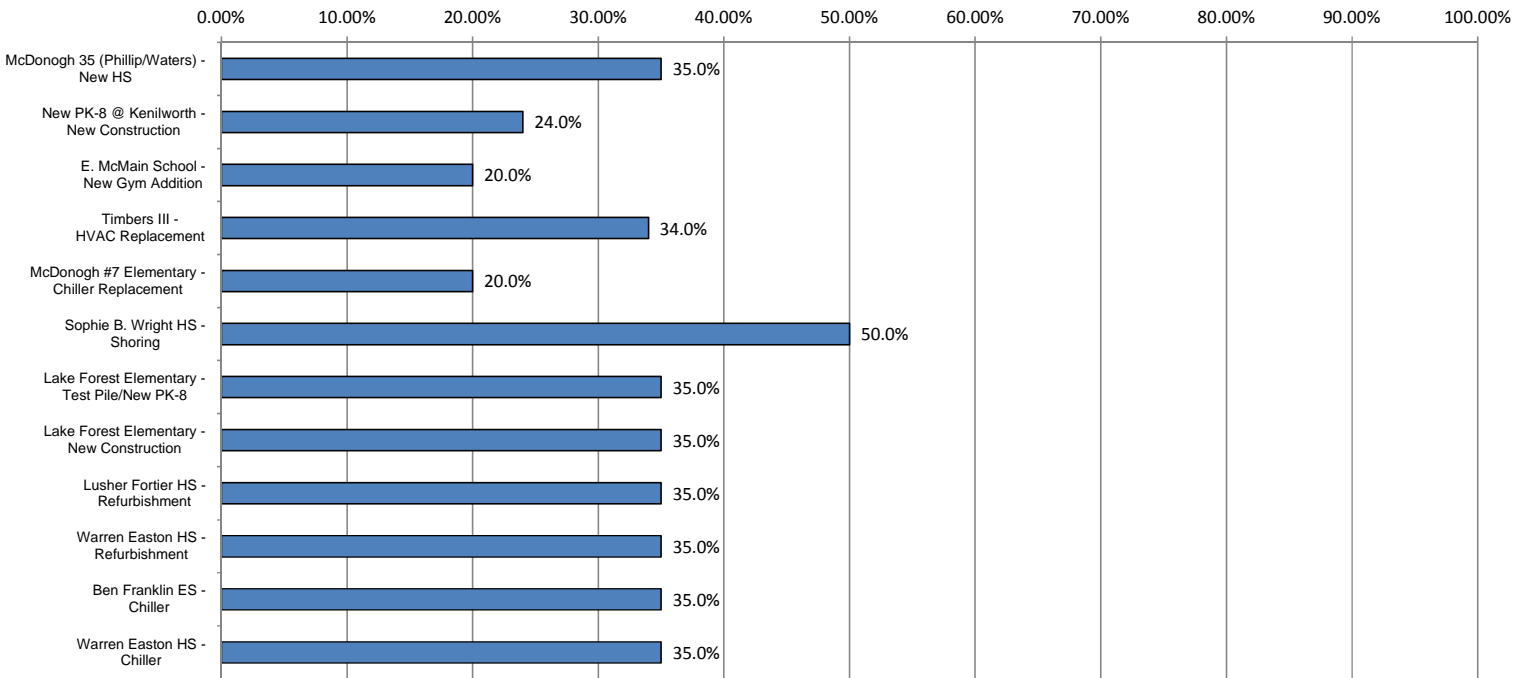

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
 OPSB DBE Participation Target = 35% of Total Contract Amount



## New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

### Ray Abrams Elementary School <sup>(RSD)</sup>

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – McDonnell Group, LLC

#### Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - May 2015
- Preconstruction meeting - April 7th



### Avery Alexander Elementary School <sup>(RSD)</sup>

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

#### Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - May 2015



### James Audubon School <sup>(OPSB)</sup>

428 Broadway Avenue, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation of existing elementary school and new addition

Funding Source – FEMA

Architect – Blitch/Knevel Architects

Contractor – FHP Tectonics Corporation

#### Construction Phase

- Structural steel has been realigned, masonry repairs continue
- Permanent power anticipate beginning of April
- Floor tile installation is ongoing in the existing building

Contractual Substantial Completion – September 2013

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – June 2015



## Stuart R. Bradley School <sup>(RSD)</sup>

2401 Humanity Street, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Landis Construction Co.

### Construction Phase

- Window installation is 90% complete
- Painting of gypsum board continues
- Roof installation is ongoing
- Installation of lighting and ceiling grid is ongoing

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – June 2015



## George Washington Carver School <sup>(RSD)</sup>

3059 Higgins Blvd., New Orleans, LA 70126 District E Ward 9

Scope of work: New High School, Design Build

Funding Source – FEMA

Contractor – Broadmoor LLC

### Construction Phase

- Metal stud framing is ongoing
- MEP above ceilings has started
- Steel erection at the convocation center to be complete in April
- Precast panels installation has started
- Sprinkler installations to start mid of April

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



## Charles R. Drew Elementary School <sup>(RSD)</sup>

3819 St. Claude Avenue, New Orleans, LA 70117 District C Ward 5

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Blich / Knevel Architects, Inc.

Contractor – Core Construction

### Construction Phase

- State Fire Marshal walk thru March 29th
- Architect is developing punch list
- Interior finishes are 90% complete

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015

School Ready for Occupancy – June 2015





## Paul L. Dunbar School <sup>(RSD)</sup>

9330 Forshey Street, New Orleans, LA 70125 District A Ward 17

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor – McDonnell Group, LLC

### Construction Phase

- Subsurface drainage work continues
- Flooring and ceiling grid installation continues
- Cast stone installation is ongoing
- Window installation is ongoing
- Roof installation is ongoing

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – June 2015



## Benjamin Franklin Elementary School Renovation <sup>(OPSB)</sup>

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - SD

- Schematic Design Documents were received March 16th
- 100% Construction Documents are due April 17th

### Procurement Phase

- Anticipated 1st Advertisement – May 2015
- Anticipated Bid Opening – June 2015



## Paul B. Habans School <sup>(RSD)</sup>

3501 Siene Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

### Construction Phase

- Grade beam pours are ongoing
- Underground drainage work is ongoing
- Foundation permit was received mid March
- Under slab plumbing work has started

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



## **New PK-8 School at North Kenilworth Park at Curran Site <sup>(OPSB)</sup>**

8500 Curran Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Mathes Brierre Architects

Contractor – Woodrow Wilson Construction Company, Inc.

### Construction Phase

- MEP work is ongoing
- Gypsum board and metal stud installation is 80% complete
- Installation of ceiling grid has started
- Installation of windows is nearly complete

Contractual Substantial Completion – September 2014

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – July 2015



## **Lake Forest PK-8 at the Greater St. Stephens Site <sup>(OPSB)</sup>**

11110 Lake Forest Boulevard 70128 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Imre Hegedus & Associates Architects

Contractor – The McDonnel Group

### Construction Phase

- MEP rough-in continues
- Window installation has started
- Installation of masonry brick is 65% complete
- Site work is 20% complete
- Permanent power was connected in March

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015

School Ready for Occupancy – August 2015



## **Alfred Lawless School <sup>(RSD)</sup>**

5300 Law Street, New Orleans, LA 70117 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

### Construction Phase

- Permanent power was connected in March
- Roof installation is 95% complete
- Installation of windows is ongoing
- Exterior brick work has ongoing
- Electric and HVAC main distribution continues

Contractual Substantial Completion – November 2015

Forecasted Substantial Completion – November 2015

School Ready for Occupancy – January 2016



## John McDonogh High School Selective Demolition <sup>(RSD)</sup>

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

### Procurement Phase

- Contract is being reviewed by the Owner
- Anticipated Notice to Proceed - May 2015



## John McDonogh High School Renovation <sup>(RSD)</sup>

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

### Design Phase - SD

- RFQ second advertisement March 4th
- RFQ third advertisement March 11th
- RFQ preconference March 19th
- Qualifications are due March 31st
- Short list to be announced the end of April



## McDonogh #35 School (Phillip/Waters Site) <sup>(OPSB)</sup>

1200 Senate Street, New Orleans, LA 70122 District D Ward 7

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler, Thompson, Brown Architects

Contractor – Citadel Builders, LLC

### Construction Phase

- Installation of MEP continues
- Brick masonry and window installation is 90% complete
- Drywall installation is finished in the north and south classroom buildings
- Metal panel installation is 80% complete

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – June 2015



## McDonogh #42 Elementary School <sup>(RSD)</sup>

1651 North Tonti Street, New Orleans, LA 70119 District A Ward 7

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA, QSCB, NMTC, Insurance Proceeds

Architect – Eskew+Dumez+Ripple

Contractor – Core Construction

### Construction Phase

- Architect is working on the 2nd and 3rd floor punch list
- Work has started on the first floor
- The forming of the basketball court has started

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – May 2015

School Ready for Occupancy – August 2015



## Eleanor L. McMain School Gymnasium <sup>(OPSB)</sup>

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source – FEMA

Architect – Jahncke & Burns Architects

Contractor – Ellis Construction

### Construction Phase

- Installation of roofing is ongoing
- Exterior sheathing installation is ongoing

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – August 2015



## Ernest "Dutch" Morial Elementary School <sup>(RSD)</sup>

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – McDonnell Group, LLC

### Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - May 2015
- Preconstruction meeting - April 7th



## Small New Orleans East High School at Abramson<sup>(RSD)</sup>

5552 Read Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

### Construction Phase

- Masonry installation continues
- MEP distribution lines are being installed
- Door and window installation is ongoing
- Installation of interior finishes is ongoing

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – October 2015

School Ready for Occupancy – November 2015



## Sherwood Forest School<sup>(RSD)</sup>

4801 Maid Marion Drive, New Orleans, LA 70128 District E Ward 9

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

### Construction Phase

- Forming and pouring of pile caps is 85% complete
- Grade beam pours are ongoing
- Underground drainage work is ongoing
- Foundation permit was received mid March

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



## Harriet R. Tubman Elementary School Renovation<sup>(RSD)</sup>

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

### Design Phase - CD

- 50% Construction Documents were received March 19th
- 50% Construction Documents are due April 9th

### Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



## Booker T. Washington School Environmental Remediation <sup>(RSD)</sup>

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The remediation of the site

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – SEMS, Inc

Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - May 2015



## Booker T. Washington School <sup>(RSD)</sup>

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – TBD

Design Phase - SD

- Qualifications were received March 24th
- The Owner is reviewing the Qualifications
- A short list will be generated mid of April



## Sophie B. Wright High School Renovation <sup>(RSD)</sup>

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Renovation of existing school and gymnasium addition

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – Core Construction

Construction Phase

- Termite damage repairs are ongoing
- Removal and refurbishment of windows continues
- Pile caps are being formed and poured
- 1st floor plumbing rough in continues

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



## REFURBISHMENTS

### Henry Allen Elementary School Refurbishment <sup>(RSD)</sup>

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Tuna Construction

Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - April 2015



### Henry Allen Elementary School Kitchen Refurbishment <sup>(RSD)</sup>

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- Bids are being reviewed



### Benjamin Banneker Elementary School Kitchen Refurbishment <sup>(RSD)</sup>

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Bid Documents are due March 25th
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – January 2016
- Anticipated Bid Opening – March 2016



## **Agnes L. Bauduit Elementary School Refurbishment** (RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor - TBD

### Design Phase - CD

- Bid Documents are due June 2015
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – June 2015
- Anticipated Bid Opening – July 2015



## **Bethune and Tureaud Elementary School Refurbishment** (OPSB)

4040 Eagle Street & 2021 Pauger Street, New Orleans, LA District A Ward 3 & District D Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - TBD

### Design Phase - DD

- Design Development Documents were received March 12th
- 50% Construction Documents are due April 17th

### Procurement Phase

- Anticipated 1st Advertisement – July 2015
- Anticipated Bid Opening – August 2015



## **Walter L. Cohen High School Kitchen Refurbishment** (RSD)

3520 Dryades, New Orleans Street, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents were received March 26th
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – January 2016
- Anticipated Bid Opening – March 2016





### **A. D. Crossman School Kitchen Refurbishment** (RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Procurement Phase

- Bids were over the AFC
- The Owner is reviewing their options



### **Frederick A. Douglass High School Science Lab** (RSD)

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovations to science lab

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

Procurement Phase

- Bids April 1, 2015

### **Warren Easton School** (OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Refurbishment of existing high school, including but not limited to structure, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - Tuna Construction

Construction Phase

- Work is ongoing in the classrooms, 2nd and 3rd floor classrooms are complete
- Restroom renovations continues
- Ceiling work has started
- Sprinkler work continues at the Gymnasium
- Structural issues involving the restrooms will extended the schedule

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



## Dwight D. Eisenhower Elementary School Refurbishment <sup>(RSD)</sup>

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Harry Baker Smith Architects II, PLLC

Contractor - CDW Construction

### Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - April 2015



## Dwight D. Eisenhower Elementary School Kitchen Refurbishment <sup>(RSD)</sup>

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Procurement Phase

- Bids are being reviewed



## William J. Fischer Elementary School Refurbishment <sup>(RSD)</sup>

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



## Fortier (Lusher) High School Refurbishment (OPSB)

5624 Freret Street, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation and repairs to the roof, masonry, plaster, windows, exterior doors, canopies, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Core Construction

### Construction Phase

- HVAC work is complete
- Wall framing is complete, and installation of gypsum has started
- Plaster repair is 95% complete
- Painting of walls and doors has started
- Installation of new doors and hardware continues
- Repairs to exterior brick work is ongoing

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



## Gaudet Elementary School Refurbishment (RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents are due April 1st
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



## Gentilly Terrace School Refurbishment (RSD)

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - One Construction

### Construction Phase

- Construction is 90% complete
- Punch List is being developed by the architect
- The contract will be extended due to added kitchen scope

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



## Gentilly Terrace School Kitchen Refurbishment <sup>(RSD)</sup>

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

### Procurement Phase

- Bids were over the AFC
- The Owner is reviewing their options



## Samuel J. Green Elementary School Refurbishment <sup>(RSD)</sup>

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Hernandez Consulting, LLC

### Construction Phase

- Installation of gypsum board at restrooms continues
- Rough in of fire suppression is nearly complete
- Electrical and plumbing renovations is ongoing
- Stripping and staining of wood floors continues
- Exterior brick repairs is ongoing
- Roof repairs continues

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015



## Edgar P. Harney Elementary School Refurbishment <sup>(RSD)</sup>

2503 Willow Street, New Orleans, LA 70113 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Hamp's Construction, LLC

### Procurement Phase

- Notice to Proceed is being delayed due to student testing
- Anticipated Notice to Proceed - May 2015



## Andrew Jackson School Refurbishment <sup>(RSD)</sup>

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

### Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - April 2015



## Andrew Jackson School Kitchen Refurbishment <sup>(RSD)</sup>

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents were received March 26th
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – January 2016
- Anticipated Bid Opening – March 2016



## J. W. Johnson Elementary School Refurbishment <sup>(RSD)</sup>

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



## Dr. Martin L. King Elementary School Kitchen Refurbishment <sup>(RSD)</sup>

1617 Caffin Avenue, New Orleans, LA 70117 District E Ward 9

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- Bids are being reviewed



## Lafayette Elementary School Refurbishment <sup>(RSD)</sup>

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – May 2015
- Anticipated Bid Opening – June 2015



## Laurel Elementary School Refurbishment <sup>(RSD)</sup>

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – June 2015
- Anticipated Bid Opening – July 2015



### **Live Oak Elementary School Refurbishment <sup>(RSD)</sup>**

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – July 2015
- Anticipated Bid Opening – August 2015



### **Lusher Elementary School Refurbishment <sup>(OPSB)</sup>**

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source – FEMA

Architect – Meyer Engineers, LTD.

Contractor - Hamps

Procurement Phase

- Owner is reviewing the Bid
- Anticipated Notice to Proceed - April 2015



### **Thurgood Marshall Elementary School Refurbishment <sup>(RSD)</sup>**

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- 50% Construction Documents are due April 3rd
- 100% Construction Documents are due May 20th

Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



### **McDonogh #28 School Refurbishment (RSD)**

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects, LLC

Contractor - Tuna Construction

#### Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - May 2015



### **McDonogh #28 School Kitchen Refurbishment (RSD)**

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

#### Design Phase - CD

- Bid Documents are due March 25th
- Procurement schedule has been adjusted pending FEMA funding approval

#### Procurement Phase

- Anticipated 1st Advertisement – January 2016
- Anticipated Bid Opening – March 2016



### **McDonogh #32 School Refurbishment (RSD)**

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

#### Design Phase – CD

- Bid Documents are due August 18th
- Procurement schedule has been adjusted pending FEMA funding approval

#### Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015





## **Nelson Elementary School Refurbishment** (OPSB)

3121 St. Bernard Avenue, New Orleans, LA 70119 District D Ward 7

Scope of work: Renovation and repairs to the roof, masonry, windows, exterior doors, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – Harry Baker Smith Architects

Contractor - Blanchard Mechanical Contractor

### Procurement Phase

- Notice to Proceed - April 3rd
- Contractor is mobilizing



## **Sarah T. Reed School Refurbishment** (RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - Tuna Construction

### Construction Phase

- Contracts are being reviewed and signed
- Anticipated Notice to Proceed - April 2nd

Contractual Substantial Completion – December 2015

Forecasted Substantial Completion – December 2015



## **Sarah T. Reed School Kitchen Refurbishment** (RSD)

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Procurement Phase

- Bids are being reviewed



## Rosenwald Elementary School Refurbishment <sup>(RSD)</sup>

6501 Berkley Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

### Procurement Phase

- Contracts are being reviewed and signed
- Anticipated Notice to Proceed - May 2015



## Henry C. Schaumburg Elementary School <sup>(RSD)</sup>

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc

Contractor - Hernandez Consulting, LLC

### Construction Phase

- Installation of sidewalks has been completed
- Dumpster pad work is 85% complete
- Roof repairs are 85% complete

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



## Village de l'Est Elementary School Refurbishment <sup>(RSD)</sup>

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CBDG

Architect – Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

### Procurement Phase

- Contracts are being reviewed
- Anticipated Notice to Proceed - April 2015



## Albert Wicker School Kitchen Refurbishment <sup>(RSD)</sup>

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- Bid Documents are due March 25th
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – January 2016
- Anticipated Bid Opening – March 2016



## Sylvanie F. Williams School Refurbishment <sup>(RSD)</sup>

3127 Martin Luther King Jr. Boulevard, New Orleans, LA 70125 District B Ward 2

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Hamps

Construction Phase

- Roof work is nearing completion
- Plumbing work is 90% complete
- Stucco repairs continues

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015



## OTHER PROJECTS

### **Eleanor L. McMain School Roof Replacement** (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Roof replacement

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – TBD

#### Design Phase - CD

- 50% Construction Documents were received March 9th
- 100% Construction Documents are due April 13th

#### Procurement Phase

- Anticipated 1st Advertisement – May 2015
- Anticipated Bid Opening – June 2015

### **Eleanor L. McMain School Maintenance Upgrades** (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work.

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – TBD

#### Design Phase - CD

- 50% Construction Documents were received March 9th
- 100% Construction Documents are due April 13th

#### Procurement Phase

- Anticipated 1st Advertisement – May 2015
- Anticipated Bid Opening – June 2015

### **Timbers III - Building Controls** (OPSB)

3520 General DeGaulle Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: Design and installation of new building controls

Funding Source – OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - TBD

#### Design Phase - PC

- Owner has placed project on hold

#### Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



## Building Automation System Integration At Recovery School

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview ES

Funding Source – FEMA

Architect – Moses Engineers

Contractor – Synergy Building Solutions, Inc.

### Construction Phase

- The five Quick Start Schools are complete, the Energy Dash Board is being implemented
- Sylvania Williams Elementary School, Sarah T. Reed Elementary School, Fannie C. Williams Elementary School, Bienville Elementary School, Charles L. Colton Elementary School, William Frantz Elementary School, Parkview Elementary School, Osborne Elementary School, Carter G. Woodson Elementary School, Walter Cohen High School, Dolores T Aaron Elementary School, A. D. Crossman Elementary School, and Albert Wicker Elementary School are complete
- New integration work is ongoing at Benjamin Banneker Elementary School
- Integration has started at Lawrence D. Crocker Elementary School

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – May 2015



## MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

### Andrew J. Bell Junior High School Mothball <sup>(RSD)</sup>

1010 N. Galvez St., New Orleans, LA 70119 District D Ward 6

Scope of work: Design Services to assist in determining the condition of the facilities both interior and exterior, make recommendations to stabilize the facilities and provide drawings required to provide a water barrier, ventilation, and rudimentary fire detection and to secure openings and entryways. Construction Services to stabilize the facility according to the designer's drawings and specifications.

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – CDW Services, LLC

Mothballing of Closed Schools - Safe & Secure

- Mothballing of the Gymnasium, Administration Building, Annex, Building "C", Building "D", Chapel, & E.A.Christy Building

Construction Phase

- Structural roof repairs on the Christy building will extend the project timeline

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015



### Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School <sup>(RSD)</sup>

1010 N. Galvez St. & 2327 St. Philip Street, New Orleans, LA 70119 District D Ward 6

Scope of work: Demolition of existing caretakers cottages

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – Concrete Busters

Construction Phase

- Contractor is 95% complete

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – April 2015



### Demolition of Modular Buildings at Gregory and Abramson <sup>(RSD)</sup>

1700 Pratt Drive & 5552 Read Boulevard, New Orleans, LA District D Ward 7 & District E Ward 9

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Holly & Smith Architects

Contractor – Ashley Savarino Unlimited Construction

Construction Phase

- Gregory - Walkways being removed
- Gregory - Utilities are disconnected
- Abramson - Demolition is complete
- Abramson - site grading is underway



## JoEllen Smith Medical Center Demolition (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

Design Phase - CD

- RFQ Package is being developed
- Anticipated 1st Advertisement of RFQ – April



## Demolition of Modular Buildings at Livingston (RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – TBD

Procurement Phase

- Anticipated 1st Advertisement – November 2015
- Anticipated Bid Opening – December 2015



## Demolition of Modular Buildings at Schwarz (RSD)

709 Park Boulevard, New Orleans, LA District E Ward 9

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – Concrete Busters

Closeout Phase

- Substantial Completion – April 2nd



## Comprehensive List - Completed Projects

- 1 Abrams | Morial | Abramson | Coghill Demolition <sup>(RSD)</sup>
- 2 A. D. Cross Elementary School Energy Conservation <sup>(RSD)</sup>
- 3 A. D. Crossman Elementary School and Benjamin Banneker Elementary School <sup>(RSD)</sup>
- 4 A. D. Crossman Elementary School Refurbishment <sup>(RSD)</sup>
- 5 A. P. Tureaud Elementary School Roof Repairs <sup>(RSD)</sup>
- 6 Agnes Bauduit Elementary School Boiler <sup>(RSD)</sup>
- 7 Albert Wicker Elementary School Refurbishment <sup>(RSD)</sup>
- 8 Albert Wicker Elementary School Roof Repairs <sup>(RSD)</sup>
- 9 Alfred Lawless Senior High Security Fencing <sup>(RSD)</sup>
- 10 Alice M. Harte Elementary School <sup>(OPSB)</sup>
- 11 Alice M. Harte Elementary School Demolition <sup>(OPSB)</sup>
- 12 Andrew J. Bell Junior High School Roof Replacement <sup>(RSD)</sup>
- 13 Andrew Jackson Elementary School Roof Repairs <sup>(RSD)</sup>
- 14 Andrew Jackson Elementary School Solar Panels <sup>(RSD)</sup>
- 15 Andrew H. Wilson Elementary School Cottage <sup>(RSD)</sup>
- 16 Arthur Ashe Elementary School Kitchen Renovation <sup>(OPSB)</sup>
- 17 Augustine Elementary School Roof <sup>(RSD)</sup>
- 18 Avery-Alexander Elementary School Demolition <sup>(RSD)</sup>
- 19 Barbara C. Jordan Elementary School Demolition <sup>(RSD)</sup>
- 20 Bell JH Shoring <sup>(RSD)</sup>
- 21 Benjamin Banneker Elementary School Energy Conservation <sup>(RSD)</sup>
- 22 Benjamin Franklin Senior High School <sup>(OPSB)</sup>
- 23 Bienville Elementary School Demolition <sup>(RSD)</sup>
- 24 Booker T. Washington High School Partial Demolition <sup>(RSD)</sup>
- 25 Carter G. Woodson Middle School Demolition <sup>(RSD)</sup>
- 26 Central Services Warehouse Demolition <sup>(OPSB)</sup>
- 27 Charles J. Colton Elementary Selective Demolition <sup>(RSD)</sup>
- 28 Charles J. Colton Elementary School <sup>(RSD)</sup>
- 29 Charles R. Drew Elementary Roof & Installation of Kitchen Hood <sup>(RSD)</sup>
- 30 Cohen High School Health Clinic <sup>(RSD)</sup>
- 31 Douglass High School Under Floor Utilities <sup>(RSD)</sup>
- 32 Dr. Martin Luther King School Roof Repairs <sup>(RSD)</sup>
- 33 Dr. Martin Luther King Jr. School Renovation <sup>(RSD)</sup>
- 34 Dwight D. Eisenhower Elementary School Roof Repairs <sup>(RSD)</sup>
- 35 East Bank Swing Space for Audubon Charter School <sup>(OPSB)</sup>
- 36 Edgar P. Harney Elementary School Roof Repairs <sup>(RSD)</sup>
- 37 Edna Karr High School - Gymnasium Repair <sup>(OPSB)</sup>
- 38 Edna Karr High School - Assessment <sup>(OPSB)</sup>
- 39 Edward Livingston Middle School Demolition <sup>(RSD)</sup>
- 40 Edward Henry Phillips Junior High School Demolition <sup>(OPSB)</sup>
- 41 New Edward Hynes School <sup>(OPSB)</sup>
- 42 Edwards | Hardin | Lockett | Lawless Demolition <sup>(RSD)</sup>



- 43 Edward Livingston High School <sup>(RSD)</sup>
- 44 Eleanor L. McMain School Replacement of Existing Chillers <sup>(OPSB)</sup>
- 45 Eleanor L. McMain School Clinic <sup>(OPSB)</sup>
- 46 Ernest N. Morial Elementary Security Fencing <sup>(RSD)</sup>
- 47 Fannie C. Williams Elementary School Demolition <sup>(RSD)</sup>
- 48 Fisk-Howard Elementary School Demolition <sup>(RSD)</sup>
- 49 Florence J. Chester Elementary School Demolition <sup>(RSD)</sup>
- 50 Francis W. Gregory Demolition <sup>(RSD)</sup>
- 51 Frederick A. Douglass High Refurbishment <sup>(RSD)</sup>
- 52 Frederick A. Douglass High Switchgear <sup>(RSD)</sup>
- 53 Frederick A. Douglass High Emergency Boiler Roof Repairs <sup>(RSD)</sup>
- 54 George Mondy Elementary School Mothball <sup>(RSD)</sup>
- 55 George Washington Carver High School Demolition <sup>(RSD)</sup>
- 56 Greater St. Stephens School <sup>(OPSB)</sup>
- 57 Harriet R. Tubman Elementary School Selective Demolition <sup>(RSD)</sup>
- 58 Henry Allen Elementary School Roof <sup>(RSD)</sup>
- 59 Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation <sup>(RSD)</sup>
- 60 Holy Cross Modular Relocation <sup>(RSD)</sup>
- 61 Israel M. Augustine Middle School Roof Replacement <sup>(RSD)</sup>
- 62 Israel M. Augustine Middle School Mothball <sup>(RSD)</sup>
- 63 James Derham Demolition <sup>(RSD)</sup>
- 64 James W. Johnson Elementary School Roof <sup>(RSD)</sup>
- 65 New Jean Batiste de Bienville School <sup>(RSD)</sup>
- 66 Jean Gordon Elementary School Demolition <sup>(RSD)</sup>
- 67 John Dibert Elementary School Roof <sup>(RSD)</sup>
- 68 John W. Hoffman Elementary School Demolition <sup>(RSD)</sup>
- 69 John F. Kennedy Modular Relocation (Schwarz Campus) <sup>(RSD)</sup>
- 70 John F. Kennedy Modular Relocation (Coghill Modular Campus) <sup>(RSD)</sup>
- 71 John F. Kennedy Modular Demolition <sup>(RSD)</sup>
- 72 John F. Kennedy High School Demolition <sup>(RSD)</sup>
- 73 John McDonogh Senior High School Bleachers and Sprinklers <sup>(RSD)</sup>
- 74 John McDonogh Senior High School Roof <sup>(RSD)</sup>
- 75 John A. Shaw Elementary School Mothball <sup>(RSD)</sup>
- 76 Joseph S. Clark Senior High School Roof Repairs <sup>(RSD)</sup>
- 77 Joseph A. Craig Elementary Canopies <sup>(RSD)</sup>
- 78 Joseph A. Craig Elementary Elevator Installation <sup>(RSD)</sup>
- 79 Joseph A. Hardin Elementary Security Fencing <sup>(RSD)</sup>
- 80 Lafayette Elementary School Roof and Masonry <sup>(RSD)</sup>
- 81 Lake Area | Landry Demolition <sup>(RSD)</sup>
- 82 Langston Hughes Elementary School (Phase I) <sup>(RSD)</sup>
- 83 Langston Hughes Elementary School - New Gymnasium (Phase II) <sup>(RSD)</sup>
- 84 Langston Hughes Elementary School - Dumpster Pad <sup>(RSD)</sup>
- 85 Lawrence D. Crocker Elementary School Demolition <sup>(RSD)</sup>
- 86 L.B. Landry Annex Demolition <sup>(RSD)</sup>
- 87 Little Woods Elementary School Demolition <sup>(RSD)</sup>

- 88 Little Woods School (Dolores T. Aaron Elementary School) <sup>(RSD)</sup>
- 89 Live Oak Elementary School Roof <sup>(RSD)</sup>
- 90 Live Oak Elementary School Exterior Door Replacement <sup>(RSD)</sup>
- 91 Lorraine Hansberry Elementary School Mothball <sup>(RSD)</sup>
- 92 Louis D. Armstrong Elementary School <sup>(RSD)</sup>
- 93 Mahalia Jackson Elementary School <sup>(OPSB)</sup>
- 94 Mahalia Jackson Elementary School Dumpster / Other Improvements <sup>(OPSB)</sup>
- 95 Mahalia Jackson Elementary School Office Renovation <sup>(OPSB)</sup>
- 96 Martin Behrman Elementary School Roof <sup>(RSD)</sup>
- 97 Martin Luther King Jr. Elementary Canopy System <sup>(RSD)</sup>
- 98 Martin Luther King Jr. School Modular Building, Deck, Canopy <sup>(RSD)</sup>
- 99 Mary Church Terrell Elementary School Demolition <sup>(RSD)</sup>
- 100 Mary M. Bethune Elementary 1st Floor Replacement <sup>(OPSB)</sup>
- 101 Mary M. Bethune Elementary Rear Yard Repair/Resurfacing <sup>(OPSB)</sup>
- 102 McDonogh #7 High School Repairs <sup>(OPSB)</sup>
- 103 McDonogh #15 Elementary Exterior Masonry to SOI Standards <sup>(RSD)</sup>
- 104 McDonogh #28 Elementary School Roof <sup>(RSD)</sup>
- 105 McDonogh #32 Roof Replacement <sup>(RSD)</sup>
- 106 McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium <sup>(OPSB)</sup>
- 107 McDonogh #42 Elementary School Roof <sup>(RSD)</sup>
- 108 McDonogh #42 Elementary School HVAC Replacement <sup>(RSD)</sup>
- 109 Mildred C. Osborne Elementary School Demolition <sup>(RSD)</sup>
- 110 Mildred C. Osborne Elementary School <sup>(RSD)</sup>
- 111 Modular Campuses Close Outs <sup>(RSD)</sup>
- 112 Modular Classroom Demolition at Fannie C. Williams Elementary School <sup>(RSD)</sup>
- 113 Modular Structures at Langston Hughes Elementary School <sup>(RSD)</sup>
- 114 Morris F.X. Jeff Elementary School Demolition <sup>(RSD)</sup>
- 115 Morris F.X. Jeff Elementary School Mothball <sup>(RSD)</sup>
- 116 Murray G. Henderson Elementary School Roof <sup>(RSD)</sup>
- 117 New Andrew H. Wilson Elementary School <sup>(RSD)</sup>
- 118 New Carter G. Woodson School <sup>(RSD)</sup>
- 119 New Fannie C. Williams School <sup>(RSD)</sup>
- 120 New Joseph A. Craig Elementary School <sup>(RSD)</sup>
- 121 New L.B. Landry High School <sup>(RSD)</sup>
- 122 New Lake Area High School <sup>(RSD)</sup>
- 123 New Lawrence D. Crocker School <sup>(RSD)</sup>
- 124 New Parkview School <sup>(RSD)</sup>
- 125 New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens <sup>(RSD)</sup>
- 126 New William Frantz Elementary School <sup>(RSD)</sup>
- 127 New Orleans High School Signature Center Study <sup>(RSD)</sup>
- 128 Oretha C. Haley Demo <sup>(RSD)</sup>
- 129 Oretha C. Haley Elementary School Mothball <sup>(RSD)</sup>
- 130 Parkview Elementary School Demolition <sup>(RSD)</sup>
- 131 Paul L. Dunbar Elementary School Demolition <sup>(RSD)</sup>

- 132 Paul B. Habans Elementary School Roof Repairs <sup>(RSD)</sup>
- 133 Phillis Wheatley Elementary School Demolition <sup>(RSD)</sup>
- 134 Phillis Wheatley Elementary School <sup>(RSD)</sup>
- 135 Robert M. Lusher Elementary Roof Removal & Replacement <sup>(OPSB)</sup>
- 136 Sarah T. Reed High School Bleachers <sup>(RSD)</sup>
- 137 Sarah T. Reed High School Auditorium Wall <sup>(RSD)</sup>
- 138 Seabrook Computer Training Center Demolition <sup>(OPSB)</sup>
- 139 Schaumburg Chillers <sup>(RSD)</sup>
- 140 Schwarz Alternative Repairs <sup>(RSD)</sup>
- 141 Schwarz Alternative Modulars Demolition <sup>(RSD)</sup>
- 142 Sherwood Forest Elementary School Demolition <sup>(RSD)</sup>
- 143 Sophie B. Wright School Selective Demolition <sup>(RSD)</sup>
- 144 Sophie B. Wright Various Repairs/Restroom Renovations <sup>(OPSB)</sup>
- 145 Stuart R. Bradley Elementary School Demolition <sup>(RSD)</sup>
- 146 Sylvanie Williams Elementary School AHU Replacement <sup>(RSD)</sup>
- 147 Sylvanie Williams Elementary School Play Yard <sup>(RSD)</sup>
- 148 Sylvanie Williams Elementary School Roof Repairs <sup>(RSD)</sup>
- 149 Sylvanie Williams Elementary School HVAC/Chiller Replacement <sup>(RSD)</sup>
- 150 Temporary Campus for McDonogh #11 Expropriation <sup>(OPSB)</sup>
- 151 Thomas A. Edison Elementary School Demolition <sup>(RSD)</sup>
- 152 Thomy Lafon Elementary School Demolition <sup>(RSD)</sup>
- 153 Thomy Lafon School Interpretative Display <sup>(RSD)</sup>
- 154 Timbers Park Office Building #1 & #2 Demolition <sup>(OPSB)</sup>
- 155 Timbers HVAC <sup>(OPSB)</sup>
- 156 Timbers III - IT Room Relocation <sup>(OPSB)</sup>
- 157 Village de L'est Elementary School Subsidence <sup>(RSD)</sup>
- 158 Village de L'est Elementary School Roof and Modular Demolition <sup>(RSD)</sup>
- 159 Vorice J. Waters Elementary School Demolition <sup>(RSD)</sup>
- 160 Valena C. Jones Elementary School <sup>(RSD)</sup>
- 161 Walter L. Cohen High School HVAC <sup>(RSD)</sup>
- 162 Warren Easton High School Window Replacement <sup>(OPSB)</sup>
- 163 West Bank Swing Space for Alice Harte Elementary School <sup>(OPSB)</sup>
- 164 New William J. Guste Elementary School <sup>(RSD)</sup>
- 165 William J. Guste Elementary School Science Lab <sup>(RSD)</sup>
- 166 William Frantz Elementary School Environmental Remediation & Selective Demolition <sup>(RSD)</sup>
- 167 William Frantz Elementary School <sup>(RSD)</sup>
- 168 William Frantz Elementary School Roof <sup>(RSD)</sup>
