


# Superintendent's Report November, 2014



**Mr. Stanley C. Smith**  
Orleans Parish School Board



**Mr. John White**  
Louisiana Department of Education  
**Mr. Patrick Dobard**  
Recovery School District

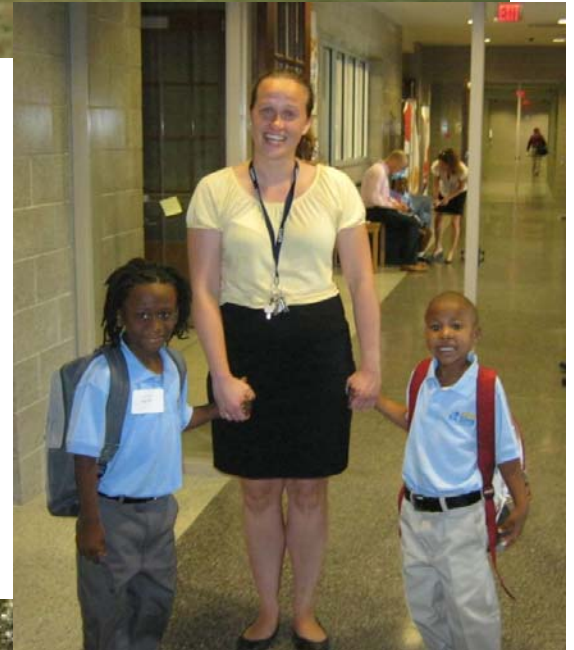

Prepared By





# Table of Contents

Right-Click on the school name to proceed to that page

<b>TABLE OF CONTENTS</b>	1
<b>FINANCIAL OVERVIEW</b>	4
<b>COMMUNITY MEETINGS</b>	5
<b>BID OPENINGS</b>	6
<b>DBE OVERVIEW MONTHLY SUMMARY</b>	7
<b>NEW &amp; MAJOR RENOVATION</b>	11
Ray Abrams Elementary School <sup>(RSD)</sup>	11
Avery Alexander Elementary School <sup>(RSD)</sup>	11
James Audubon School <sup>(OPSB)</sup>	11
Stuart R. Bradley School <sup>(RSD)</sup>	12
George Washington Carver School <sup>(RSD)</sup>	12
Charles R. Drew Elementary School <sup>(RSD)</sup>	12
Paul L. Dunbar School <sup>(RSD)</sup>	13
Fisk-Howard School <sup>(RSD)</sup>	13
Paul B. Habans School <sup>(RSD)</sup>	13
Alice Harte School <sup>(OPSB)</sup>	14
New PK-8 School at North Kenilworth Park at Curran Site <sup>(OPSB)</sup>	14
Lake Forest PK-8 at the Greater St. Stephens Site <sup>(OPSB)</sup>	14
Alfred Lawless School <sup>(RSD)</sup>	15
Edward Livingston High School <sup>(RSD)</sup>	15
John McDonogh High School Selective Demolition <sup>(RSD)</sup>	15
John McDonogh High School Renovation <sup>(RSD)</sup>	16
McDonogh #35 School (Phillip/Waters Site) <sup>(OPSB)</sup>	16
McDonogh #42 Elementary School <sup>(RSD)</sup>	16
Eleanor L. McMain School Gymnasium <sup>(OPSB)</sup>	17
Ernest "Dutch" Morial Elementary School <sup>(RSD)</sup>	17
Small New Orleans East High School at Abramson <sup>(RSD)</sup>	17
Sherwood Forest School <sup>(RSD)</sup>	18
Harriet R. Tubman Elementary School Selective Demolition <sup>(RSD)</sup>	18
Harriet R. Tubman Elementary School Renovation <sup>(RSD)</sup>	18
Booker T. Washington School Environmental Remediation <sup>(RSD)</sup>	19
Booker T. Washington School <sup>(RSD)</sup>	19
Sophie B. Wright School <sup>(RSD)</sup>	19

<b>REFURBISHMENTS</b>	20
Henry Allen Elementary School Refurbishment <sup>(RSD)</sup>	20
Henry Allen Elementary School Kitchen Refurbishment <sup>(RSD)</sup>	20
Benjamin Banneker Elementary Kitchen School Refurbishment <sup>(RSD)</sup>	20
Agnes L. Bauduit Elementary School Refurbishment <sup>(RSD)</sup>	21
Walter L. Cohen High School Kitchen Refurbishment <sup>(RSD)</sup>	21
A. D. Crossman School Kitchen Refurbishment <sup>(RSD)</sup>	21
Frederick A. Douglass High School Science Lab <sup>(RSD)</sup>	22
Warren Easton School Refurbishment <sup>(OPSB)</sup>	22
Dwight D. Eisenhower Elementary School Refurbishment <sup>(RSD)</sup>	22
Dwight D. Eisenhower Elementary School Kitchen Refurbishment <sup>(RSD)</sup>	23
Benjamin Franklin Elementary School Renovation <sup>(OPSB)</sup>	23
William J. Fischer Elementary Refurbishment <sup>(RSD)</sup>	23
Fortier (Lusher) High School Refurbishment <sup>(OPSB)</sup>	24
Gaudet Elementary School Refurbishment <sup>(RSD)</sup>	24
Gentilly Terrace School Refurbishment <sup>(RSD)</sup>	24
Gentilly Terrace School Kitchen Refurbishment <sup>(RSD)</sup>	25
Samuel J. Green Elementary School Refurbishment <sup>(RSD)</sup>	25
Edgar P. Harney Elementary School Refurbishment <sup>(RSD)</sup>	25
Andrew Jackson School Refurbishment <sup>(RSD)</sup>	26
Andrew Jackson School Kitchen Refurbishment <sup>(RSD)</sup>	26
J. W. Johnson Elementary School Refurbishment <sup>(RSD)</sup>	26
Dr. Martin L. King Elementary School Refurbishment <sup>(RSD)</sup>	27
Dr. Martin L. King Elementary School Kitchen Refurbishment <sup>(RSD)</sup>	27
Lafayette Elementary School Refurbishment <sup>(RSD)</sup>	27
Laurel Elementary School Refurbishment <sup>(RSD)</sup>	28
Live Oak Elementary School Refurbishment <sup>(RSD)</sup>	28
Lusher Elementary School Refurbishment <sup>(OPSB)</sup>	28
Thurgood Marshall Elementary School Refurbishment <sup>(RSD)</sup>	29
McDonogh #28 School Refurbishment <sup>(RSD)</sup>	29
McDonogh #28 School Kitchen Refurbishment <sup>(RSD)</sup>	29
McDonogh #32 School Refurbishment <sup>(RSD)</sup>	30
Nelson Elementary School Refurbishment <sup>(OPSB)</sup>	30
Sarah T. Reed School Refurbishment <sup>(RSD)</sup>	30
Sarah T. Reed School Kitchen Refurbishment <sup>(RSD)</sup>	31
Rosenwald Elementary School Refurbishment <sup>(RSD)</sup>	31
Henry C. Schaumburg Elementary School Refurbishment <sup>(RSD)</sup>	31
Village de l'Est Elementary School Refurbishment <sup>(RSD)</sup>	32
Albert Wicker School Kitchen Refurbishment <sup>(RSD)</sup>	32
Sylvanie F. Williams School Refurbishment <sup>(RSD)</sup>	32

<b>OTHER PROJECTS</b>	33
Eleanor L. McMain School Roof Replacement <sup>(OPSB)</sup>	33
Eleanor L. McMain School Maintenance Upgrades <sup>(OPSB)</sup>	33
Timbers III - Building Controls <sup>(OPSB)</sup>	33
Timbers III - IT Room Relocation <sup>(OPSB)</sup>	34
Building Automation System Integration At Recovery School District Central And Remote Offices <sup>(RSD)</sup>	34
 <b>MOTHBALL OR SAFE &amp; SECURE OF SELECTED SCHOOLS</b>	35
Andrew J. Bell Junior High School Shoring and Mothball <sup>(RSD)</sup>	35
Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School <sup>(RSD)</sup>	35
Demolition of Modular Buildings Gregory and Abramson <sup>(RSD)</sup>	35
Demolition of Modulares at Livingston and Schwarz <sup>(RSD)</sup>	36
JoEllen Smith Medical Center Demolition <sup>(OPSB)</sup>	36
 <b>COMPLETED PROJECTS</b>	37

# Overview

## FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$602 million in open contracts for the capital program after issuing \$335 thousand in new contracts and \$1.2 million in change orders and amendments in November. In addition, the total change orders to date, \$7.6 million, account for approximately one percent (1.44%) of the total open construction contracts. RSD anticipates issuing approximately \$85 thousand in construction contracts/change orders, and \$848 thousand in professional service contracts/amendments in December.



The OPSB has \$231 million in open contracts for the capital program after issuing \$352 thousand in new contracts and \$(-84 thousand) in change orders and amendments in November. In addition, the total change orders to date, \$3 million, account for approximately two percent (1.61%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 thousand in construction contracts/change orders and \$492 thousand in professional service contracts/amendments in December.

## Community Meetings



### Future Community Meetings

**January 15, 2015**

Fisk Howard Elementary School Ribbon Cutting  
211 South Lopez Street, New Orleans Louisiana 70119

# Bid Openings

## Bids that were opened in November, 2014

### November 12, 2014

- Edgar P. Harney School Refurbishment

## The following projects are scheduled to bid in the next 60 days:

### December 2, 2014

- Demolition of Caretaker's Cottage at George Mondy Elementary School and Andrew J. Bell Jr. High School
  - Demolition of Modular Buildings at Livingston and Schwarz

### December 10, 2014

- Gregory Modular Demolition and Abramson Modular Demolition
  - Sarah T. Reed School Refurbishment

### December 17, 2014

- Dwight D. Eisenhower School Refurbishment

### January 14, 2014

- Henry Allen School Refurbishment

### January 21, 2014

- Ray Abrams & Ernest "Dutch" Morial Elementary Schools

### January 28, 2014

- Andrew Jackson School Refurbishment
- McDonogh #28 School Refurbishment

### February 4, 2014

- Village de l'Est School Refurbishment
- Avery Alexander Elementary School

### February 11, 2014

- Selective Demolition at John McDonogh High School
- Soil Remediation at Booker T. Washington High School

### February 18, 2014

- Rosenwald Elementary School Refurbishment



# Disadvantaged Business Enterprises (DBE) Monthly Summary

## Recovery School District



### New & Renovations:

DBE Contractors secured subcontracts on 16 projects as of November 30, 2014. The DBE subcontracts value is \$41,110,779 of the \$227,677,077 total of awarded contracts.

### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 22 projects as of November 30, 2014. The DBE subcontracts value is \$6,731,044 of the \$22,827,776 total of awarded contracts.

### Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of November 30, 2014. The DBE subcontracts value is \$37,326,581 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$ 359,642,410

## Orleans Parish School Board

### New & Renovations:


DBE Contractors secured subcontracts on 8 projects as of November 30, 2014. The DBE subcontracts value is \$52,546,433 of the \$193,549,360 total of awarded contracts.

### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of November 30, 2014. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.


Total Amount of Contracts: \$194,452,359

## Current RSD Program DBE Participation

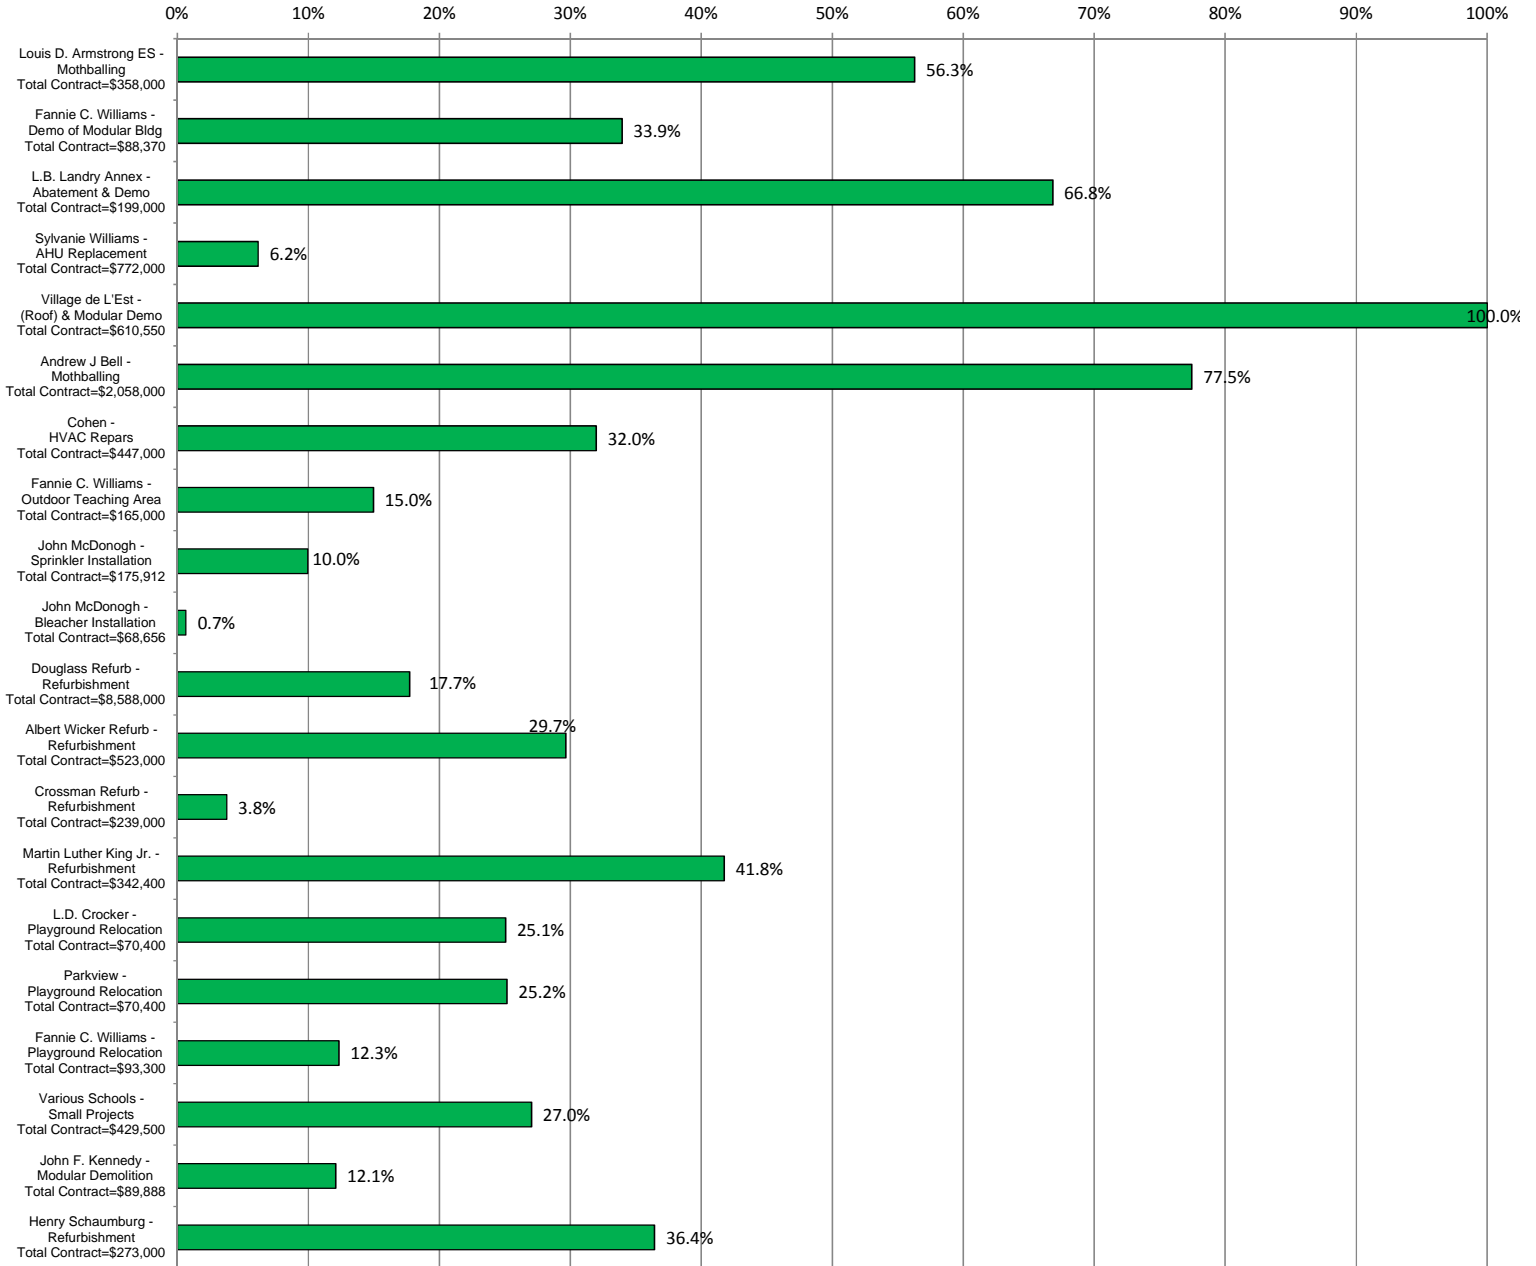


**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

## Current RSD Program DBE Participation

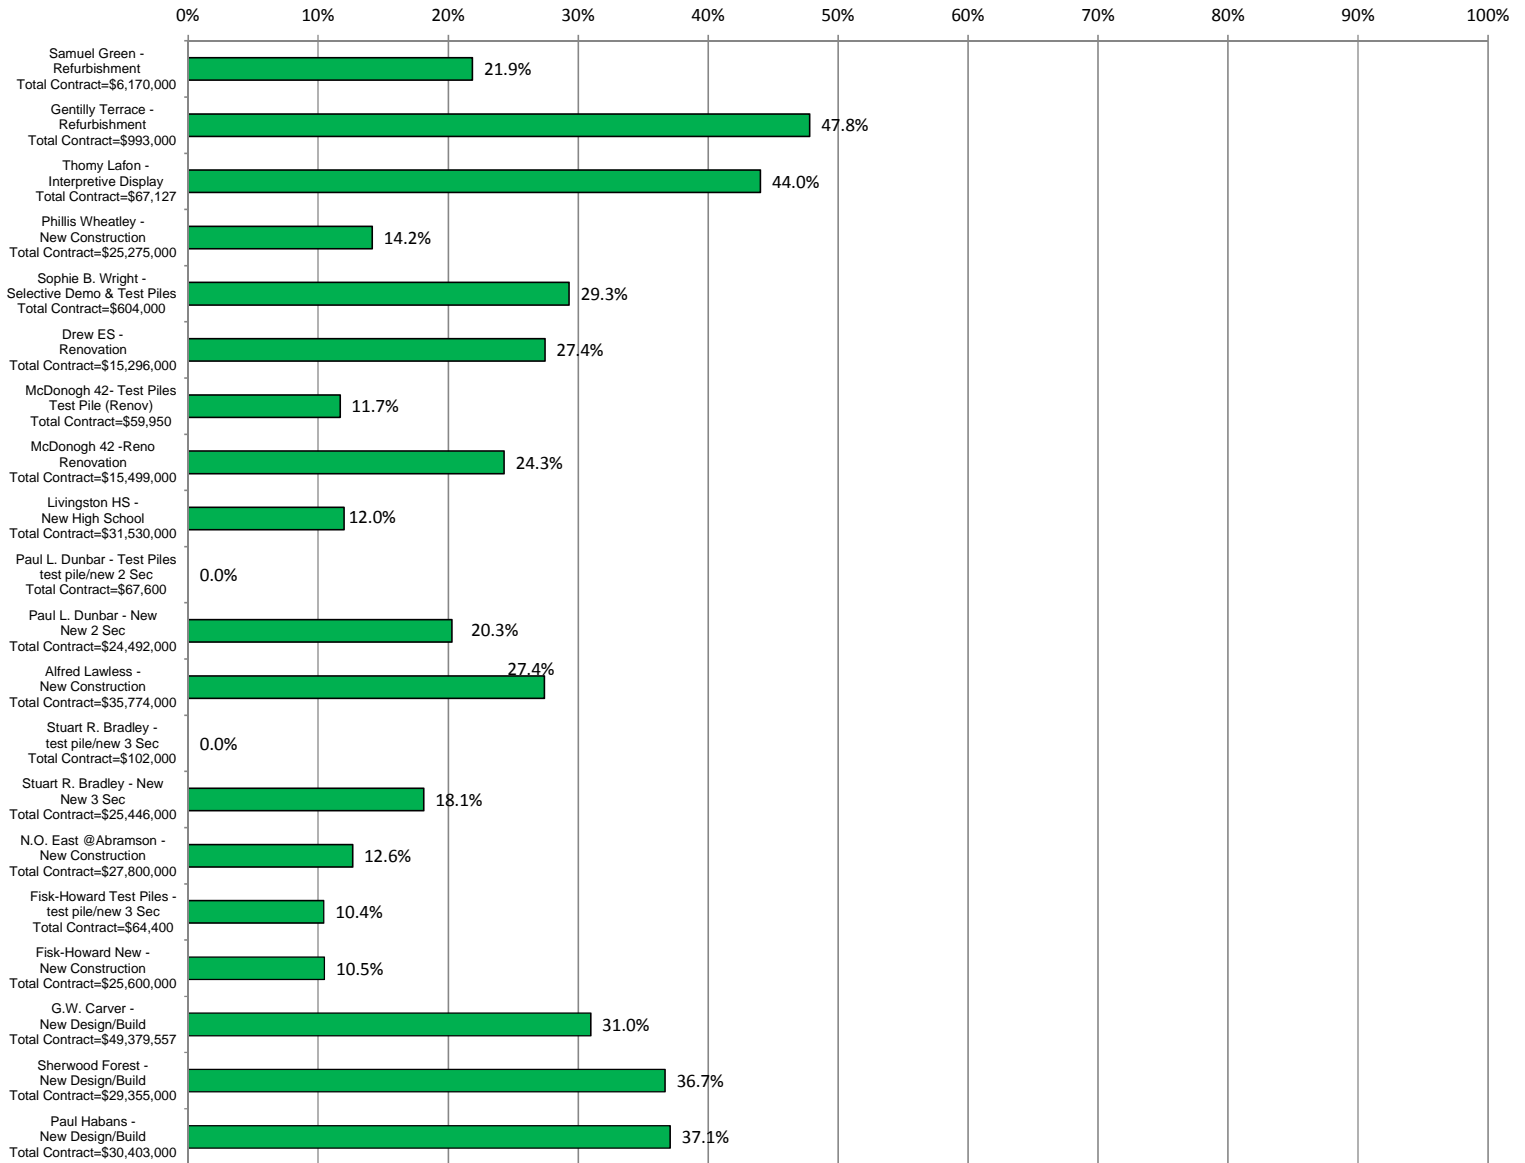

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

### Current OPSB Program DBE Participation

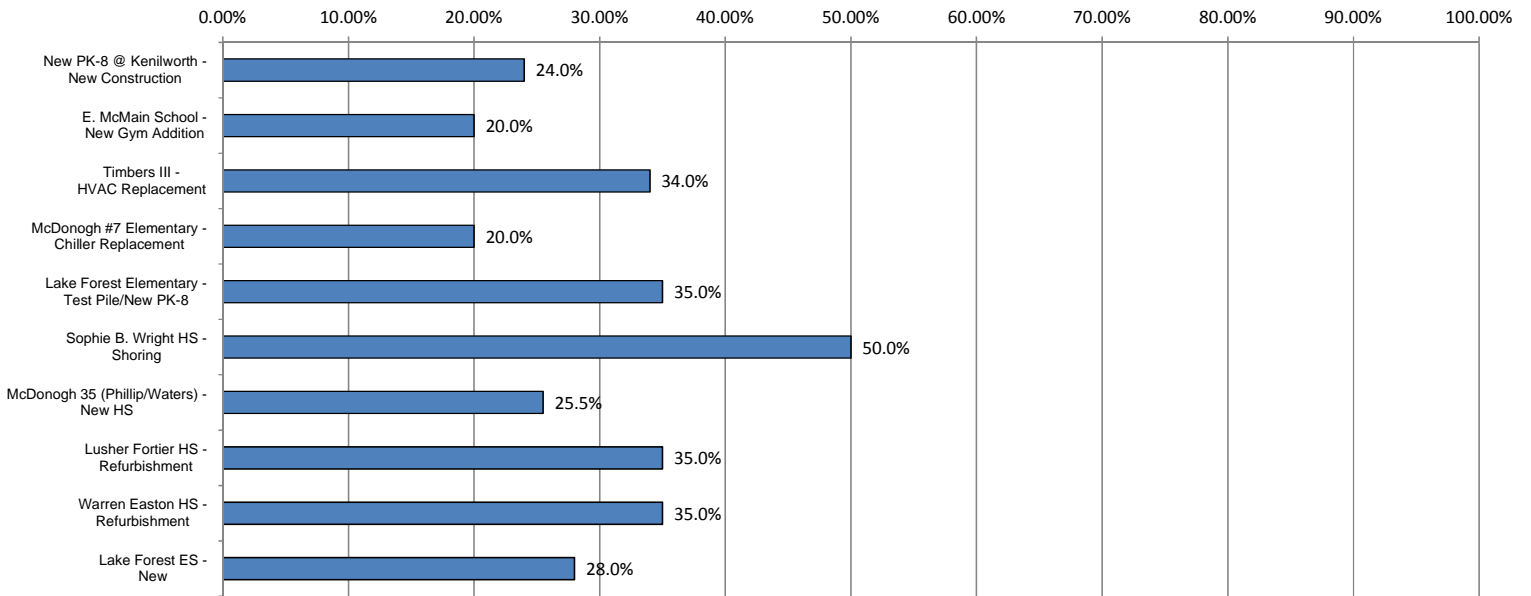

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
 OPSB DBE Participation Target = 35% of Total Contract Amount

## New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

### Ray Abrams Elementary School <sup>(RSD)</sup>

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – TBD

#### Procurement Phase

- Morial and Abrams will be packaged together as (1) project for the procurement process.
- 1st Advertisement – December 17th
- 2nd Advertisement – December 24th
- 3rd Advertisement – December 31st
- Pre-Bid Conference – January 6th
- Bid Opening – January 21st



### Avery Alexander Elementary School <sup>(RSD)</sup>

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – TBD

#### Procurement Phase

- 1st Advertisement – December 31st
- 2nd Advertisement – January 7th
- 3rd Advertisement – January 14th
- Pre-Bid Conference – January 15th
- Bid Opening – February 4th



### James Audubon School <sup>(OPSB)</sup>

428 Broadway Avenue, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation of existing elementary school and new addition

Funding Source – FEMA

Architect – Blich/Knevel Architects

Contractor – FHP Tectonics Corporation


#### Construction Phase

- Phase two & three of the corrective plan is ongoing
- Installation of refurbished windows is nearly complete
- Installation of historic millwork and doors is nearing completion

Contractual Substantial Completion – September 2013

Forecasted Substantial Completion – June 2015

School Ready for Occupancy – June 2015

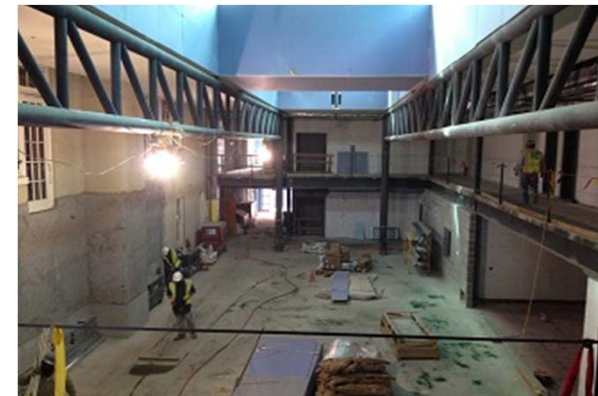

## Stuart R. Bradley School <sup>(RSD)</sup>

2401 Humanity Street, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Landis Construction Co.

### Construction Phase

- Window installation is ongoing
- Installation of brick and concrete masonry units is ongoing
- Installation of interior metal studs is ongoing
- Roof installation his ongoing
- Contractor has started to dehumidified the building

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – May 2015

School Ready for Occupancy – June 2015



## George Washington Carver School <sup>(RSD)</sup>

3059 Higgins Blvd., New Orleans, LA 70126 District E Ward 9

Scope of work: New High School, Design Build

Funding Source – FEMA

Contractor – Broadmoor LLC

### Construction Phase

- Pile caps are complete
- Grade beam pours are ongoing
- Pouring of slabs has started
- Precast mock up will be installed mid December

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



## Charles R. Drew Elementary School <sup>(RSD)</sup>

3819 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Blich / Knevel Architects, Inc.

Contractor – Core Construction

### Construction Phase

- Installation of metal studs and gypsum board continues
- Courtyard area was poured
- Window refurbishment is ongoing
- Tiling of restrooms continues

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – March 2015

School Ready for Occupancy – June 2015



## Paul L. Dunbar School <sup>(RSD)</sup>

9330 Forshey Street, New Orleans, LA 70125 District A Ward 17

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor – McDonnell Group, LLC

### Construction Phase

- Subsurface drainage work continues
- Installation of CMU and metal studs is ongoing
- Brick and cast stone installation is ongoing
- MEP installation continues
- Roof installation is ongoing

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – May 2015

School Ready for Occupancy – June 2015



## Fisk-Howard School <sup>(RSD)</sup>

211 South Lopez Street, New Orleans, LA 70119 District B Ward 3

Scope of work: New Pre-K – 8 School

Funding Source - FEMA

Architect - VergesRome Architects+Fanning Howey

Contractor – FHP Tectonics Corporation


### Construction Phase

- Installation of interior finishes is nearing completion
- Punch list work has started
- Site work is ongoing
- Anticipated Substantial Completion December 12th

Contractual Substantial Completion – December 2014

Forecasted Substantial Completion – December 2014

School Ready for Occupancy – January 2015

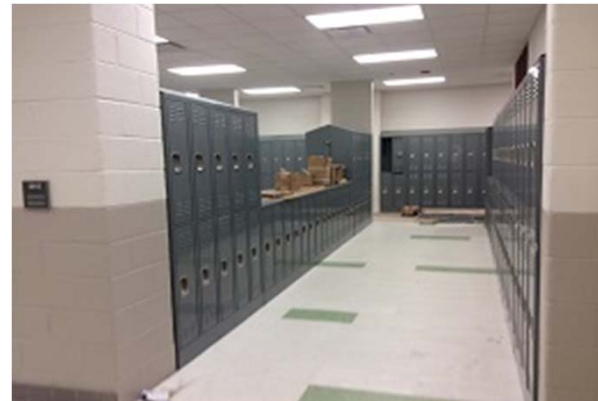

## Paul B. Habans School <sup>(RSD)</sup>

3501 Siene Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

### Construction Phase

- Clearing and grubbing of site is ongoing
- Work continues on the building pad
- Pile driving is scheduled to begin mid December

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



## Alice Harte School (OPSB)

5300 Berkley Drive, New Orleans, La 70131 District C Ward 15

Scope of work: New Pre-K – 8 School

Funding Source – CDBG & FEMA

Architect – WDG Architects Engineers

Contractor – Woodrow Wilson Construction Company, Inc.

### Construction Phase

- Commissioning is ongoing
- Substantial Completion November 19th
- School moved into building December 3rd

Contractual Substantial Completion – January 2014

Forecasted Substantial Completion – November 18, 2104

School Ready for Occupancy – November 2014



## New PK-8 School at North Kenilworth Park at Curran Site (OPSB)

8500 Curran Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Mathes Brierre Architects

Contractor – Woodrow Wilson Construction Company, Inc.

### Construction Phase

- MEP work is ongoing
- Finishes and quarry tile installation is ongoing
- Gypsum board and metal stud installation is ongoing
- Site work including sidewalks is 25% complete
- Installation of windows is nearly complete

Contractual Substantial Completion – September 2014

Forecasted Substantial Completion – March 2015

School Ready for Occupancy – July 2015



## Lake Forest PK-8 at the Greater St. Stephens Site (OPSB)

11110 Lake Forest Boulevard 70128 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Imre Hegedus & Associates Architects

Contractor – The McDonnel Group

### Construction Phase

- MEP rough-in is ongoing
- Exterior concrete masonry is complete at assembly areas
- Roof deck installation is complete
- Site work is ongoing

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015

School Ready for Occupancy – August 2015





## Alfred Lawless School (RSD)

5300 Law Street, New Orleans, LA 70117 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

### Construction Phase

- Installation of site utilities is ongoing
- Roof installation & waterproofing is ongoing
- Installation of concrete masonry is complete
- Exterior brick work has started
- Electric and HVAC rough-in continues

Contractual Substantial Completion – November 2015

Forecasted Substantial Completion – November 2015

School Ready for Occupancy – January 2016



## Edward Livingston High School (RSD)

7301 Dwyer Road, New Orleans, LA 70126 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

### Construction Phase

- Commissioning has started
- Landscaping and final grading ongoing

Contractual Substantial Completion – February 2015

Forecasted Substantial Completion – December 2014

School Ready for Occupancy – June 2015



## John McDonogh High School Selective Demolition (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

### Procurement Phase

- 1st Advertisement – December 7th
- 2nd Advertisement – December 14th
- 3rd Advertisement – December 21st
- Pre-Bid Conference – December 22nd
- Bid Opening – January 11th



## John McDonogh High School Renovation <sup>(RSD)</sup>

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

### Design Phase - SD

- Program Completion Documents were received November 14th
- Schematic Design Documents are due January 16th

### Procurement Phase

- Procurement schedule dependent on Selective Demolition completion
- Anticipated 1st Advertisement – 3rd Quarter 2015
- Anticipated Bid Opening – 4th Quarter 2015



## McDonogh #35 School (Phillip/Waters Site) <sup>(OPSB)</sup>

1200 Senate Street, New Orleans, LA 70122 District D Ward 7

Scope of work: New High School

Funding Source – FEMA

Architect – Sizeler, Thompson, Brown Architects

Contractor – Citadel Builders, LLC

### Construction Phase

- Installation of CMU walls is ongoing
- Installation of MEP is ongoing
- Brick masonry and window installation continues
- Drywall installation continues in north and south classroom buildings
- Metal panel installation continues

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – May 2015

School Ready for Occupancy – June 2015



## McDonogh #42 Elementary School <sup>(RSD)</sup>

1651 North Tonti Street, New Orleans, LA 70119 District A Ward 7

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA, QSCB, NMTC, Insurance Proceeds

Architect – Eskew+Dumez+Ripple

Contractor – Core Construction

### Construction Phase

- Refurbishment of windows continues
- Ceiling grid on 2nd & 3rd floors ongoing
- Curtain wall and storefront are being installed
- Painting ongoing
- Doors are being hung

Contractual Substantial Completion – June 2015

Forecasted Substantial Completion – May 2015

School Ready for Occupancy – August 2015



## Eleanor L. McMain School Gymnasium <sup>(OPSB)</sup>

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: A new gym will be added to the site with a connecting breezeway to the main building.

Funding Source – FEMA

Architect – Jahncke & Burns Architects

Contractor – Ellis Construction

### Construction Phase

- Interior & exterior masonry installation continues
- Roof decking installation is ongoing
- Structural steel installation is complete
- MEP rough-in is ongoing

Contractual Substantial Completion – April 2015

Forecasted Substantial Completion – April 2015



## Ernest "Dutch" Morial Elementary School <sup>(RSD)</sup>

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – TBD

### Procurement Phase

- Morial and Abrams will be packaged together as (1) project for the procurement process.
- 1st Advertisement – December 17th
- 2nd Advertisement – December 24th
- 3rd Advertisement – December 31st
- Pre-Bid Conference – January 6th
- Bid Opening – January 21st



## Small New Orleans East High School at Abramson <sup>(RSD)</sup>

5552 Read Boulevard, New Orleans, LA 70127 District E Ward 9

Scope of work: New High School

Funding Source – FEMA

Architect – RozasWard / a.i.a. architects, Inc.

Contractor – Gibbs Construction

### Construction Phase

- Masonry installation continues
- Structural steel erection is complete
- Installation of site utilities is ongoing
- MEP rough-in continues
- Waterproofing and roof installation ongoing

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015

School Ready for Occupancy – November 2015



## Sherwood Forest School <sup>(RSD)</sup>

4801 Maid Marion Drive, New Orleans, LA 70128 District E Ward 9

Scope of work: New School, Design Build

Funding Source – FEMA

Architect – Grace Hebert

Contractor – Core Construction

### Construction Phase

- 100% Construction Documents were received December 1st
- Foundation package was submitted to the City of New Orleans
- Building pad has been cut
- Pile driving is scheduled to start early December

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



## Harriet R. Tubman Elementary School Selective Demolition <sup>(RSD)</sup>

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Exploratory and selective demolition of the existing school

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Insulation Technologies

### Construction Phase

- Demolition is 90% complete
- Added scope of work to extend time

Contractual Substantial Completion – December 2014

Forecasted Substantial Completion – January 2015



## Harriet R. Tubman Elementary School Renovation <sup>(RSD)</sup>

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

### Design Phase - DD

- Design Development submittal due January 22, 2015
- 50% Construction Documents due March 19, 2015

### Procurement Phase

- Anticipated 1st Advertisement – June 2015
- Anticipated Bid Opening – August 2015



## **Booker T. Washington School Environmental Remediation** (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The remediation of the site

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – TBD

### Procurement Phase

- 1st Advertisement – January 7th
- 2nd Advertisement – January 14th
- 3rd Advertisement – January 21st
- Pre-Bid Conference – January 22nd
- Bid Opening – February 11th



## **Booker T. Washington School** (RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – TBD

### Design Phase - CD

- Procurement will be delayed until Environmental concerns have been addressed

### Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



## **Sophie B. Wright High School Renovation** (RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Renovation of existing school and gymnasium addition

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – Core Construction

### Construction Phase

- Removal of windows is ongoing
- Interior wall demolition has started

Contractual Substantial Completion – May 2016

Forecasted Substantial Completion – May 2016



## REFURBISHMENTS

### Henry Allen Elementary School Refurbishment <sup>(RSD)</sup>

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

#### Procurement Phase

- 1st Advertisement – December 10th
- 2nd Advertisement – December 17th
- 3rd Advertisement – December 24th
- Pre-Bid Conference – December 30th
- Bid Opening – January 14th



### Henry Allen Elementary School Kitchen Refurbishment <sup>(RSD)</sup>

5626 Loyola Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

#### Design Phase - CD

- 100% Construction Documents are due December 15th

#### Procurement Phase

- Anticipated 1st Advertisement – February 2015
- Anticipated Bid Opening – March 2015



### Benjamin Banneker Elementary School Kitchen Refurbishment <sup>(RSD)</sup>

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

#### Design Phase - CD

- 100% Construction Documents are due December 20th
- Procurement schedule has been adjusted pending FEMA funding approval

#### Procurement Phase

- Anticipated 1st Advertisement – March 2015
- Anticipated Bid Opening – April 2015



## **Agnes L. Bauduit Elementary School Refurbishment** <sup>(RSD)</sup>

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor - TBD

### Design Phase - CD

- Bid Documents are being adjusted to include an alternate for the windows
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – June 2015
- Anticipated Bid Opening – July 2015



## **Walter L. Cohen High School Kitchen Refurbishment** <sup>(RSD)</sup>

3520 Dryades, New Orleans Street, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents are due December 15th
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – March 2015
- Anticipated Bid Opening – April 2015



## **A. D. Crossman School Kitchen Refurbishment** <sup>(RSD)</sup>

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents are due December 20th

### Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – March 2015



## Frederick A. Douglass High School Science Lab <sup>(RSD)</sup>

3820 St. Claude Avenue, New Orleans, LA 70117 District C Ward 9

Scope of work: Renovations to science lab

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

### Design Phase - CD

- 50% Construction Documents were received November 24th
- Added elevator scope will delay Construction Documents
- 100% Construction Documents are due January 21st

### Procurement Phase

- Anticipated 1st Advertisement – April 2015
- Anticipated Bid Opening – May 2015

## Warren Easton School <sup>(OPSB)</sup>

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Refurbishment of existing high school, including but not limited to structure, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - Tuna Construction

### Construction Phase

- Work has begun in the classrooms
- Installation of emergency lighting is ongoing
- Radiator repairs have started

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



## Dwight D. Eisenhower Elementary School Refurbishment <sup>(RSD)</sup>

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Harry Baker Smith Architects II, PLLC

Contractor - TBD

### Procurement Phase

- 1st Advertisement – November 12th
- 2nd Advertisement – November 19th
- 3rd Advertisement – November 26th
- Pre-Bid Conference – December 2nd
- Bid Opening – December 17th





## Dwight D. Eisenhower Elementary School Kitchen Refurbishment <sup>(RSD)</sup>

3700 Tall Pines Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are due December 15th

Procurement Phase

- Anticipated 1st Advertisement – February 2015
- Anticipated Bid Opening – March 2015



## Benjamin Franklin Elementary School Renovation <sup>(OPSB)</sup>

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - SD

- Program Completion Documents were received November 19th
- Schematic Design Documents are due December 15th

Procurement Phase

- Anticipated 1st Advertisement – March 2015
- Anticipated Bid Opening – April 2015



## William J. Fischer Elementary School Refurbishment <sup>(RSD)</sup>

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are due December 27th
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



## Fortier (Lusher) High School Refurbishment <sup>(OPSB)</sup>

5624 Freret Street, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation and repairs to the roof, masonry, plaster, windows, exterior doors, canopies, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Core Construction

### Construction Phase

- Mechanical and electrical demolition is ongoing
- Window mock-up will be complete mid December
- Plaster repair has started
- Asbestos remediation will take place over the break

Contractual Substantial Completion – March 2016

Forecasted Substantial Completion – March 2016



## Gaudet Elementary School Refurbishment <sup>(RSD)</sup>

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - CD

- 50% Construction Documents were received November 11th
- 100% Construction Documents are due December 28th
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



## Gentilly Terrace School Refurbishment <sup>(RSD)</sup>

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - One Construction

### Construction Phase

- Floor demolition is ongoing

Contractual Substantial Completion – May 2015

Forecasted Substantial Completion – May 2015



## **Gentilly Terrace School Kitchen Refurbishment <sup>(RSD)</sup>**

4720 Painters Street, New Orleans, LA 70122 District D Ward 8

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 50% Construction Documents were received October 6th
- 100% Construction Documents are due December 20th

Procurement Phase

- Anticipated 1st Advertisement – January 2015
- Anticipated Bid Opening – March 2015



## **Samuel J. Green Elementary School Refurbishment <sup>(RSD)</sup>**

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Hernandez Consulting, LLC

Construction Phase

- Demolition of restrooms is ongoing
- Rough in of fire suppression has started
- Electrical and plumbing renovations have started

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015



## **Edgar P. Harney Elementary School Refurbishment <sup>(RSD)</sup>**

2503 Willow Street, New Orleans, LA 70113 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Hamilton Anderson Associates

Contractor - Hamp's Construction, LLC

Procurement Phase

- Contracts are being reviewed



## Andrew Jackson School Refurbishment <sup>(RSD)</sup>

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Procurement Phase

- 1st Advertisement – December 24th
- 2nd Advertisement – December 31st
- 3rd Advertisement – January 7th
- Pre-Bid Conference – January 8th
- Bid Opening – January 28th



## Andrew Jackson School Kitchen Refurbishment <sup>(RSD)</sup>

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents are due December 15th
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – March 2015
- Anticipated Bid Opening – April 2015



## J. W. Johnson Elementary School Refurbishment <sup>(RSD)</sup>

1800 Monroe Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents are due December 27th
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



## Dr. Martin L. King Elementary School Refurbishment (RSD)

1617 Caffin Avenue, New Orleans, LA 70117 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Hamp's Construction, LLC

### Construction

- Anticipated Substantial Completion - December 15th

Contractual Substantial Completion – December 2014

Forecasted Substantial Completion – December 2014



## Dr. Martin L. King Elementary School Kitchen Refurbishment (RSD)

1617 Caffin Avenue, New Orleans, LA 70117 District E Ward 9

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents are due December 15th

### Procurement Phase

- Anticipated 1st Advertisement – February 2015
- Anticipated Bid Opening – March 2015



## Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

### Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – March 2014
- Anticipated Bid Opening – April 2015



## Laurel Elementary School Refurbishment <sup>(RSD)</sup>

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

### Design Phase - CD

- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – June 2015
- Anticipated Bid Opening – July 2015



## Live Oak Elementary School Refurbishment <sup>(RSD)</sup>

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

### Design Phase - CD

- 100% Construction Documents are complete
- Procurement schedule has been adjusted pending FEMA funding approval

### Procurement Phase

- Anticipated 1st Advertisement – April 2015
- Anticipated Bid Opening – May 2015



## Lusher Elementary School Refurbishment <sup>(OPSB)</sup>

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source – FEMA

Architect – Meyer Engineers, LTD.

Contractor - TBD

### Procurement Phase

- 1st Advertisement – December 17th
- 2nd Advertisement – December 24th
- 3rd Advertisement – December 31st
- Pre-Bid Conference – January 5th
- Bid Opening – January 21st



## Thurgood Marshall Elementary School Refurbishment <sup>(RSD)</sup>

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - PC

- Program Completion Documents are due December 15th
- Schematic Design Documents are due January 29th

Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



## McDonogh #28 School Refurbishment <sup>(RSD)</sup>

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects, LLC

Contractor - TBD

Design Phase – CD

- Bid Documents are due December 9th
- Procurement will be delayed so that installation of windows will commence during summer break

Procurement Phase

- Anticipated 1st Advertisement – December 2014
- Anticipated Bid Opening – January 2015



## McDonogh #28 School Kitchen Refurbishment <sup>(RSD)</sup>

2733 Esplanade Avenue, New Orleans, LA 70119 District A Ward 7

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are due December 20th
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – March 2015
- Anticipated Bid Opening – April 2015



### **McDonogh #32 School Refurbishment (RSD)**

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – September 2015
- Anticipated Bid Opening – October 2015



### **Nelson Elementary School Refurbishment (OPSB)**

3121 St. Bernard Avenue, New Orleans, LA 70119 District D Ward 7

Scope of work: Renovation and repairs to the roof, masonry, windows, exterior doors, mechanical systems, and electrical systems.

Funding Source – FEMA

Architect – Harry Baker Smith Architects

Contractor - TBD

Design Phase - CD

- Bid Documents are due December 10th

Procurement Phase

- Anticipated 1st Advertisement – December 2014
- Anticipated Bid Opening – February 2015



### **Sarah T. Reed School Refurbishment (RSD)**

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Procurement Phase

- 1st Advertisement – November 5th
- 2nd Advertisement – November 12th
- 3rd Advertisement – November 19th
- Pre-Bid Conference – November 20th
- Bid Opening – December 10th





## **Sarah T. Reed School Kitchen Refurbishment <sup>(RSD)</sup>**

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are due December 15th

Procurement Phase

- Anticipated 1st Advertisement – February 2015
- Anticipated Bid Opening – March 2015



## **Rosenwald Elementary School Refurbishment <sup>(RSD)</sup>**

6501 Berkley Drive, New Orleans, LA 70131 District C Ward 15

Scope of work: Refurbishment of existing high school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- 100% Construction Documents are due December 12th

Procurement Phase

- 1st Advertisement – January 14th
- 2nd Advertisement – January 21st
- 3rd Advertisement – January 28th
- Pre-Bid Conference – January 29th
- Bid Opening – February 18th



## **Henry C. Schaumburg Elementary School <sup>(RSD)</sup>**

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc

Contractor - Hernandez Consulting, LLC

Construction Phase

- Electrical work has started

Contractual Substantial Completion – July 2015

Forecasted Substantial Completion – July 2015



## Village de l'Est Elementary School Refurbishment <sup>(RSD)</sup>

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CBDG

Architect – Duplantis Design Group, PC

Contractor - TBD

Design Phase - CD

- 100% Construction Documents were received November 17th

Procurement Phase

- Anticipated 1st Advertisement – December 2014
- Anticipated Bid Opening – February 2015



## Albert Wicker School Kitchen Refurbishment <sup>(RSD)</sup>

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Design Phase - CD

- 100% Construction Documents are due December 20th
- Procurement schedule has been adjusted pending FEMA funding approval

Procurement Phase

- Anticipated 1st Advertisement – March 2015
- Anticipated Bid Opening – April 2015



## Sylvanie F. Williams School Refurbishment <sup>(RSD)</sup>

3127 Martin Luther King Jr. Boulevard, New Orleans, LA 70125 District B Ward 2

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Hamps

Construction Phase

- Abatement of window caulk has been completed
- Plumbing has started

Contractual Substantial Completion – August 2015

Forecasted Substantial Completion – August 2015



## OTHER PROJECTS

### **Eleanor L. McMain School Roof Replacement** (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Roof replacement

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – TBD

Design Phase - PC

- Program Completion Documents are due December 8th

Procurement Phase

- Anticipated 1st Advertisement – May 2015
- Anticipated Bid Opening – June 2015

### **Eleanor L. McMain School Maintenance Upgrades** (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work.

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – TBD

Design Phase - PC

- Program Completion Documents are due December 8th

Procurement Phase

- Anticipated 1st Advertisement – May 2015
- Anticipated Bid Opening – June 2015

### **Timbers III - Building Controls** (OPSB)

3520 General DeGaulle Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: Design and installation of new building controls

Funding Source – OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - PC

- Owner has placed project on hold

Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



## Timbers III - IT Room Relocation (OPSB)

3520 General DeGaulle Drive, New Orleans, LA 70114 District C Ward 15

Scope of work: Relocation of the Information Technology Room

Funding Source – OPSB General Fund

Architect – N-Y Associates, Inc.

Contractor - Huda, LLC

### Construction Phase

- Contractor has mobilized
- Submittals are being reviewed
- Demolition has started



## Building Automation System Integration At Recovery School

Various Addresses

Scope of work: Implementation of a Central Remote Building Automation System that integrates the existing Building Automation Systems of the 4 Quick Start Schools (Andrew H. Wilson ES, Langston Hughes ES, L.B. Landry HS, and Lake Area HS) and Joseph A. Craig ES into a central remote monitoring workstation that will include Fannie C. Williams ES, Lawrence D. Crocker ES, Mildred Osborne ES, William Frantz ES, Bienville ES, Charles J. Colton ES, Carter G. Woodson ES and Parkview ES

Funding Source – FEMA

Architect – Moses Engineers

Contractor – Synergy Building Solutions, Inc.

### Construction Phase

- The five Quick Start Schools are complete, the Energy Dash Board is being implemented
- Sylvanie Williams Elementary School, Sarah T. Reed Elementary School, Fannie C. Williams Elementary School, Bienville Elementary School, Charles L. Colton Elementary School, William Frantz Elementary School, Parkview Elementary School, Osborne Elementary School, Carter G. Woodson Elementary School, Walter Cohen High School, Dolores T Aaron Elementary School, and Albert Wicker Elementary School are complete
- New integration work is ongoing at A. D. Crossman Elementary School, and Benjamin Banneker Elementary School
- Integration has started at Lawrence D. Crocker Elementary School

Contractual Substantial Completion – January 2015

Forecasted Substantial Completion – January 2015



# MOTHBALL OR SAFE AND SECURE OF SELECTED SCHOOLS

## Andrew J. Bell Junior High School Mothball <sup>(RSD)</sup>

1010 N. Galvez St., New Orleans, LA 70119 District D Ward 6

Scope of work: Design Services to assist in determining the condition of the facilities both interior and exterior, make recommendations to stabilize the facilities and provide drawings required to provide a water barrier, ventilation, and rudimentary fire detection and to secure openings and entryways. Construction Services to stabilize the facility according to the designer's drawings and specifications.

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – CDW Services, LLC

Mothballing of Closed Schools - Safe & Secure

- Mothballing of the Gymnasium, Administration Building, Annex, Building "C", Building "D", Chapel, & E.A.Christy Building

Construction Phase

- Structural roof repairs on the Christy building will extend the project timeline

Contractual Substantial Completion – May 2014

Forecasted Substantial Completion – January 2015



## Demolition of Caretakers Cottage at George Mondy School and Andrew J. Bell School <sup>(RSD)</sup>

1010 N. Galvez St. & 2327 St. Philip Street, New Orleans, LA 70119 District D Ward 6

Scope of work: Demolition of existing caretakers cottages

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

Procurement Phase

- 1st Advertisement – October 29th
- 2nd Advertisement – November 5th
- 3rd Advertisement – November 12th
- Pre-Bid Conference – November 13th
- Bid Opening – December 2nd



## Demolition of Modular Buildings at Gregory and Abramson <sup>(RSD)</sup>

1700 Pratt Drive & 5552 Read Boulevard, New Orleans, LA District D Ward 7 & District E Ward 9

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Holly & Smith Architects

Contractor – TBD

Procurement Phase

- 1st Advertisement – November 5th
- 2nd Advertisement – November 12th
- 3rd Advertisement – November 19th
- Pre-Bid Conference – November 20th
- Bid Opening – December 10th



## Demolition of Modular Buildings at Livingston and Schwarz <sup>(RSD)</sup>

7301 Dwyer Road & 709 Park Boulevard, New Orleans, LA District E Ward 9 & District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – TBD

### Procurement Phase

- 1st Advertisement – October 29th
- 2nd Advertisement – November 5th
- 3rd Advertisement – November 12th
- Pre-Bid Conference – November 13th
- Bid Opening – December 2nd



## JoEllen Smith Medical Center Demolition <sup>(OPSB)</sup>

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – TBD

### Design Phase - CD

- Bid Documents are due Dec 31st
- School Board is reviewing the increase in the AFC

### Procurement Phase

- Anticipated 1st Advertisement – TBD
- Anticipated Bid Opening – TBD



## Comprehensive List - Completed Projects

- 1 Abrams | Morial | Abramson | Coghill Demolition <sup>(RSD)</sup>
- 2 A. D. Cross Elementary School Energy Conservation <sup>(RSD)</sup>
- 3 A. D. Crossman Elementary School and Benjamin Banneker Elementary School <sup>(RSD)</sup>
- 4 A. D. Crossman Elementary School Refurbishment <sup>(RSD)</sup>
- 5 A. P. Tureaud Elementary School Roof Repairs <sup>(RSD)</sup>
- 6 Agnes Bauduit Elementary School Boiler <sup>(RSD)</sup>
- 7 Albert Wicker Elementary School Refurbishment <sup>(RSD)</sup>
- 8 Albert Wicker Elementary School Roof Repairs <sup>(RSD)</sup>
- 9 Alfred Lawless Senior High Security Fencing <sup>(RSD)</sup>
- 10 Alice M. Harte Elementary School Demolition <sup>(OPSB)</sup>
- 11 Andrew J. Bell Junior High School Roof Replacement <sup>(RSD)</sup>
- 12 Andrew Jackson Elementary School Roof Repairs <sup>(RSD)</sup>
- 13 Andrew Jackson Elementary School Solar Panels <sup>(RSD)</sup>
- 14 Andrew H. Wilson Elementary School Cottage <sup>(RSD)</sup>
- 15 Arthur Ashe Elementary School Kitchen Renovation <sup>(OPSB)</sup>
- 16 Augustine Elementary School Roof <sup>(RSD)</sup>
- 17 Avery-Alexander Elementary School Demolition <sup>(RSD)</sup>
- 18 Barbara C. Jordan Elementary School Demolition <sup>(RSD)</sup>
- 19 Bell JH Shoring <sup>(RSD)</sup>
- 20 Benjamin Banneker Elementary School Energy Conservation <sup>(RSD)</sup>
- 21 Benjamin Franklin Senior High School <sup>(OPSB)</sup>
- 22 Bienville Elementary School Demolition <sup>(RSD)</sup>
- 23 Booker T. Washington High School Partial Demolition <sup>(RSD)</sup>
- 24 Carter G. Woodson Middle School Demolition <sup>(RSD)</sup>
- 25 Central Services Warehouse Demolition <sup>(OPSB)</sup>
- 26 Charles J. Colton Elementary Selective Demolition <sup>(RSD)</sup>
- 27 Charles J. Colton Elementary School <sup>(RSD)</sup>
- 28 Charles R. Drew Elementary Roof & Installation of Kitchen Hood <sup>(RSD)</sup>
- 29 Cohen High School Health Clinic <sup>(RSD)</sup>
- 30 Douglass High School Under Floor Utilities <sup>(RSD)</sup>
- 31 Dr. Martin Luther King School Roof Repairs <sup>(RSD)</sup>
- 32 Dr. Martin Luther King Jr. School Renovation <sup>(RSD)</sup>
- 33 Dwight D. Eisenhower Elementary School Roof Repairs <sup>(RSD)</sup>
- 34 East Bank Swing Space for Audubon Charter School <sup>(OPSB)</sup>
- 35 Edgar P. Harney Elementary School Roof Repairs <sup>(RSD)</sup>
- 36 Edna Karr High School - Gymnasium Repair <sup>(OPSB)</sup>
- 37 Edna Karr High School - Assessment <sup>(OPSB)</sup>
- 38 Edward Livingston Middle School Demolition <sup>(RSD)</sup>
- 39 Edward Henry Phillips Junior High School Demolition <sup>(OPSB)</sup>
- 40 New Edward Hynes School <sup>(OPSB)</sup>
- 41 Edwards | Hardin | Lockett | Lawless Demolition <sup>(RSD)</sup>
- 42 Eleanor L. McMains School Replacement of Existing Chillers <sup>(OPSB)</sup>

- 43 Eleanor L. McMain School Clinic <sup>(OPSB)</sup>
- 44 Ernest N. Morial Elementary Security Fencing <sup>(RSD)</sup>
- 45 Fannie C. Williams Elementary School Demolition <sup>(RSD)</sup>
- 46 Fisk-Howard Elementary School Demolition <sup>(RSD)</sup>
- 47 Florence J. Chester Elementary School Demolition <sup>(RSD)</sup>
- 48 Francis W. Gregory Demolition <sup>(RSD)</sup>
- 49 Frederick A. Douglass High Refurbishment <sup>(RSD)</sup>
- 50 Frederick A. Douglass High Switchgear <sup>(RSD)</sup>
- 51 Frederick A. Douglass High Emergency Boiler Roof Repairs <sup>(RSD)</sup>
- 52 George Mondy Elementary School Mothball <sup>(RSD)</sup>
- 53 George Washington Carver High School Demolition <sup>(RSD)</sup>
- 54 Greater St. Stephens School <sup>(OPSB)</sup>
- 55 Henry Allen Elementary School Roof <sup>(RSD)</sup>
- 56 Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation <sup>(RSD)</sup>
- 57 Holy Cross Modular Relocation <sup>(RSD)</sup>
- 58 Israel M. Augustine Middle School Roof Replacement <sup>(RSD)</sup>
- 59 Israel M. Augustine Middle School Mothball <sup>(RSD)</sup>
- 60 James Derham Demolition <sup>(RSD)</sup>
- 61 James W. Johnson Elementary School Roof <sup>(RSD)</sup>
- 62 New Jean Batiste de Bienville School <sup>(RSD)</sup>
- 63 Jean Gordon Elementary School Demolition <sup>(RSD)</sup>
- 64 John Dibert Elementary School Roof <sup>(RSD)</sup>
- 65 John W. Hoffman Elementary School Demolition <sup>(RSD)</sup>
- 66 John F. Kennedy Modular Relocation (Schwarz Campus) <sup>(RSD)</sup>
- 67 John F. Kennedy Modular Relocation (Coghill Modular Campus) <sup>(RSD)</sup>
- 68 John F. Kennedy Modular Demolition <sup>(RSD)</sup>
- 69 John F. Kennedy High School Demolition <sup>(RSD)</sup>
- 70 John McDonogh Senior High School Bleachers and Sprinklers <sup>(RSD)</sup>
- 71 John McDonogh Senior High School Roof <sup>(RSD)</sup>
- 72 John A. Shaw Elementary School Mothball <sup>(RSD)</sup>
- 73 Joseph S. Clark Senior High School Roof Repairs <sup>(RSD)</sup>
- 74 Joseph A. Craig Elementary Canopies <sup>(RSD)</sup>
- 75 Joseph A. Craig Elementary Elevator Installation <sup>(RSD)</sup>
- 76 Joseph A. Hardin Elementary Security Fencing <sup>(RSD)</sup>
- 77 Lafayette Elementary School Roof and Masonry <sup>(RSD)</sup>
- 78 Lake Area | Landry Demolition <sup>(RSD)</sup>
- 79 Langston Hughes Elementary School (Phase I) <sup>(RSD)</sup>
- 80 Langston Hughes Elementary School - New Gymnasium (Phase II) <sup>(RSD)</sup>
- 81 Langston Hughes Elementary School - Dumpster Pad <sup>(RSD)</sup>
- 82 Lawrence D. Crocker Elementary School Demolition <sup>(RSD)</sup>
- 83 L.B. Landry Annex Demolition <sup>(RSD)</sup>
- 84 Little Woods Elementary School Demolition <sup>(RSD)</sup>
- 85 Little Woods School (Dolores T. Aaron Elementary School) <sup>(RSD)</sup>
- 86 Live Oak Elementary School Roof <sup>(RSD)</sup>
- 87 Live Oak Elementary School Exterior Door Replacement <sup>(RSD)</sup>



- 88 Lorraine Hansberry Elementary School Mothball <sup>(RSD)</sup>
- 89 Louis D. Armstrong Elementary School <sup>(RSD)</sup>
- 90 Mahalia Jackson Elementary School <sup>(OPSB)</sup>
- 91 Mahalia Jackson Elementary School Dumpster / Other Improvements <sup>(OPSB)</sup>
- 92 Mahalia Jackson Elementary School Office Renovation <sup>(OPSB)</sup>
- 93 Martin Behrman Elementary School Roof <sup>(RSD)</sup>
- 94 Martin Luther King Jr. Elementary Canopy System <sup>(RSD)</sup>
- 95 Martin Luther King Jr. School Modular Building, Deck, Canopy <sup>(RSD)</sup>
- 96 Mary Church Terrell Elementary School Demolition <sup>(RSD)</sup>
- 97 Mary M. Bethune Elementary 1st Floor Replacement <sup>(OPSB)</sup>
- 98 Mary M. Bethune Elementary Rear Yard Repair/Resurfacing <sup>(OPSB)</sup>
- 99 McDonogh #7 High School Repairs <sup>(OPSB)</sup>
- 100 McDonogh #15 Elementary Exterior Masonry to SOI Standards <sup>(RSD)</sup>
- 101 McDonogh #28 Elementary School Roof <sup>(RSD)</sup>
- 102 McDonogh #32 Roof Replacement <sup>(RSD)</sup>
- 103 McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium <sup>(OPSB)</sup>
- 104 McDonogh #42 Elementary School Roof <sup>(RSD)</sup>
- 105 McDonogh #42 Elementary School HVAC Replacement <sup>(RSD)</sup>
- 106 Mildred C. Osborne Elementary School Demolition <sup>(RSD)</sup>
- 107 Mildred C. Osborne Elementary School <sup>(RSD)</sup>
- 108 Modular Campuses Close Outs <sup>(RSD)</sup>
- 109 Modular Classroom Demolition at Fannie C. Williams Elementary School <sup>(RSD)</sup>
- 110 Modular Structures at Langston Hughes Elementary School <sup>(RSD)</sup>
- 111 Morris F.X. Jeff Elementary School Demolition <sup>(RSD)</sup>
- 112 Morris F.X. Jeff Elementary School Mothball <sup>(RSD)</sup>
- 113 Murray G. Henderson Elementary School Roof <sup>(RSD)</sup>
- 114 New Andrew H. Wilson Elementary School <sup>(RSD)</sup>
- 115 New Carter G. Woodson School <sup>(RSD)</sup>
- 116 New Fannie C. Williams School <sup>(RSD)</sup>
- 117 New Joseph A. Craig Elementary School <sup>(RSD)</sup>
- 118 New L.B. Landry High School <sup>(RSD)</sup>
- 119 New Lake Area High School <sup>(RSD)</sup>
- 120 New Lawrence D. Crocker School <sup>(RSD)</sup>
- 121 New Parkview School <sup>(RSD)</sup>
- 122 New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens <sup>(RSD)</sup>
- 123 New William Frantz Elementary School <sup>(RSD)</sup>
- 124 New Orleans High School Signature Center Study <sup>(RSD)</sup>
- 125 Oretha C. Haley Demo <sup>(RSD)</sup>
- 126 Oretha C. Haley Elementary School Mothball <sup>(RSD)</sup>
- 127 Parkview Elementary School Demolition <sup>(RSD)</sup>
- 128 Paul L. Dunbar Elementary School Demolition <sup>(RSD)</sup>
- 129 Paul B. Habans Elementary School Roof Repairs <sup>(RSD)</sup>
- 130 Phillis Wheatley Elementary School Demolition <sup>(RSD)</sup>
- 131 Phillis Wheatley Elementary School <sup>(RSD)</sup>

- 132 Robert M. Lusher Elementary Roof Removal & Replacement <sup>(OPSB)</sup>
- 133 Sarah T. Reed High School Bleachers <sup>(RSD)</sup>
- 134 Sarah T. Reed High School Auditorium Wall <sup>(RSD)</sup>
- 135 Seabrook Computer Training Center Demolition <sup>(OPSB)</sup>
- 136 Schaumburg Chillers <sup>(RSD)</sup>
- 137 Schwarz Alternative Repairs <sup>(RSD)</sup>
- 138 Schwarz Alternative Modulares Demolition <sup>(RSD)</sup>
- 139 Sherwood Forest Elementary School Demolition <sup>(RSD)</sup>
- 140 Sophie B. Wright School Selective Demolition <sup>(RSD)</sup>
- 141 Sophie B. Wright Various Repairs/Restroom Renovations <sup>(OPSB)</sup>
- 142 Stuart R. Bradley Elementary School Demolition <sup>(RSD)</sup>
- 143 Sylvanie Williams Elementary School AHU Replacement <sup>(RSD)</sup>
- 144 Sylvanie Williams Elementary School Play Yard <sup>(RSD)</sup>
- 145 Sylvanie Williams Elementary School Roof Repairs <sup>(RSD)</sup>
- 146 Sylvanie Williams Elementary School HVAC/Chiller Replacement <sup>(RSD)</sup>
- 147 Temporary Campus for McDonogh #11 Expropriation <sup>(OPSB)</sup>
- 148 Thomas A. Edison Elementary School Demolition <sup>(RSD)</sup>
- 149 Thomy Lafon Elementary School Demolition <sup>(RSD)</sup>
- 150 Thomy Lafon School Interpretative Display <sup>(RSD)</sup>
- 151 Timbers Park Office Building #1 & #2 Demolition <sup>(OPSB)</sup>
- 152 Timbers HVAC <sup>(OPSB)</sup>
- 153 Village de L'est Elementary School Subsidence <sup>(RSD)</sup>
- 154 Village de L'est Elementary School Roof and Modular Demolition <sup>(RSD)</sup>
- 155 Vorice J. Waters Elementary School Demolition <sup>(RSD)</sup>
- 156 Valena C. Jones Elementary School <sup>(RSD)</sup>
- 157 Walter L. Cohen High School HVAC <sup>(RSD)</sup>
- 158 Warren Easton High School Window Replacement <sup>(OPSB)</sup>
- 159 West Bank Swing Space for Alice Harte Elementary School <sup>(OPSB)</sup>
- 160 New William J. Guste Elementary School <sup>(RSD)</sup>
- 161 William J. Guste Elementary School Science Lab <sup>(RSD)</sup>
- 162 William Frantz Elementary School Environmental Remediation & Selective Demolition <sup>(RSD)</sup>
- 163 William Frantz Elementary School <sup>(RSD)</sup>
- 164 William Frantz Elementary School Roof <sup>(RSD)</sup>
