


Superintendent's Report March, 2017



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District

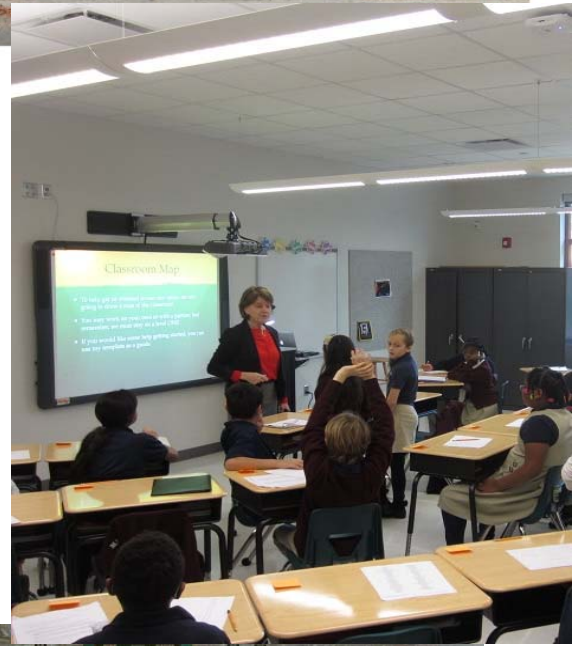

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	10
Ray Abrams Elementary School ^(RSD)	10
Avery Alexander Elementary School ^(RSD)	10
Benjamin Franklin Elementary School Renovation ^(OPSB)	10
New Karr High School, CMAR ^(RSD)	11
John McDonogh High School Renovation CMAR ^(RSD)	11
Ernest "Dutch" Morial Elementary School ^(RSD)	11
Harriet R. Tubman Elementary School Renovation ^(RSD)	12
Booker T. Washington School CMAR ^(RSD)	12
REFURBISHMENTS	13
Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)	13
Agnes L. Bauduit Elementary School Refurbishment ^(RSD)	13
Mary M. Bethune Elementary School Refurbishment ^(OPSB)	13
Warren Easton Courtyard Waterproofing ^(OPSB)	14
William J. Fischer Elementary Refurbishment ^(RSD)	14
William J. Fischer Elementary School HVAC Replacement ^(RSD)	14
Samuel J. Green Elementary School Refurbishment ^(RSD)	15
Andrew Jackson School Refurbishment ^(RSD)	15
Lafayette Elementary School Refurbishment ^(RSD)	15
Laurel Elementary School Refurbishment ^(RSD)	16
Thurgood Marshall Elementary School Refurbishment (RSD)	16
McDonogh #28 School Flooring Refurbishment ^(RSD)	16
McDonogh #32 School Refurbishment ^(RSD)	17
Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing ^(RSD)	17
DEMOLITIONS	17
Demolition of Modulars at Abramson 3 ^(RSD)	17
COMPLETED PROJECTS	18

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$564 million in open contracts for the capital program after issuing \$505 thousand in new contracts, change orders and amendments in March. In addition, the total change orders to date, \$10 million, account for one percent (1.87%) of the total open construction contracts. RSD anticipates issuing approximately \$637 thousand in construction contracts/change orders, and \$1.5 million in professional service contracts/amendments in April.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$232 million in open contracts for the capital program after issuing \$775 thousand in new contracts, change orders and amendments in March. In addition, the total change orders to date, \$9.3 million, account for approximately four percent (4.74%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 thousand in construction contracts/change orders and \$96 thousand in professional service contracts and amendments in April.

Community Meetings



Future Community Meetings

Bid Openings

Projects which are scheduled to bid in the next 60 days

April 5, 2017

Fisher Elementary School HVAC Replacement Bid Opening

April 12, 2017

McDonogh #28 Flooring Renovation Bid Opening

June 7, 2017

Abramson Modular Demolition Phase 3 Bid Opening

Disadvantaged Business Enterprises (DBE) Monthly Summary



Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 24 projects as of March 31, 2017. The DBE subcontracts value is \$81,086,676 of the \$363,307,364 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 48 projects as of March 31, 2017. The DBE subcontracts value is \$20,227,521 of the \$65,106,535 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of March 31, 2017. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 31 projects as of March 31, 2017. The DBE subcontracts value is \$11,638,373 of the \$31,996,589 total of awarded contracts.

Total Amount of Contracts: \$ 569,548,045

Orleans Parish School Board



New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of March 31, 2017. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of March 31, 2017. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$231,354,830

* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

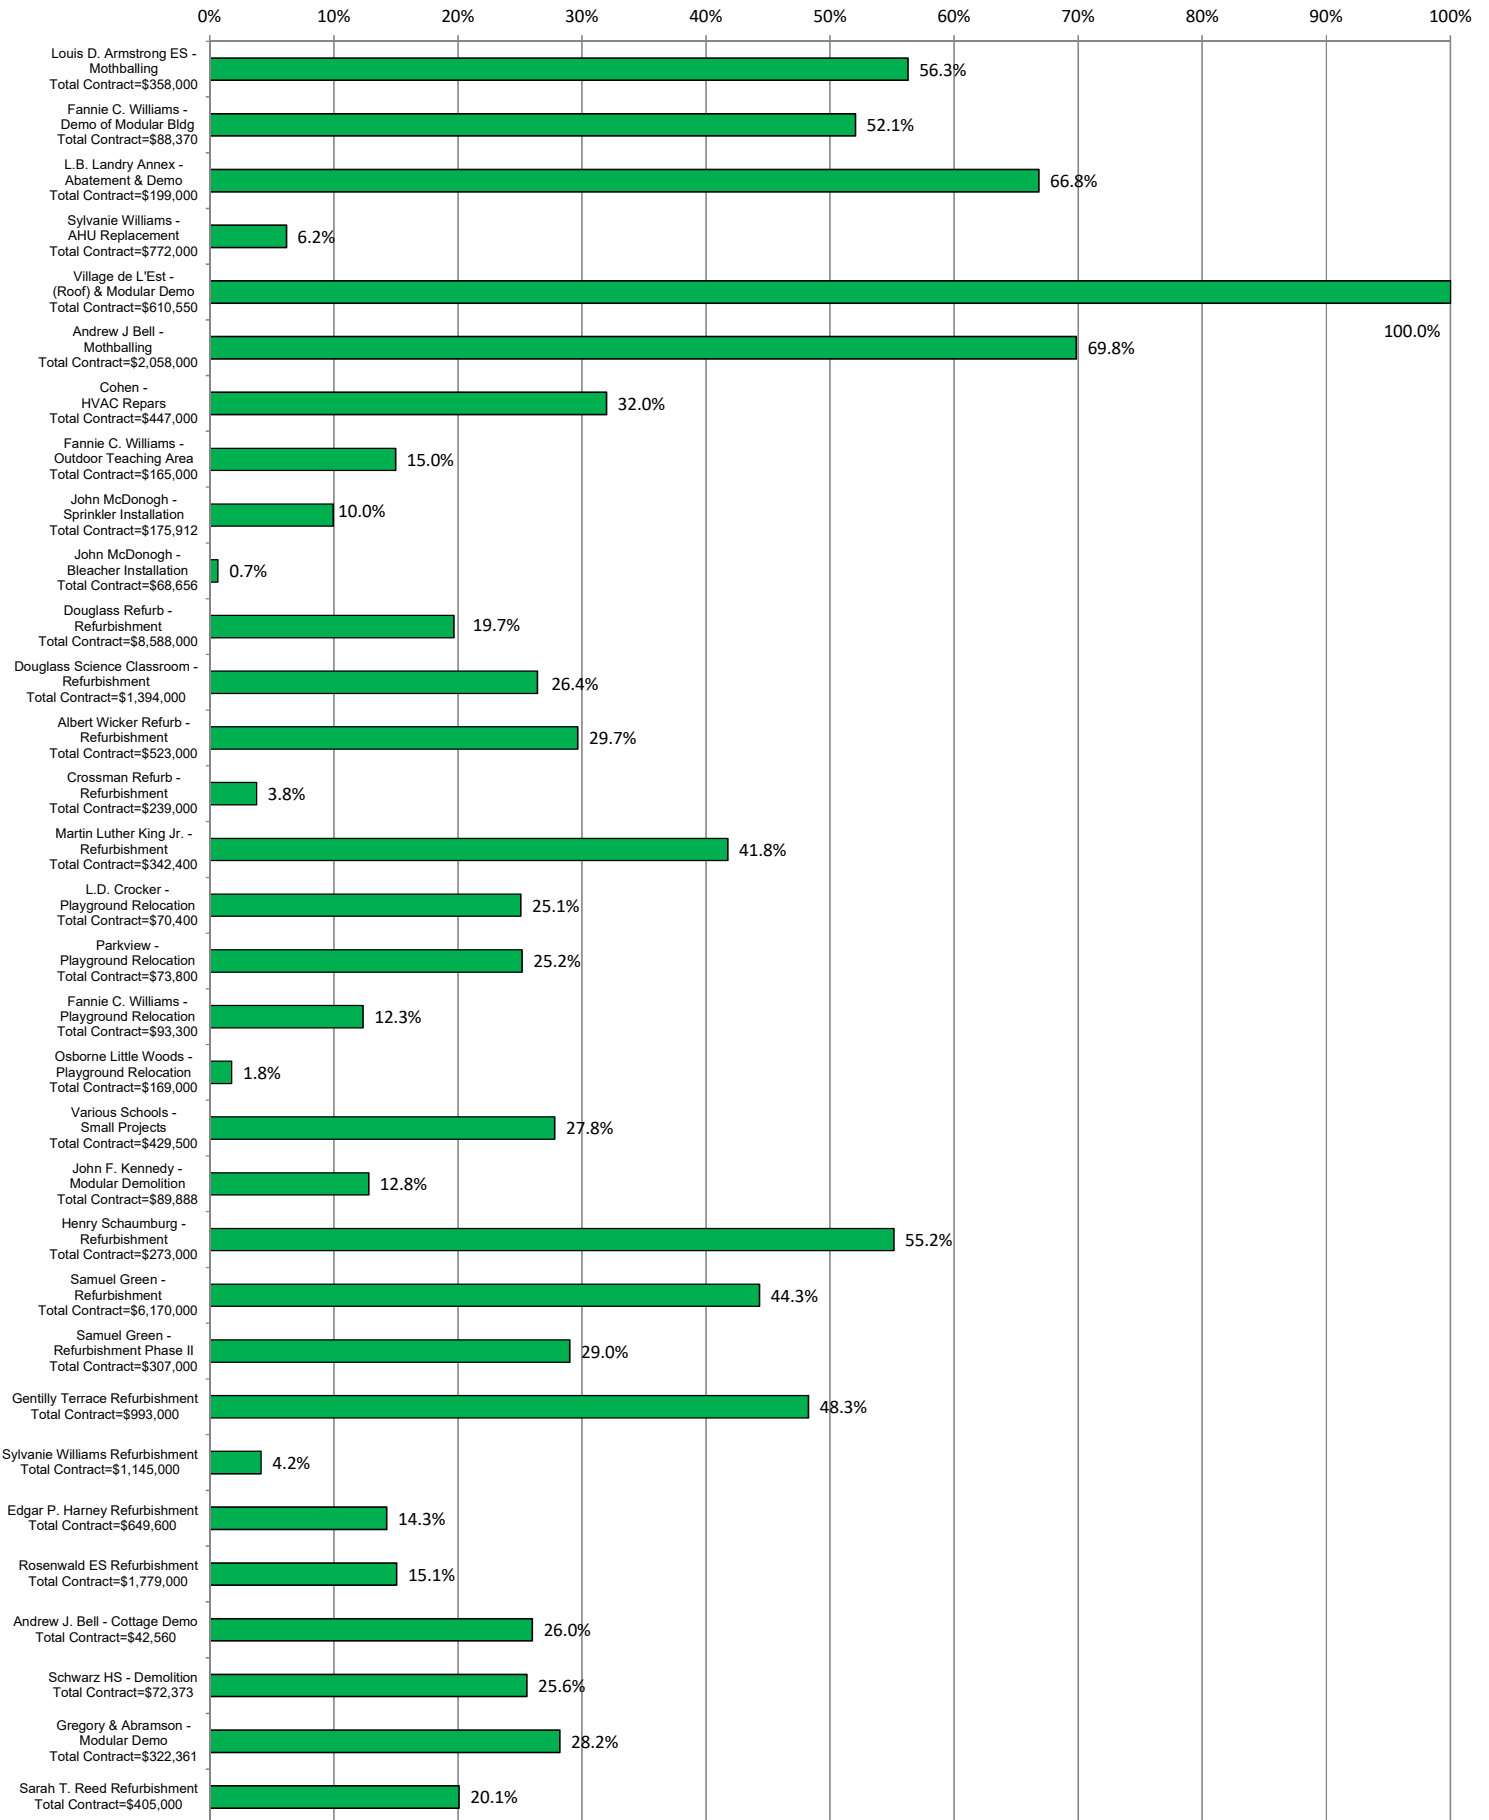


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Status Date: 31 March 2017

Current RSD Program DBE Participation


(Continued)

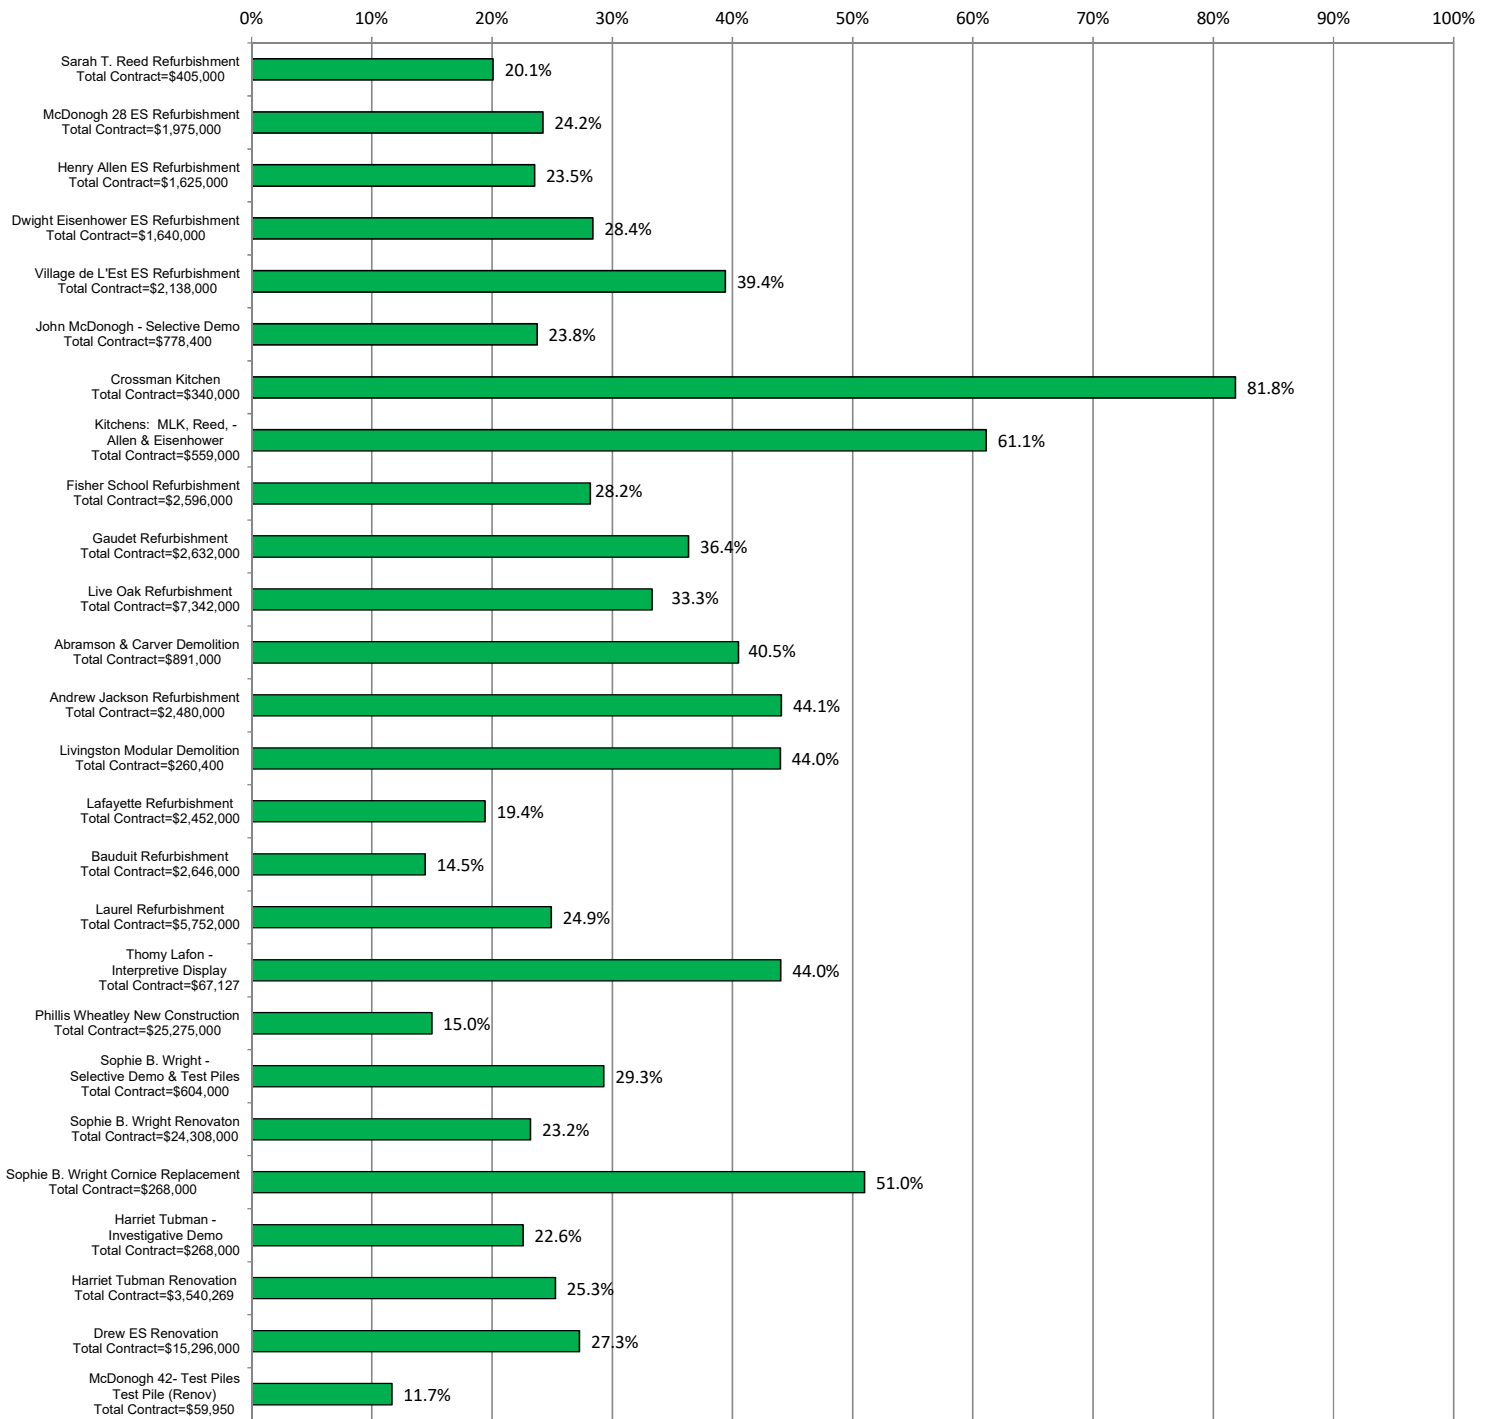

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

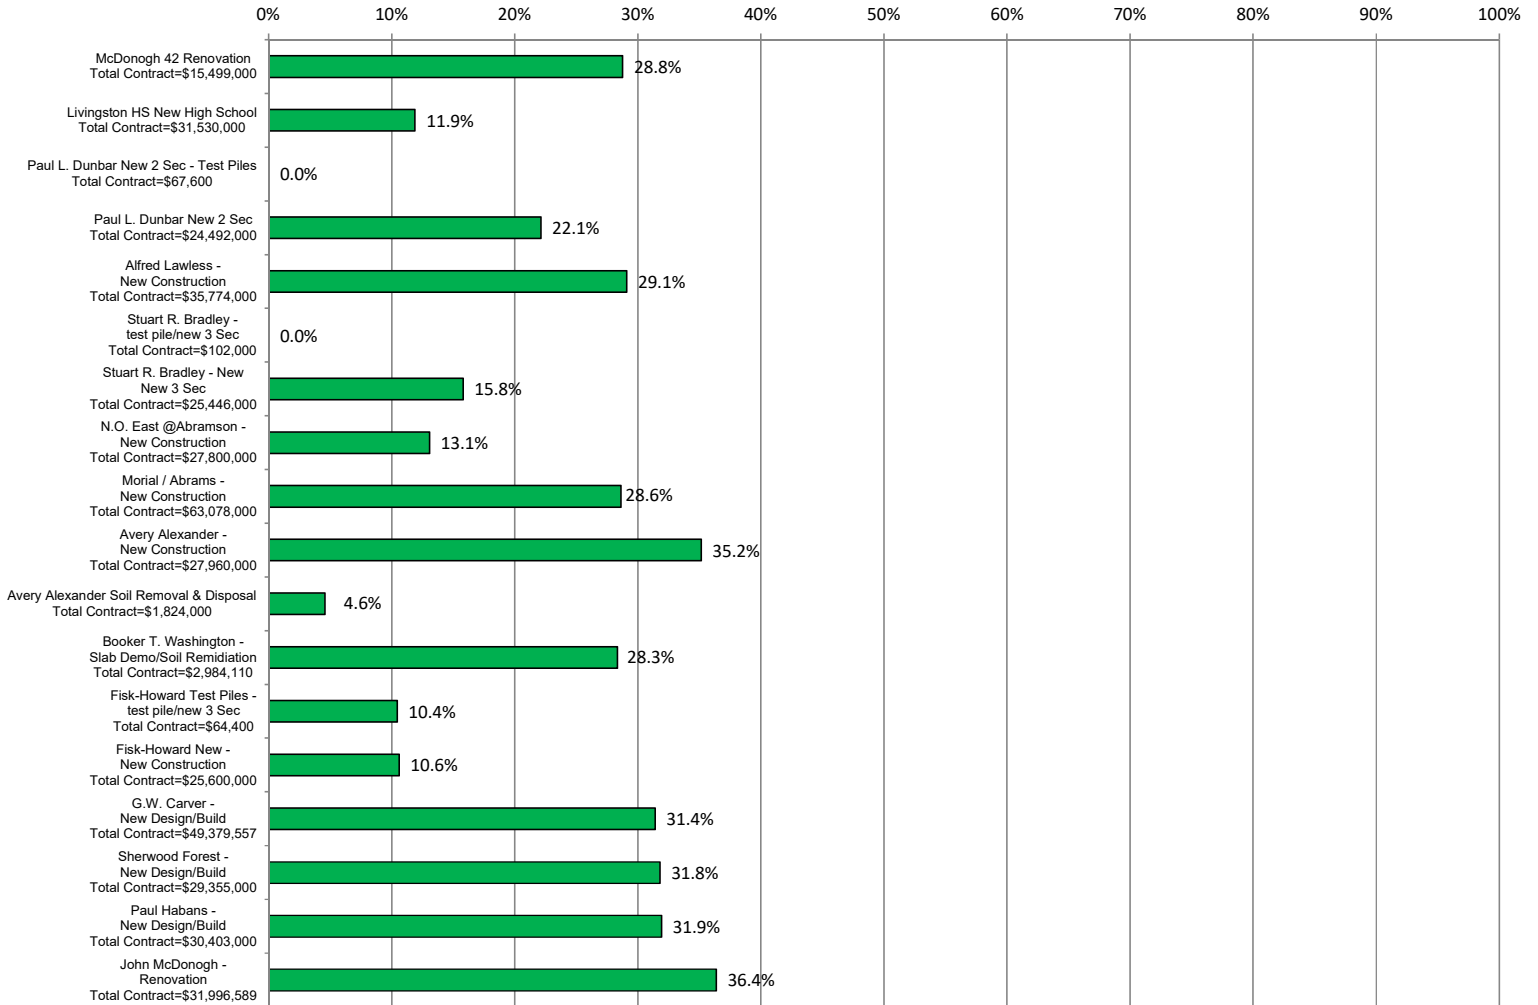

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

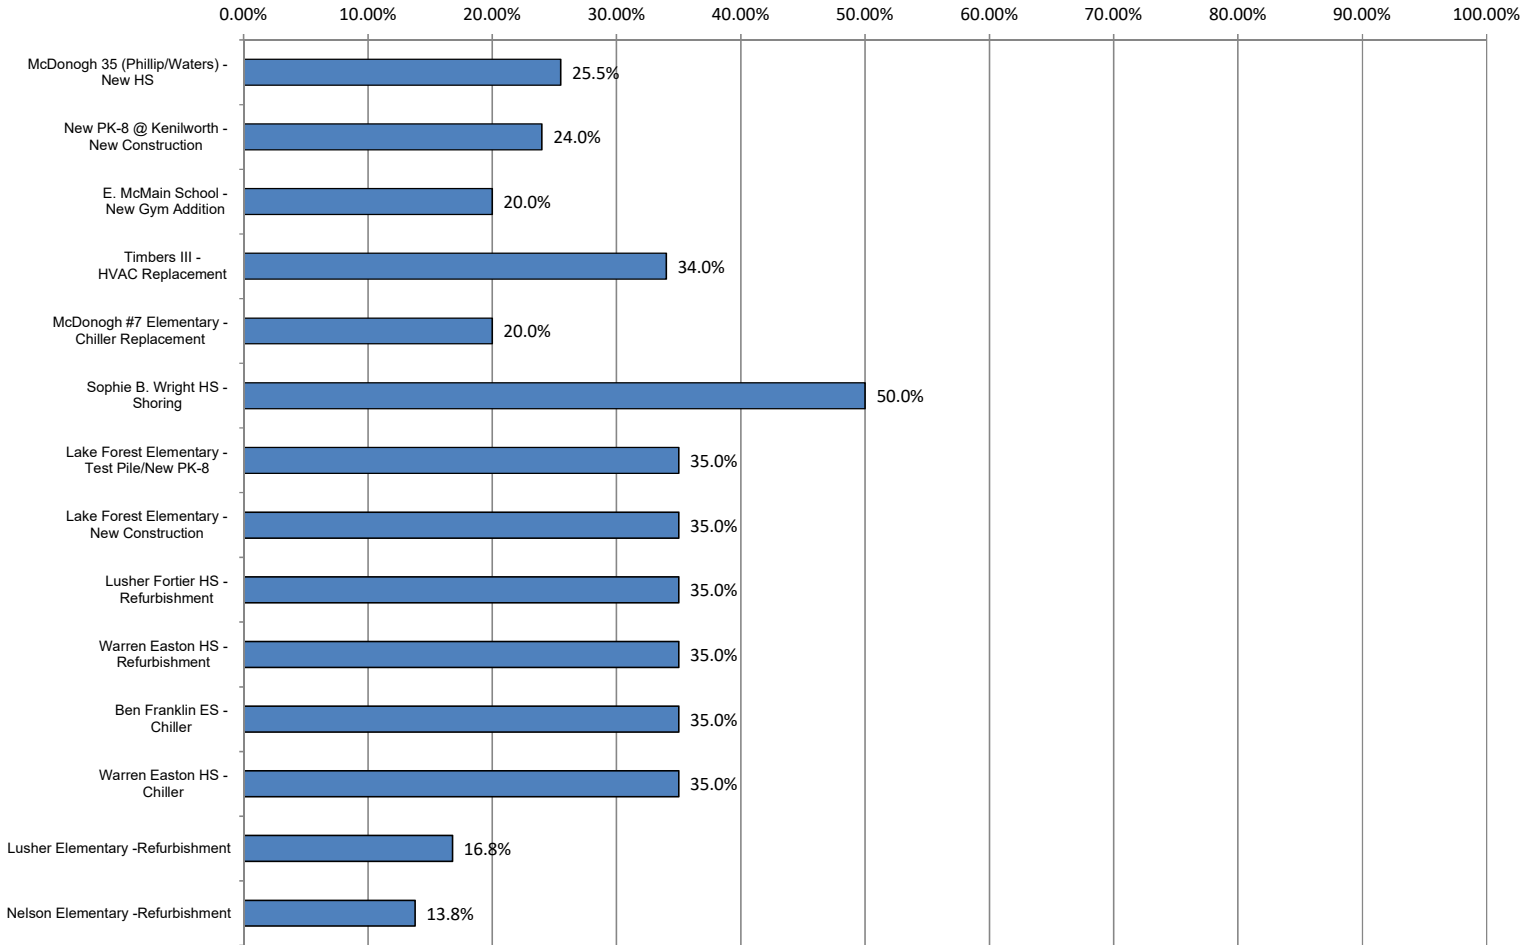

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School ^(RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Substantial Completion March 17th
- Contractor is working on the punch list
- Commissioning is ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – March 2017



Avery Alexander Elementary School ^(RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- Interior finishes are wrapping up
- Final site grading continues
- Bleacher installation will begin in May
- Gymnasium flooring continues

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- A&E continues work on construction documents for the repairs of the exterior and the windows



New Karr High School CMAR ^(RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - TBD

Design Phase

- 90% Construction Documents are due May 10th
- 100% Construction Documents are due June 7th

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



John McDonogh High School Renovation CMAR ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- Window refurbishment continues at the main building
- Cutting of main building slab for new unground utilities
- Electrical rough-in work is ongoing

Contractual Substantial Completion – August 2018

Forecasted Substantial Completion – August 2018



Ernest "Dutch" Morial Elementary School ^(RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Substantial Completion March 17th
- Contractor is working on the punch list
- Commissioning is ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – March 2017



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

Construction Phase

- Roof installation is nearing completion
- Refurbishment of windows continues
- Damaged existing framing repair ongoing
- MEP installation continues
- Exterior plaster repairs ongoing

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Slab on grade pours continue
- Underground utility rough-in work continues
- Excavation and forming of pile caps continue

Contractual Substantial Completion – 2018

Forecasted Substantial Completion – 2018



REFURBISHMENTS

Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

2300 Dumaine Street, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen at Banneker and addition of grease trap at Wheatley

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Commander Corp

Construction Phase

- Anticipated Notice to Proceed April



Agnes L. Bauduit Elementary School Refurbishment ^(RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor – One Construction

Construction Phase

- Window refurbishment continues
- HVAC work is ongoing
- Roofing work continues
- Tuck pointing and stucco work is underway

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – July 2017



Mary M. Bethune Elementary School Refurbishment ^(OPSB)

4040 Eagle Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects

Contractor – Construction Masters Inc.

Construction Phase

- Anticipated Notice to Proceed April 2



Warren Easton School Courtyard Waterproofing ^(OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Repairs to courtyard waterproofing

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - TBD

Procurement Phase

- Owner is review bids



William J. Fischer Elementary School Refurbishment ^(RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Perez

Construction Phase

- Work continues on intercom
- Contractor to fix rear gate and fencing issues

Contractual Substantial Completion – February 2017

Forecasted Substantial Completion – April 2017



William J. Fischer Elementary School HVAC Replacement ^(RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Replacement of existing HVAC

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement - February 15th
- 2nd Advertisement - February 22nd
- 3rd Advertisement - March 1st
- Pre-Bid Conference - March 2nd
- Bid Opening - April 5th



Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD)

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Crescent Commercial

Construction Phase

- Architect developing punch list
- Contractor working on their own punch list

Contractual Substantial Completion – March 2017

Forecasted Substantial Completion – March 2017



Andrew Jackson School Refurbishment ^(RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Construction Phase

- Window refurb is ongoing
- Roof work is complete
- Forming new concrete dumpster pad

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



Lafayette Elementary School Refurbishment ^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Tuna Construction

Construction Phase

- Window refurbishment is ongoing
- Installation of new light fixtures has started
- Work on 3rd floor classrooms continue

Contractual Substantial Completion – July 2017

Forecasted Substantial Completion – July 2017



Laurel Elementary School Refurbishment ^(RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Duct work installation continues
- Ceiling grid and lights are being installed on the 2nd floor
- Window replacement continues
- Brick Mock-up is being reviewed

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017



Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Procurement Phase

- Holding for FEMA review
- FEMA archeological dig contractor to start May 25th
- Owner is reviewing funding source



McDonogh #28 School Flooring Refurbishment ^(RSD)

2733 Esplanade Boulevard, New Orleans, LA 70114 District A Ward 7

Scope of work: Refurbishment of existing elementary school flooring

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement - February 22nd
- 2nd Advertisement - March 1st
- 3rd Advertisement - March 8th
- Pre-Bid Conference - March 9th
- Bid Opening - April 12th



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - HMS Architects

Design Phase - CD

- Project place "On Hold"



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - Industrial and Mechanical Contractors, Inc

Procurement Phase

- General contractor is reviewing the contract



DEMOLITIONS

Demolition of Modular Buildings at Abramson 3 ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – TBD

Procurement Phase

- 1st Advertisement - May 3rd
- 2nd Advertisement - May 10th
- 3rd Advertisement - May 17th
- Pre-Bid Conference - May 18th
- Bid Opening - June 7th



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment ^(RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
7	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
8	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
9	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
10	Alfred Lawless Senior ^(RSD)	12/18/2015
11	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
12	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
13	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
14	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
15	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
16	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
17	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
18	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
19	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
20	Augustine Elementary School Roof ^(RSD)	04/13/2012
21	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
22	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
23	Bell JH Shoring ^(RSD)	06/28/2011
24	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
25	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
26	Bienville Elementary School Demolition ^(RSD)	05/04/2009
27	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
28	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
29	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
30	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
31	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
32	Charles J. Colton Elementary School ^(RSD)	05/23/2013
33	Charles R. Drew Elementary School ^(RSD)	04/17/2015
34	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
35	Cohen High School Health Clinic ^(RSD)	12/24/2008
36	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
37	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
38	Demolition of Modular Buildings at Abramson and Carver ^(RSD)	01/18/2017
39	Demolition of Modular Buildings at Livingston ^(RSD)	01/18/2017
40	Douglass High School Under Floor Utilities ^(RSD)	
41	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
42	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
43	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016

44	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
45	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
46	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011
47	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
48	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
49	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
50	Edna Karr High School - Assessment ^(OPSB)	
51	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
52	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
53	New Edward Hynes School ^(OPSB)	02/06/2012
54	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
55	Edward Livingston High School ^(RSD)	01/05/2015
56	Eleanor L. McMMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
57	Eleanor L. McMMain School Clinic ^(OPSB)	07/24/2013
58	Eleanor L. McMMain School Maintenance Upgrades ^(OPSB)	12/12/2016
59	Eleanor L. McMMain School Roof Replacement ^(OPSB)	05/13/2016
60	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
61	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
62	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
63	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
64	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
65	Francis W. Gregory Demolition ^(RSD)	12/21/2011
66	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
67	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
68	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
69	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
70	Gaudet Elementary School Refurbishment ^(RSD)	12/20/2016
71	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
72	George Mondy Elementary School Mothball ^(RSD)	
73	George Washington Carver School ^(RSD)	03/07/2016
74	George Washington Carver High School Demolition ^(RSD)	08/24/2011
75	Greater St. Stephens School ^(OPSB)	03/18/2013
76	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
77	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
78	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
79	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
80	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
81	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
82	Holy Cross Modular Relocation ^(RSD)	12/14/2010
83	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
84	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
85	James Derham Demolition ^(RSD)	02/23/2012
86	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
87	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
88	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
89	JoEllen Smith Medical Center Demolition ^(OPSB)	

90	John Dibert Elementary School Roof ^(RSD)	08/20/2010
91	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
92	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
93	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
94	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
95	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
96	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
97	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
98	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
99	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
100	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
101	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
102	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
103	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
104	Lake Area Landry Demolition ^(RSD)	05/01/2008
105	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
106	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
107	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
108	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
109	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
110	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
111	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
112	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
113	Live Oak Elementary School Refurbishment ^(RSD)	01/06/2017
114	Live Oak Elementary School Roof ^(RSD)	08/04/2011
115	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
116	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
117	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
118	Lusher Elementary School Refurbishment ^(OPSB)	10/31/2016
119	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
120	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
121	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
122	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
123	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
124	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
125	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
126	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
127	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
128	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
129	McDonogh #7 High School Repairs ^(OPSB)	
130	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
131	McDonogh #28 School Refurbishment ^(RSD)	03/15/2016
132	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
133	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
134	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014

135	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
136	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
137	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
138	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
139	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
140	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
141	Modular Campuses Close Outs ^(RSD)	
142	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
143	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010
144	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
145	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
146	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
147	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
148	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
149	New Carter G. Woodson School ^(RSD)	09/14/2012
150	New Fannie C. Williams School ^(RSD)	08/24/2012
151	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
152	New L.B. Landry High School ^(RSD)	06/30/2010
153	New Lake Area High School ^(RSD)	12/28/2009
154	New Lawrence D. Crocker School ^(RSD)	04/29/2013
155	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
156	New Parkview School ^(RSD)	10/12/2012
157	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
158	New William Frantz Elementary School ^(RSD)	
159	New Orleans High School Signature Center Study ^(RSD)	
160	Oretha C. Haley Demo ^(RSD)	05/07/2012
161	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
162	Parkview Elementary School Demolition ^(RSD)	08/06/2009
163	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
164	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
165	Paul B. Habans Elementary School ^(RSD)	06/30/2016
166	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
167	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
168	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
169	Rosenwald Elementary School Refurbishment ^(RSD)	04/07/2016
170	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
171	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
172	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
173	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
174	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
175	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
176	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
177	Schaumburg Chillers ^(RSD)	11/14/2008
178	Schwarz Alternative Repairs ^(RSD)	07/14/2009
179	Schwarz Alternative Modulars Demolition ^(RSD)	04/02/2015
180	Schwarz Modular Building Demolition ^(RSD)	04/02/2015

181	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
182	Sherwood Forest Elementary School ^(RSD)	06/30/2016
183	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
184	Sophie B. Wright School Renovation ^(RSD)	06/08/2016
185	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
186	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
187	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
188	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
189	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
190	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
191	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
192	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
193	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
194	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
195	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
196	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
197	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
198	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
199	Timbers HVAC ^(OPSB)	09/11/2013
200	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
201	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
202	Village de L'est Elementary School Refurbishment ^(RSD)	10/12/2016
203	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
204	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
205	Valena C. Jones Elementary School ^(RSD)	01/10/2013
206	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
207	Warren Easton High School Renovation ^(OPSB)	12/15/2015
208	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
209	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
210	New William J. Guste Elementary School ^(RSD)	10/06/2008
211	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
212	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
213	William Frantz Elementary School Roof ^(RSD)	08/12/2010
