




# Superintendent's Report March 2018



**Dr. Henderson Lewis Jr.**  
Orleans Parish School Board



**Mr. John White**  
Louisiana Department of  
Education  
**Ms. Kunjan Narechania**  
Recovery School District



Prepared By





# Table of Contents

Right-Click on the school name to proceed to that page

<b>TABLE OF CONTENTS</b>	1
<b>FINANCIAL OVERVIEW</b>	2
<b>COMMUNITY MEETINGS</b>	3
<b>BID OPENINGS</b>	4
<b>DBE OVERVIEW MONTHLY SUMMARY</b>	5
<b>NEW &amp; MAJOR RENOVATION</b>	10
Benjamin Franklin Elementary School Renovation <sup>(OPSB)</sup>	10
New Karr High School, CMAR <sup>(RSD)</sup>	10
New Orleans Charter Science and Mathematics High School <sup>(OPSB)</sup>	10
John McDonogh High School Renovation CMAR <sup>(RSD)</sup>	11
Harriet R. Tubman Elementary School Renovation <sup>(RSD)</sup>	11
Booker T. Washington School CMAR <sup>(RSD)</sup>	11
<b>REFURBISHMENTS</b>	12
Harney Elementary School Downspout and Gutter Repairs <sup>(RSD)</sup>	12
Harney Elementary School Interior Lighting <sup>(RSD)</sup>	12
Lafayette Elementary School Refurbishment <sup>(RSD)</sup>	12
Thurgood Marshall Elementary School Refurbishment <sup>(RSD)</sup>	13
McDonogh #28 School Flooring Refurbishment <sup>(RSD)</sup>	13
McDonogh #32 School Refurbishment <sup>(RSD)</sup>	13
McDonogh #32 School Refurbishment <sup>(RSD)</sup>	14
Eleanor McMain School Envelope Repairs <sup>(OPSB)</sup>	14
Harriet R. Tubman Elementary School Cottage Renovation <sup>(RSD)</sup>	14
Schaumburg Elementary School Roof Repairs <sup>(RSD)</sup>	15
Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing <sup>(RSD)</sup>	15
Sophie B. Wright High School - Phase 2 Interior Painting and Wood Flooring Repairs <sup>(RSD)</sup>	15
<b>DEMOLITIONS</b>	16
Demolition of Modulars at Abramson 3 <sup>(RSD)</sup>	16
Demolition of Modulars at Coghill <sup>(RSD)</sup>	16
<b>COMPLETED PROJECTS</b>	17

# Overview

## FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$306 million in open contracts for the capital program after issuing \$163 thousand in new contracts, change orders and amendments in March. In addition, the total change orders to date, \$5.8 million, account for two percent (2.41%) of the total open construction contracts. RSD anticipates issuing \$397 thousand in construction contracts/change orders, and \$326 thousand in professional service contracts/amendments in April.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$176 million in open contracts for the capital program after issuing \$1 hundred in new contracts, change orders and amendments in March. In addition, the total change orders to date, \$7.1 million, account for approximately five percent (5.05%) of the total open construction contracts. OPSB anticipates issuing approximately \$35 thousand in construction contracts/change orders and \$0 thousand in professional service contracts and amendments in April.

# Community Meetings



## Future Community Meetings

**April 10, 2018**

New Karr High School Groundbreaking  
4400 General Meyer Avenue, New Orleans, LA 70131

# Bid Openings

## Projects which are scheduled to bid in the next 60 days

### **April 4, 2018**

Harney Interior Lighting Bid Opening

### **April 18, 2018**

Harney Gutters and Downspouts Bid Opening

### **April 18, 2018**

Booker T. Washington High School Reconstruction of Prieur Street Bid Opening

### **May 9, 2018**

New Orleans Charter Science & Mathematics High School Bid Opening

### **May 9, 2018**

McMain Envelope Repairs Bid Opening

### **May 23, 2018**

McDonogh #42 Drainage Bid Opening

# Disadvantaged Business Enterprises (DBE) Monthly Summary



## Recovery School District

### New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of March 31, 2018. The DBE subcontracts value is \$82,153,443 of the \$362,866,202 total of awarded contracts.

### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 54 projects as of March 31, 2018. The DBE subcontracts value is \$23,174,027 of the \$73,075,270 total of awarded contracts.

### Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of March 31, 2018. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

### CMAR New:

DBE Contractors secured subcontracts on 2 projects as of March 31, 2018. The DBE subcontracts value is \$29,865,002 of the \$86,846,352 total of awarded contracts.

Total Amount of Contracts: \$ 632,202,381

## Orleans Parish School Board



### New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of March 31, 2018. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.


### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of March 31, 2018. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$231,354,830

\* DBE provisions were included in projects bid after June 30, 2012

## Current RSD Program DBE Participation

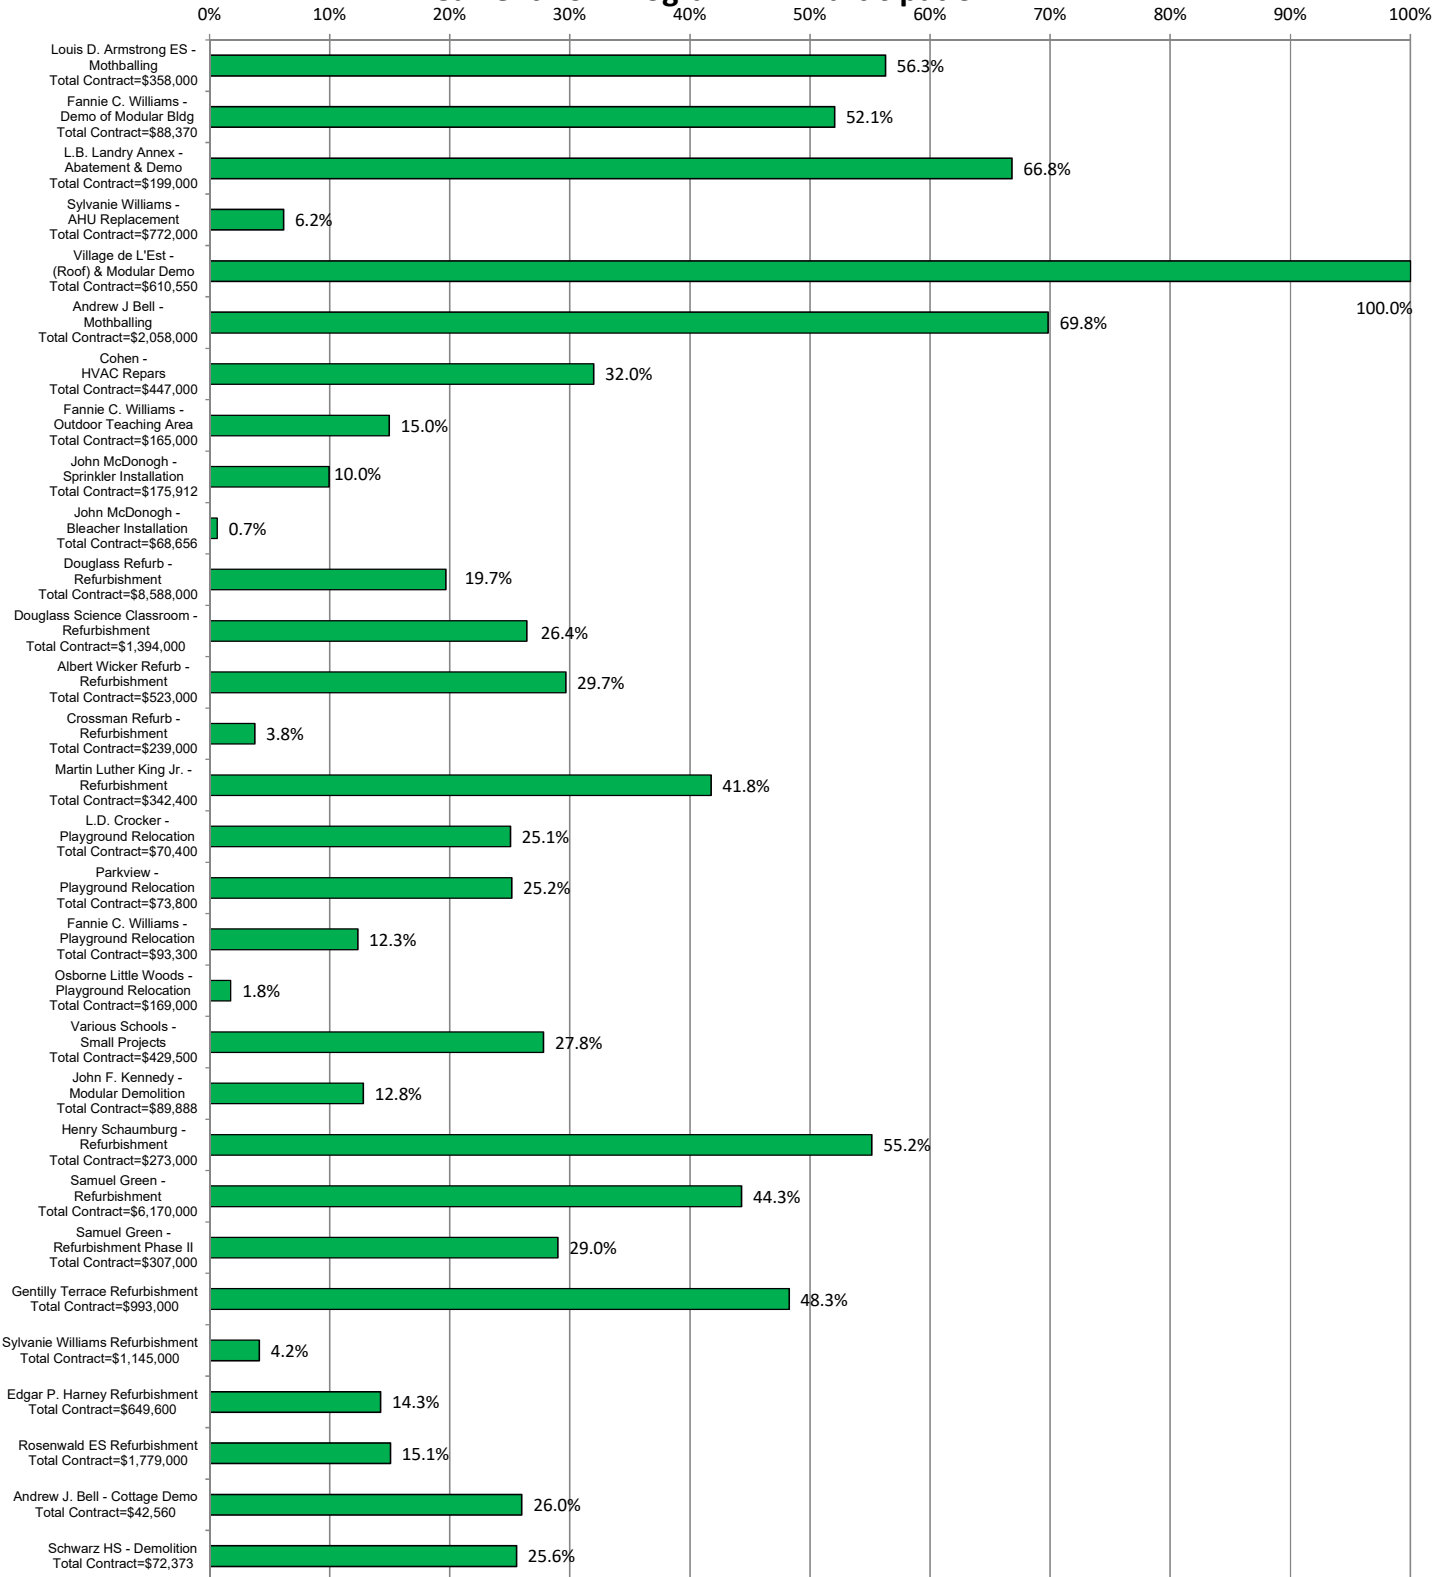


Notes: Data Based On Pre-Construction and/or 6 monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

Status Date: 31 March 2018




## Current RSD Program DBE Participation

(Continued)

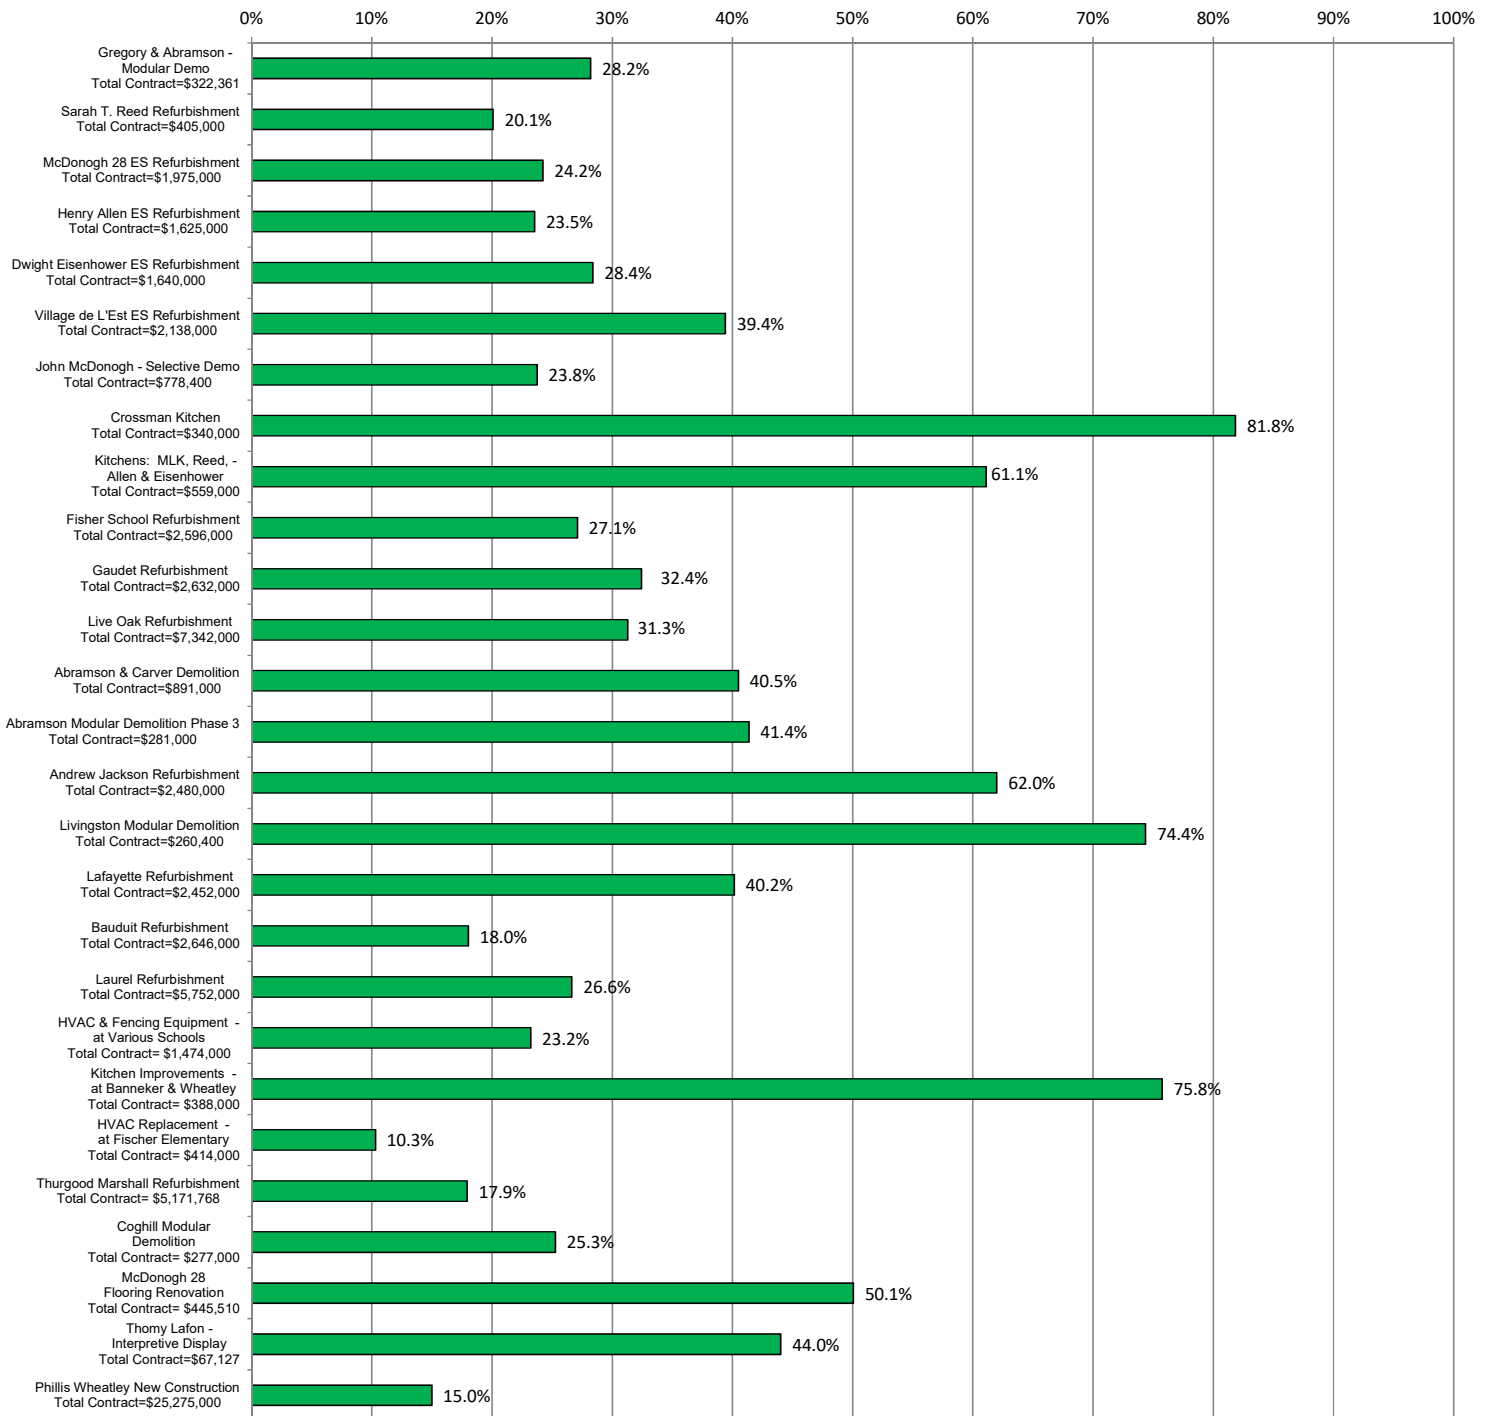


**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

## Current RSD Program DBE Participation (Continued)

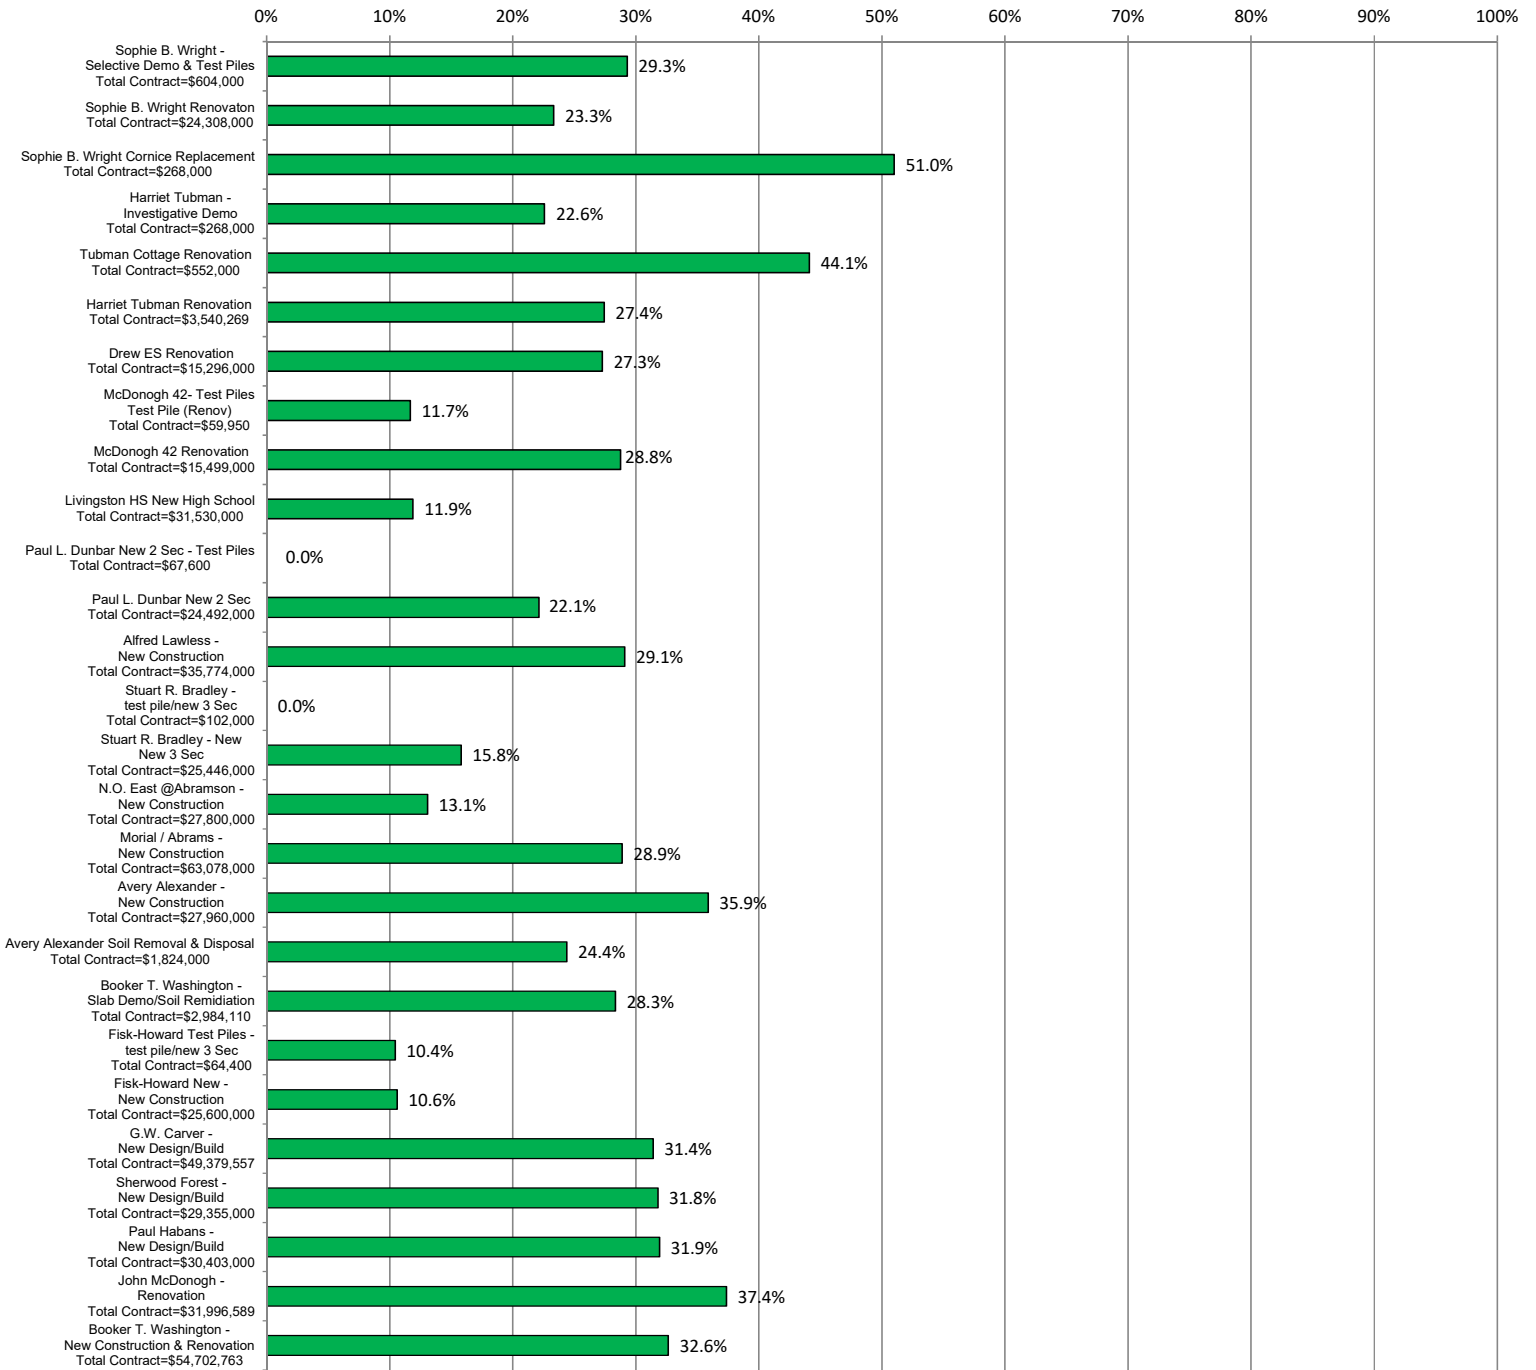

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

### Current OPSB Program DBE Participation

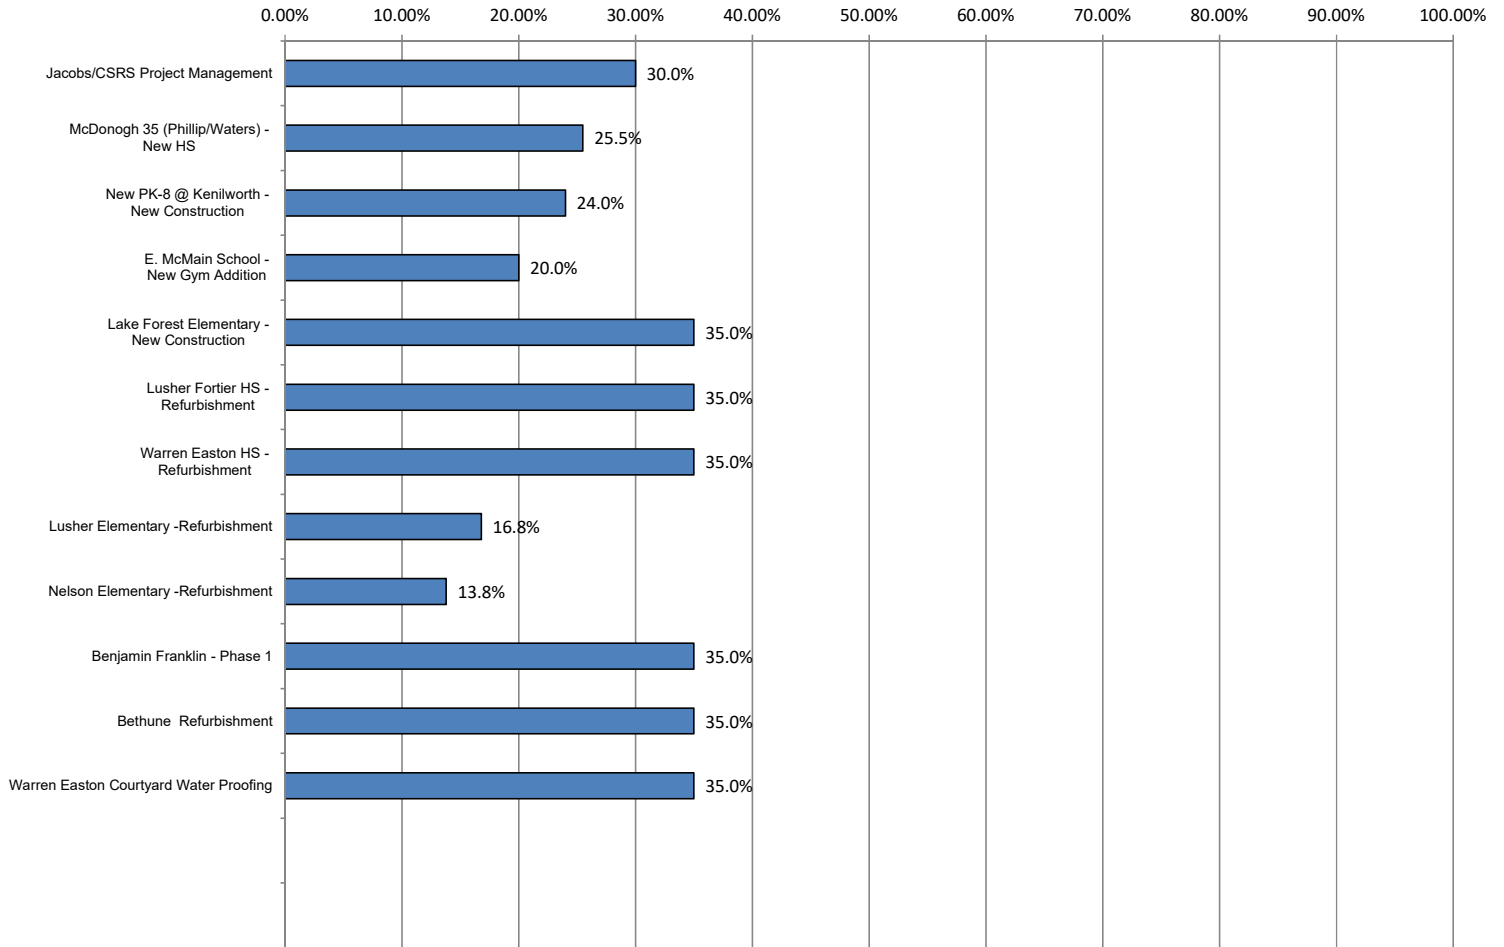

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
 OPSB DBE Participation Target = 35% of Total Contract Amount

## New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

### Benjamin Franklin Elementary School Renovation <sup>(OPSB)</sup>

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Construction Masters

#### Construction Phase

- Phase 2 - 50% Construction Documents are due June 26th
- Demolition continues

Contractual Substantial Completion Phase 1 – August 2018

Forecasted Substantial Completion Phase 1 – August 2018



### New Karr High School CMAR <sup>(RSD)</sup>

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - Core Construction

#### Construction Phase

- River height is impacting the work schedule
- Site demolition is ongoing
- Contractor working on submittals

Contractual Substantial Completion – Summer 2020

Forecasted Substantial Completion – Summer 2020



### New Orleans Charter Science and Mathematics High School <sup>(OPSB)</sup>

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - TBD

#### Design Phase

- 100% Construction documents are being developed
- Bid is anticipated in May 2018

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



## John McDonogh High School Renovation CMAR <sup>(RSD)</sup>

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

### Construction Phase

- Installation of light fixtures on 2nd and 3rd floor continues
- Site civil work is ongoing
- Final coat of paint is underway
- Rough in of MEP at gymnasium continues

Contractual Substantial Completion – October 2018

Forecasted Substantial Completion – October 2018



## Harriet R. Tubman Elementary School Renovation <sup>(RSD)</sup>

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

### Construction Phase

- Wood floor refinishing continues
- MEP system installation ongoing
- Painting is proceeding
- Data cabling continues

Contractual Substantial Completion – July 2018

Forecasted Substantial Completion – July 2018



## Booker T. Washington School CMAR <sup>(RSD)</sup>

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

### Construction Phase

- Contractor emphasis is on closing the building envelope
- Roofing work continues
- Sprinkler work has started
- Steel structure stabilization on the auditorium continues

Contractual Substantial Completion – January 2019

Forecasted Substantial Completion – January 2019



## REFURBISHMENTS

### Harney Elementary School Downspout and Gutter Repairs <sup>(RSD)</sup>

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of downspouts and gutters

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - TBD

#### Procurement Phase

- 1st Advertisement - February 28th
- 2nd Advertisement - March 7th
- 3rd Advertisement - March 14th
- Pre-Bid Conference - March 28th
- Bid Opening - April 18th



### Harney Elementary School Interior Lighting <sup>(RSD)</sup>

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement interior lighting

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - TBD

#### Procurement Phase

- 1st Advertisement - February 28th
- 2nd Advertisement - March 7th
- 3rd Advertisement - March 14th
- Pre-Bid Conference - March 15th
- Bid Opening - April 4th



### Lafayette Elementary School Refurbishment Phase 2 <sup>(RSD)</sup>

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to floor replacement

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

#### Procurement Phase

- Bids are being reviewed



## Thurgood Marshall Elementary School Refurbishment <sup>(RSD)</sup>

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Blanchard Mechanical Contractors

### Construction Phase

- Window installation is nearing completion
- Elevator steel is being erected
- Mechanical work in ongoing
- Tile work has started in restrooms

Contractual Substantial Completion – June 2018

Forecasted Substantial Completion – June 2018



## McDonogh #28 School Flooring Refurbishment Phase 2 <sup>(RSD)</sup>

2733 Esplanade Boulevard, New Orleans, LA 70114 District A Ward 7

Scope of work: Refurbishment of existing elementary school flooring

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Insul-Tech

### Procurement Phase

- Contracts are being signed
- Notice to Proceed will be after school is out for summer break



## McDonogh #32 School Refurbishment <sup>(RSD)</sup>

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – HMS Architects

Contractor - TBD

### Design Phase

- Owner has place project on hold



## McDonogh #42 School Drainage <sup>(RSD)</sup>

1651 North Tonti Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Site Drainage

Funding Source – FEMA, CDBG

Architect – Eskew+Dumez+Ripple

Contractor - TBD

### Procurement Phase

- 1st Advertisement - April 18th
- 2nd Advertisement - April 25th
- 3rd Advertisement - May 2nd
- Pre-Bid Conference - May 3rd
- Bid Opening - May 23rd



## Eleanor McMain School Envelope Repairs <sup>(OPSB)</sup>

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Exterior stucco and window repairs

Funding Source – General Fund & Harrah's

Architect – Concordia, LLC

Contractor – TBD

### Procurement Phase

- 1st Advertisement - April 4th
- 2nd Advertisement - April 11th
- 3rd Advertisement - April 18th
- Pre-Bid Conference - April 19th
- Bid Opening - May 9th



## Harriet R. Tubman Elementary School Cottage Renovation <sup>(RSD)</sup>

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing cottage to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

### Construction Phase

- Framing repairs are complete
- Installation of siding has started
- Window frames have been installed

Contractual Substantial Completion – June 2018

Forecasted Substantial Completion – June 2018





## Schaumburg Elementary School Roof Repairs <sup>(RSD)</sup>

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - Laperouse Metal Works, Inc

### Construction Phase

- Trees and fencing have been removed
- Roof panels have been delivered and installation will start soon

Contractual Substantial Completion – August 2018

Forecasted Substantial Completion – August 2018



## Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing <sup>(RSD)</sup>

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

6501 Berkley Drive, New Orleans, LA 70131 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - Industrial and Mechanical Contractors, Inc

### Construction Phase

- Reed - Window mockup installation has been approved

Contractual Substantial Completion – December 2017

Forecasted Substantial Completion – June 2018



## Sophie B. Wright High School Phase 2 Interior Painting and Wood Floor Repairs <sup>(RSD)</sup>

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Interior painting and wood floor repairs

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – TBD

### Procurement Phase

- 1st Advertisement - February 21st
- 2nd Advertisement - February 28th
- 3rd Advertisement - March 7th
- Pre-Bid Conference - March 8th
- Bid Opening - March 28th



## DEMOLITIONS

### Demolition of Modular Buildings at Abramson 3 <sup>(RSD)</sup>

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – Ashley Savarino Unlimited Construction

#### Construction Phase

- Replacement of topsoil is underway
- Entergy to remove power poles
- Vegetation removal at perimeter fencing continues

Contractual Substantial Completion – February 2018

Forecasted Substantial Completion – May 2018



### Demolition of Modular Buildings at Coghill <sup>(RSD)</sup>

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – Construction Management Enterprises

#### Construction Phase

- Electrical demolition has started
- Contractor is removing skirt boards from modulars

Contractual Substantial Completion – August 2018

Forecasted Substantial Completion – August 2018



## Comprehensive List - Completed Projects

1	Abrams   Morial   Abramson   Coghill Demolition <sup>(RSD)</sup>	11/17/2008
2	A. D. Cross Elementary School Energy Conservation <sup>(RSD)</sup>	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School <sup>(RSD)</sup>	06/12/2012
4	A. D. Crossman Elementary School Refurbishment <sup>(RSD)</sup>	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment <sup>(RSD)</sup>	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs <sup>(RSD)</sup>	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment <sup>(RSD)</sup>	10/31/2017
8	Agnes Bauduit Elementary School Boiler <sup>(RSD)</sup>	12/07/2009
9	Albert Wicker Elementary School Refurbishment <sup>(RSD)</sup>	03/27/2014
10	Albert Wicker Elementary School Roof Repairs <sup>(RSD)</sup>	06/13/2013
11	Alfred Lawless Senior <sup>(RSD)</sup>	12/18/2015
12	Alfred Lawless Senior High Security Fencing <sup>(RSD)</sup>	06/15/2011
13	Alice M. Harte Elementary School <sup>(OPSB)</sup>	11/19/2014
14	Alice M. Harte Elementary School Demolition <sup>(OPSB)</sup>	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement <sup>(RSD)</sup>	02/08/2014
16	Andrew J. Bell Junior High School Mothball <sup>(RSD)</sup>	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs <sup>(RSD)</sup>	07/27/2012
18	Andrew Jackson Elementary School Solar Panels <sup>(RSD)</sup>	01/14/2013
19	Andrew H. Wilson Elementary School Cottage <sup>(RSD)</sup>	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation <sup>(OPSB)</sup>	
21	Augustine Elementary School Roof <sup>(RSD)</sup>	04/13/2012
22	Avery-Alexander Elementary School <sup>(RSD)</sup>	06/19/2017
23	Avery-Alexander Elementary School Demolition <sup>(RSD)</sup>	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad <sup>(RSD)</sup>	10/30/2017
25	Barbara C. Jordan Elementary School Demolition <sup>(RSD)</sup>	05/30/2011
26	Bell JH Shoring <sup>(RSD)</sup>	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation <sup>(RSD)</sup>	
28	Benjamin Franklin Senior High School <sup>(OPSB)</sup>	08/23/2013
29	Bienville Elementary School Demolition <sup>(RSD)</sup>	05/04/2009
30	Booker T. Washington High School Environmental Remediation <sup>(RSD)</sup>	12/13/2015
31	Booker T. Washington High School Partial Demolition <sup>(RSD)</sup>	04/07/2013
32	Carter G. Woodson Middle School Demolition <sup>(RSD)</sup>	02/09/2010
33	Central Services Warehouse Demolition <sup>(OPSB)</sup>	01/05/2012
34	Charles J. Colton Elementary Selective Demolition <sup>(RSD)</sup>	07/26/2010
35	Charles J. Colton Elementary School <sup>(RSD)</sup>	05/23/2013
36	Charles R. Drew Elementary School <sup>(RSD)</sup>	04/17/2015
37	Charles R. Drew Elementary Roof & Installation of Kitchen Hood <sup>(RSD)</sup>	06/08/2011
38	Cohen High School Health Clinic <sup>(RSD)</sup>	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School <sup>(RSD)</sup>	
40	Demolition of Modular Buildings at Gregory and Abramson <sup>(RSD)</sup>	06/23/2015
41	Demolition of Modular Buildings at Abramson and Carver <sup>(RSD)</sup>	01/18/2017
42	Demolition of Modular Buildings at Livingston <sup>(RSD)</sup>	01/18/2017
43	Douglass High School Under Floor Utilities <sup>(RSD)</sup>	

44	Dr. Martin Luther King School Roof Repairs <sup>(RSD)</sup>	06/13/2012
45	Dr. Martin Luther King Jr. School Renovation <sup>(RSD)</sup>	12/15/2014
46	Dwight D. Eisenhower Elementary School Kitchen Refurbishment <sup>(RSD)</sup>	02/18/2016
47	Dwight D. Eisenhower Elementary School Roof Repairs <sup>(RSD)</sup>	07/27/2012
48	Dwight D. Eisenhower Elementary School Refurbishment <sup>(RSD)</sup>	12/23/2015
49	East Bank Swing Space for Audubon Charter School <sup>(OPSB)</sup>	12/30/2011
50	Edgar P. Harney Elementary School Refurbishment <sup>(RSD)</sup>	
51	Edgar P. Harney Elementary School Roof Repairs <sup>(RSD)</sup>	06/13/2012
52	Edna Karr High School - Gymnasium Repair <sup>(OPSB)</sup>	12/23/2013
53	Edna Karr High School - Assessment <sup>(OPSB)</sup>	
54	Edward Livingston Middle School Demolition <sup>(RSD)</sup>	09/28/2010
55	Edward Henry Phillips Junior High School Demolition <sup>(OPSB)</sup>	11/19/2010
56	New Edward Hynes School <sup>(OPSB)</sup>	02/06/2012
57	Edwards   Hardin   Lockett   Lawless Demolition <sup>(RSD)</sup>	11/03/2008
58	Edward Livingston High School <sup>(RSD)</sup>	01/05/2015
59	Eleanor L. McMMain School Replacement of Existing Chillers <sup>(OPSB)</sup>	08/30/2011
60	Eleanor L. McMMain School Clinic <sup>(OPSB)</sup>	07/24/2013
61	Eleanor L. McMMain School Maintenance Upgrades <sup>(OPSB)</sup>	12/12/2016
62	Eleanor L. McMMain School Roof Replacement <sup>(OPSB)</sup>	05/13/2016
63	Ernest "Dutch" Morial Elementary <sup>(RSD)</sup>	03/17/2017
64	Ernest N. Morial Elementary Security Fencing <sup>(RSD)</sup>	05/10/2011
65	Fannie C. Williams Elementary School Demolition <sup>(RSD)</sup>	03/10/2009
66	Fisk-Howard Elementary School Demolition <sup>(RSD)</sup>	10/04/2011
67	Florence J. Chester Elementary School Demolition <sup>(RSD)</sup>	06/05/2011
68	Fortier (Lusher) High School Refurbishment <sup>(OPSB)</sup>	02/05/2016
69	Francis W. Gregory Demolition <sup>(RSD)</sup>	12/21/2011
70	Frederick A. Douglass High Refurbishment <sup>(RSD)</sup>	10/28/2014
71	Frederick A. Douglass High School Science Lab <sup>(RSD)</sup>	07/05/2016
72	Frederick A. Douglass High Switchgear <sup>(RSD)</sup>	08/04/2009
73	Frederick A. Douglass High Emergency Boiler Roof Repairs <sup>(RSD)</sup>	
74	Gaudet Elementary School Refurbishment <sup>(RSD)</sup>	12/20/2016
75	Gentilly Terrace Elementary School Refurbishment <sup>(RSD)</sup>	09/22/2015
76	George Mondy Elementary School Mothball <sup>(RSD)</sup>	
77	George Washington Carver School <sup>(RSD)</sup>	03/07/2016
78	George Washington Carver High School Demolition <sup>(RSD)</sup>	08/24/2011
79	Greater St. Stephens School <sup>(OPSB)</sup>	03/18/2013
80	Harriet R. Tubman Elementary School Selective Demolition <sup>(RSD)</sup>	12/14/2014
81	Henry Allen Elementary School Refurbishment <sup>(RSD)</sup>	03/08/2016
82	Henry Allen Elementary School Kitchen Refurbishment <sup>(RSD)</sup>	02/18/2016
83	Henry Allen Elementary School Roof <sup>(RSD)</sup>	05/24/2010
84	Henry C. Schaumburg School Refurbishment <sup>(RSD)</sup>	06/26/2015
85	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation <sup>(RSD)</sup>	12/16/2011
86	Holy Cross Modular Relocation <sup>(RSD)</sup>	12/14/2010
87	Israel M. Augustine Middle School Roof Replacement <sup>(RSD)</sup>	04/13/2012
88	Israel M. Augustine Middle School Mothball <sup>(RSD)</sup>	01/18/2013
89	James Derham Demolition <sup>(RSD)</sup>	02/23/2012

90	James W. Johnson Elementary School Roof <sup>(RSD)</sup>	07/31/2010
91	New Jean Batiste de Bienville School <sup>(RSD)</sup>	06/15/2012
92	Jean Gordon Elementary School Demolition <sup>(RSD)</sup>	08/16/2010
93	JoEllen Smith Medical Center Demolition <sup>(OPSB)</sup>	
94	John Dibert Elementary School Roof <sup>(RSD)</sup>	08/20/2010
95	John W. Hoffman Elementary School Demolition <sup>(RSD)</sup>	05/25/2010
96	John F. Kennedy Modular Relocation (Schwarz Campus) <sup>(RSD)</sup>	11/05/2010
97	John F. Kennedy Modular Relocation (Coghill Modular Campus) <sup>(RSD)</sup>	08/05/2011
98	John F. Kennedy Modular Demolition <sup>(RSD)</sup>	09/16/2014
99	John F. Kennedy High School Demolition <sup>(RSD)</sup>	01/12/2012
100	John McDonogh Senior High School Bleachers and Sprinklers <sup>(RSD)</sup>	03/27/2014
101	John McDonogh Senior High School Roof <sup>(RSD)</sup>	05/04/2010
102	John A. Shaw Elementary School Mothball <sup>(RSD)</sup>	12/12/2012
103	Joseph S. Clark Senior High School Roof Repairs <sup>(RSD)</sup>	07/27/2012
104	Joseph A. Craig Elementary Canopies <sup>(RSD)</sup>	06/06/2011
105	Joseph A. Craig Elementary Elevator Installation <sup>(RSD)</sup>	01/20/2012
106	Joseph A. Hardin Elementary Security Fencing <sup>(RSD)</sup>	05/10/2011
107	Lafayette Elementary School Roof and Masonry <sup>(RSD)</sup>	06/22/2012
108	Lake Area   Landry Demolition <sup>(RSD)</sup>	05/01/2008
109	Lake Forest PK-8 at the Greater St. Stephens Site <sup>(OPSB)</sup>	11/13/2015
110	Langston Hughes Elementary School (Phase I) <sup>(RSD)</sup>	08/11/2009
111	Langston Hughes Elementary School - New Gymnasium (Phase II) <sup>(RSD)</sup>	11/10/2010
112	Langston Hughes Elementary School - Dumpster Pad <sup>(RSD)</sup>	10/12/2012
113	Lawrence D. Crocker Elementary School Demolition <sup>(RSD)</sup>	04/02/2010
114	Laurel Elementary School Refurbishment <sup>(RSD)</sup>	01/03/2018
115	L.B. Landry Annex Demolition <sup>(RSD)</sup>	05/02/2013
116	Little Woods Elementary School Demolition <sup>(RSD)</sup>	08/09/2010
117	Little Woods School (Dolores T. Aaron Elementary School) <sup>(RSD)</sup>	08/01/2013
118	Live Oak Elementary School Refurbishment <sup>(RSD)</sup>	01/06/2017
119	Live Oak Elementary School Roof <sup>(RSD)</sup>	08/04/2011
120	Live Oak Elementary School Exterior Door Replacement <sup>(RSD)</sup>	08/26/2011
121	Lorraine Hansberry Elementary School Mothball <sup>(RSD)</sup>	12/27/2012
122	Louis D. Armstrong Elementary School <sup>(RSD)</sup>	02/18/2013
123	Lusher Elementary School Refurbishment <sup>(OPSB)</sup>	10/31/2016
124	Mahalia Jackson Elementary School <sup>(OPSB)</sup>	05/11/2010
125	Mahalia Jackson Elementary School Dumpster / Other Improvements <sup>(OPSB)</sup>	03/06/2012
126	Mahalia Jackson Elementary School Office Renovation <sup>(OPSB)</sup>	04/30/2013
127	Martin Behrman Elementary School Roof <sup>(RSD)</sup>	02/23/2010
128	Martin Luther King Jr. Elementary Canopy System <sup>(RSD)</sup>	11/05/2011
129	Martin Luther King Jr. School Modular Building, Deck, Canopy <sup>(RSD)</sup>	07/31/2012
130	Martin Luther King Jr. School Kitchen Refurbishment <sup>(RSD)</sup>	02/18/2016
131	Mary Church Terrell Elementary School Demolition <sup>(RSD)</sup>	04/17/2013
132	Mary M. Bethune Elementary School Refurbishment <sup>(OPSB)</sup>	10/26/2017
133	Mary M. Bethune Elementary 1st Floor Replacement <sup>(OPSB)</sup>	01/24/2011
134	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing <sup>(OPSB)</sup>	01/21/2011
135	McDonogh #7 High School Repairs <sup>(OPSB)</sup>	

136	McDonogh #15 Elementary Exterior Masonry to SOI Standards <sup>(RSD)</sup>	06/11/2012
137	McDonogh #28 School Refurbishment <sup>(RSD)</sup>	03/15/2016
138	McDonogh #28 Elementary School Roof <sup>(RSD)</sup>	11/19/2011
139	McDonogh #32 Roof Replacement <sup>(RSD)</sup>	02/24/2012
140	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium <sup>(OPSB)</sup>	01/17/2014
141	McDonogh #35 School at the Phillip/ Waters Site <sup>(OPSB)</sup>	09/23/2015
142	McDonogh #42 Elementary School Renovation <sup>(RSD)</sup>	05/28/2015
143	McDonogh #42 Elementary School Roof <sup>(RSD)</sup>	12/21/2011
144	McDonogh #42 Elementary School HVAC Replacement <sup>(RSD)</sup>	08/09/2010
145	Mildred C. Osborne Elementary School Demolition <sup>(RSD)</sup>	02/18/2010
146	Mildred C. Osborne Elementary School <sup>(RSD)</sup>	12/03/2012
147	Modular Campuses Close Outs <sup>(RSD)</sup>	
148	Modular Classroom Demolition at Fannie C. Williams Elementary School <sup>(RSD)</sup>	05/22/2013
149	Modular Structures at Langston Hughes Elementary School <sup>(RSD)</sup>	04/05/2010
150	Morris F.X. Jeff Elementary School Demolition <sup>(RSD)</sup>	
151	Morris F.X. Jeff Elementary School Mothball <sup>(RSD)</sup>	01/15/2013
152	Murray G. Henderson Elementary School Roof <sup>(RSD)</sup>	06/23/2012
153	Nelson Elementary School Refurbishment <sup>(OPSB)</sup>	04/18/2016
154	New Andrew H. Wilson Elementary School <sup>(RSD)</sup>	10/11/2009
155	New Carter G. Woodson School <sup>(RSD)</sup>	09/14/2012
156	New Fannie C. Williams School <sup>(RSD)</sup>	08/24/2012
157	New Joseph A. Craig Elementary School <sup>(RSD)</sup>	12/09/2009
158	New L.B. Landry High School <sup>(RSD)</sup>	06/30/2010
159	New Lake Area High School <sup>(RSD)</sup>	12/28/2009
160	New Lawrence D. Crocker School <sup>(RSD)</sup>	04/29/2013
161	New PK-8 School at North Kenilworth Park at Curran Site <sup>(OPSB)</sup>	01/29/2016
162	New Parkview School <sup>(RSD)</sup>	10/12/2012
163	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens <sup>(RSD)</sup>	
164	New William Frantz Elementary School <sup>(RSD)</sup>	
165	New Orleans High School Signature Center Study <sup>(RSD)</sup>	
166	Oretha C. Haley Demo <sup>(RSD)</sup>	05/07/2012
167	Oretha C. Haley Elementary School Mothball <sup>(RSD)</sup>	09/17/2012
168	Parkview Elementary School Demolition <sup>(RSD)</sup>	08/06/2009
169	Paul L. Dunbar Elementary School Demolition <sup>(RSD)</sup>	06/16/2010
170	Paul L. Dunbar Elementary School <sup>(RSD)</sup>	06/02/2015
171	Paul B. Habans Elementary School <sup>(RSD)</sup>	06/30/2016
172	Paul B. Habans Elementary School Roof Repairs <sup>(RSD)</sup>	07/27/2012
173	Phillis Wheatley Elementary School Demolition <sup>(RSD)</sup>	09/26/2011
174	Phillis Wheatley Elementary School <sup>(RSD)</sup>	07/10/2014
175	Ray Abrams Elementary School <sup>(RSD)</sup>	03/17/2017
176	Rosenwald Elementary School Refurbishment <sup>(RSD)</sup>	04/07/2016
177	Robert M. Lusher Elementary Roof Removal & Replacement <sup>(OPSB)</sup>	07/14/2011
178	Samuel J. Green Elementary School Refurbishment <sup>(RSD)</sup>	02/15/2016
179	Samuel J. Green Elementary School Refurbishment Phase 2 <sup>(RSD)</sup>	02/15/2016
180	Sarah T. Reed High School Bleachers <sup>(RSD)</sup>	01/11/2012

181	Sarah T. Reed High School Auditorium Wall <sup>(RSD)</sup>	03/29/2010
182	Sarah T. Reed High School Kitchen Refurbishment <sup>(RSD)</sup>	02/18/2016
183	Sarah T. Reed High School Refurbishment <sup>(RSD)</sup>	12/01/2015
184	Seabrook Computer Training Center Demolition <sup>(OPSB)</sup>	06/25/2010
185	Schaumburg Chillers <sup>(RSD)</sup>	11/14/2008
186	Schwarz Alternative Repairs <sup>(RSD)</sup>	07/14/2009
187	Schwarz Alternative Modularity Demolition <sup>(RSD)</sup>	04/02/2015
188	Schwarz Modular Building Demolition <sup>(RSD)</sup>	04/02/2015
189	Sherwood Forest Elementary School Demolition <sup>(RSD)</sup>	10/28/2010
190	Sherwood Forest Elementary School <sup>(RSD)</sup>	06/30/2016
191	Small New Orleans East High School at Abramson <sup>(RSD)</sup>	09/24/2015
192	Sophie B. Wright School Renovation <sup>(RSD)</sup>	06/08/2016
193	Sophie B. Wright School Selective Demolition <sup>(RSD)</sup>	01/31/2014
194	Sophie B. Wright Various Repairs/Restroom Renovations <sup>(OPSB)</sup>	07/26/2011
195	Stuart R. Bradley Elementary School Demolition <sup>(RSD)</sup>	01/27/2010
196	Stuart R. Bradley Elementary School <sup>(RSD)</sup>	06/26/2015
197	Sylvanie Williams Elementary School AHU Replacement <sup>(RSD)</sup>	07/30/2013
198	Sylvanie Williams Elementary School Play Yard <sup>(RSD)</sup>	09/23/2010
199	Sylvanie Williams Elementary School Roof Repairs <sup>(RSD)</sup>	07/27/2012
200	Sylvanie Williams Elementary School HVAC/Chiller Replacement <sup>(RSD)</sup>	04/13/2012
201	Sylvanie Williams Elementary School Refurbishment <sup>(RSD)</sup>	02/18/2016
202	Temporary Campus for McDonogh #11 Expropriation <sup>(OPSB)</sup>	
203	Thomas A. Edison Elementary School Demolition <sup>(RSD)</sup>	03/25/2010
204	Thomy Lafon Elementary School Demolition <sup>(RSD)</sup>	11/27/2011
205	Thomy Lafon School Interpretative Display <sup>(RSD)</sup>	10/15/2013
206	Timbers Park Office Building #1 & #2 Demolition <sup>(OPSB)</sup>	09/18/2011
207	Timbers HVAC <sup>(OPSB)</sup>	09/11/2013
208	Timbers III - IT Room Relocation <sup>(OPSB)</sup>	02/11/2015
209	Village de L'est Elementary School Subsidence <sup>(RSD)</sup>	06/18/2012
210	Village de L'est Elementary School Refurbishment <sup>(RSD)</sup>	10/12/2016
211	Village de L'est Elementary School Roof and Modular Demolition <sup>(RSD)</sup>	06/16/2013
212	Vorice J. Waters Elementary School Demolition <sup>(RSD)</sup>	01/14/2010
213	Valena C. Jones Elementary School <sup>(RSD)</sup>	01/10/2013
214	Walter L. Cohen High School HVAC <sup>(RSD)</sup>	04/04/2014
215	Warren Easton High School Renovation <sup>(OPSB)</sup>	12/15/2015
216	Warren Easton School Courtyard Waterproofing <sup>(OPSB)</sup>	11/24/2017
217	Warren Easton High School Window Replacement <sup>(OPSB)</sup>	09/07/2012
218	West Bank Swing Space for Alice Harte Elementary School <sup>(OPSB)</sup>	07/11/1931
219	New William J. Guste Elementary School <sup>(RSD)</sup>	10/06/2008
220	William J. Guste Elementary School Science Lab <sup>(RSD)</sup>	08/04/2009
221	William Frantz Elementary School Environmental Remediation & Selective Demolition <sup>(RSD)</sup>	04/15/2010
222	William Frantz Elementary School Roof <sup>(RSD)</sup>	08/12/2010
