


Superintendent's Report October 2017



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Ms. Kunjan Narechania
Recovery School District

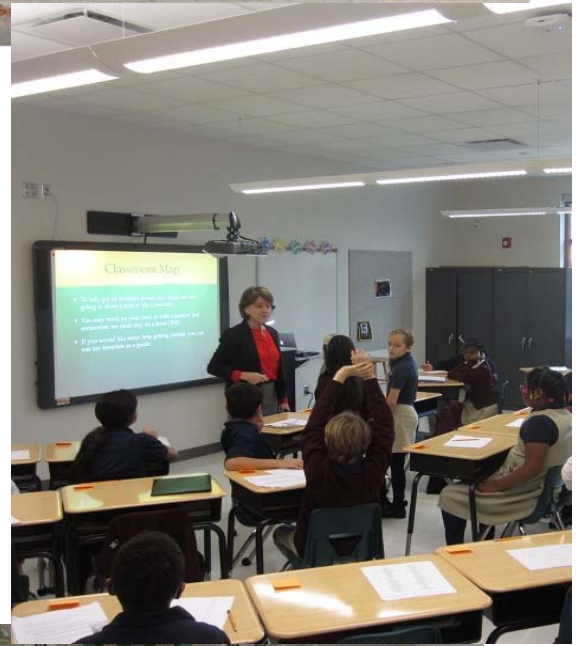

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	10
Benjamin Franklin Elementary School Renovation ^(OPSB)	10
New Karr High School, CMAR ^(RSD)	10
John McDonogh High School Renovation CMAR ^(RSD)	10
Harriet R. Tubman Elementary School Renovation ^(RSD)	11
Booker T. Washington School CMAR ^(RSD)	11
REFURBISHMENTS	12
Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)	12
Agnes L. Bauduit Elementary School Refurbishment ^(RSD)	12
Mary M. Bethune Elementary School Refurbishment ^(OPSB)	12
Warren Easton Courtyard Waterproofing ^(OPSB)	13
Harney Elementary School Downspout and Gutter Repairs ^(RSD)	13
Lafayette Elementary School Refurbishment ^(RSD)	13
Laurel Elementary School Refurbishment ^(RSD)	14
Thurgood Marshall Elementary School Refurbishment ^(RSD)	14
McDonogh #28 School Flooring Refurbishment ^(RSD)	14
McDonogh #32 School Refurbishment ^(RSD)	15
Harriet R. Tubman Elementary School Cottage Renovation ^(RSD)	15
Schaumburg Elementary School Roof Repairs ^(RSD)	15
Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing ^(RSD)	16
DEMOLITIONS	17
Demolition of Modulares at Abramson 3 ^(RSD)	17
Demolition of Modulares at Coghill ^(RSD)	17
COMPLETED PROJECTS	18

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$464 million in open contracts for the capital program after issuing \$2.4 million in new contracts, change orders and amendments in October. In addition, the total change orders to date, \$6.9 million, account for one percent (1.71%) of the total open construction contracts. RSD anticipates issuing \$96 thousand in construction contracts/change orders, and \$7 million in professional service contracts/amendments in November.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$233 million in open contracts for the capital program after issuing \$0 thousand in new contracts, change orders and amendments in October. In addition, the total change orders to date, \$9.3 million, account for approximately four percent (4.74%) of the total open construction contracts. OPSB anticipates issuing approximately \$1.9 million in construction contracts/change orders and \$113 thousand in professional service contracts and amendments in November.

Community Meetings



Future Community Meetings

No Community Meeting are Scheduled

Bid Openings

Projects which are scheduled to bid in the next 60 days

November 1, 2017

Coghill Modular Demolition Bid Opening
Village de L'est Elementary School Environmental Bid Opening

November 15, 2017

Harney Roof Bid Opening

Disadvantaged Business Enterprises (DBE) Monthly Summary



Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of October 31, 2017. The DBE subcontracts value is \$82,298,918 of the \$362,866,202 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 54 projects as of October 31, 2017. The DBE subcontracts value is \$22,992,362 of the \$73,380,038 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of October 31, 2017. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 2 projects as of October 31, 2017. The DBE subcontracts value is \$29,764,319 of the \$86,699,352 total of awarded contracts.

Total Amount of Contracts: \$ 632,083,149

Orleans Parish School Board



New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of October 31, 2017. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of October 31, 2017. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$231,354,830


* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

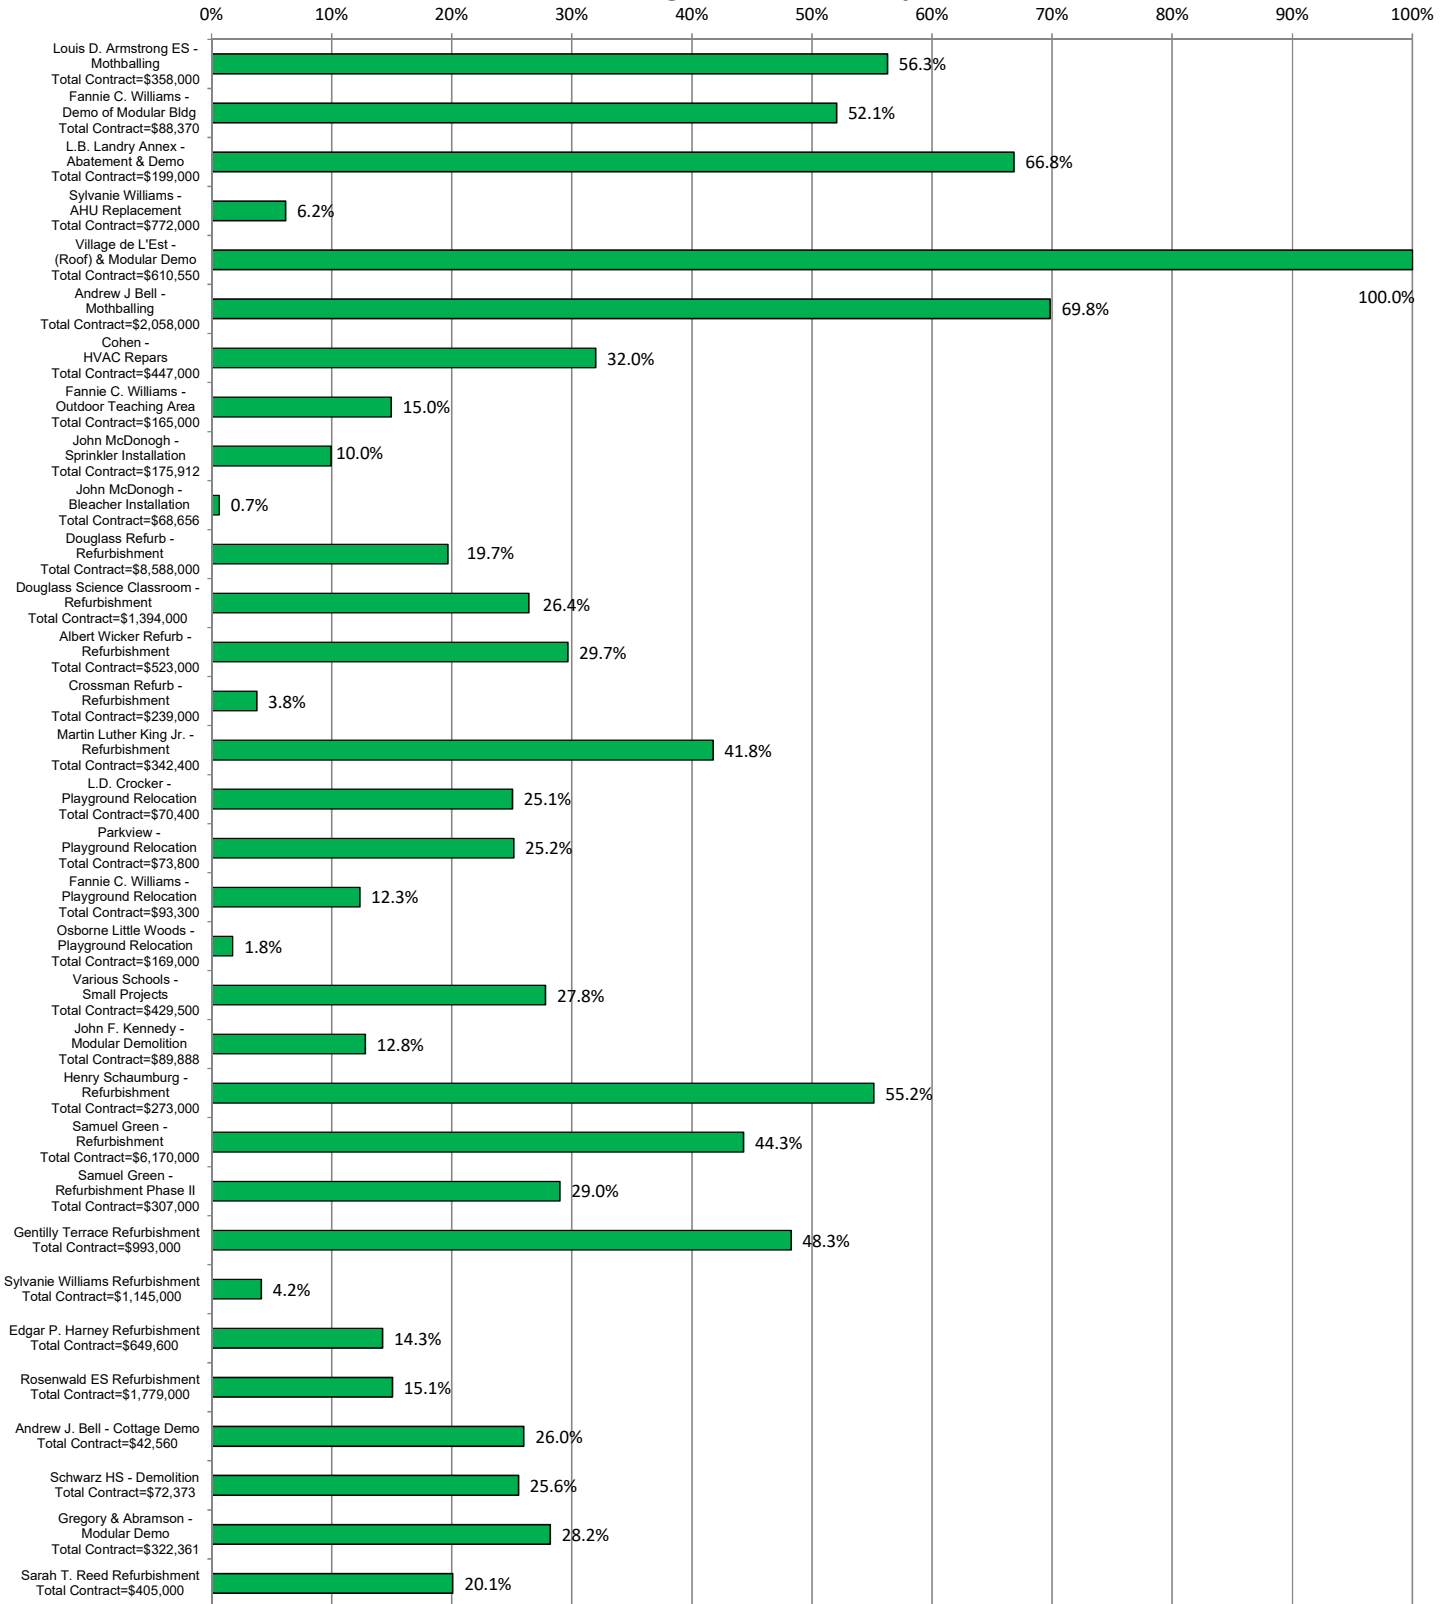

Current RSD Program DBE Participation


(Continued)

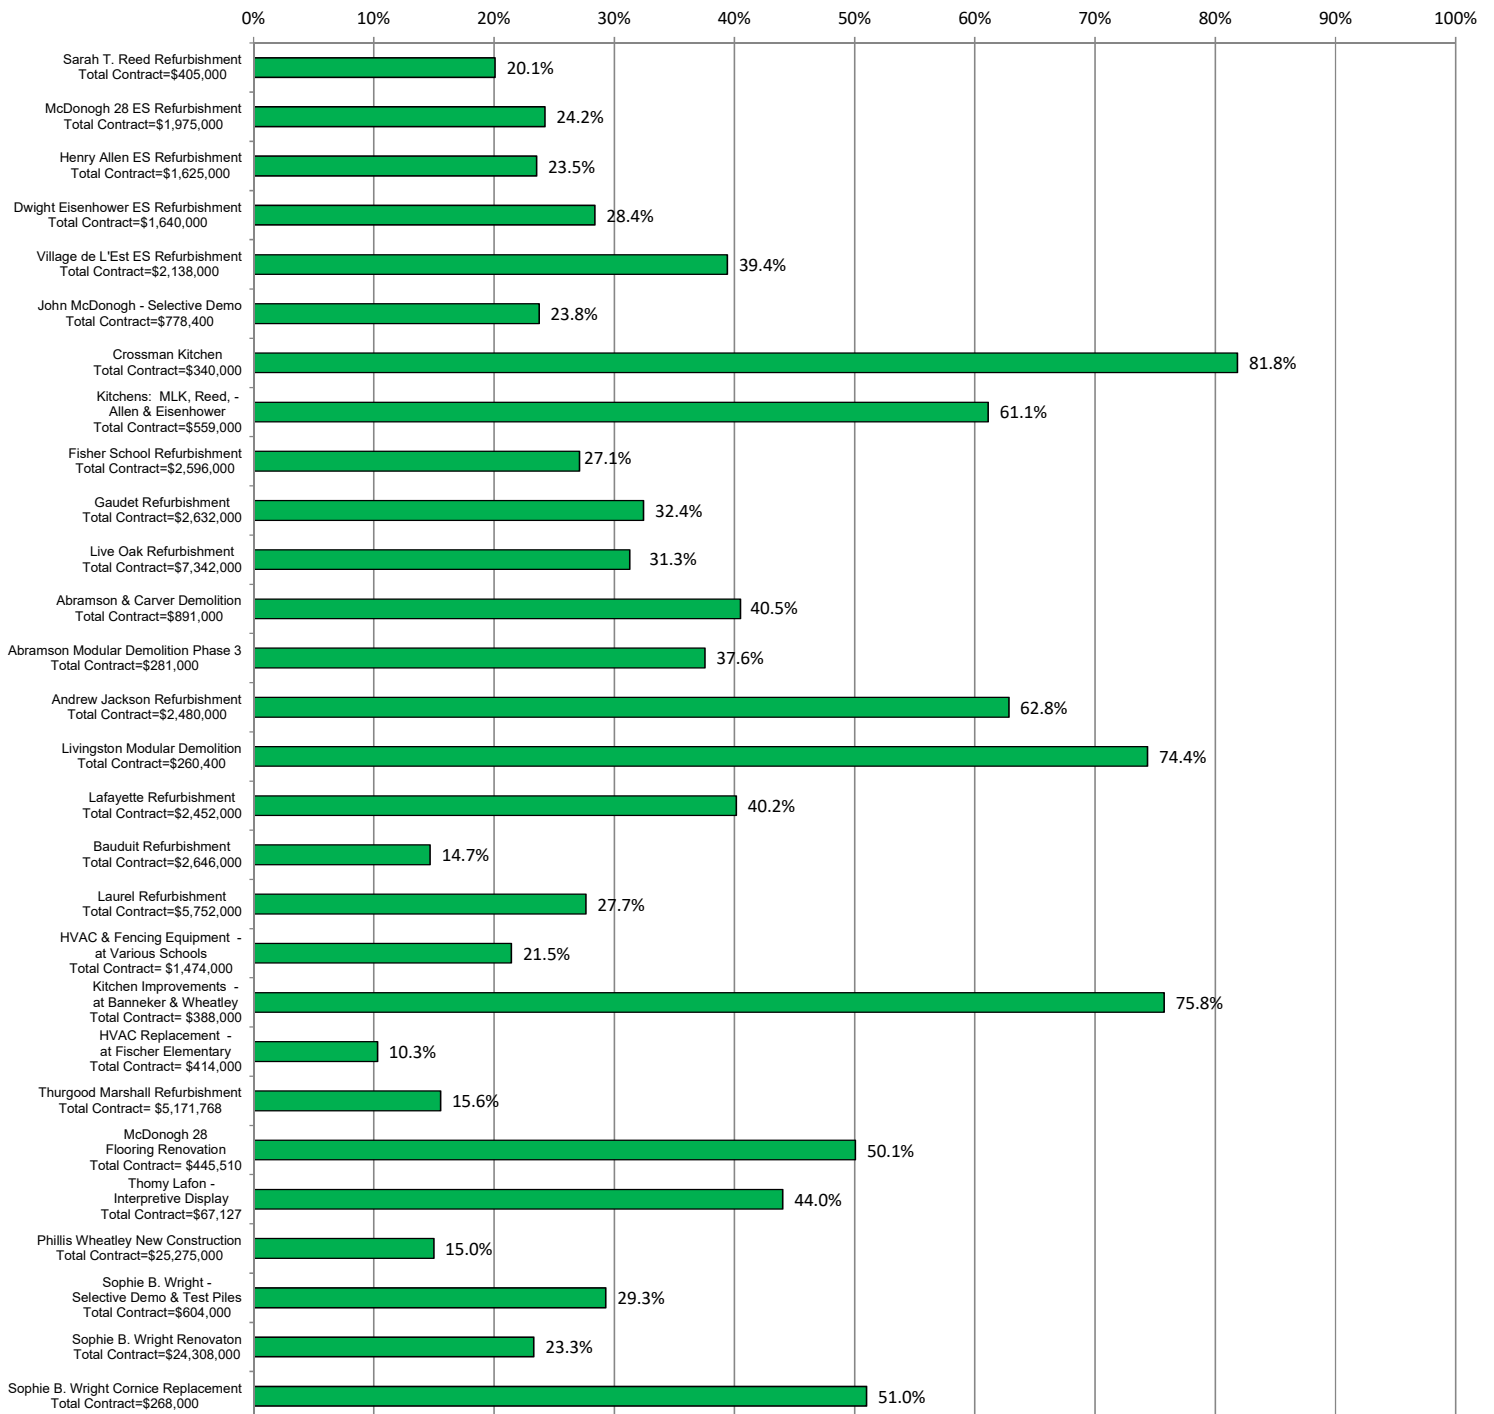

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

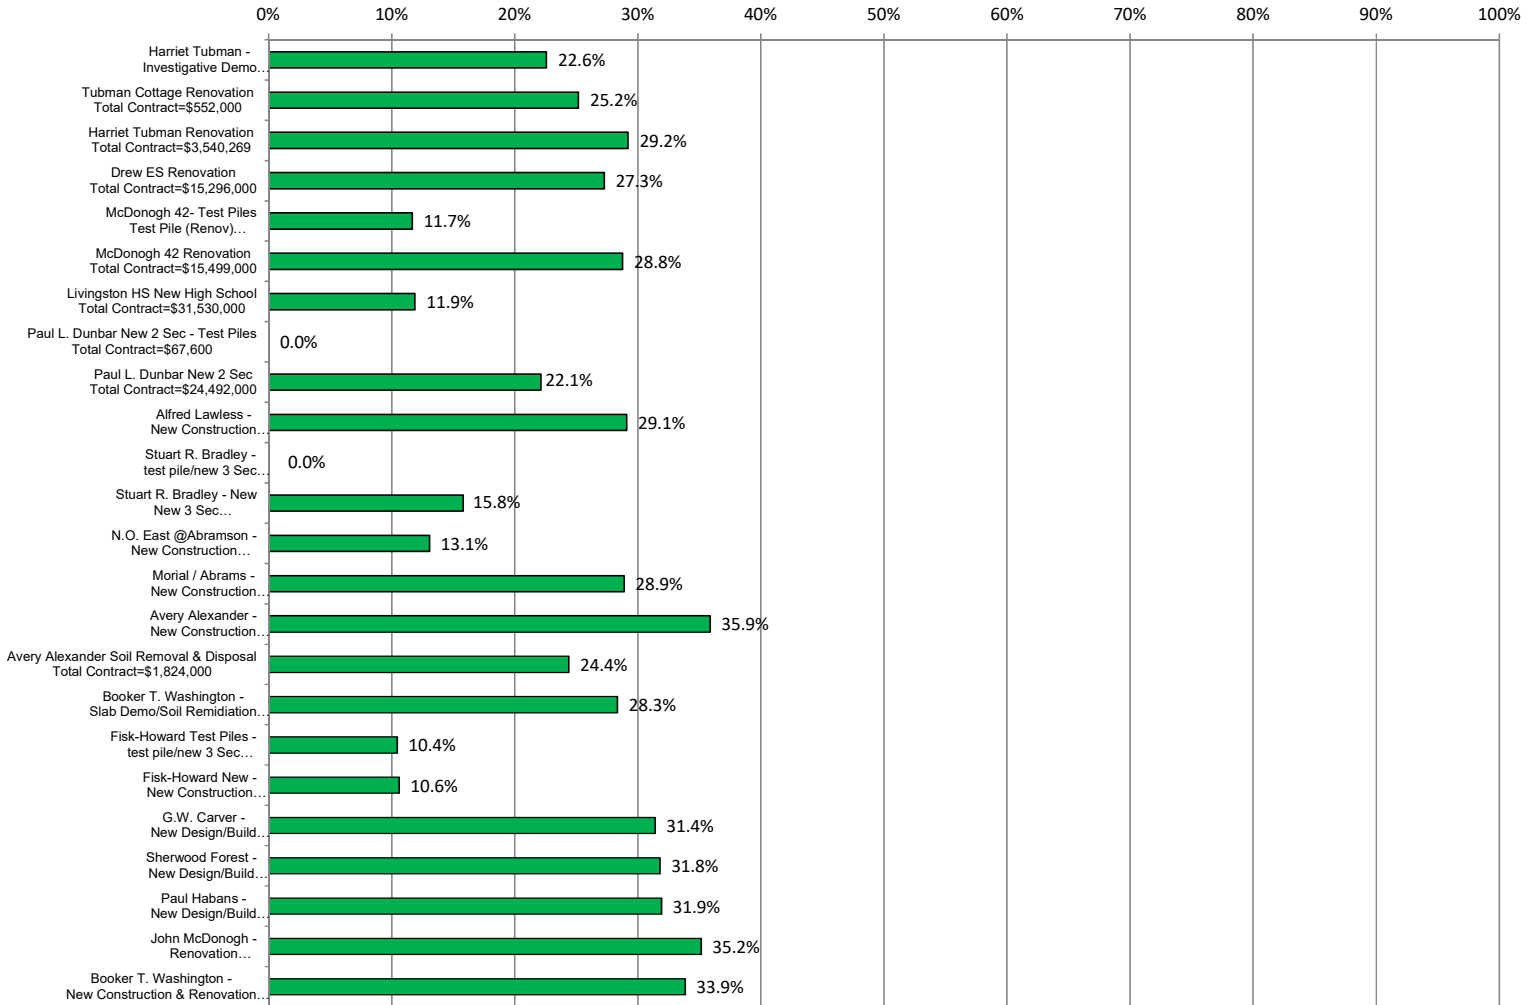

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

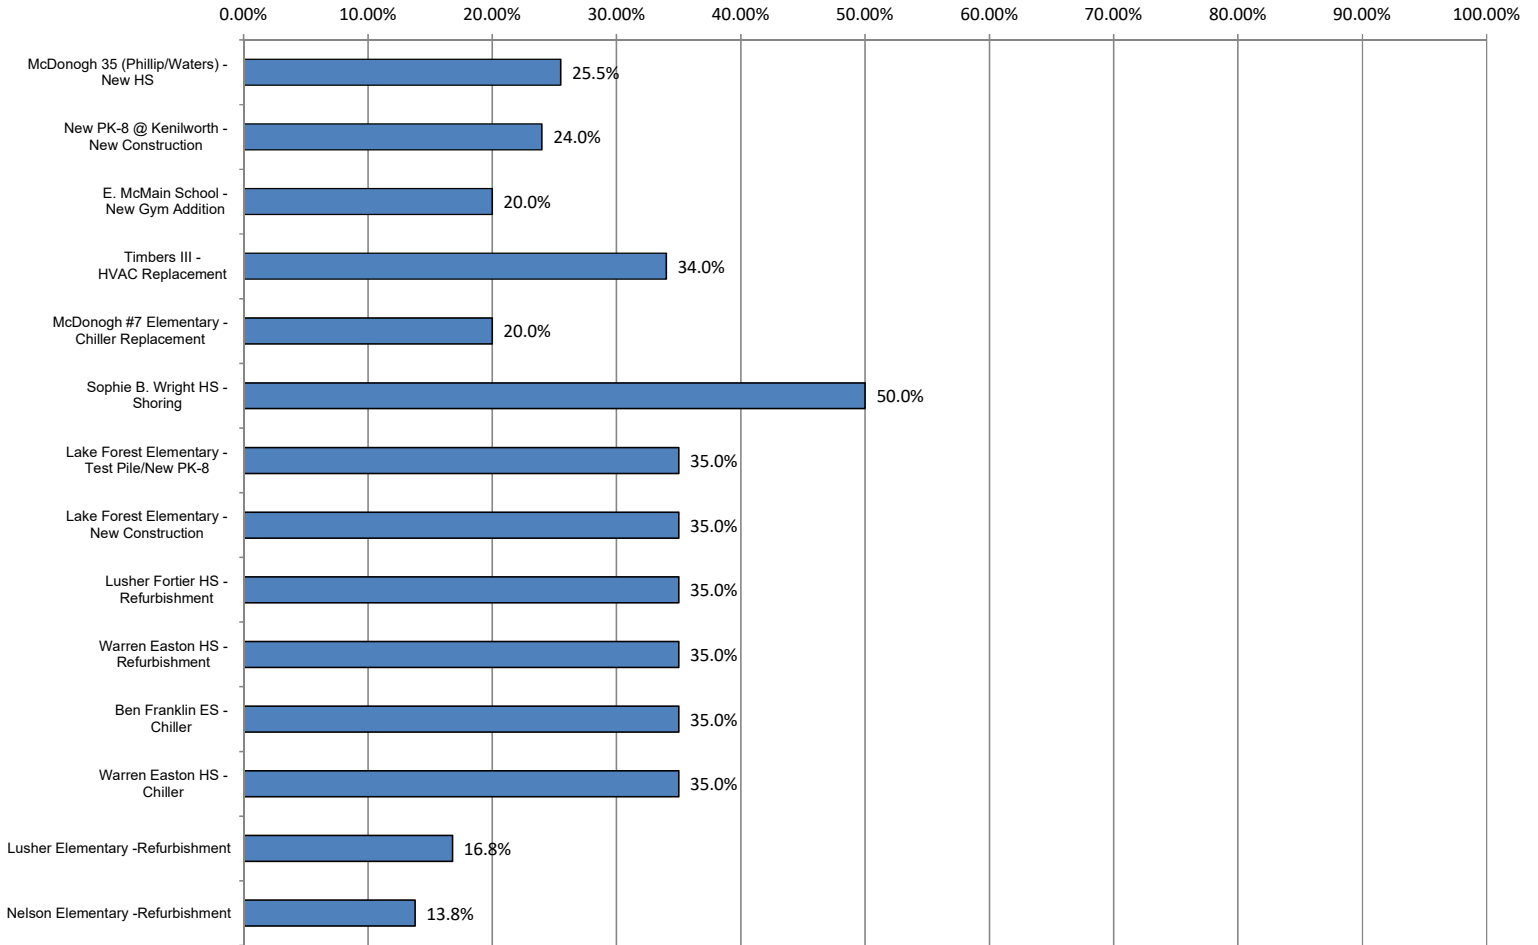

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Construction Masters

Procurement Phase

- Contracts are being reviewed



New Karr High School CMAR ^(RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - TBD

Design Phase

- 100% Construction documents were received
- GMP is due November 2017

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



John McDonogh High School Renovation CMAR ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- Activities ongoing at the Main Building include, interior partitions, window refurbishment and MEP rough-in
- Plaster repairs and window painting continues on the exterior
- Gymnasium steel erection is ongoing

Contractual Substantial Completion – October 2018

Forecasted Substantial Completion – October 2018



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

Construction Phase

- Floor replacement is ongoing on second floor
- MEP system installation ongoing
- Exterior plaster repair and painting continues
- New fence installation is ongoing

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates


Contractor – Core Construction

Construction Phase

- Erection of steel continues in Area E
- Roof decking is being installed over the kitchen area
- CMU walls construction at the gymnasium continues

Contractual Substantial Completion – January 2019

Forecasted Substantial Completion – January 2019

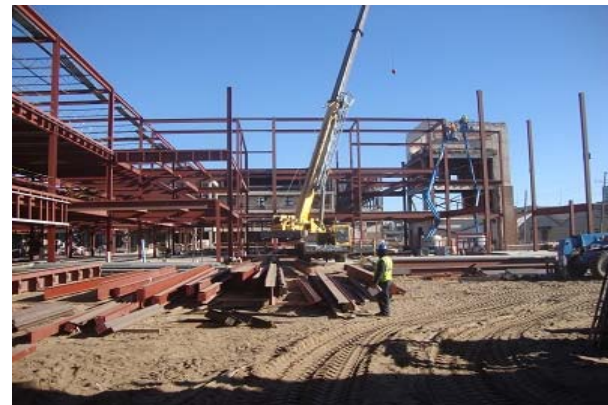

REFURBISHMENTS

Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

2300 Dumaine Street, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen at Banneker and addition of grease trap at Wheatley

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Commander Corp

Construction Phase

- Wheatley - Nearing completion
- Banneker kitchen - Contractor working on punchlist

Contractual Substantial Completion – September 2017

Forecasted Substantial Completion – October 2017



Agnes L. Bauduit Elementary School Refurbishment ^(RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor – One Construction

Construction Phase

- Project Substantial Complete October 31st
- Punch list work continues

Contractual Substantial Completion – May 2017

Actual Substantial Completion – October 2017



Mary M. Bethune Elementary School Refurbishment ^(OPSB)

4040 Eagle Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects

Contractor – Construction Masters Inc.

Construction Phase

- Exterior tuck pointing is ongoing
- Roof work is nearing completion

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017



Warren Easton School Courtyard Waterproofing^(OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Repairs to courtyard waterproofing

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - Thigpen Construction Company

Construction Phase

- Coping repairs are nearing completion

Contractual Substantial Completion – November 2017

Forecasted Substantial Completion – November 2017



Harney Elementary School Downspout and Gutter Repairs^(RSD)

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of downspouts and gutters

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - TBD

Procurement Phase

- 1st Advertisement - October 11th
- 2nd Advertisement - October 18th
- 3rd Advertisement - October 25th
- Pre-Bid Conference - October 26th
- Bid Opening - November 15th



Lafayette Elementary School Refurbishment Phase 2^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase 2

- 90% Construction Documents due December 1st



Laurel Elementary School Refurbishment ^(RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Dumpster pad work continues
- Alarm system is being replaced
- Additional HVAC work at IT room

Contractual Substantial Completion – November 2017

Forecasted Substantial Completion – October 2017



Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Blanchard Mechanical Contractors

Construction Phase

- Windows are being removed and stripped
- HVAC units are being removed
- Electrical rough in continues

Contractual Substantial Completion – June 2018

Forecasted Substantial Completion – June 2018



McDonogh #28 School Flooring Refurbishment Phase 2 ^(RSD)

2733 Esplanade Boulevard, New Orleans, LA 70114 District A Ward 7

Scope of work: Refurbishment of existing elementary school flooring

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase

- 90% Construction Documents due November 15th



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – HMS Architects

Contractor - TBD

Design Phase

- Owner is reviewing scope
- Project placed on hold



Harriet R. Tubman Elementary School Cottage Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing cottage to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Interior abatement is ongoing
- Exterior siding removal has started
- Removal of the roof continues



Schaumburg Elementary School Roof Repairs ^(RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - TBD

Procurement Phase

- Bids are under advisement



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

6501 Berkley Drive, New Orleans, LA 70131 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - Industrial and Mechanical Contractors, Inc

Construction Phase

- Village - AC units work continues
- Village - Ductwork installation is ongoing
- Reed - Fencing is nearing completion
- Reed - Piping for the new cooling tower is being installed
- Rosenwald - Contractor is installing the fan coils units

Contractual Substantial Completion – December 2017

Forecasted Substantial Completion – December 2017



DEMOLITIONS

Demolition of Modular Buildings at Abramson 3 ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – Ashley Savarino Unlimited Construction

Construction Phase

- Excavation of limestone continues
- Hauling of debris continues

Contractual Substantial Completion – February 2018

Forecasted Substantial Completion – February 2018



Demolition of Modular Buildings at Coghill ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – TBD

Procurement Phase

- 1st Advertisement - September 27th
- 2nd Advertisement - October 4th
- 3rd Advertisement - October 11th
- Pre-Bid Conference - October 12th
- Bid Opening - November 1st



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment ^(RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
7	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
8	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
9	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
10	Alfred Lawless Senior ^(RSD)	12/18/2015
11	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
12	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
13	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
14	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
15	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
16	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
17	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
18	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
19	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
20	Augustine Elementary School Roof ^(RSD)	04/13/2012
21	Avery-Alexander Elementary School ^(RSD)	06/19/2017
21	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
22	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
23	Bell JH Shoring ^(RSD)	06/28/2011
24	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
25	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
26	Bienville Elementary School Demolition ^(RSD)	05/04/2009
27	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
28	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
29	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
30	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
31	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
32	Charles J. Colton Elementary School ^(RSD)	05/23/2013
33	Charles R. Drew Elementary School ^(RSD)	04/17/2015
34	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
35	Cohen High School Health Clinic ^(RSD)	12/24/2008
36	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
37	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
38	Demolition of Modular Buildings at Abramson and Carver ^(RSD)	01/18/2017
39	Demolition of Modular Buildings at Livingston ^(RSD)	01/18/2017
40	Douglass High School Under Floor Utilities ^(RSD)	
41	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
42	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014

43	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
44	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
45	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
46	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011
47	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
48	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
49	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
50	Edna Karr High School - Assessment ^(OPSB)	
51	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
52	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
53	New Edward Hynes School ^(OPSB)	02/06/2012
54	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
55	Edward Livingston High School ^(RSD)	01/05/2015
56	Eleanor L. McMMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
57	Eleanor L. McMMain School Clinic ^(OPSB)	07/24/2013
58	Eleanor L. McMMain School Maintenance Upgrades ^(OPSB)	12/12/2016
59	Eleanor L. McMMain School Roof Replacement ^(OPSB)	05/13/2016
60	Ernest "Dutch" Morial Elementary ^(RSD)	03/17/2017
61	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
62	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
63	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
64	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
65	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
66	Francis W. Gregory Demolition ^(RSD)	12/21/2011
67	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
68	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
69	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
70	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
71	Gaudet Elementary School Refurbishment ^(RSD)	12/20/2016
72	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
73	George Mondy Elementary School Mothball ^(RSD)	
74	George Washington Carver School ^(RSD)	03/07/2016
75	George Washington Carver High School Demolition ^(RSD)	08/24/2011
76	Greater St. Stephens School ^(OPSB)	03/18/2013
77	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
78	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
79	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
80	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
81	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
82	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
83	Holy Cross Modular Relocation ^(RSD)	12/14/2010
84	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
85	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
86	James Derham Demolition ^(RSD)	02/23/2012
87	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
88	New Jean Batiste de Bienville School ^(RSD)	06/15/2012

89	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
90	JoEllen Smith Medical Center Demolition ^(OPSB)	
91	John Dibert Elementary School Roof ^(RSD)	08/20/2010
92	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
93	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
94	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
95	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
96	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
97	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
98	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
99	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
100	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
101	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
102	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
103	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
104	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
105	Lake Area Landry Demolition ^(RSD)	05/01/2008
106	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
107	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
108	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
109	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
110	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
111	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
112	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
113	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
114	Live Oak Elementary School Refurbishment ^(RSD)	01/06/2017
115	Live Oak Elementary School Roof ^(RSD)	08/04/2011
116	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
117	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
118	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
119	Lusher Elementary School Refurbishment ^(OPSB)	10/31/2016
120	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
121	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
122	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
123	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
124	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
125	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
126	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
127	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
128	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
129	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
130	McDonogh #7 High School Repairs ^(OPSB)	
131	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
132	McDonogh #28 School Refurbishment ^(RSD)	03/15/2016
133	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
134	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012

135	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
136	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
137	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
138	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
139	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
140	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
141	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
142	Modular Campuses Close Outs ^(RSD)	
143	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
144	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010
145	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
146	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
147	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
148	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
149	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
150	New Carter G. Woodson School ^(RSD)	09/14/2012
151	New Fannie C. Williams School ^(RSD)	08/24/2012
152	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
153	New L.B. Landry High School ^(RSD)	06/30/2010
154	New Lake Area High School ^(RSD)	12/28/2009
155	New Lawrence D. Crocker School ^(RSD)	04/29/2013
156	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
157	New Parkview School ^(RSD)	10/12/2012
158	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
159	New William Frantz Elementary School ^(RSD)	
160	New Orleans High School Signature Center Study ^(RSD)	
161	Oretha C. Haley Demo ^(RSD)	05/07/2012
162	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
163	Parkview Elementary School Demolition ^(RSD)	08/06/2009
164	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
165	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
166	Paul B. Habans Elementary School ^(RSD)	06/30/2016
167	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
168	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
169	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
170	Ray Abrams Elementary School ^(RSD)	03/17/2017
171	Rosenwald Elementary School Refurbishment ^(RSD)	04/07/2016
172	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
173	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
174	Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD)	02/15/2016
175	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
176	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
177	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
178	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
179	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010

180	Schaumburg Chillers ^(RSD)	11/14/2008
181	Schwarz Alternative Repairs ^(RSD)	07/14/2009
182	Schwarz Alternative Modulars Demolition ^(RSD)	04/02/2015
183	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
184	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
185	Sherwood Forest Elementary School ^(RSD)	06/30/2016
186	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
187	Sophie B. Wright School Renovation ^(RSD)	06/08/2016
188	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
189	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
190	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
191	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
192	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
193	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
194	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
195	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
196	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
197	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
198	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
199	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
200	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
201	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
202	Timbers HVAC ^(OPSB)	09/11/2013
203	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
204	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
205	Village de L'est Elementary School Refurbishment ^(RSD)	10/12/2106
206	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
207	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
208	Valena C. Jones Elementary School ^(RSD)	01/10/2013
209	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
210	Warren Easton High School Renovation ^(OPSB)	12/15/2015
211	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
212	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
213	New William J. Guste Elementary School ^(RSD)	10/06/2008
214	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
215	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
216	William Frantz Elementary School Roof ^(RSD)	08/12/2010
