





Superintendent's Report October 2018



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department
of Education
Ms. Kunjan Narechania
Recovery School District



Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

| | |
|---|----|
| TABLE OF CONTENTS | 1 |
| FINANCIAL OVERVIEW | 2 |
| COMMUNITY MEETINGS | 3 |
| BID OPENINGS | 4 |
| DBE OVERVIEW MONTHLY SUMMARY | 5 |
| NEW & MAJOR RENOVATION | 11 |
| Benjamin Franklin Elementary School Renovation ^(OPSB) | 11 |
| Career Technical Education High School at Kerlerec Street CMaR ^(RSD) | 11 |
| New Cohen High School CMaR ^(RSD) | 11 |
| New Karr High School, CMAR ^(RSD) | 12 |
| New Orleans Charter Science and Mathematics High School ^(OPSB) | 12 |
| John McDonogh High School Renovation CMAR ^(RSD) | 12 |
| Booker T. Washington School CMAR ^(RSD) | 13 |
| REFURBISHMENTS | 14 |
| Fisk Howard Exterior Envelope Repairs ^(RSD) | 14 |
| Harney Elementary School Downspout and Gutter Repairs ^(RSD) | 14 |
| Lafayette Elementary School Refurbishment ^(RSD) | 14 |
| McDonogh #42 School Refurbishment ^(RSD) | 15 |
| Eleanor McMain School Envelope Repairs ^(OPSB) | 15 |
| Schaumburg Elementary School Roof Repairs ^(RSD) | 15 |
| DEMOLITIONS | 16 |
| Demolition of Modulars at Coghill ^(RSD) | 16 |
| COMPLETED PROJECTS | 17 |

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$266 million in open contracts for the capital program after issuing \$17 thousand in new contracts, change orders and amendments in October. In addition, the total change orders to date, \$3.7 million, account for one percent (1.69%) of the total open construction contracts. RSD anticipates issuing \$85 million in construction contracts/change orders, and \$809 thousand in professional service contracts/amendments in November.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$167 million in open contracts for the capital program after issuing \$0 thousand in new contracts, change orders and amendments in October. In addition, the total change orders to date, \$5.6 million, account for approximately four percent (4.24%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 thousand in construction contracts/change orders and \$(-186) thousand in professional service contracts and amendments in November.

Community Meetings



Future Community Meetings

NOVEMBER 27, 2018

New Orleans Charter Science and Mathematics High School Ground
Breaking
2011 Bienville Street, New Orleans LA 70112

DECEMBER 4, 2018

John McDonogh High School Ribbon Cutting
2426 Esplanade Avenue, New Orleans LA 70119

Bid Openings

Projects which are scheduled to bid in the next 60 days

November 28, 2018

Ben Franklin Elementary School Renovation Phase II

Disadvantaged Business Enterprises (DBE) Monthly Summary



Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 26 projects as of October 31, 2018. The DBE subcontracts value is \$82,609,571 of the \$364,282,232 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 61 projects as of October 31, 2018. The DBE subcontracts value is \$23,971,683 of the \$77,657,520 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of October 31, 2018. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 3 projects as of October 31, 2018. The DBE subcontracts value is \$44,890,702 of the 134,245,850 total of awarded contracts.

Total Amount of Contracts: \$ 685,323,252

Orleans Parish School Board



New & Renovations:

DBE Contractors secured subcontracts on 17 projects as of October 31, 2018. The DBE subcontracts value is \$65,999,022 of the \$263,467,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 4 projects as of October 31, 2018. The DBE subcontracts value is \$569,422 of the \$1,540,999 total of awarded contracts.


Total Amount of Contracts: \$265,008,830

* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

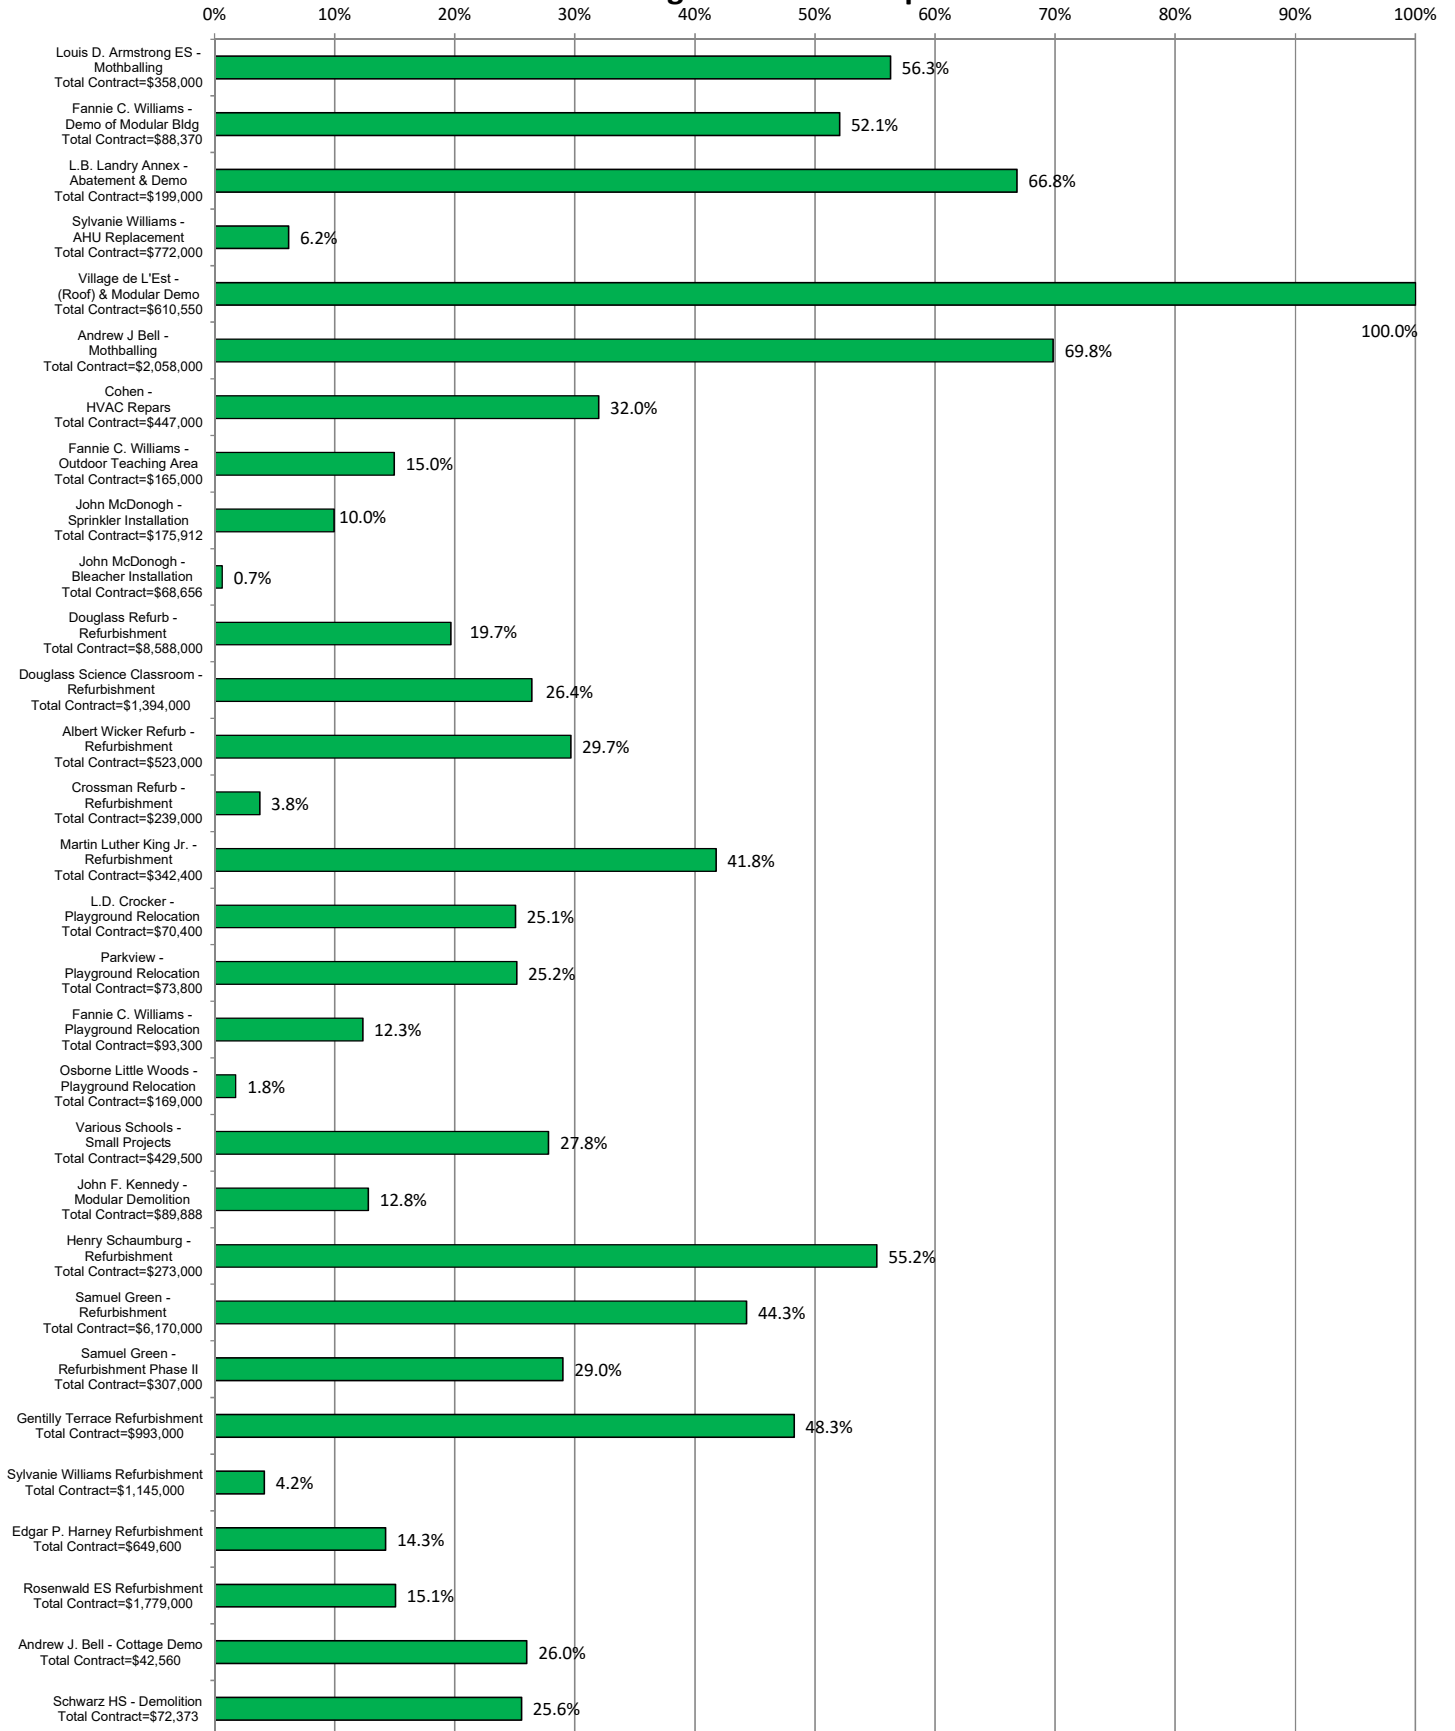


Current RSD Program DBE Participation (Continued)

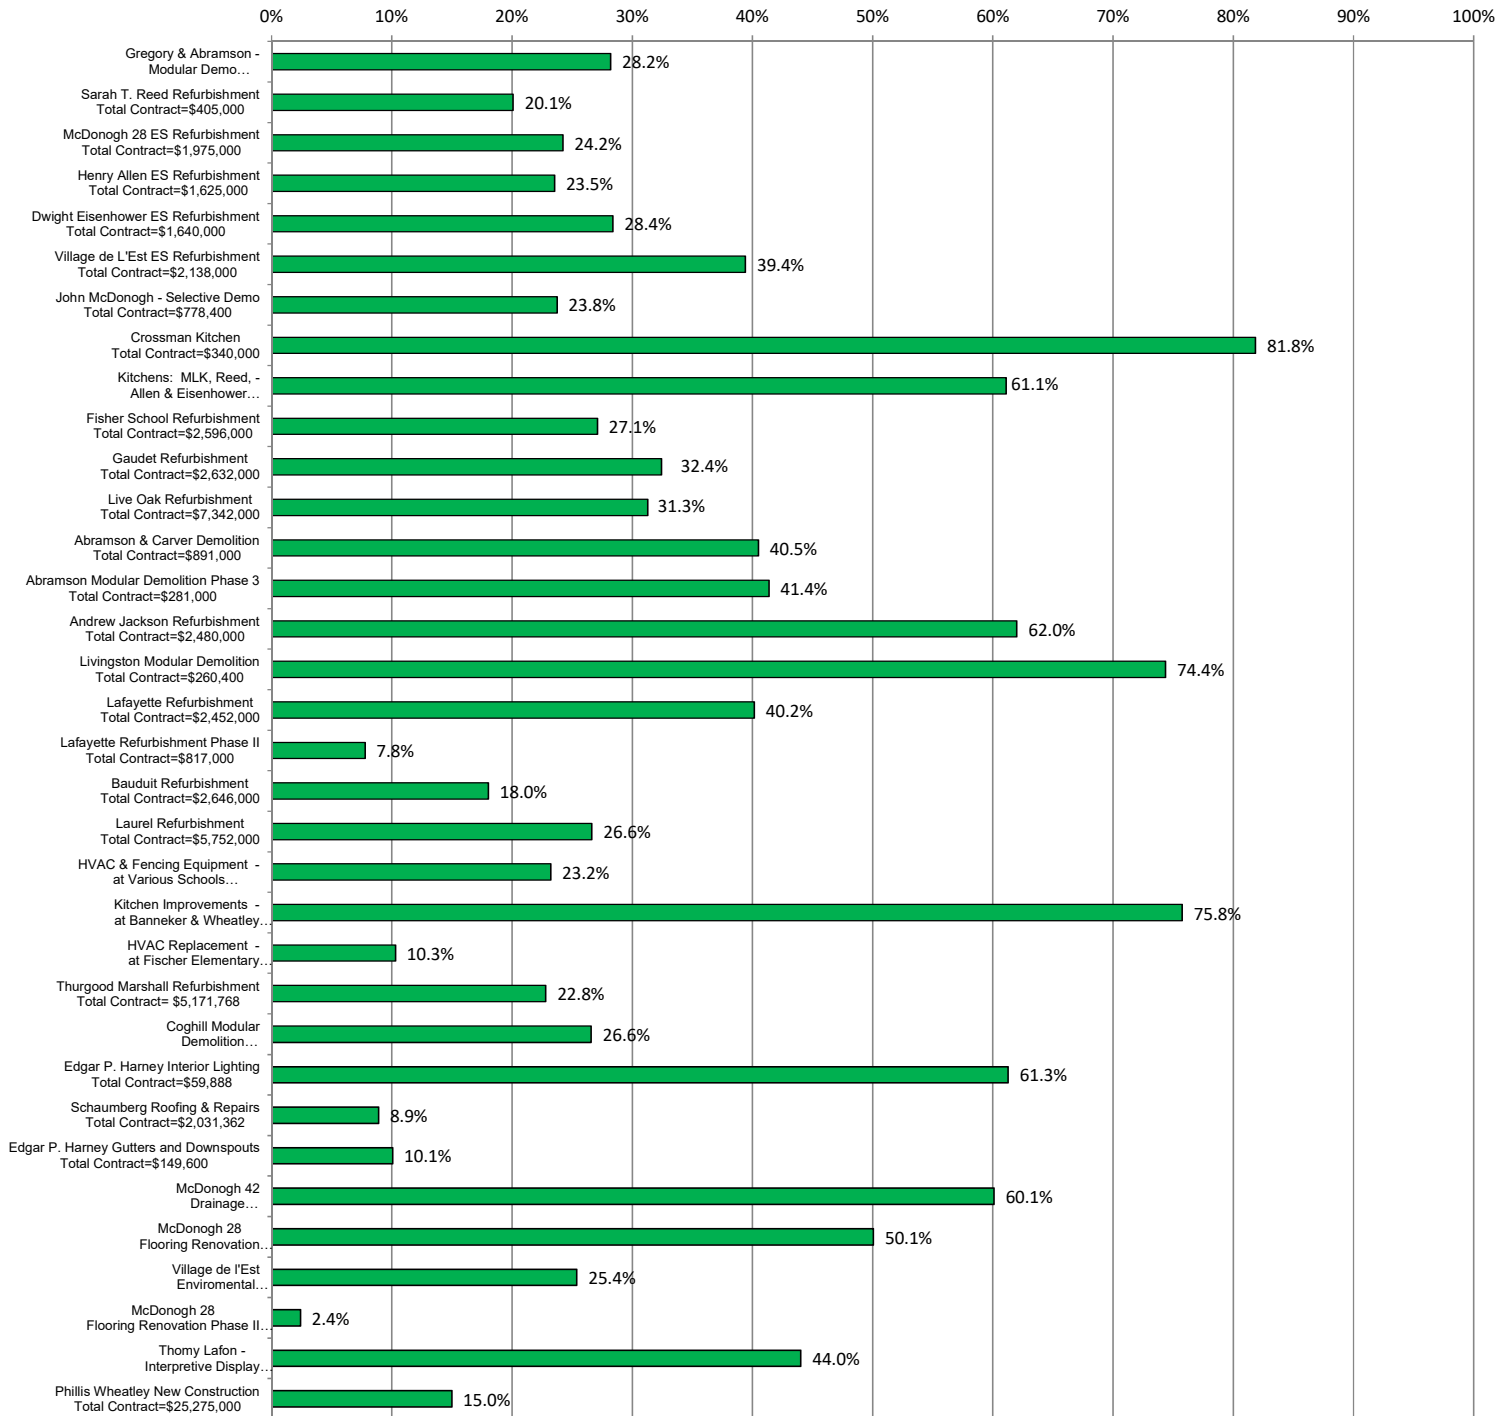

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

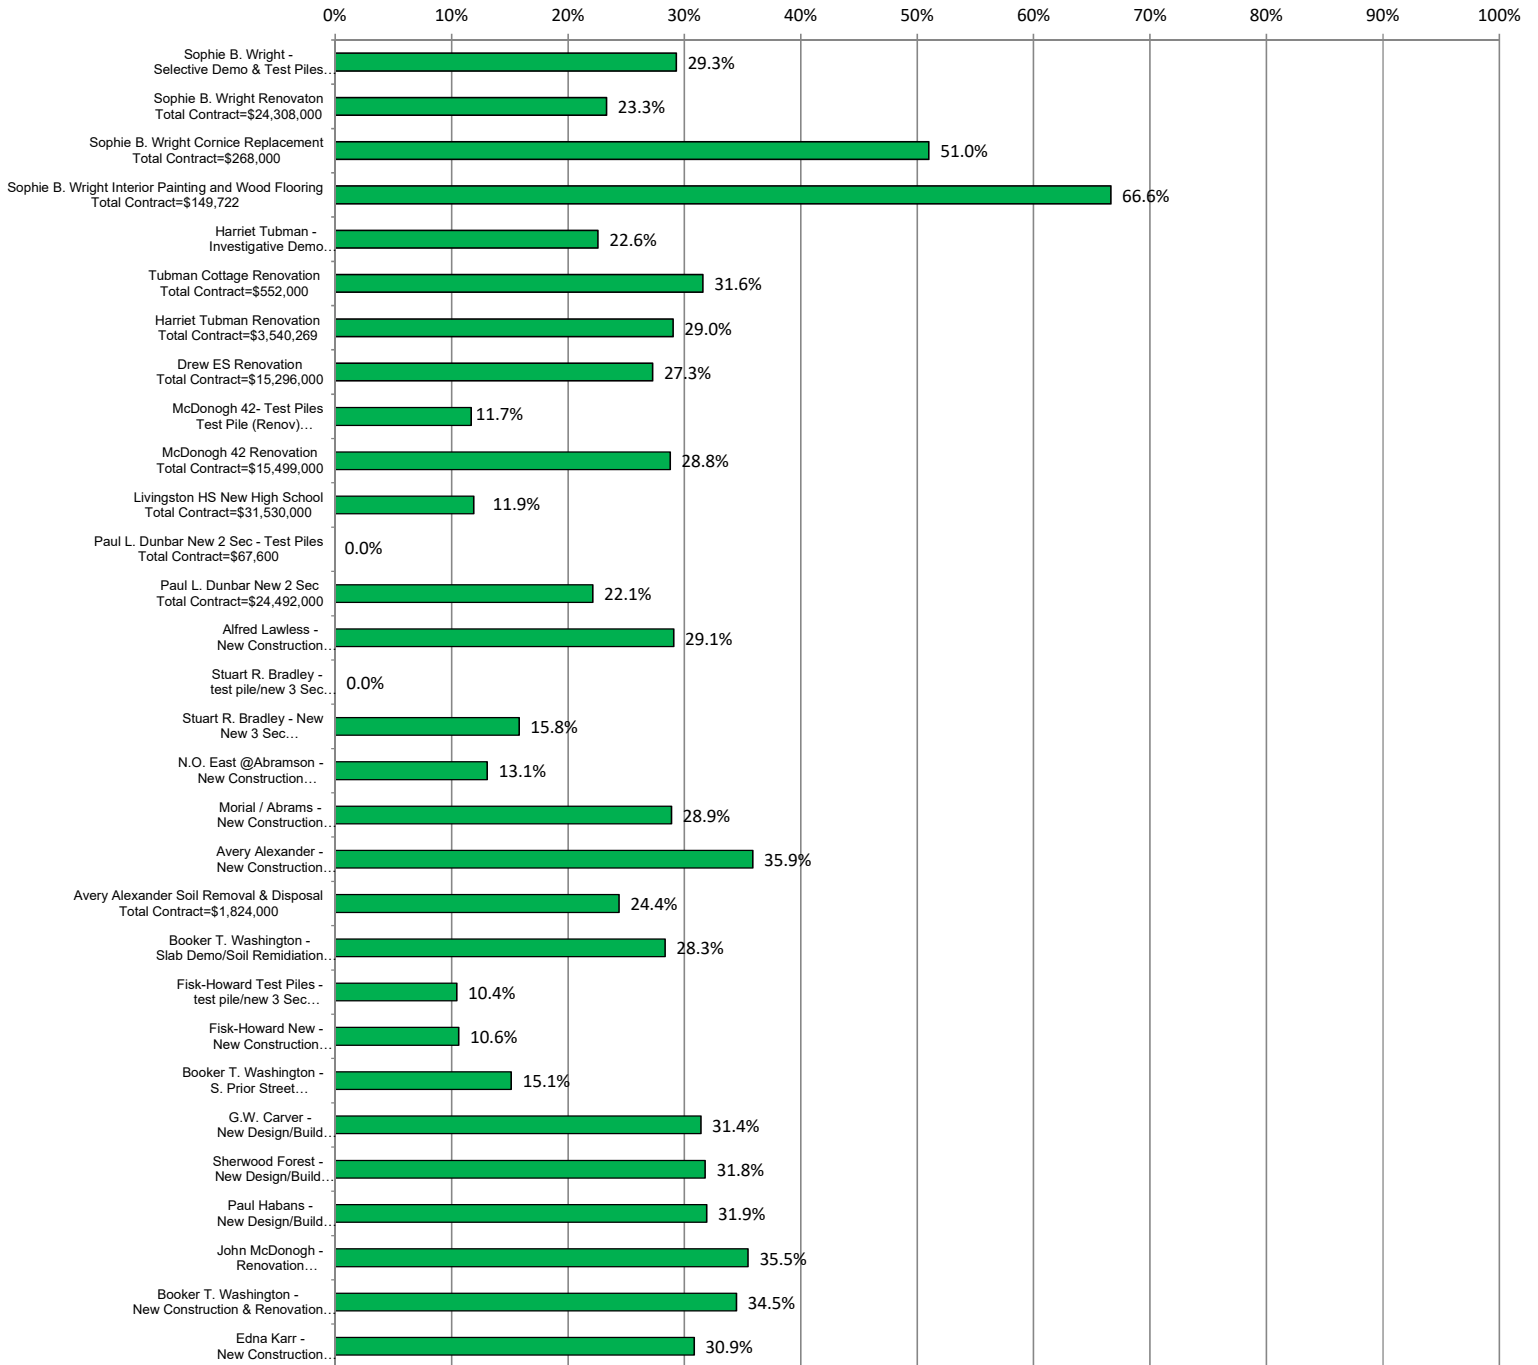

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

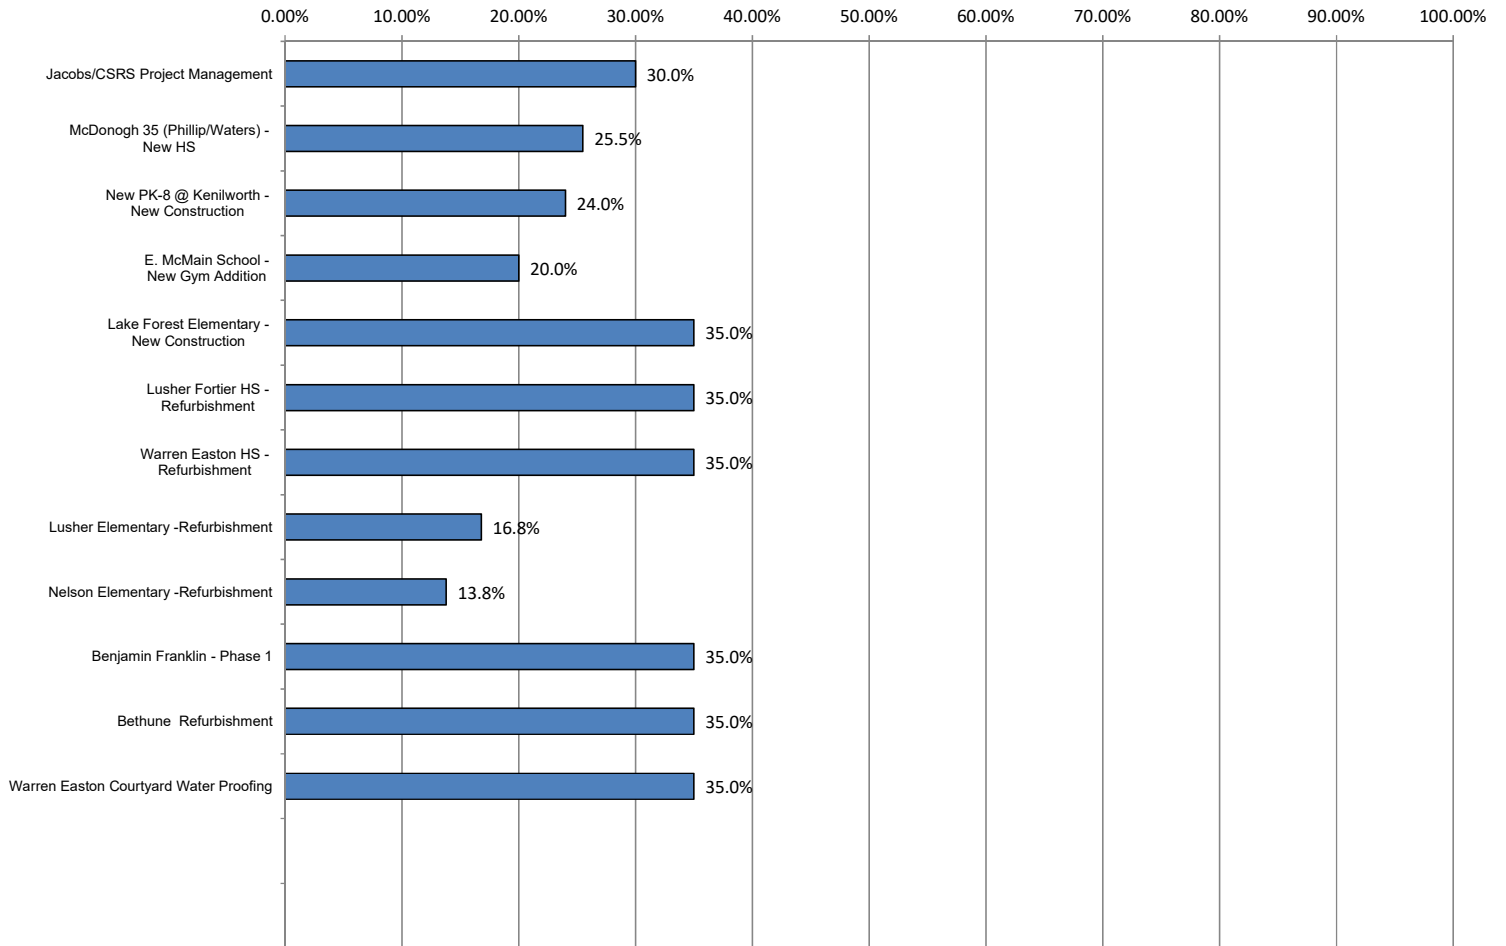

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Benjamin Franklin Elementary School Renovation Phase 2 ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- 1st Advertisement - October 24th
- 2nd Advertisement - October 31st
- 3rd Advertisement - November 7th
- Pre-Bid Conference - November 8th
- Bid Opening - November 28th



Career Technical Education High School at Kerlerec Street CMAR ^(RSD)

1331 Kerlerec Street, New Orleans, LA 70116 District D Ward 7

Scope of work: Renovation of existing high school

Funding Source – FEMA /CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase

- Schematic Design is due December 14th
- CMAR RFQ's are being reviewed



New Cohen High School CMAR ^(RSD)

3520 Dryades Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – HMS Architects

Contractor - TBD

Design Phase

- CMAR RFQ's are being reviewed
- Space usage charts were being reviewed with the charter



New Karr High School CMAR ^(RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - Core Construction

Construction Phase

- Grade beams are being poured in area 5
- Structural steel and decking is being installed in area 2
- Forming of slab continues
- Framing of walls is expected to start in November

Contractual Substantial Completion – April 2020

Forecasted Substantial Completion – April 2020



New Orleans Charter Science and Mathematics High School ^(OPSB)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - The McDonnel Group

Construction Phase

- Demolition is ongoing

Contractual Substantial Completion – January 2021

Forecasted Substantial Completion – January 2021



John McDonogh High School Renovation CMAR ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction


Close out Phase

- Contractor working on school punch list
- Ribbon Cutting December 4th
- Gymnasium Work continues

Contractual Substantial Completion – October 2018

Actual Substantial Completion - Main Building – September 2018

Forecasted Substantial Completion - Gymnasium – November 2018

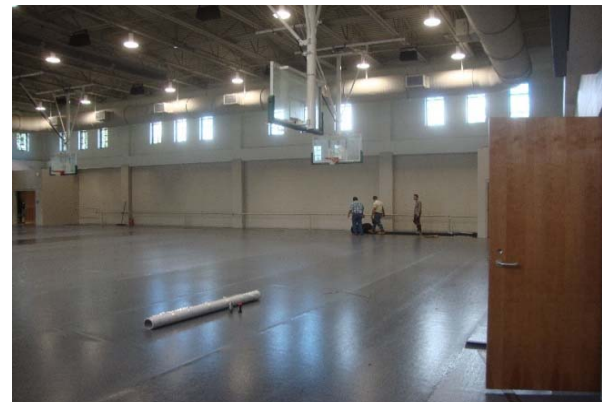

Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Contractor's emphasis is on closing the building envelope
- Exterior brick work continues
- Terrazzo Installation continues
- Work on the Cube has started

Contractual Substantial Completion – January 2019

Forecasted Substantial Completion – May 2019



REFURBISHMENTS

Fisk Howard Exterior Envelope Repairs ^(RSD)

211 South Lopez Street New Orleans, LA 70119, District B Ward 3

Scope of work: Repairs to exterior

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - LLJ Environmental Construction

Procurement Phase

- Contracts are being reviewed and signed
- Preconstruction meeting is October 23rd



Harney Elementary School Downspout and Gutter Repairs ^(RSD)

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of downspouts and gutters

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - Crescent Commercial

Construction Phase

- Contractor submitted a recovery schedule
- Work is proceeding on the gutters

Contractual Substantial Completion – September 2018

Forecasted Substantial Completion – November 2018



Lafayette Elementary School Refurbishment Phase 2 ^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to floor replacement

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Law Industries

Construction Phase

- Substandard containment exposes building to environmental contamination
- General Contractor has been terminated (16th July)
- Building being assessed for remediation



McDonogh #42 School Drainage ^(RSD)

1651 North Tonti Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Site Drainage

Funding Source – Insurance / Tax Credit

Architect – Eskew+Dumez+Ripple

Contractor - Commander Corporation

Close Out Phase

- Project is Substantial Complete October 15th
- Contractor is finishing punch list

Contractual Substantial Completion – October 2018

Actual Substantial Completion – October 2018



Eleanor McMain School Envelope Repairs ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Exterior stucco and window repairs

Funding Source – General Fund & Harrah's

Architect – Concordia, LLC

Contractor – Tuna Construction

Construction Phase

- Exterior painting continues
- Contractor is refurbishing wood windows
- Plaster repairs on interior lightwells has started

Contractual Substantial Completion – April 2019

Forecasted Substantial Completion – April 2019



Schaumburg Elementary School Roof Repairs ^(RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - Laperouse Metal Works, Inc

Construction Phase

- Installation of roof panels is ongoing
- Spray foam has started at main roof
- Fencing is complete

Contractual Substantial Completion – August 2018

Forecasted Substantial Completion – December 2018



DEMOLITIONS

Demolition of Modular Buildings at Coghill ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – Construction Management Enterprises

Construction Phase

- Additional topsoil was added to the site
- Concrete sidewalks are finished at Mithra street side
- Project is nearing completion

Contractual Substantial Completion – August 2018

Forecasted Substantial Completion – November 2018



Comprehensive List - Completed Projects

| | | |
|----|---|------------|
| 1 | Abrams Morial Abramson Coghill Demolition ^(RSD) | 11/17/2008 |
| 2 | A. D. Cross Elementary School Energy Conservation ^(RSD) | |
| 3 | A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD) | 06/12/2012 |
| 4 | A. D. Crossman Elementary School Refurbishment ^(RSD) | 06/04/2014 |
| 5 | A. D. Crossman School Kitchen Refurbishment ^(RSD) | 01/15/2017 |
| 6 | A. P. Tureaud Elementary School Roof Repairs ^(RSD) | 06/13/2013 |
| 7 | Agnes Bauduit Elementary School Refurbishment ^(RSD) | 10/31/2017 |
| 8 | Agnes Bauduit Elementary School Boiler ^(RSD) | 12/07/2009 |
| 9 | Albert Wicker Elementary School Refurbishment ^(RSD) | 03/27/2014 |
| 10 | Albert Wicker Elementary School Roof Repairs ^(RSD) | 06/13/2013 |
| 11 | Alfred Lawless Senior ^(RSD) | 12/18/2015 |
| 12 | Alfred Lawless Senior High Security Fencing ^(RSD) | 06/15/2011 |
| 13 | Alice M. Harte Elementary School ^(OPSB) | 11/19/2014 |
| 14 | Alice M. Harte Elementary School Demolition ^(OPSB) | 12/14/2011 |
| 15 | Andrew J. Bell Junior High School Roof Replacement ^(RSD) | 02/08/2014 |
| 16 | Andrew J. Bell Junior High School Mothball ^(RSD) | 06/28/2011 |
| 17 | Andrew Jackson Elementary School Roof Repairs ^(RSD) | 07/27/2012 |
| 18 | Andrew Jackson Elementary School Solar Panels ^(RSD) | 01/14/2013 |
| 19 | Andrew H. Wilson Elementary School Cottage ^(RSD) | 10/11/2010 |
| 20 | Arthur Ashe Elementary School Kitchen Renovation ^(OPSB) | |
| 21 | Augustine Elementary School Roof ^(RSD) | 04/13/2012 |
| 22 | Avery-Alexander Elementary School ^(RSD) | 06/19/2017 |
| 23 | Avery-Alexander Elementary School Demolition ^(RSD) | 06/15/2012 |
| 24 | Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD) | 10/30/2017 |
| 25 | Barbara C. Jordan Elementary School Demolition ^(RSD) | 05/30/2011 |
| 26 | Bell JH Shoring ^(RSD) | 06/28/2011 |
| 27 | Benjamin Banneker Elementary School Energy Conservation ^(RSD) | |
| 28 | Benjamin Franklin Senior High School ^(OPSB) | 08/23/2013 |
| 29 | Bienville Elementary School Demolition ^(RSD) | 05/04/2009 |
| 30 | Booker T. Washington High School Environmental Remediation ^(RSD) | 12/13/2015 |
| 31 | Booker T. Washington High School Partial Demolition ^(RSD) | 04/07/2013 |
| 32 | Carter G. Woodson Middle School Demolition ^(RSD) | 02/09/2010 |
| 33 | Central Services Warehouse Demolition ^(OPSB) | 01/05/2012 |
| 34 | Charles J. Colton Elementary Selective Demolition ^(RSD) | 07/26/2010 |
| 35 | Charles J. Colton Elementary School ^(RSD) | 05/23/2013 |
| 36 | Charles R. Drew Elementary School ^(RSD) | 04/17/2015 |
| 37 | Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD) | 06/08/2011 |
| 38 | Cohen High School Health Clinic ^(RSD) | 12/24/2008 |
| 39 | Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD) | |
| 40 | Demolition of Modular Buildings at Gregory and Abramson ^(RSD) | 06/23/2015 |
| 41 | Demolition of Modular Buildings at Abramson and Carver ^(RSD) | 01/18/2017 |
| 42 | Demolition of Modular Buildings at Livingston ^(RSD) | 01/18/2017 |
| 43 | Douglass High School Under Floor Utilities ^(RSD) | |

| | | |
|----|---|------------|
| 44 | Dr. Martin Luther King School Roof Repairs ^(RSD) | 06/13/2012 |
| 45 | Dr. Martin Luther King Jr. School Renovation ^(RSD) | 12/15/2014 |
| 46 | Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD) | 02/18/2016 |
| 47 | Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD) | 07/27/2012 |
| 48 | Dwight D. Eisenhower Elementary School Refurbishment ^(RSD) | 12/23/2015 |
| 49 | East Bank Swing Space for Audubon Charter School ^(OPSB) | 12/30/2011 |
| 50 | Edgar P. Harney Elementary School Refurbishment ^(RSD) | |
| 51 | Edgar P. Harney Elementary School Roof Repairs ^(RSD) | 06/13/2012 |
| 52 | Edgar P. Harney Elementary School Lighting Repairs ^(RSD) | 08/08/2018 |
| 53 | Edna Karr High School - Gymnasium Repair ^(OPSB) | 12/23/2013 |
| 54 | Edna Karr High School - Assessment ^(OPSB) | |
| 55 | Edward Livingston Middle School Demolition ^(RSD) | 09/28/2010 |
| 56 | Edward Henry Phillips Junior High School Demolition ^(OPSB) | 11/19/2010 |
| 57 | New Edward Hynes School ^(OPSB) | 02/06/2012 |
| 58 | Edwards Hardin Lockett Lawless Demolition ^(RSD) | 11/03/2008 |
| 59 | Edward Livingston High School ^(RSD) | 01/05/2015 |
| 60 | Eleanor L. McMMain School Replacement of Existing Chillers ^(OPSB) | 08/30/2011 |
| 61 | Eleanor L. McMMain School Clinic ^(OPSB) | 07/24/2013 |
| 62 | Eleanor L. McMMain School Maintenance Upgrades ^(OPSB) | 12/12/2016 |
| 63 | Eleanor L. McMMain School Roof Replacement ^(OPSB) | 05/13/2016 |
| 64 | Ernest "Dutch" Morial Elementary ^(RSD) | 03/17/2017 |
| 65 | Ernest N. Morial Elementary Security Fencing ^(RSD) | 05/10/2011 |
| 66 | Fannie C. Williams Elementary School Demolition ^(RSD) | 03/10/2009 |
| 67 | Fisk-Howard Elementary School Demolition ^(RSD) | 10/04/2011 |
| 68 | Florence J. Chester Elementary School Demolition ^(RSD) | 06/05/2011 |
| 69 | Fortier (Lusher) High School Refurbishment ^(OPSB) | 02/05/2016 |
| 70 | Francis W. Gregory Demolition ^(RSD) | 12/21/2011 |
| 71 | Frederick A. Douglass High Refurbishment ^(RSD) | 10/28/2014 |
| 72 | Frederick A. Douglass High School Science Lab ^(RSD) | 07/05/2016 |
| 73 | Frederick A. Douglass High Switchgear ^(RSD) | 08/04/2009 |
| 74 | Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD) | |
| 75 | Gaudet Elementary School Refurbishment ^(RSD) | 12/20/2016 |
| 76 | Gentilly Terrace Elementary School Refurbishment ^(RSD) | 09/22/2015 |
| 77 | George Mondy Elementary School Mothball ^(RSD) | |
| 78 | George Washington Carver School ^(RSD) | 03/07/2016 |
| 79 | George Washington Carver High School Demolition ^(RSD) | 08/24/2011 |
| 80 | Greater St. Stephens School ^(OPSB) | 03/18/2013 |
| 81 | Harriet R. Tubman Elementary School Selective Demolition ^(RSD) | 12/14/2014 |
| 82 | Harriet R. Tubman Elementary School Renovation ^(RSD) | 08/01/2018 |
| 83 | Harriet R. Tubman Cottage Renovation ^(RSD) | 08/02/2018 |
| 84 | Henry Allen Elementary School Refurbishment ^(RSD) | 03/08/2016 |
| 85 | Henry Allen Elementary School Kitchen Refurbishment ^(RSD) | 02/18/2016 |
| 86 | Henry Allen Elementary School Roof ^(RSD) | 05/24/2010 |
| 87 | Henry C. Schaumburg School Refurbishment ^(RSD) | 06/26/2015 |
| 88 | Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD) | 12/16/2011 |
| 89 | Holy Cross Modular Relocation ^(RSD) | 12/14/2010 |

| | | |
|-----|---|------------|
| 90 | Israel M. Augustine Middle School Roof Replacement ^(RSD) | 04/13/2012 |
| 91 | Israel M. Augustine Middle School Mothball ^(RSD) | 01/18/2013 |
| 92 | James Derham Demolition ^(RSD) | 02/23/2012 |
| 93 | James W. Johnson Elementary School Roof ^(RSD) | 07/31/2010 |
| 94 | New Jean Batiste de Bienville School ^(RSD) | 06/15/2012 |
| 95 | Jean Gordon Elementary School Demolition ^(RSD) | 08/16/2010 |
| 96 | JoEllen Smith Medical Center Demolition ^(OPSB) | |
| 97 | John Dibert Elementary School Roof ^(RSD) | 08/20/2010 |
| 98 | John W. Hoffman Elementary School Demolition ^(RSD) | 05/25/2010 |
| 99 | John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD) | 11/05/2010 |
| 100 | John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD) | 08/05/2011 |
| 101 | John F. Kennedy Modular Demolition ^(RSD) | 09/16/2014 |
| 102 | John F. Kennedy High School Demolition ^(RSD) | 01/12/2012 |
| 103 | John McDonogh Senior High School Bleachers and Sprinklers ^(RSD) | 03/27/2014 |
| 104 | John McDonogh Senior High School Roof ^(RSD) | 05/04/2010 |
| 105 | John A. Shaw Elementary School Mothball ^(RSD) | 12/12/2012 |
| 106 | Joseph S. Clark Senior High School Roof Repairs ^(RSD) | 07/27/2012 |
| 107 | Joseph A. Craig Elementary Canopies ^(RSD) | 06/06/2011 |
| 108 | Joseph A. Craig Elementary Elevator Installation ^(RSD) | 01/20/2012 |
| 109 | Joseph A. Hardin Elementary Security Fencing ^(RSD) | 05/10/2011 |
| 110 | Lafayette Elementary School Roof and Masonry ^(RSD) | 06/22/2012 |
| 111 | Lake Area Landry Demolition ^(RSD) | 05/01/2008 |
| 112 | Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB) | 11/13/2015 |
| 113 | Langston Hughes Elementary School (Phase I) ^(RSD) | 08/11/2009 |
| 114 | Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD) | 11/10/2010 |
| 115 | Langston Hughes Elementary School - Dumpster Pad ^(RSD) | 10/12/2012 |
| 116 | Lawrence D. Crocker Elementary School Demolition ^(RSD) | 04/02/2010 |
| 117 | Laurel Elementary School Refurbishment ^(RSD) | 01/03/2018 |
| 118 | L.B. Landry Annex Demolition ^(RSD) | 05/02/2013 |
| 119 | Little Woods Elementary School Demolition ^(RSD) | 08/09/2010 |
| 120 | Little Woods School (Dolores T. Aaron Elementary School) ^(RSD) | 08/01/2013 |
| 121 | Live Oak Elementary School Refurbishment ^(RSD) | 01/06/2017 |
| 122 | Live Oak Elementary School Roof ^(RSD) | 08/04/2011 |
| 123 | Live Oak Elementary School Exterior Door Replacement ^(RSD) | 08/26/2011 |
| 124 | Lorraine Hansberry Elementary School Mothball ^(RSD) | 12/27/2012 |
| 125 | Louis D. Armstrong Elementary School ^(RSD) | 02/18/2013 |
| 126 | Lusher Elementary School Refurbishment ^(OPSB) | 10/31/2016 |
| 127 | Mahalia Jackson Elementary School ^(OPSB) | 05/11/2010 |
| 128 | Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB) | 03/06/2012 |
| 129 | Mahalia Jackson Elementary School Office Renovation ^(OPSB) | 04/30/2013 |
| 130 | Martin Behrman Elementary School Roof ^(RSD) | 02/23/2010 |
| 131 | Martin Luther King Jr. Elementary Canopy System ^(RSD) | 11/05/2011 |
| 132 | Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD) | 07/31/2012 |
| 133 | Martin Luther King Jr. School Kitchen Refurbishment ^(RSD) | 02/18/2016 |
| 134 | Mary Church Terrell Elementary School Demolition ^(RSD) | 04/17/2013 |
| 135 | Mary M. Bethune Elementary School Refurbishment ^(OPSB) | 10/26/2017 |

| | | |
|-----|--|------------|
| 136 | Mary M. Bethune Elementary 1st Floor Replacement (OPSB) | 01/24/2011 |
| 137 | Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB) | 01/21/2011 |
| 138 | McDonogh #7 High School Repairs (OPSB) | |
| 139 | McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD) | 06/11/2012 |
| 140 | McDonogh #28 School Refurbishment (RSD) | 03/15/2016 |
| 141 | McDonogh #28 Elementary School Roof (RSD) | 11/19/2011 |
| 142 | McDonogh #32 Roof Replacement (RSD) | 02/24/2012 |
| 143 | McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium (OPSB) | 01/17/2014 |
| 144 | McDonogh #35 School at the Phillip/ Waters Site (OPSB) | 09/23/2015 |
| 145 | McDonogh #42 Elementary School Renovation (RSD) | 05/28/2015 |
| 146 | McDonogh #42 Elementary School Roof (RSD) | 12/21/2011 |
| 147 | McDonogh #42 Elementary School HVAC Replacement (RSD) | 08/09/2010 |
| 148 | Mildred C. Osborne Elementary School Demolition (RSD) | 02/18/2010 |
| 149 | Mildred C. Osborne Elementary School (RSD) | 12/03/2012 |
| 150 | Modular Campuses Close Outs (RSD) | |
| 151 | Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD) | 05/22/2013 |
| 152 | Modular Structures at Langston Hughes Elementary School (RSD) | 04/05/2010 |
| 153 | Morris F.X. Jeff Elementary School Demolition (RSD) | |
| 154 | Morris F.X. Jeff Elementary School Mothball (RSD) | 01/15/2013 |
| 155 | Murray G. Henderson Elementary School Roof (RSD) | 06/23/2012 |
| 156 | Nelson Elementary School Refurbishment (OPSB) | 04/18/2016 |
| 157 | New Andrew H. Wilson Elementary School (RSD) | 10/11/2009 |
| 158 | New Carter G. Woodson School (RSD) | 09/14/2012 |
| 159 | New Fannie C. Williams School (RSD) | 08/24/2012 |
| 160 | New Joseph A. Craig Elementary School (RSD) | 12/09/2009 |
| 161 | New L.B. Landry High School (RSD) | 06/30/2010 |
| 162 | New Lake Area High School (RSD) | 12/28/2009 |
| 163 | New Lawrence D. Crocker School (RSD) | 04/29/2013 |
| 164 | New PK-8 School at North Kenilworth Park at Curran Site (OPSB) | 01/29/2016 |
| 165 | New Parkview School (RSD) | 10/12/2012 |
| 166 | New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD) | |
| 167 | New William Frantz Elementary School (RSD) | |
| 168 | New Orleans High School Signature Center Study (RSD) | |
| 169 | Oretha C. Haley Demo (RSD) | 05/07/2012 |
| 170 | Oretha C. Haley Elementary School Mothball (RSD) | 09/17/2012 |
| 171 | Parkview Elementary School Demolition (RSD) | 08/06/2009 |
| 172 | Paul L. Dunbar Elementary School Demolition (RSD) | 06/16/2010 |
| 173 | Paul L. Dunbar Elementary School (RSD) | 06/02/2015 |
| 174 | Paul B. Habans Elementary School (RSD) | 06/30/2016 |
| 175 | Paul B. Habans Elementary School Roof Repairs (RSD) | 07/27/2012 |
| 176 | Phillis Wheatley Elementary School Demolition (RSD) | 09/26/2011 |
| 177 | Phillis Wheatley Elementary School (RSD) | 07/10/2014 |
| 178 | Ray Abrams Elementary School (RSD) | 03/17/2017 |
| 179 | Rosenwald Elementary School Refurbishment (RSD) | 04/07/2016 |
| 180 | Robert M. Lusher Elementary Roof Removal & Replacement (OPSB) | 07/14/2011 |

| | | |
|-----|--|------------|
| 181 | Samuel J. Green Elementary School Refurbishment ^(RSD) | 02/15/2016 |
| 182 | Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD) | 02/15/2016 |
| 183 | Sarah T. Reed High School Bleachers ^(RSD) | 01/11/2012 |
| 184 | Sarah T. Reed High School Auditorium Wall ^(RSD) | 03/29/2010 |
| 185 | Sarah T. Reed High School Kitchen Refurbishment ^(RSD) | 02/18/2016 |
| 186 | Sarah T. Reed High School Refurbishment ^(RSD) | 12/01/2015 |
| 187 | Seabrook Computer Training Center Demolition ^(OPSB) | 06/25/2010 |
| 188 | Schaumburg Chillers ^(RSD) | 11/14/2008 |
| 189 | Schwarz Alternative Repairs ^(RSD) | 07/14/2009 |
| 190 | Schwarz Alternative Modularity Demolition ^(RSD) | 04/02/2015 |
| 191 | Schwarz Modular Building Demolition ^(RSD) | 04/02/2015 |
| 192 | Sherwood Forest Elementary School Demolition ^(RSD) | 10/28/2010 |
| 193 | Sherwood Forest Elementary School ^(RSD) | 06/30/2016 |
| 194 | Small New Orleans East High School at Abramson ^(RSD) | 09/24/2015 |
| 195 | Sophie B. Wright School Renovation ^(RSD) | 06/08/2016 |
| 196 | Sophie B. Wright School Selective Demolition ^(RSD) | 01/31/2014 |
| 197 | Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB) | 07/26/2011 |
| 198 | Stuart R. Bradley Elementary School Demolition ^(RSD) | 01/27/2010 |
| 199 | Stuart R. Bradley Elementary School ^(RSD) | 06/26/2015 |
| 200 | Sylvanie Williams Elementary School AHU Replacement ^(RSD) | 07/30/2013 |
| 201 | Sylvanie Williams Elementary School Play Yard ^(RSD) | 09/23/2010 |
| 202 | Sylvanie Williams Elementary School Roof Repairs ^(RSD) | 07/27/2012 |
| 203 | Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD) | 04/13/2012 |
| 204 | Sylvanie Williams Elementary School Refurbishment ^(RSD) | 02/18/2016 |
| 205 | Temporary Campus for McDonogh #11 Expropriation ^(OPSB) | |
| 206 | Thomas A. Edison Elementary School Demolition ^(RSD) | 03/25/2010 |
| 207 | Thomy Lafon Elementary School Demolition ^(RSD) | 11/27/2011 |
| 208 | Thomy Lafon School Interpretative Display ^(RSD) | 10/15/2013 |
| 209 | Thurgood Marshall Elementary School Refurbishment ^(RSD) | 08/10/2018 |
| 210 | Timbers Park Office Building #1 & #2 Demolition ^(OPSB) | 09/18/2011 |
| 211 | Timbers HVAC ^(OPSB) | 09/11/2013 |
| 212 | Timbers III - IT Room Relocation ^(OPSB) | 02/11/2015 |
| 213 | Village de L'est Elementary School Subsidence ^(RSD) | 06/18/2012 |
| 214 | Village de L'est Elementary School Refurbishment ^(RSD) | 10/12/2016 |
| 215 | Village de L'est Elementary School Roof and Modular Demolition ^(RSD) | 06/16/2013 |
| 216 | Vorice J. Waters Elementary School Demolition ^(RSD) | 01/14/2010 |
| 217 | Valena C. Jones Elementary School ^(RSD) | 01/10/2013 |
| 218 | Walter L. Cohen High School HVAC ^(RSD) | 04/04/2014 |
| 219 | Warren Easton High School Renovation ^(OPSB) | 12/15/2015 |
| 220 | Warren Easton School Courtyard Waterproofing ^(OPSB) | 11/24/2017 |
| 221 | Warren Easton High School Window Replacement ^(OPSB) | 09/07/2012 |
| 222 | West Bank Swing Space for Alice Harte Elementary School ^(OPSB) | 07/11/1931 |
| 223 | New William J. Guste Elementary School ^(RSD) | 10/06/2008 |
| 224 | William J. Guste Elementary School Science Lab ^(RSD) | 08/04/2009 |
| 225 | William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD) | 04/15/2010 |
| 226 | William Frantz Elementary School Roof ^(RSD) | 08/12/2010 |
