




Superintendent's Report February 2019



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department
of Education
Ms. Kunjan Narechania
Recovery School District



Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	11
Behrman Elementary School CMaR ^(OPSB)	11
Benjamin Franklin Elementary School Renovation ^(OPSB)	11
Career Technical Education High School at Kerlerec Street CMaR ^(RSD)	11
New Cohen High School CMaR ^(RSD)	12
New Karr High School, CMAR ^(RSD)	12
New Orleans Charter Science and Mathematics High School ^(OPSB)	12
Booker T. Washington School CMAR ^(RSD)	13
REFURBISHMENTS	14
Fisk Howard Exterior Envelope Repairs ^(RSD)	14
Lafayette Elementary School Environmental ^(RSD)	14
Live Oak Drainage and John McDonogh Waterproofing ^(RSD)	14
Eleanor McMain School Envelope Repairs ^(OPSB)	15
Schaumburg Elementary School Roof Repairs ^(RSD)	15
Village de L'est Elementary School Environmental ^(RSD)	15
COMPLETED PROJECTS	16

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$266 million in open contracts for the capital program after issuing \$182 thousand in new contracts, change orders and amendments in February. In addition, the total change orders to date, \$4.4 million, account for two percent (2.14%) of the total open construction contracts. RSD anticipates issuing \$90 million in construction contracts/change orders, and \$291 thousand in professional service contracts/amendments in March.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$165 million in open contracts for the capital program after issuing \$0 million in new contracts, change orders and amendments in February. In addition, the total change orders to date, \$5.7 million, account for approximately four percent (4.39%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 million in construction contracts/change orders and \$155 thousand in professional service contracts and amendments in March.

Community Meetings



Future Community Meetings

Bid Openings

Projects which are scheduled to bid in the next 60 days

April 10, 2019

Live Oak Drainage & John McDonogh Waterproofing Bid Opening

Disadvantaged Business Enterprises (DBE) Monthly Summary



Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 26 projects as of February 28, 2019. The DBE subcontracts value is \$82,812,192 of the \$364,282,325 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 61 projects as of February 28, 2019. The DBE subcontracts value is \$24,392,825 of the \$78,428,685 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of February 28, 2019. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 3 projects as of February 28, 2019. The DBE subcontracts value is \$45,555,185 of the 134,245,850 total of awarded contracts.

Total Amount of Contracts: \$ 686,094,417

Orleans Parish School Board



New & Renovations:

DBE Contractors secured subcontracts on 17 projects as of February 28, 2019. The DBE subcontracts value is \$65,999,022 of the \$263,467,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 4 projects as of February 28, 2019. The DBE subcontracts value is \$569,422 of the \$1,540,999 total of awarded contracts.

Total Amount of Contracts: \$265,008,830

* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

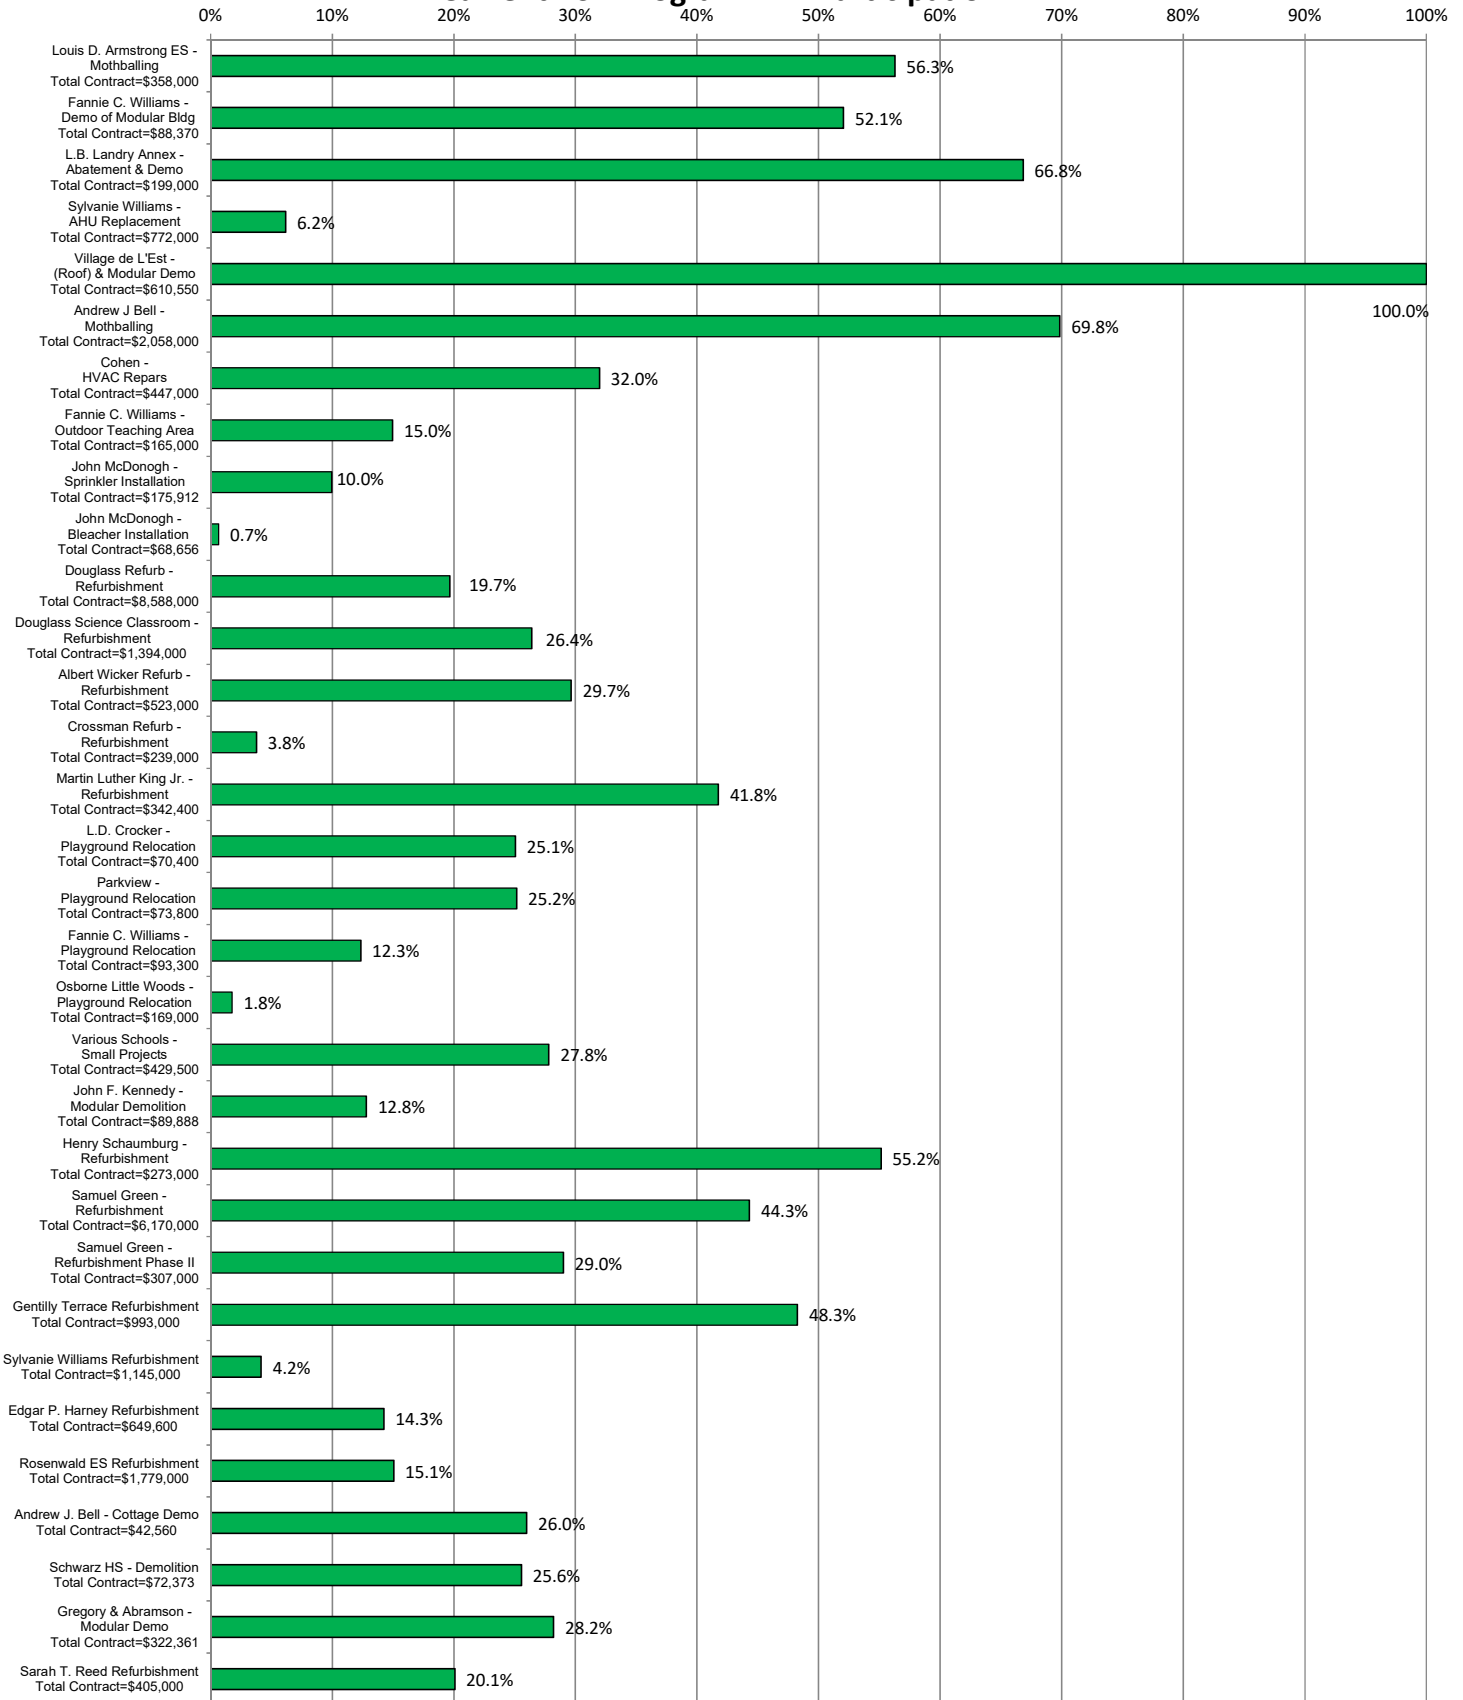


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Status Date: 28 February 2019


Current RSD Program DBE Participation

(Continued)

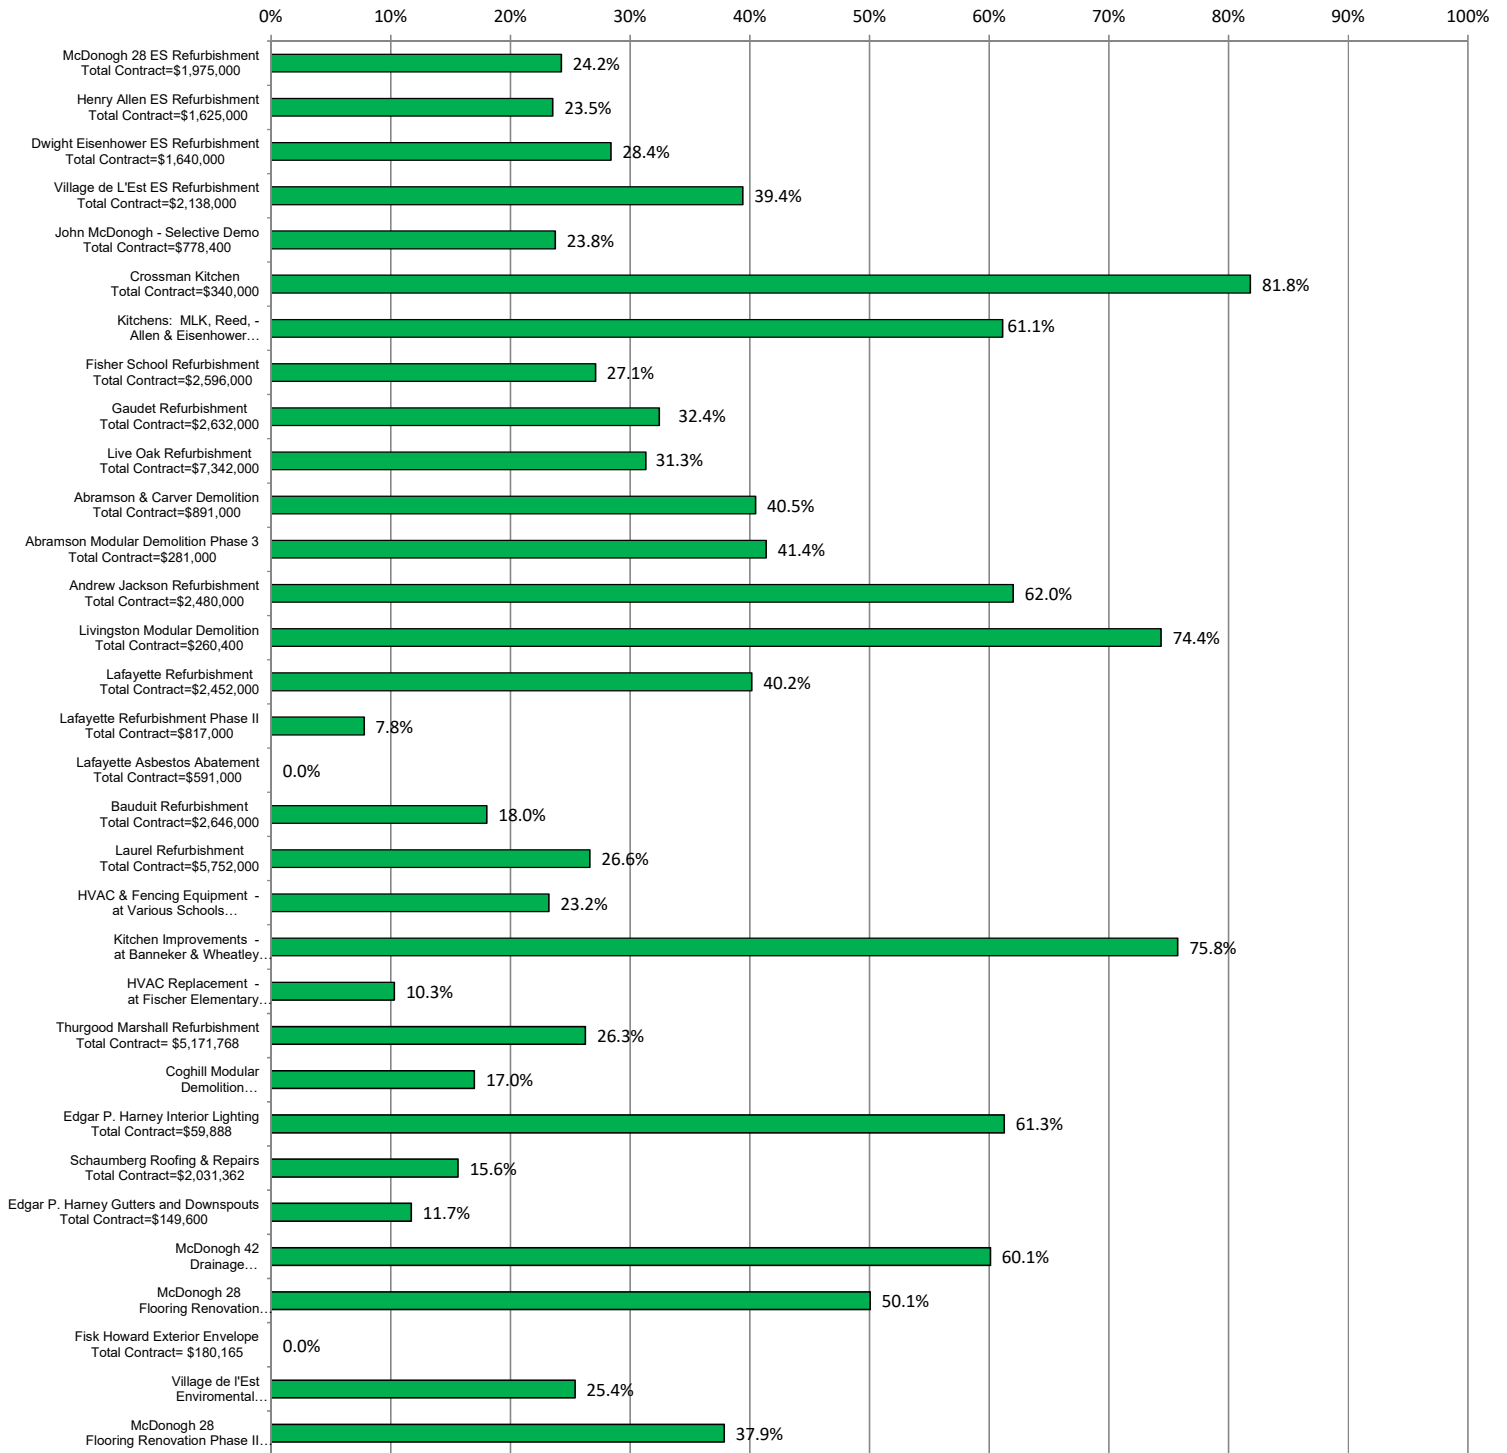


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current RSD Program DBE Participation (Continued)

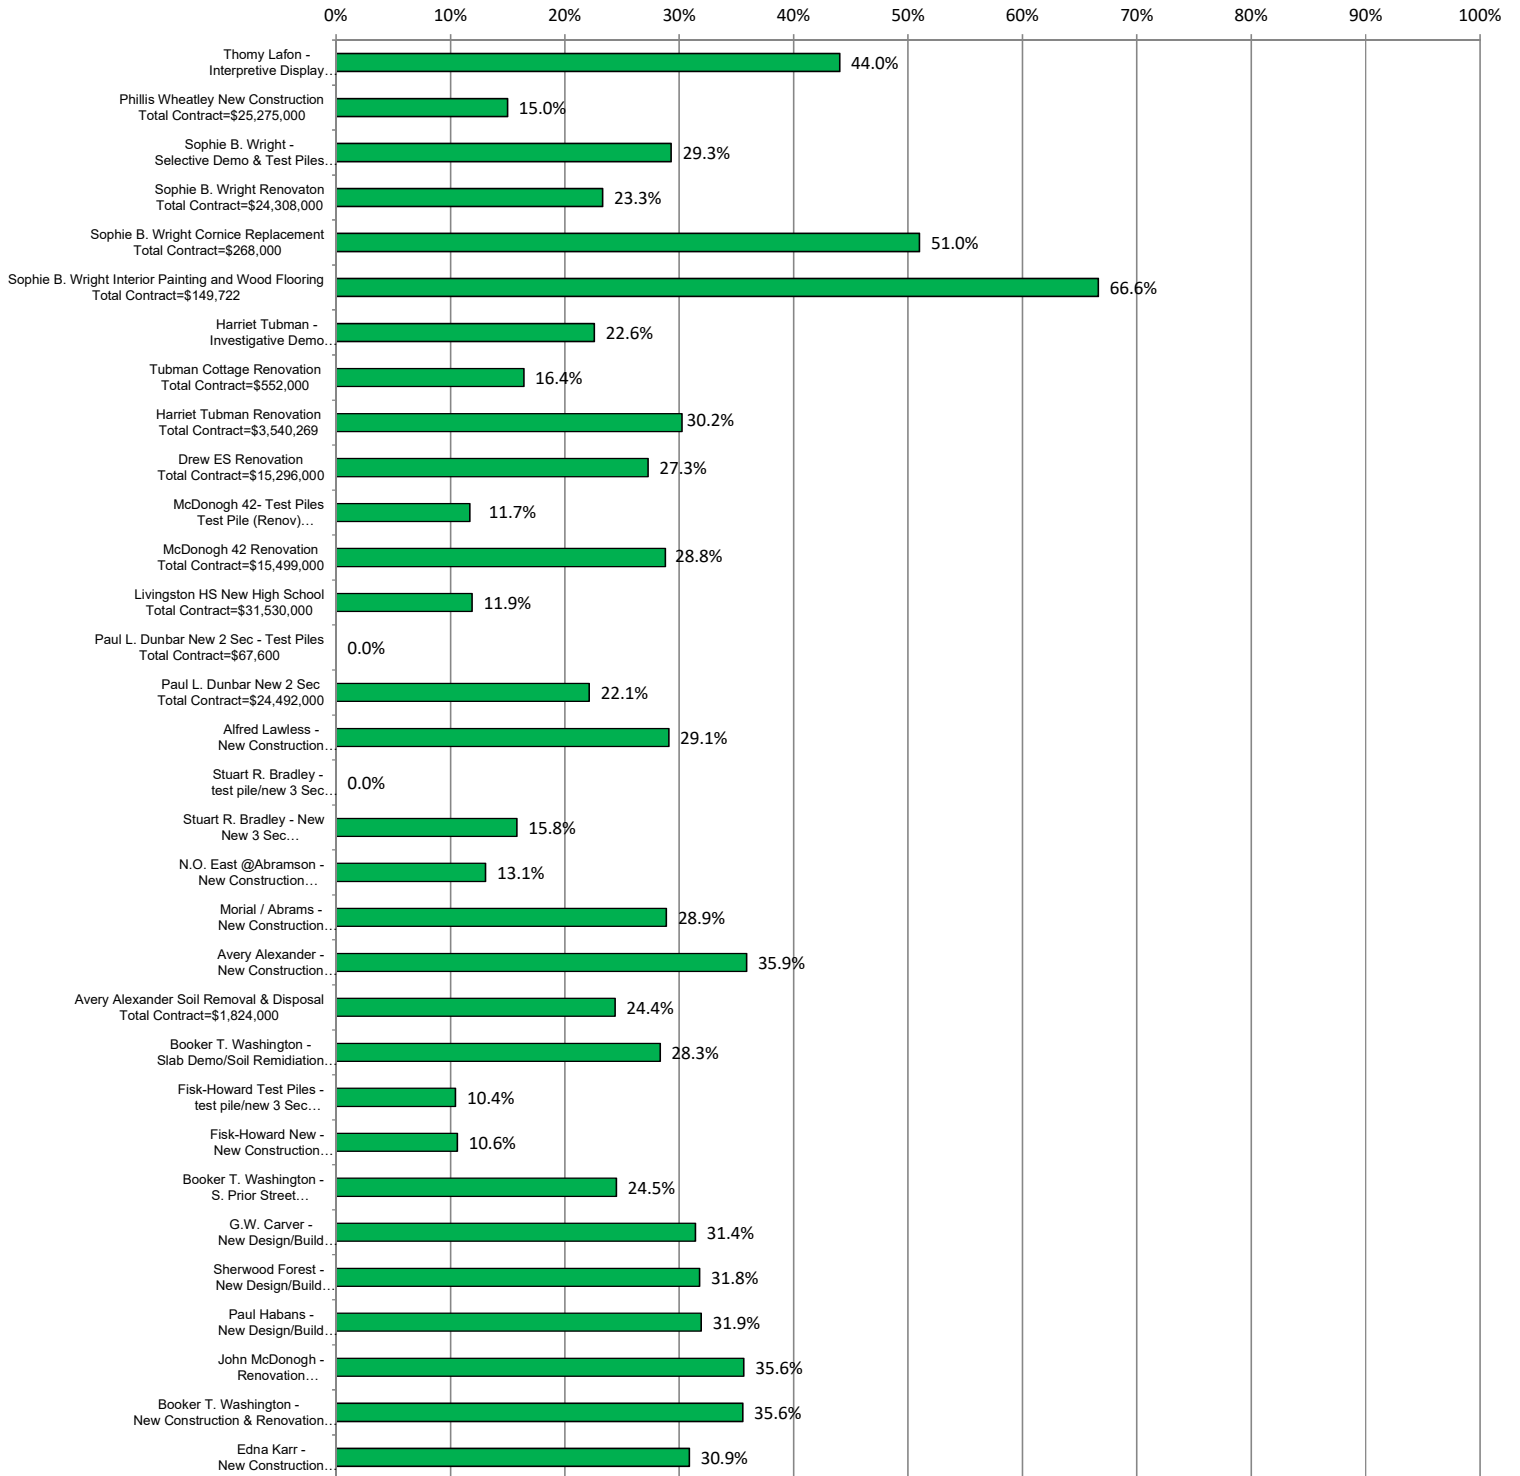

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

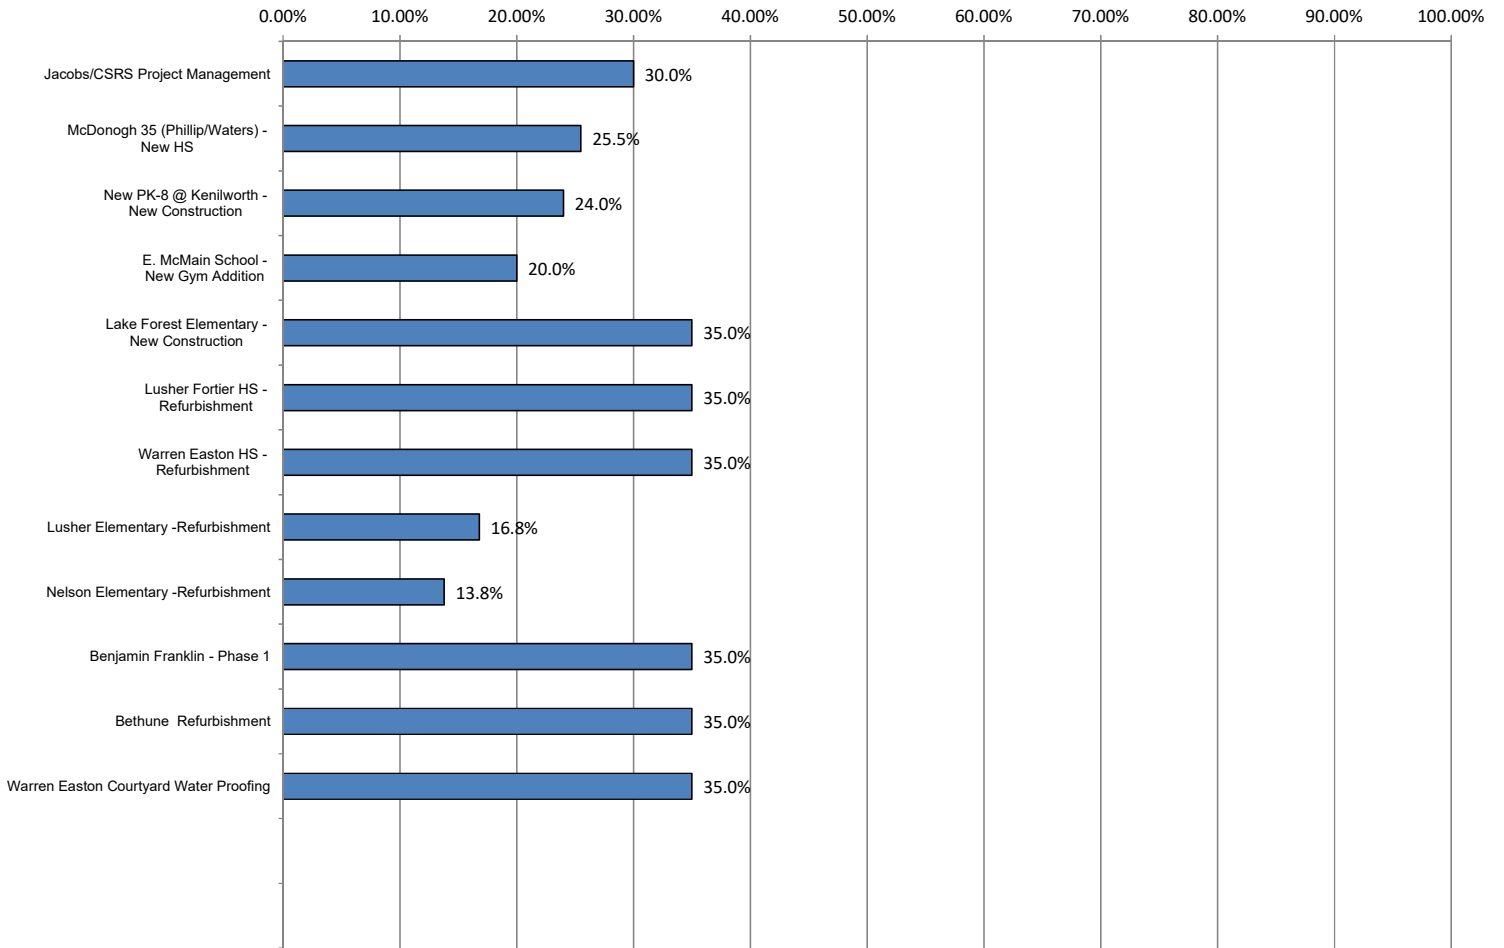

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Behrman Elementary School CMaR ^(RSD)

3819 Hershel Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – Waggoner & Ball Architects

Contractor - TBD

Design Phase

- CMaR RFQ's are being reviewed
- A&E has started Program Completion



Benjamin Franklin Elementary School Renovation Phase 2 ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Construction Masters

Construction Phase

- Gypsum board installation is ongoing
- Floor installation and refinishing has started
- HVAC installation continues
- Window repairs are ongoing



Career Technical Education High School at Kerlerec Street CMAR ^(RSD)

1331 Kerlerec Street, New Orleans, LA 70116 District D Ward 7

Scope of work: Renovation of existing high school

Funding Source – FEMA /CDBG

Architect – SCNZ Architects

Contractor - Broadmoor Construction

Design Phase

- A&E are working on Design Development drawings



New Cohen High School CMAR ^(RSD)

3520 Dryades Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – HMS Architects

Contractor - TBD

Design Phase

- CMaR RFQ is being reviewed
- A&E has started Schematic Design drawings



New Karr High School CMAR ^(RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - Core Construction

Construction Phase

- High river levels will delay subsurface work
- Exterior sheathing installation continues
- Installation of roof decking and curbs has started
- MEP rough in continues

Contractual Substantial Completion – April 2020

Forecasted Substantial Completion – April 2020



New Orleans Charter Science and Mathematics High School ^(OPSB)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - The McDonnell Group

Construction Phase

- First floor slabs are being poured
- Forming and pouring of columns has started
- Underground rough-ins are underway

Contractual Substantial Completion – January 2021

Forecasted Substantial Completion – January 2021



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Contractor is working on closing light well
- Installation of window shades and lockers has started
- Brick work continues on auditorium
- Installation of ceiling tiles continues

Contractual Substantial Completion – June 2019

Forecasted Substantial Completion – June 2019



REFURBISHMENTS

Fisk Howard Exterior Envelope Repairs (RSD)

211 South Lopez Street New Orleans, LA 70119, District B Ward 3

Scope of work: Repairs to exterior

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - LLJ Environmental Construction

Close Out Phase

- Project is Substantial Complete January 2019
- Contractual Substantial Completion – January 2019
- Forecasted Substantial Completion – January 2019



Lafayette Elementary School Environmental (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Environmental remediation

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Insul Tech

Procurement Phase

- Contracts are being signed
- Project is expected to start beginning of April



Live Oak Drainage and John McDonogh Waterproofing (RSD)

3128 Constance Street and 2426 Esplanade Avenue, New Orleans, LA

Scope of work: Drainage and Waterproofing

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement - March 6th
- 2nd Advertisement - March 13th
- 3rd Advertisement - March 20th
- Pre-Bid Conference - March 21st
- Bid Opening - April 10th



Eleanor McMain School Envelope Repairs ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Exterior stucco and window repairs

Funding Source – General Fund & Harrah's

Architect – Concordia, LLC

Contractor – Tuna Construction

Construction Phase

- Exterior painting continues
- Installation of refurbished windows in ongoing
- Exterior repairs has started at the auditorium

Contractual Substantial Completion – April 2019

Forecasted Substantial Completion – April 2019



Schaumburg Elementary School Roof Repairs ^(RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - Laperouse Metal Works, Inc

Construction Phase

- Installation of gutters and downspouts has started
- Contractor to provide hydro-seeding after school year ends

Contractual Substantial Completion – March 2018

Forecasted Substantial Completion – April 2019



Village de l'Est Elementary School Environmental ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Environmental remediation

Funding Source – FEMA, CBDG

Architect – MMG

Contractor - Insul Tech

Procurement Phase

- Owner is reviewing contractors claim



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment ^(RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment ^(RSD)	10/31/2017
8	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
9	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
10	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
11	Alfred Lawless Senior ^(RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
13	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
21	Augustine Elementary School Roof ^(RSD)	04/13/2012
22	Avery-Alexander Elementary School ^(RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)	10/30/2017
25	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
26	Bell JH Shoring ^(RSD)	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
28	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
29	Bienville Elementary School Demolition ^(RSD)	05/04/2009
30	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
31	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
32	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
33	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
34	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
35	Charles J. Colton Elementary School ^(RSD)	05/23/2013
36	Charles R. Drew Elementary School ^(RSD)	04/17/2015
37	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
38	Cohen High School Health Clinic ^(RSD)	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
40	Demolition of Modular Buildings at Coghill ^(RSD)	12/26/2018
41	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
42	Demolition of Modular Buildings at Abramson and Carver ^(RSD)	01/18/2017
43	Demolition of Modular Buildings at Livingston ^(RSD)	01/18/2017

44	Douglass High School Under Floor Utilities ^(RSD)	
45	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
46	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
47	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
48	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
49	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
50	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011
51	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
52	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
53	Edgar P. Harney Elementary School Downspouts and Gutters ^(RSD)	01/09/2019
54	Edgar P. Harney Elementary School Lighting Repairs ^(RSD)	08/08/2018
55	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
56	Edna Karr High School - Assessment ^(OPSB)	
57	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
58	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
59	New Edward Hynes School ^(OPSB)	02/06/2012
60	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
61	Edward Livingston High School ^(RSD)	01/05/2015
62	Eleanor L. McMMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
63	Eleanor L. McMMain School Clinic ^(OPSB)	07/24/2013
64	Eleanor L. McMMain School Maintenance Upgrades ^(OPSB)	12/12/2016
65	Eleanor L. McMMain School Roof Replacement ^(OPSB)	05/13/2016
66	Ernest "Dutch" Morial Elementary ^(RSD)	03/17/2017
67	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
68	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
69	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
70	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
71	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
72	Francis W. Gregory Demolition ^(RSD)	12/21/2011
73	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
74	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
75	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
76	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
77	Gaudet Elementary School Refurbishment ^(RSD)	12/20/2016
78	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
79	George Mondy Elementary School Mothball ^(RSD)	
80	George Washington Carver School ^(RSD)	03/07/2016
81	George Washington Carver High School Demolition ^(RSD)	08/24/2011
82	Greater St. Stephens School ^(OPSB)	03/18/2013
83	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
84	Harriet R. Tubman Elementary School Renovation ^(RSD)	08/01/2018
85	Harriet R. Tubman Cottage Renovation ^(RSD)	08/02/2018
86	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
87	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
88	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
89	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015

90	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
91	Holy Cross Modular Relocation ^(RSD)	12/14/2010
92	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
93	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
94	James Derham Demolition ^(RSD)	02/23/2012
95	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
96	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
97	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
98	JoEllen Smith Medical Center Demolition ^(OPSB)	
99	John Dibert Elementary School Roof ^(RSD)	08/20/2010
100	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
101	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
102	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
103	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
104	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
105	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
106	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
107	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
108	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
109	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
110	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
111	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
112	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
113	Lake Area Landry Demolition ^(RSD)	05/01/2008
114	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
115	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
116	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
117	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
118	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
119	Laurel Elementary School Refurbishment ^(RSD)	01/03/2018
120	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
121	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
122	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
123	Live Oak Elementary School Refurbishment ^(RSD)	01/06/2017
124	Live Oak Elementary School Roof ^(RSD)	08/04/2011
125	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
126	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
127	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
128	Lusher Elementary School Refurbishment ^(OPSB)	10/31/2016
129	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
130	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
131	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
132	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
133	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
134	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
135	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016

136	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
137	Mary M. Bethune Elementary School Refurbishment ^(OPSB)	10/26/2017
138	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
139	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
140	McDonogh #7 High School Repairs ^(OPSB)	
141	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
142	McDonogh #28 School Refurbishment ^(RSD)	03/15/2016
143	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
144	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
145	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
146	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
147	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
148	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
149	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
150	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
151	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
152	Modular Campuses Close Outs ^(RSD)	
153	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
154	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010
155	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
156	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
157	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
158	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
159	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
160	New Carter G. Woodson School ^(RSD)	09/14/2012
161	New Fannie C. Williams School ^(RSD)	08/24/2012
162	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
163	New L.B. Landry High School ^(RSD)	06/30/2010
164	New Lake Area High School ^(RSD)	12/28/2009
165	New Lawrence D. Crocker School ^(RSD)	04/29/2013
166	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
167	New Parkview School ^(RSD)	10/12/2012
168	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
169	New William Frantz Elementary School ^(RSD)	
170	New Orleans High School Signature Center Study ^(RSD)	
171	Oretha C. Haley Demo ^(RSD)	05/07/2012
172	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
173	Parkview Elementary School Demolition ^(RSD)	08/06/2009
174	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
175	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
176	Paul B. Habans Elementary School ^(RSD)	06/30/2016
177	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
178	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
179	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
180	Ray Abrams Elementary School ^(RSD)	03/17/2017

181	Rosenwald Elementary School Refurbishment ^(RSD)	04/07/2016
182	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
183	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
184	Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD)	02/15/2016
185	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
186	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
187	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
188	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
189	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
190	Schaumburg Chillers ^(RSD)	11/14/2008
191	Schwarz Alternative Repairs ^(RSD)	07/14/2009
192	Schwarz Alternative Modularity Demolition ^(RSD)	04/02/2015
193	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
194	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
195	Sherwood Forest Elementary School ^(RSD)	06/30/2016
196	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
197	Sophie B. Wright School Renovation ^(RSD)	06/08/2016
198	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
199	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
200	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
201	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
202	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
203	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
204	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
205	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
206	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
207	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
208	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
209	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
210	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
211	Thurgood Marshall Elementary School Refurbishment ^(RSD)	08/10/2018
212	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
213	Timbers HVAC ^(OPSB)	09/11/2013
214	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
215	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
216	Village de L'est Elementary School Refurbishment ^(RSD)	10/12/2016
217	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
218	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
219	Valena C. Jones Elementary School ^(RSD)	01/10/2013
220	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
221	Warren Easton High School Renovation ^(OPSB)	12/15/2015
222	Warren Easton School Courtyard Waterproofing ^(OPSB)	11/24/2017
223	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
224	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
225	New William J. Guste Elementary School ^(RSD)	10/06/2008
226	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009

227	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
228	William Frantz Elementary School Roof ^(RSD)	08/12/2010
