





Superintendent's Report January 2019



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department
of Education
Ms. Kunjan Narechania
Recovery School District

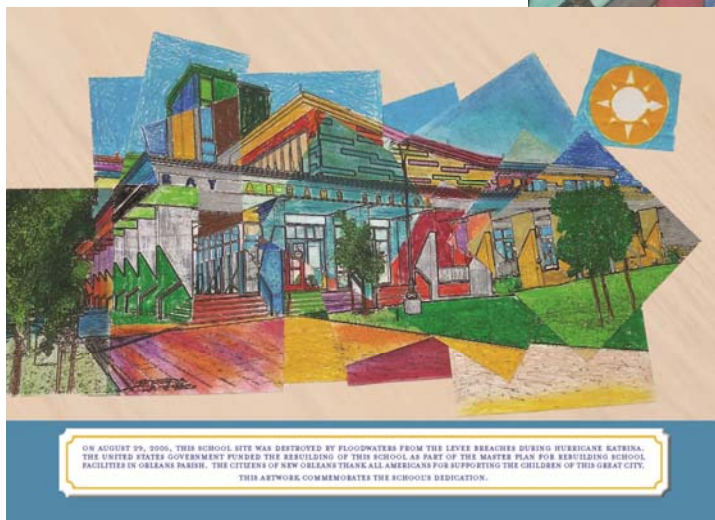

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	11
Behrman Elementary School CMaR ^(OPSB)	11
Benjamin Franklin Elementary School Renovation ^(OPSB)	11
Career Technical Education High School at Kerlerec Street CMaR ^(RSD)	11
New Cohen High School CMaR ^(RSD)	12
New Karr High School, CMAR ^(RSD)	12
New Orleans Charter Science and Mathematics High School ^(OPSB)	12
Booker T. Washington School CMAR ^(RSD)	13
REFURBISHMENTS	14
Fisk Howard Exterior Envelope Repairs ^(RSD)	14
Harney Elementary School Downspout and Gutter Repairs ^(RSD)	14
Lafayette Elementary School Environmental ^(RSD)	14
Live Oak Drainage and John McDonogh Waterproofing ^(RSD)	15
Eleanor McMMain School Envelope Repairs ^(OPSB)	15
Schaumburg Elementary School Roof Repairs ^(RSD)	15
Village de L'est Elementary School Environmental ^(RSD)	16
COMPLETED PROJECTS	17

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$263 million in open contracts for the capital program after issuing \$285 thousand in new contracts, change orders and amendments in January. In addition, the total change orders to date, \$4 million, account for one percent (1.99%) of the total open construction contracts. RSD anticipates issuing \$90 million in construction contracts/change orders, and \$0 thousand in professional service contracts/amendments in February.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 million in new contracts, change orders and amendments in January. The OPSB has \$168 million in open contracts for the capital program after issuing \$0 million in new contracts, change orders and amendments in January. In addition, the total change orders to date, \$5.6 million, account for approximately four percent (4.31%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 million in construction contracts/change orders and \$0 thousand in professional service contracts and amendments in February.

Community Meetings



Future Community Meetings

Bid Openings

Projects which are scheduled to bid in the next 60 days

February 6, 2019

Lafayette Elementary Asbestos Abatement

Disadvantaged Business Enterprises (DBE) Monthly Summary



Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 26 projects as of January 31, 2019. The DBE subcontracts value is \$82,789,518 of the \$364,282,325 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 61 projects as of January 31, 2019. The DBE subcontracts value is \$24,341,240 of the \$77,657,520 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of January 31, 2019. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 3 projects as of January 31, 2019. The DBE subcontracts value is \$45,517,428 of the 134,245,850 total of awarded contracts.

Total Amount of Contracts: \$ 685,323,252

Orleans Parish School Board



New & Renovations:

DBE Contractors secured subcontracts on 17 projects as of January 31, 2019. The DBE subcontracts value is \$65,999,022 of the \$263,467,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 4 projects as of January 31, 2019. The DBE subcontracts value is \$569,422 of the \$1,540,999 total of awarded contracts.


Total Amount of Contracts: \$265,008,830

* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

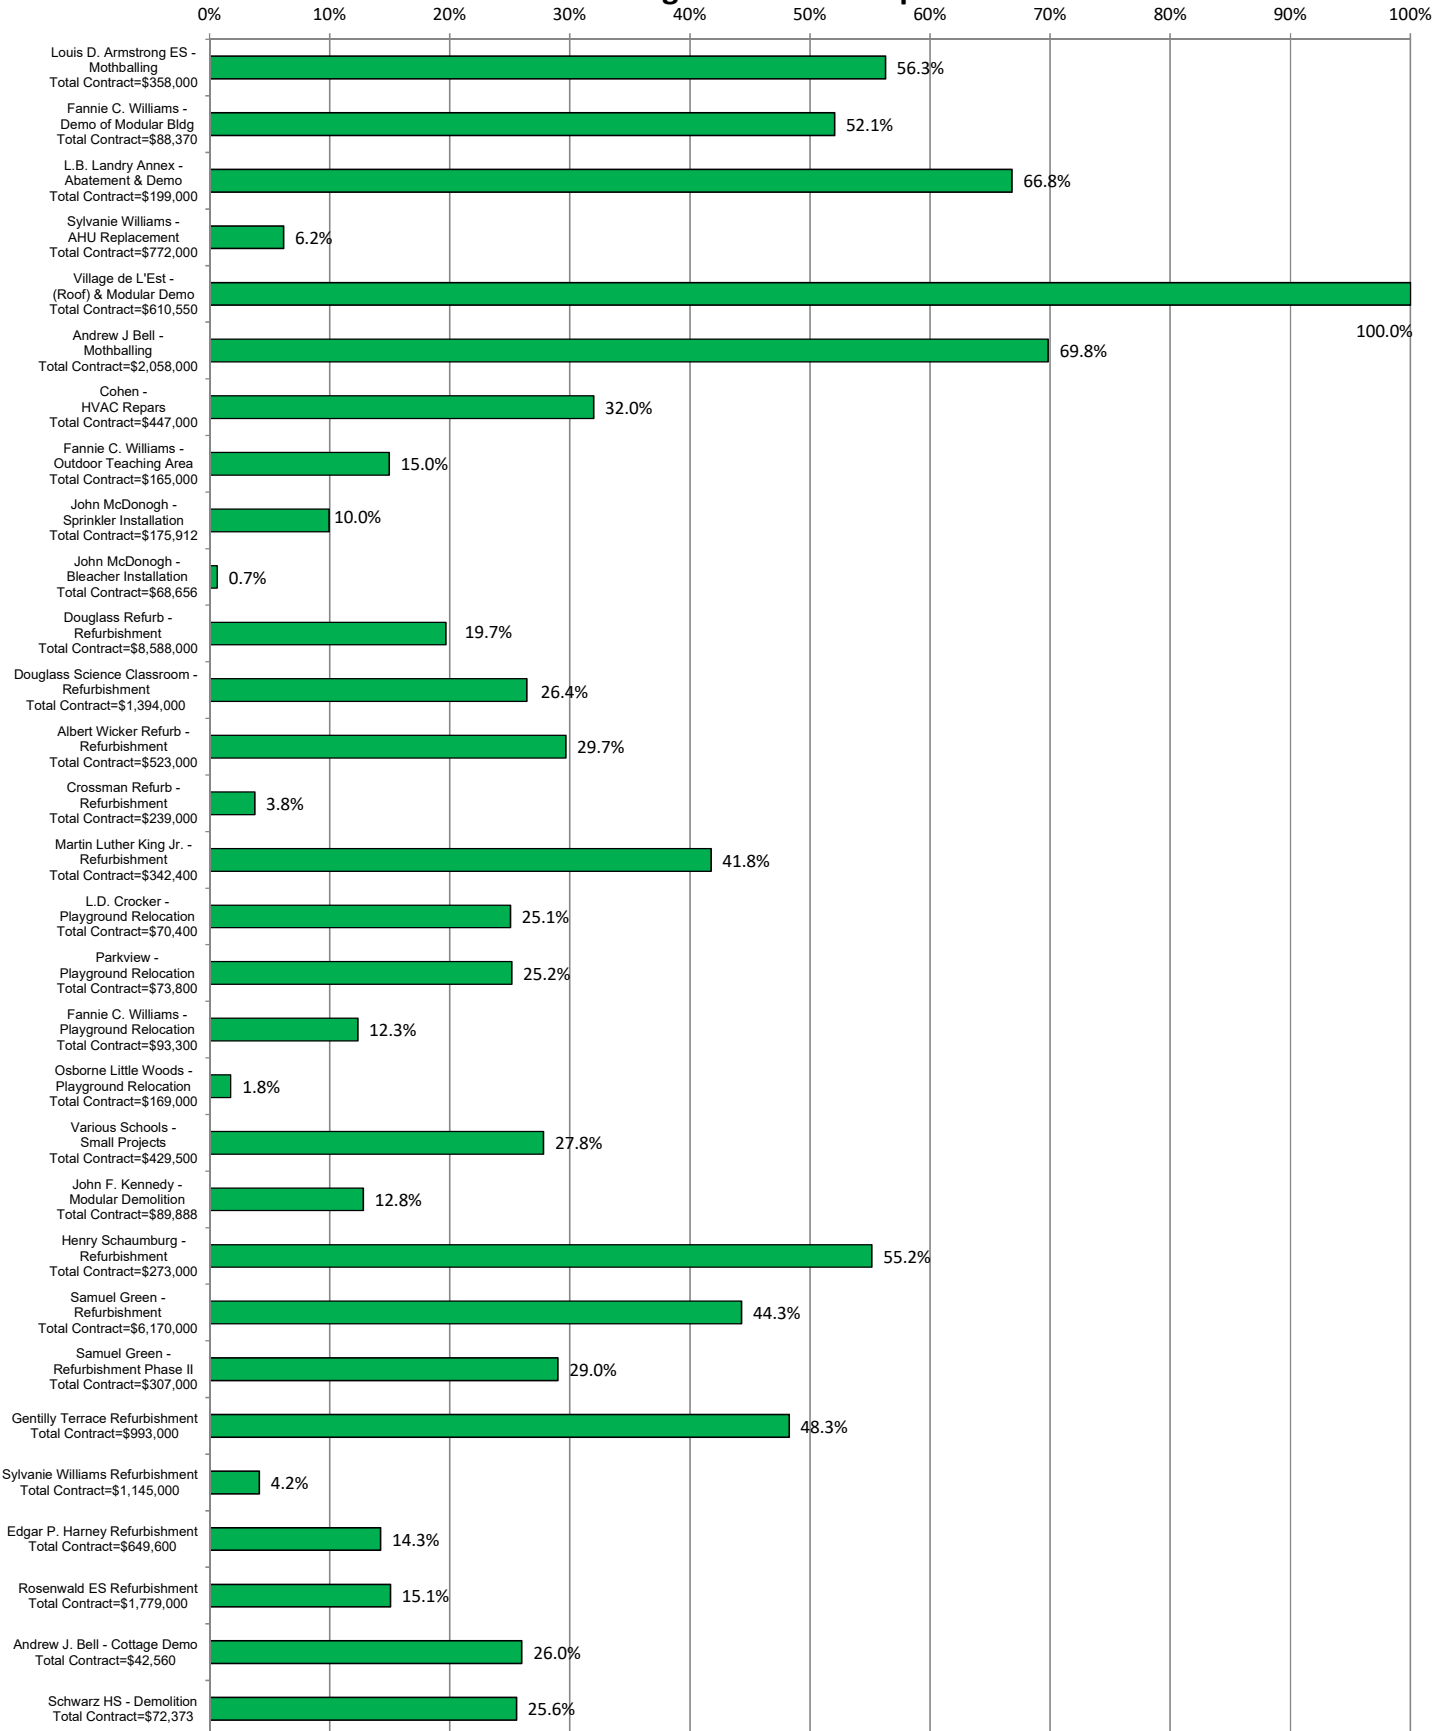


Current RSD Program DBE Participation (Continued)

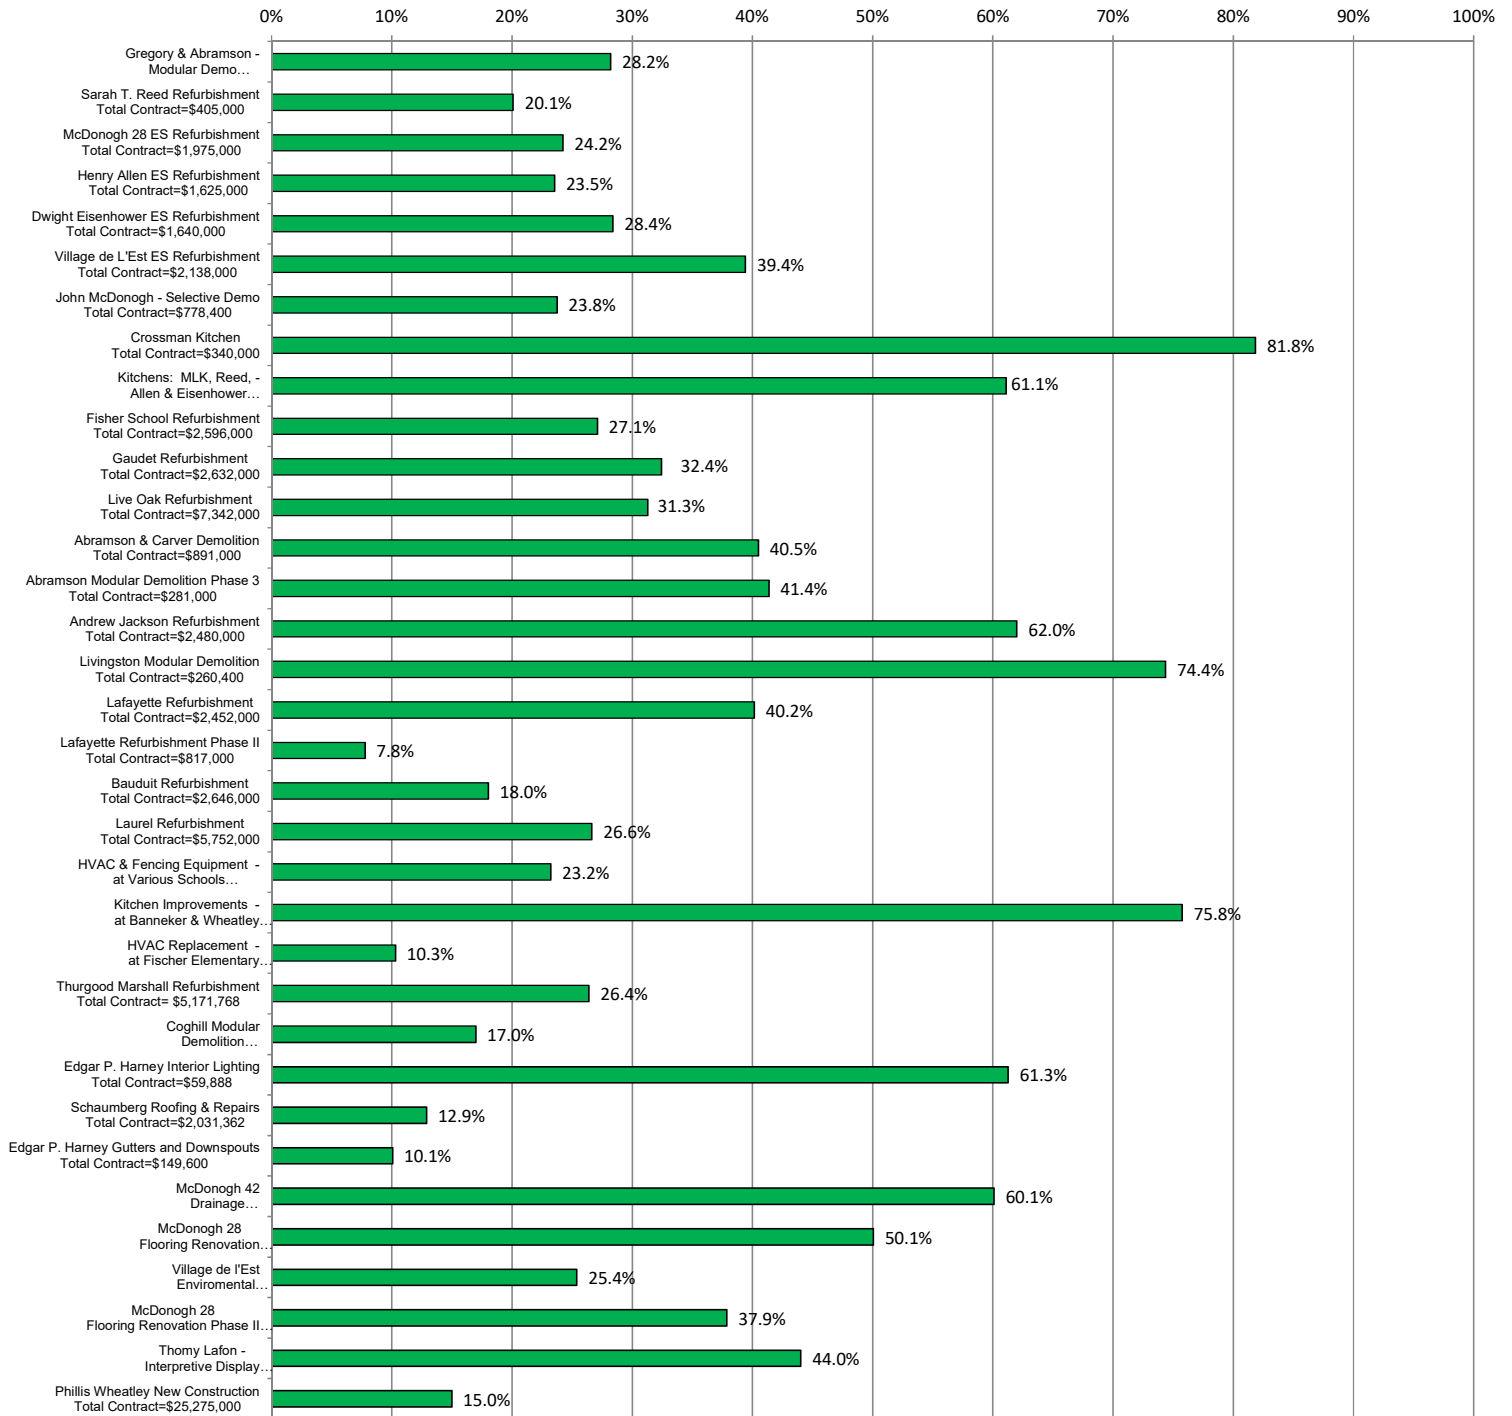

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

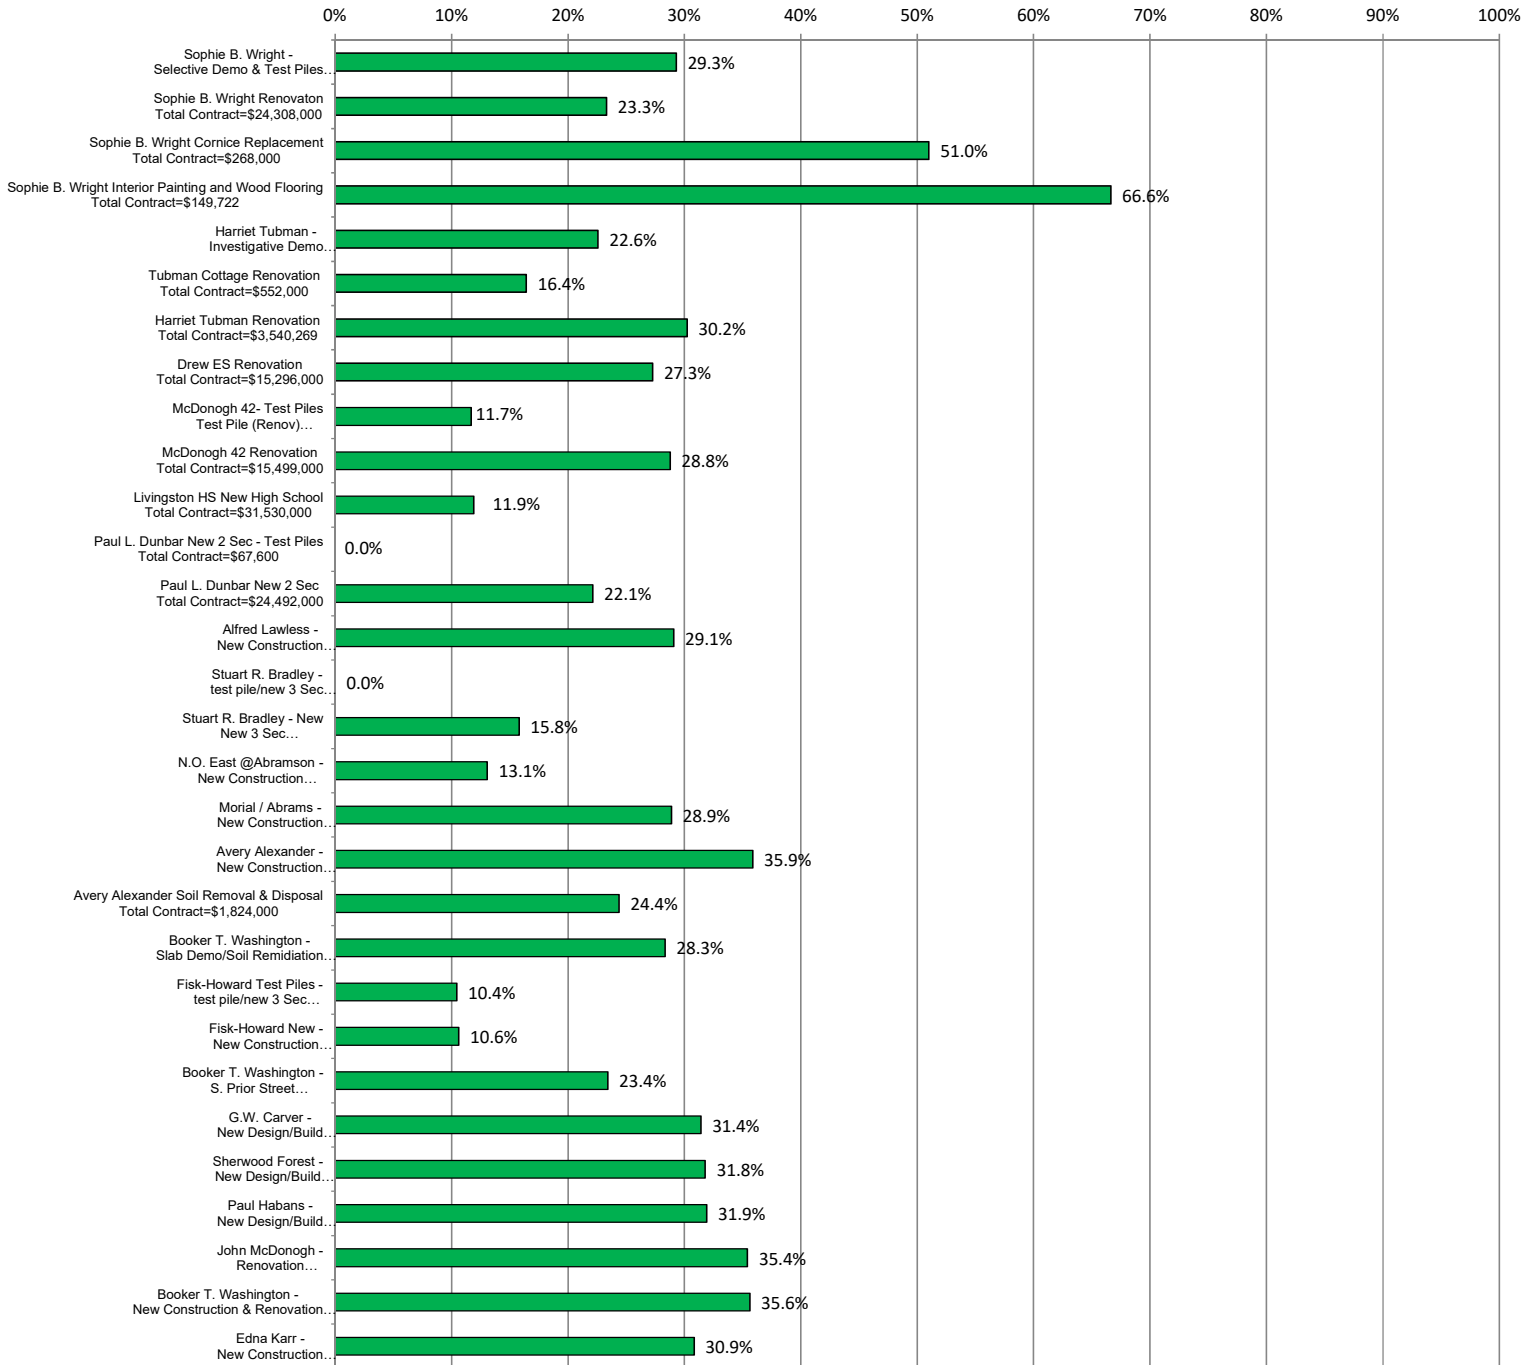

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

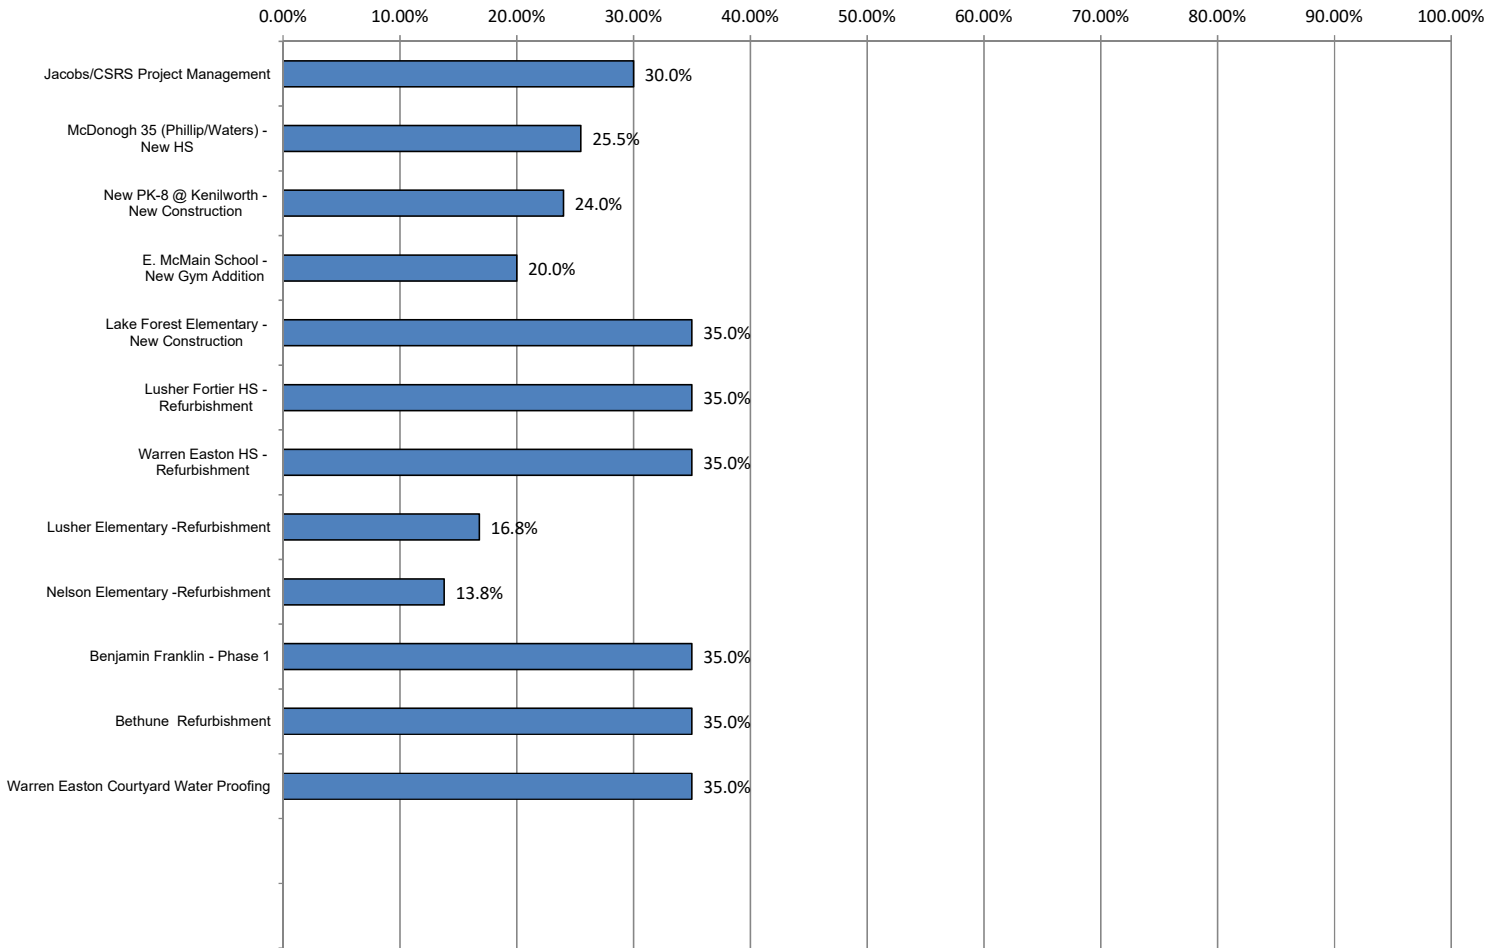

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Behrman Elementary School CMaR ^(RSD)

3819 Hershel Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – Waggoner & Ball Architects

Contractor - TBD

Design Phase

- CMaR RFQ's are being reviewed



Benjamin Franklin Elementary School Renovation Phase 2 ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Construction Masters

Construction Phase

- Demolition of mechanical and electrical equipment is on going on 2nd and 3rd floors
- Door demolition is complete
- Floor joist are being shored-up
- Survey of termite damage is complete



Career Technical Education High School at Kerlerec Street CMAR ^(RSD)

1331 Kerlerec Street, New Orleans, LA 70116 District D Ward 7

Scope of work: Renovation of existing high school

Funding Source – FEMA /CDBG

Architect – SCNZ Architects

Contractor - TBD

Design Phase

- Schematic Design submission was received and is being reviewed
- CMaR RFQ's are being reviewed



New Cohen High School CMAR ^(RSD)

3520 Dryades Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – HMS Architects

Contractor - TBD

Design Phase

- CMaR RFQ's are being reviewed
- Program Completion phase submission is due February 26th



New Karr High School CMAR ^(RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - Core Construction

Construction Phase

- High river levels will delay subsurface work
- Exterior sheathing installation has started
- Steel erection is ongoing
- MEP rough in continues

Contractual Substantial Completion – April 2020

Forecasted Substantial Completion – April 2020



New Orleans Charter Science and Mathematics High School ^(OPSB)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - The McDonnell Group

Construction Phase

- Pile caps and grade beams are being formed
- Resteel for columns is being set

Contractual Substantial Completion – January 2021

Forecasted Substantial Completion – January 2021



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Contractor's emphasis is on closing the auditorium envelope
- Interior painting continues
- Brick work continues on auditorium
- Installation of flooring and ceiling tiles continue

Contractual Substantial Completion – June 2019

Forecasted Substantial Completion – June 2019



REFURBISHMENTS

Fisk Howard Exterior Envelope Repairs ^(RSD)

211 South Lopez Street New Orleans, LA 70119, District B Ward 3

Scope of work: Repairs to exterior

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - LLJ Environmental Construction

Close Out Phase

- Installation of spray foam is complete

Contractual Substantial Completion – January 2019

Forecasted Substantial Completion – January 2019



Harney Elementary School Downspout and Gutter Repairs ^(RSD)

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of downspouts and gutters

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - Crescent Commercial

Close Out Phase

- Project is Substantial Complete January 2019

Contractual Substantial Completion – September 2018

Actual Substantial Completion – January 2019



Lafayette Elementary School Environmental ^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Environmental remediation

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- 1st Advertisement - December 26th
- 2nd Advertisement - January 2nd
- 3rd Advertisement - January 9th
- Pre-Bid Conference - January 10th
- Bid Opening - February 6th



Live Oak Drainage and John McDonogh Waterproofing ^(RSD)

3128 Constance Street and 2426 Esplanade Avenue, New Orleans, LA

Scope of work: Drainage and Waterproofing

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement - March 6th
- 2nd Advertisement - March 13th
- 3rd Advertisement - March 20th
- Pre-Bid Conference - March 21st
- Bid Opening - April 10th



Eleanor McMain School Envelope Repairs ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Exterior stucco and window repairs

Funding Source – General Fund & Harrah's

Architect – Concordia, LLC

Contractor – Tuna Construction

Construction Phase

- Exterior painting continues
- Installation of refurbished windows in ongoing
- Plaster repairs on exterior continues

Contractual Substantial Completion – April 2019

Forecasted Substantial Completion – April 2019



Schaumburg Elementary School Roof Repairs ^(RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - Laperouse Metal Works, Inc

Construction Phase

- Installing flashing at eaves and penetrations
- Project nearing completion

Contractual Substantial Completion – August 2018

Forecasted Substantial Completion – March 2019



Village de l'Est Elementary School Environmental (RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Environmental remediation

Funding Source – FEMA, CBDG

Architect – MMG

Contractor - Insul Tech

Procurement Phase

- Owner is reviewing contractors claim



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment ^(RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment ^(RSD)	10/31/2017
8	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
9	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
10	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
11	Alfred Lawless Senior ^(RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
13	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
21	Augustine Elementary School Roof ^(RSD)	04/13/2012
22	Avery-Alexander Elementary School ^(RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)	10/30/2017
25	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
26	Bell JH Shoring ^(RSD)	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
28	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
29	Bienville Elementary School Demolition ^(RSD)	05/04/2009
30	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
31	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
32	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
33	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
34	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
35	Charles J. Colton Elementary School ^(RSD)	05/23/2013
36	Charles R. Drew Elementary School ^(RSD)	04/17/2015
37	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
38	Cohen High School Health Clinic ^(RSD)	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
40	Demolition of Modular Buildings at Coghill ^(RSD)	12/26/2018
41	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
42	Demolition of Modular Buildings at Abramson and Carver ^(RSD)	01/18/2017
43	Demolition of Modular Buildings at Livingston ^(RSD)	01/18/2017

44	Douglass High School Under Floor Utilities ^(RSD)	
45	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
46	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
47	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
48	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
49	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
50	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011
51	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
52	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
53	Edgar P. Harney Elementary School Lighting Repairs ^(RSD)	08/08/2018
54	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
55	Edna Karr High School - Assessment ^(OPSB)	
56	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
57	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
58	New Edward Hynes School ^(OPSB)	02/06/2012
59	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
60	Edward Livingston High School ^(RSD)	01/05/2015
61	Eleanor L. McMains School Replacement of Existing Chillers ^(OPSB)	08/30/2011
62	Eleanor L. McMains School Clinic ^(OPSB)	07/24/2013
63	Eleanor L. McMains School Maintenance Upgrades ^(OPSB)	12/12/2016
64	Eleanor L. McMains School Roof Replacement ^(OPSB)	05/13/2016
65	Ernest "Dutch" Morial Elementary ^(RSD)	03/17/2017
66	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
67	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
68	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
69	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
70	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
71	Francis W. Gregory Demolition ^(RSD)	12/21/2011
72	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
73	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
74	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
75	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
76	Gaudet Elementary School Refurbishment ^(RSD)	12/20/2016
77	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
78	George Mondy Elementary School Mothball ^(RSD)	
79	George Washington Carver School ^(RSD)	03/07/2016
80	George Washington Carver High School Demolition ^(RSD)	08/24/2011
81	Greater St. Stephens School ^(OPSB)	03/18/2013
82	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
83	Harriet R. Tubman Elementary School Renovation ^(RSD)	08/01/2018
84	Harriet R. Tubman Cottage Renovation ^(RSD)	08/02/2018
85	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
86	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
87	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
88	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
89	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011

90	Holy Cross Modular Relocation ^(RSD)	12/14/2010
91	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
92	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
93	James Derham Demolition ^(RSD)	02/23/2012
94	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
95	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
96	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
97	JoEllen Smith Medical Center Demolition ^(OPSB)	
98	John Dibert Elementary School Roof ^(RSD)	08/20/2010
99	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
100	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
101	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
102	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
103	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
104	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
105	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
106	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
107	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
108	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
109	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
110	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
111	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
112	Lake Area Landry Demolition ^(RSD)	05/01/2008
113	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
114	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
115	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
116	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
117	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
118	Laurel Elementary School Refurbishment ^(RSD)	01/03/2018
119	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
120	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
121	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
122	Live Oak Elementary School Refurbishment ^(RSD)	01/06/2017
123	Live Oak Elementary School Roof ^(RSD)	08/04/2011
124	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
125	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
126	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
127	Lusher Elementary School Refurbishment ^(OPSB)	10/31/2016
128	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
129	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
130	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
131	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
132	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
133	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
134	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
135	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013

136	Mary M. Bethune Elementary School Refurbishment (OPSB)	10/26/2017
137	Mary M. Bethune Elementary 1st Floor Replacement (OPSB)	01/24/2011
138	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing (OPSB)	01/21/2011
139	McDonogh #7 High School Repairs (OPSB)	
140	McDonogh #15 Elementary Exterior Masonry to SOI Standards (RSD)	06/11/2012
141	McDonogh #28 School Refurbishment (RSD)	03/15/2016
142	McDonogh #28 Elementary School Roof (RSD)	11/19/2011
143	McDonogh #32 Roof Replacement (RSD)	02/24/2012
144	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium (OPSB)	01/17/2014
145	McDonogh #35 School at the Phillip/ Waters Site (OPSB)	09/23/2015
146	McDonogh #42 Elementary School Renovation (RSD)	05/28/2015
147	McDonogh #42 Elementary School Roof (RSD)	12/21/2011
148	McDonogh #42 Elementary School HVAC Replacement (RSD)	08/09/2010
149	Mildred C. Osborne Elementary School Demolition (RSD)	02/18/2010
150	Mildred C. Osborne Elementary School (RSD)	12/03/2012
151	Modular Campuses Close Outs (RSD)	
152	Modular Classroom Demolition at Fannie C. Williams Elementary School (RSD)	05/22/2013
153	Modular Structures at Langston Hughes Elementary School (RSD)	04/05/2010
154	Morris F.X. Jeff Elementary School Demolition (RSD)	
155	Morris F.X. Jeff Elementary School Mothball (RSD)	01/15/2013
156	Murray G. Henderson Elementary School Roof (RSD)	06/23/2012
157	Nelson Elementary School Refurbishment (OPSB)	04/18/2016
158	New Andrew H. Wilson Elementary School (RSD)	10/11/2009
159	New Carter G. Woodson School (RSD)	09/14/2012
160	New Fannie C. Williams School (RSD)	08/24/2012
161	New Joseph A. Craig Elementary School (RSD)	12/09/2009
162	New L.B. Landry High School (RSD)	06/30/2010
163	New Lake Area High School (RSD)	12/28/2009
164	New Lawrence D. Crocker School (RSD)	04/29/2013
165	New PK-8 School at North Kenilworth Park at Curran Site (OPSB)	01/29/2016
166	New Parkview School (RSD)	10/12/2012
167	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens (RSD)	
168	New William Frantz Elementary School (RSD)	
169	New Orleans High School Signature Center Study (RSD)	
170	Oretha C. Haley Demo (RSD)	05/07/2012
171	Oretha C. Haley Elementary School Mothball (RSD)	09/17/2012
172	Parkview Elementary School Demolition (RSD)	08/06/2009
173	Paul L. Dunbar Elementary School Demolition (RSD)	06/16/2010
174	Paul L. Dunbar Elementary School (RSD)	06/02/2015
175	Paul B. Habans Elementary School (RSD)	06/30/2016
176	Paul B. Habans Elementary School Roof Repairs (RSD)	07/27/2012
177	Phillis Wheatley Elementary School Demolition (RSD)	09/26/2011
178	Phillis Wheatley Elementary School (RSD)	07/10/2014
179	Ray Abrams Elementary School (RSD)	03/17/2017
180	Rosenwald Elementary School Refurbishment (RSD)	04/07/2016

181	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
182	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
183	Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD)	02/15/2016
184	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
185	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
186	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
187	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
188	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
189	Schaumburg Chillers ^(RSD)	11/14/2008
190	Schwarz Alternative Repairs ^(RSD)	07/14/2009
191	Schwarz Alternative Modularity Demolition ^(RSD)	04/02/2015
192	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
193	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
194	Sherwood Forest Elementary School ^(RSD)	06/30/2016
195	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
196	Sophie B. Wright School Renovation ^(RSD)	06/08/2016
197	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
198	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
199	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
200	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
201	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
202	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
203	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
204	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
205	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
206	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
207	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
208	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
209	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
210	Thurgood Marshall Elementary School Refurbishment ^(RSD)	08/10/2018
211	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
212	Timbers HVAC ^(OPSB)	09/11/2013
213	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
214	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
215	Village de L'est Elementary School Refurbishment ^(RSD)	10/12/2016
216	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
217	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
218	Valena C. Jones Elementary School ^(RSD)	01/10/2013
219	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
220	Warren Easton High School Renovation ^(OPSB)	12/15/2015
221	Warren Easton School Courtyard Waterproofing ^(OPSB)	11/24/2017
222	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
223	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
224	New William J. Guste Elementary School ^(RSD)	10/06/2008
225	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
226	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010

