





Superintendent's Report March 2019



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department
of Education
Ms. Kunjan Narechania
Recovery School District

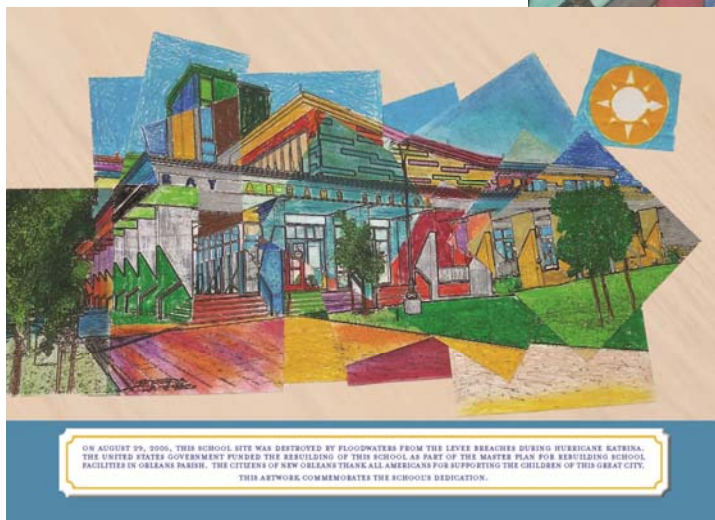

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	11
Behrman Elementary School CMaR ^(RSD)	11
Benjamin Franklin Elementary School Renovation ^(OPSB)	11
Career Technical Education High School at Kerlerec Street CMaR ^(RSD)	11
New Cohen High School CMaR ^(RSD)	12
New Karr High School, CMAR ^(RSD)	12
New Orleans Charter Science and Mathematics High School ^(OPSB)	12
Booker T. Washington School CMAR ^(RSD)	13
REFURBISHMENTS	14
Lafayette Elementary School Environmental ^(RSD)	14
Live Oak Drainage and John McDonogh Waterproofing ^(RSD)	14
Eleanor McMain School Envelope Repairs ^(OPSB)	14
Schaumburg Elementary School Roof Repairs ^(RSD)	15
Village de L'est Elementary School Environmental ^(RSD)	15
COMPLETED PROJECTS	16

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$262 million in open contracts for the capital program after issuing \$206 thousand in new contracts, change orders and amendments in March. In addition, the total change orders to date, \$4.5 million, account for two percent (2.23%) of the total open construction contracts. RSD anticipates issuing \$93 million in construction contracts/change orders, and \$290 thousand in professional service contracts/amendments in April.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 million in new contracts, change orders and amendments in March. In addition, the total change orders to date, \$3.9 million, account for approximately four percent (3.46%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 million in construction contracts/change orders and \$320 thousand in professional service contracts and amendments in April.

Community Meetings



Future Community Meetings

Bid Openings

Projects which are scheduled to bid in the next 60 days

April 10, 2019

Live Oak Drainage & John McDonogh Waterproofing Bid Opening

Disadvantaged Business Enterprises (DBE) Monthly Summary



Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 26 projects as of March 31, 2019. The DBE subcontracts value is \$82,782,214 of the \$364,282,325 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 64 projects as of March 31, 2019. The DBE subcontracts value is \$24,413,986 of the \$78,428,685 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of March 31, 2019. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 3 projects as of March 31, 2019. The DBE subcontracts value is \$45,128,505 of the 134,245,850 total of awarded contracts.

Total Amount of Contracts: \$ 686,094,417

Orleans Parish School Board



New & Renovations:

DBE Contractors secured subcontracts on 17 projects as of March 31, 2019. The DBE subcontracts value is \$65,999,022 of the \$263,467,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 4 projects as of March 31, 2019. The DBE subcontracts value is \$569,422 of the \$1,540,999 total of awarded contracts.

Total Amount of Contracts: \$265,008,830

* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

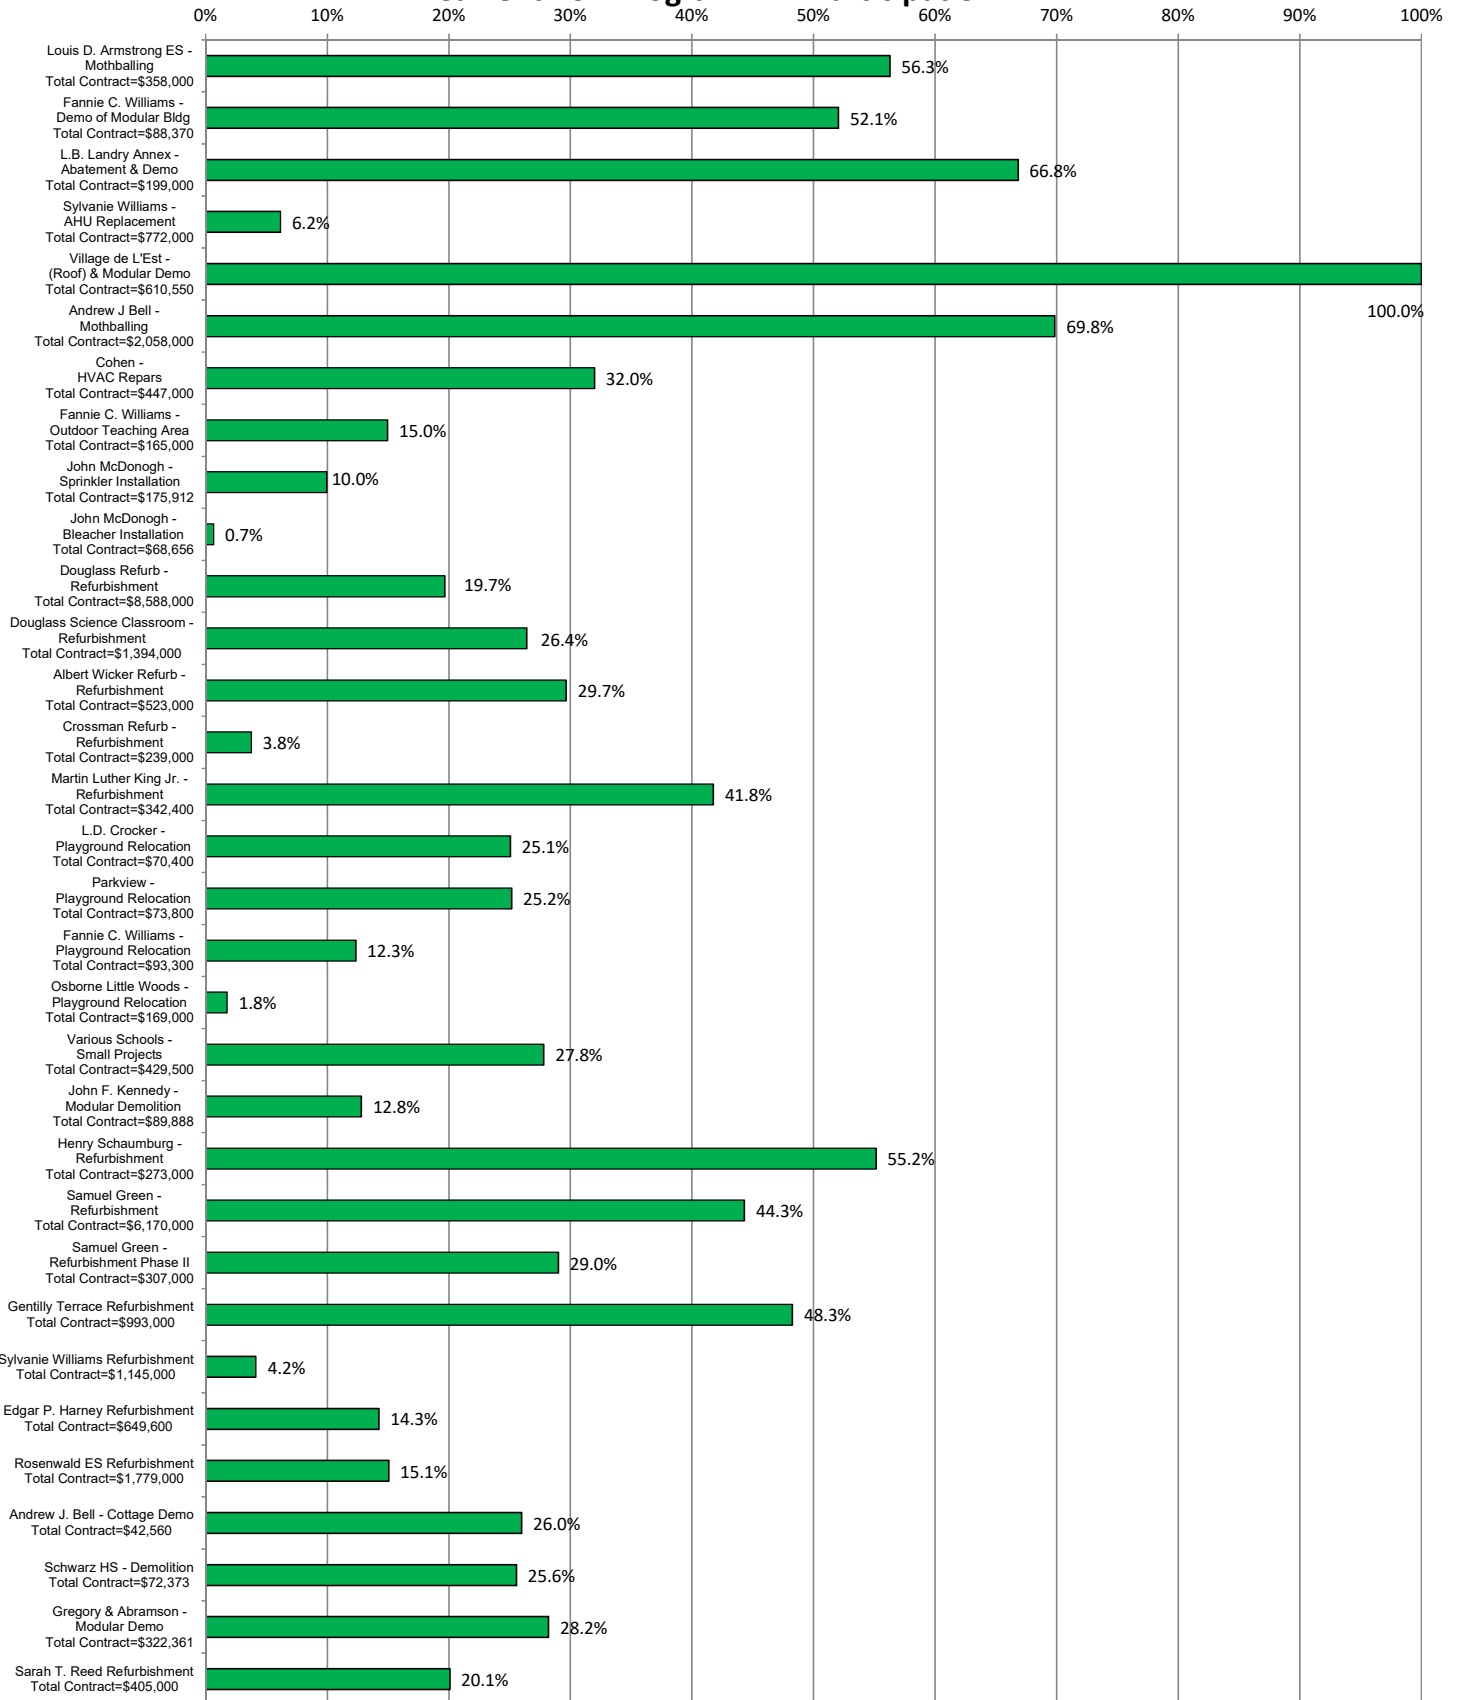


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Status Date: 31 March 2019

Current RSD Program DBE Participation


(Continued)

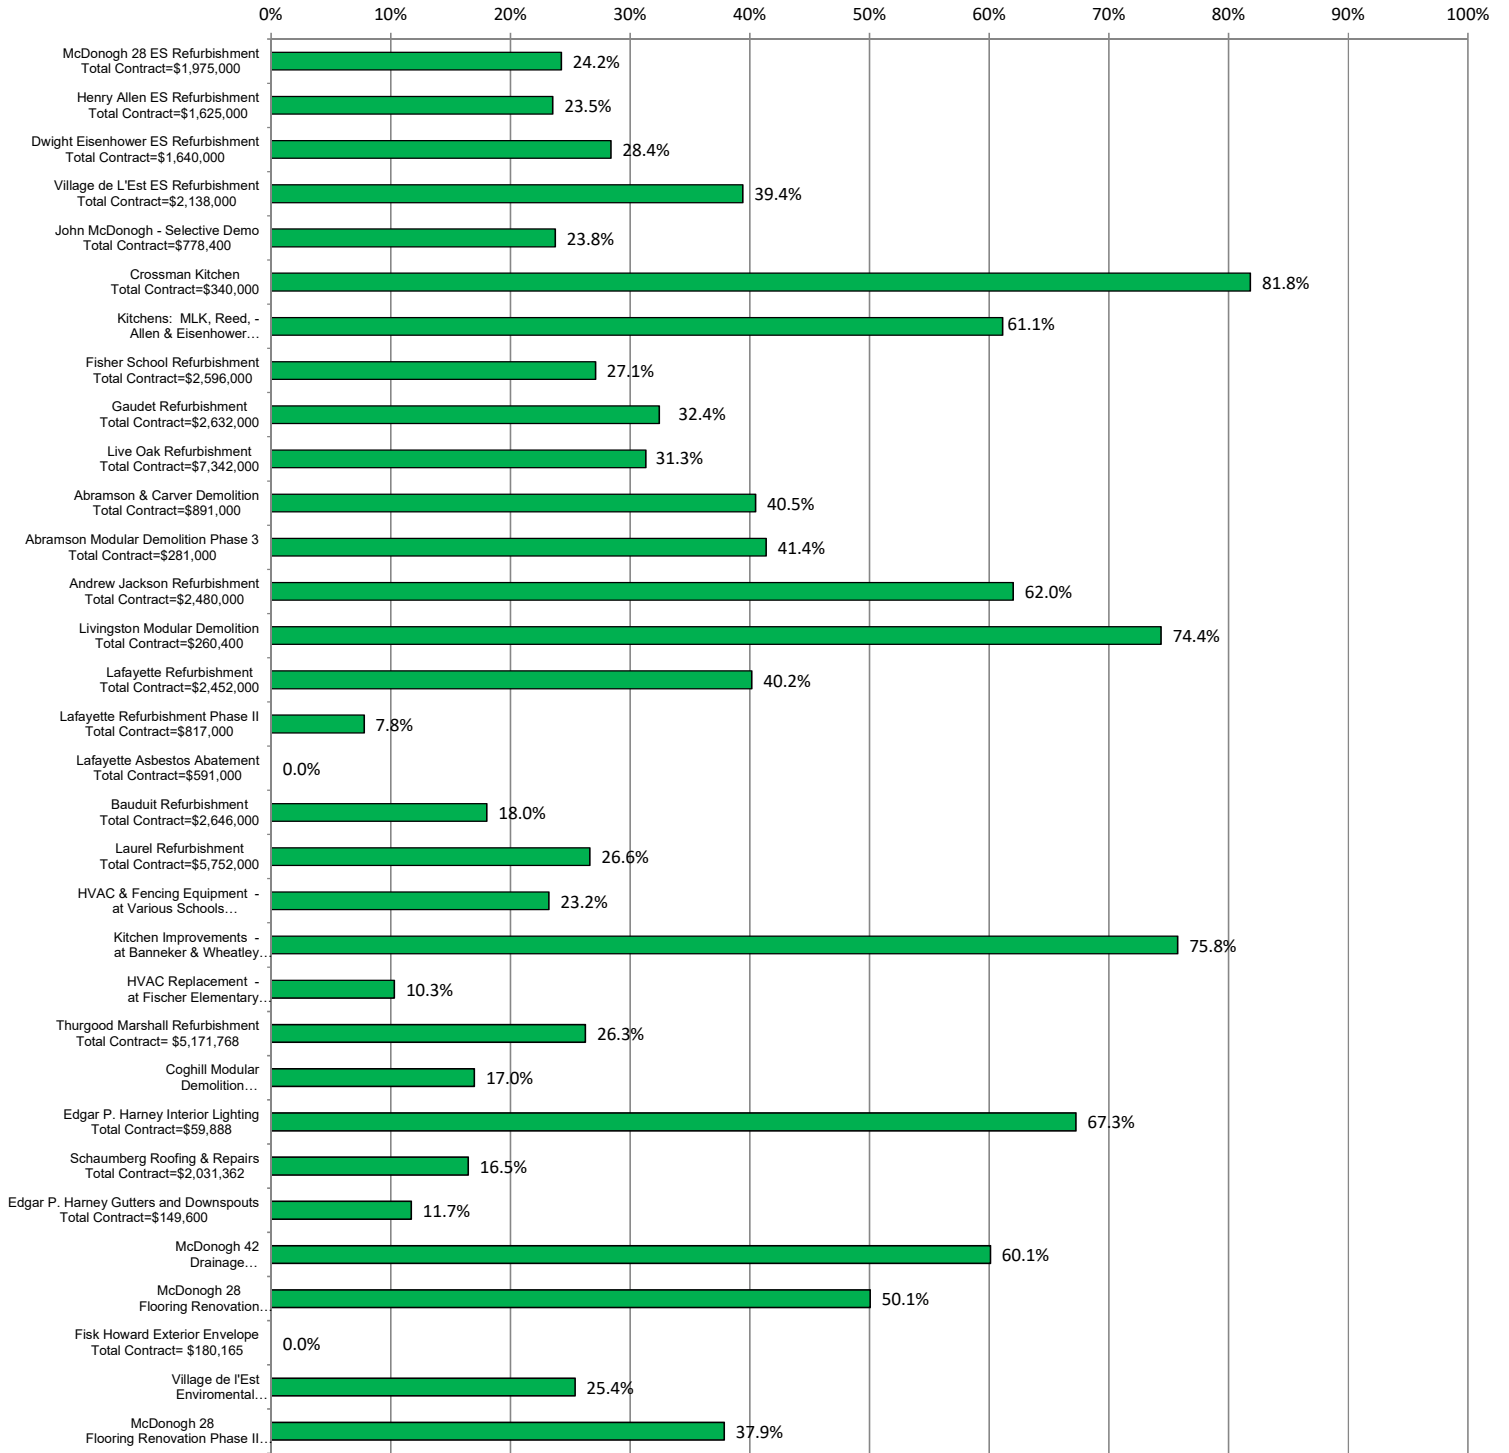

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

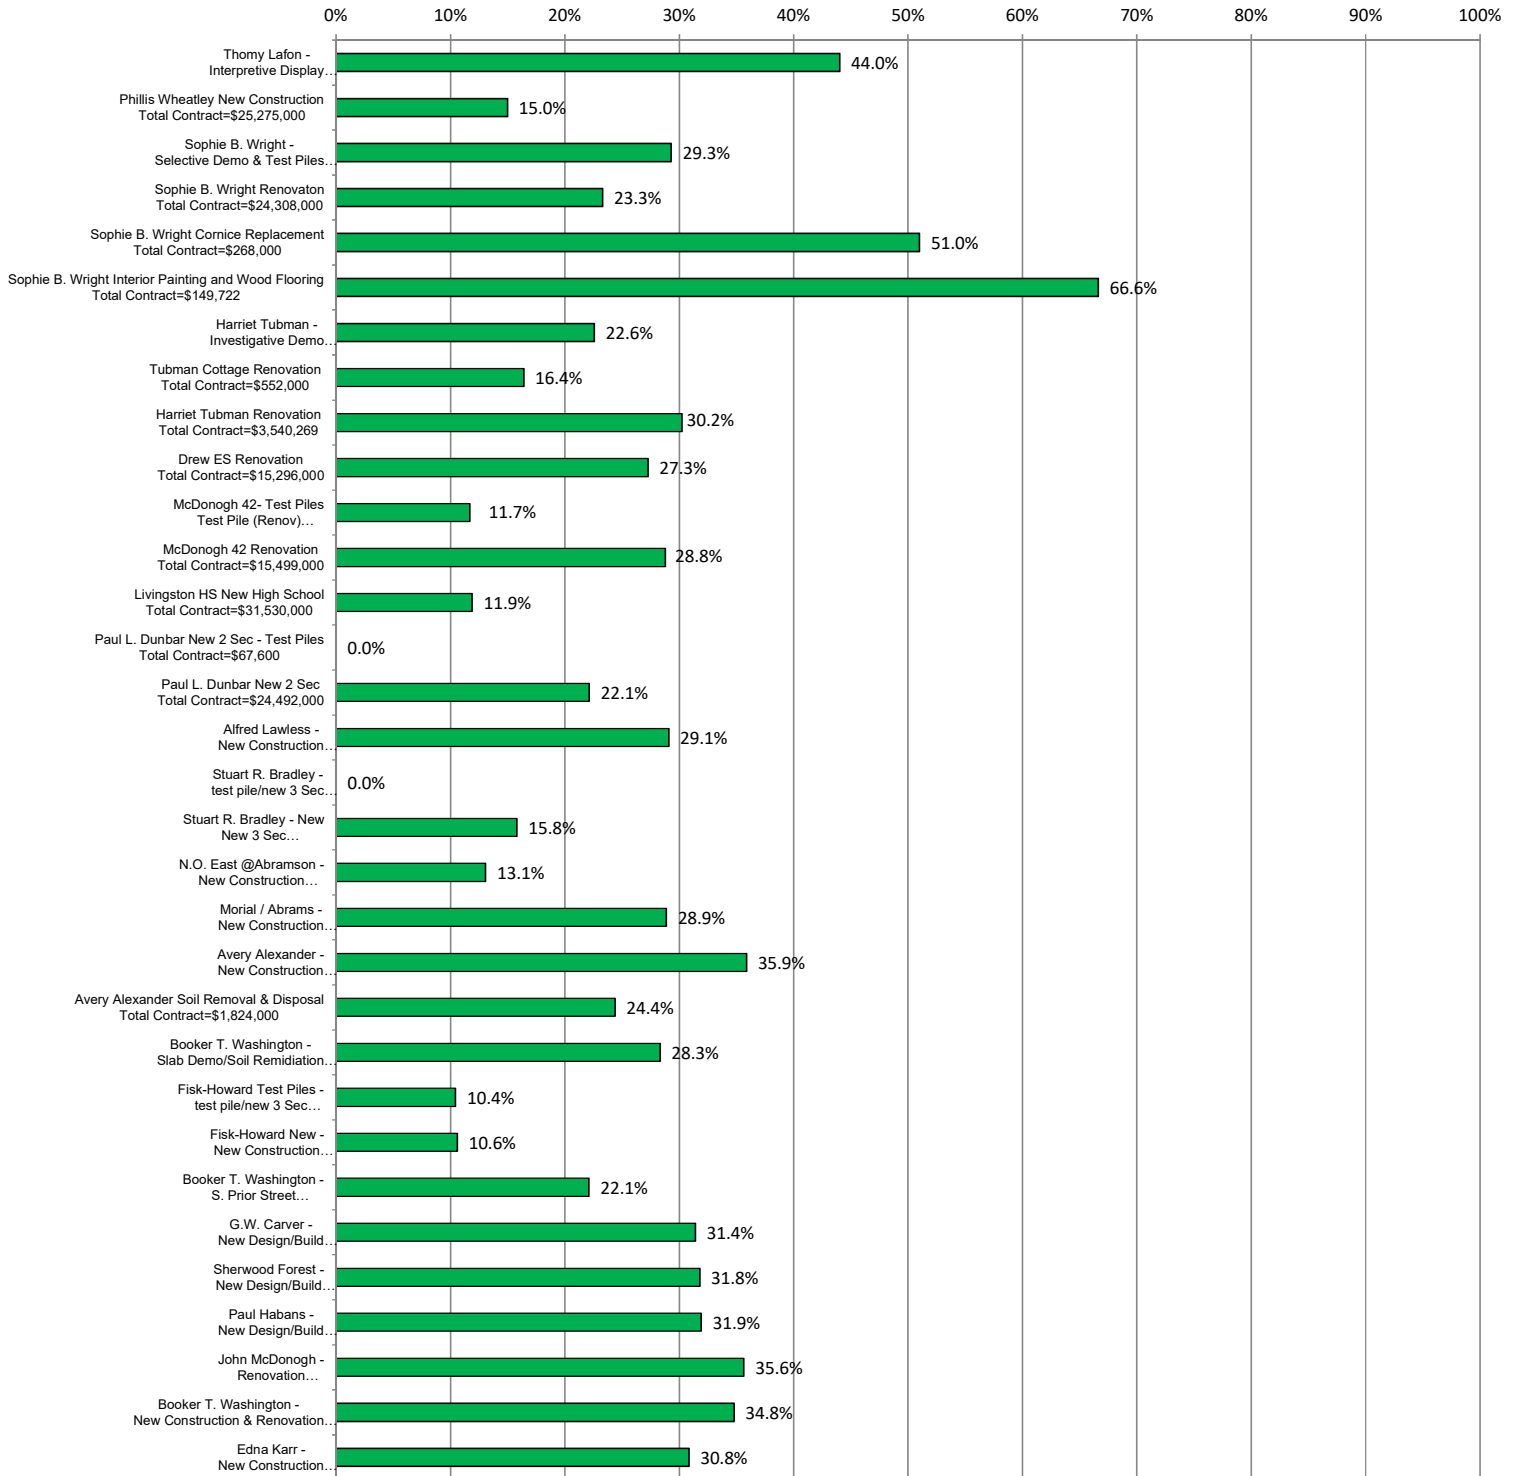

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

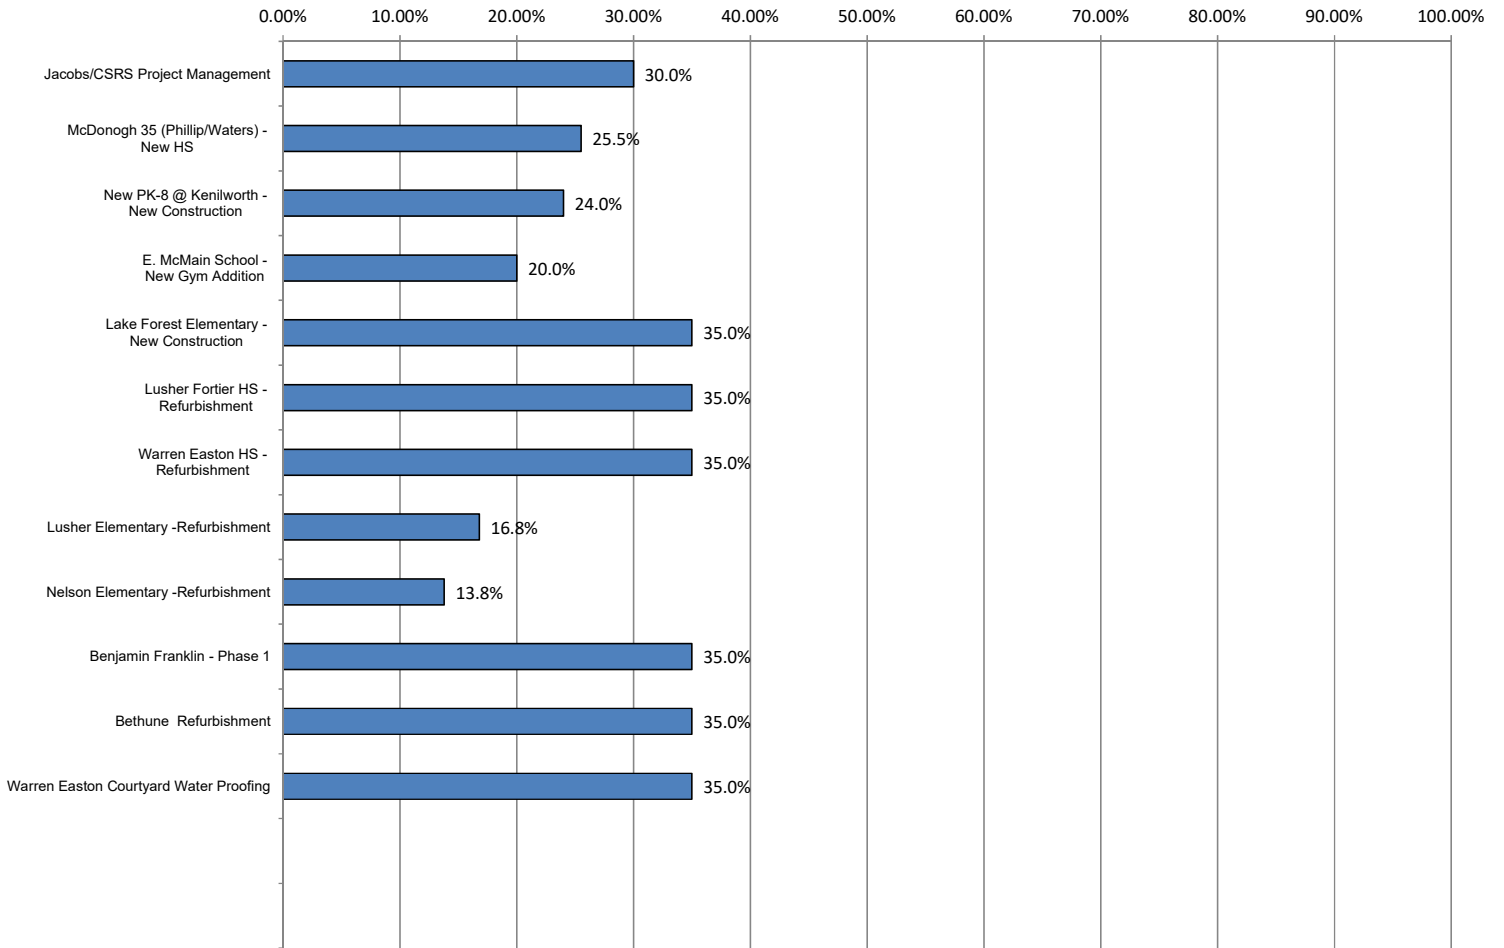

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Behrman Elementary School CMaR ^(RSD)

3819 Hershel Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – Waggoner & Ball Architects

Contractor - TBD

Design Phase

- CMaR RFQ's are being reviewed and scored
- A&E is working on existing building condition documents



Benjamin Franklin Elementary School Renovation Phase 2 ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District A Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Construction Masters

Construction Phase

- Gypsum board installation is ongoing on 2nd floor
- Floor installation and refinishing is ongoing
- HVAC installation continues on the 2nd floor
- Window repairs are ongoing



Career Technical Education High School at Kerlerec Street CMAR ^(RSD)

1331 Kerlerec Street, New Orleans, LA 70116 District D Ward 7

Scope of work: Renovation of existing high school

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Broadmoor Construction

Design Phase

- A&E continues to work on Design Development drawings



New Cohen High School CMAR ^(RSD)

3520 Dryades Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Construction of new high school

Funding Source – FEMA / CDBG

Architect – HMS Architects

Contractor - TBD

Design Phase

- Revised RFQ schedule
- Pre-Proposal Conference April 18th
- SOQ Submission May 8th
- A&E is working on Schematic Design drawings



New Karr High School CMAR ^(RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - Core Construction

Construction Phase

- High river levels will delay subsurface work
- Exterior waterproofing installation continues
- Structural steel installation is complete
- Brick installation has started

Contractual Substantial Completion – Summer 2020

Forecasted Substantial Completion – Summer 2020



New Orleans Charter Science and Mathematics High School ^(OPSB)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - The McDonnell Group

Construction Phase

- Slab on grade concrete pours continues
- Forming and pouring of columns continues
- Underground rough-ins are underway

Contractual Substantial Completion – January 2021

Forecasted Substantial Completion – January 2021



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Contractor is working on prefunction space
- Dry erase boards and tack boards are being installed
- Brick work continues on auditorium
- Exterior handrails and guardrails are being installed

Contractual Substantial Completion – June 2019 Academic Building

Forecasted Substantial Completion – June 2019 Academic Building

Contractual Substantial Completion – March 2020 Prefunction & Auditorium

Forecasted Substantial Completion – March 2020 Prefunction & Auditorium



REFURBISHMENTS

Lafayette Elementary School Environmental (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Environmental remediation

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Insul Tech

Procurement Phase

- Contracts are being reviewed by LDOE
- Project is expected to start beginning of April



Live Oak Drainage and John McDonogh Waterproofing (RSD)

3128 Constance Street and 2426 Esplanade Avenue, New Orleans, LA

Scope of work: Drainage and Waterproofing

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement - March 6th
- 2nd Advertisement - March 13th
- 3rd Advertisement - March 20th
- Pre-Bid Conference - March 21st
- Bid Opening - April 10th



Eleanor McMain School Envelope Repairs (OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Exterior stucco and window repairs

Funding Source – General Fund & Harrah's

Architect – Concordia, LLC

Contractor – Tuna Construction

Construction Phase

- Exterior painting continues
- Installation of refurbished windows in ongoing
- Exterior repairs have started at the auditorium

Contractual Substantial Completion – April 2019

Forecasted Substantial Completion – April 2019



Schaumburg Elementary School Roof Repairs ^(RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - Laperouse Metal Works, Inc

Construction Phase

- Installation of gutters and downspouts continues
- Contractor to provide hydro-seeding after school year ends

Contractual Substantial Completion – March 2018

Forecasted Substantial Completion – April 2019



Village de l'Est Elementary School Environmental ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Environmental remediation

Funding Source – FEMA, CBDG

Architect – MMG

Contractor - Insul Tech

Procurement Phase

- Remediation work to start in May 2019



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment ^(RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment ^(RSD)	10/31/2017
8	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
9	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
10	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
11	Alfred Lawless Senior ^(RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
13	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
21	Augustine Elementary School Roof ^(RSD)	04/13/2012
22	Avery-Alexander Elementary School ^(RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)	10/30/2017
25	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
26	Bell JH Shoring ^(RSD)	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
28	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
29	Bienville Elementary School Demolition ^(RSD)	05/04/2009
30	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
31	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
32	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
33	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
34	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
35	Charles J. Colton Elementary School ^(RSD)	05/23/2013
36	Charles R. Drew Elementary School ^(RSD)	04/17/2015
37	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
38	Cohen High School Health Clinic ^(RSD)	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
40	Demolition of Modular Buildings at Coghill ^(RSD)	12/26/2018
41	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
42	Demolition of Modular Buildings at Abramson and Carver ^(RSD)	01/18/2017
43	Demolition of Modular Buildings at Livingston ^(RSD)	01/18/2017

44	Douglass High School Under Floor Utilities ^(RSD)	
45	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
46	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
47	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
48	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
49	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
50	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011
51	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
52	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
53	Edgar P. Harney Elementary School Downspouts and Gutters ^(RSD)	01/09/2019
54	Edgar P. Harney Elementary School Lighting Repairs ^(RSD)	08/08/2018
55	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
56	Edna Karr High School - Assessment ^(OPSB)	
57	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
58	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
59	New Edward Hynes School ^(OPSB)	02/06/2012
60	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
61	Edward Livingston High School ^(RSD)	01/05/2015
62	Eleanor L. McMMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
63	Eleanor L. McMMain School Clinic ^(OPSB)	07/24/2013
64	Eleanor L. McMMain School Maintenance Upgrades ^(OPSB)	12/12/2016
65	Eleanor L. McMMain School Roof Replacement ^(OPSB)	05/13/2016
66	Ernest "Dutch" Morial Elementary ^(RSD)	03/17/2017
67	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
68	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
69	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
70	Fisk Howard Exterior Envelope Repairs ^(RSD)	
71	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
72	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
73	Francis W. Gregory Demolition ^(RSD)	12/21/2011
74	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
75	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
76	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
77	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
78	Gaudet Elementary School Refurbishment ^(RSD)	12/20/2016
79	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
80	George Mondy Elementary School Mothball ^(RSD)	
81	George Washington Carver School ^(RSD)	03/07/2016
82	George Washington Carver High School Demolition ^(RSD)	08/24/2011
83	Greater St. Stephens School ^(OPSB)	03/18/2013
84	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
85	Harriet R. Tubman Elementary School Renovation ^(RSD)	08/01/2018
86	Harriet R. Tubman Cottage Renovation ^(RSD)	08/02/2018
87	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
88	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
89	Henry Allen Elementary School Roof ^(RSD)	05/24/2010

90	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
91	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
92	Holy Cross Modular Relocation ^(RSD)	12/14/2010
93	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
94	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
95	James Derham Demolition ^(RSD)	02/23/2012
96	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
97	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
98	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
99	JoEllen Smith Medical Center Demolition ^(OPSB)	
100	John Dibert Elementary School Roof ^(RSD)	08/20/2010
101	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
102	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
103	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
104	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
105	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
106	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
107	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
108	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
109	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
110	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
111	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
112	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
113	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
114	Lake Area Landry Demolition ^(RSD)	05/01/2008
115	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
116	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
117	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
118	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
119	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
120	Laurel Elementary School Refurbishment ^(RSD)	01/03/2018
121	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
122	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
123	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
124	Live Oak Elementary School Refurbishment ^(RSD)	01/06/2017
125	Live Oak Elementary School Roof ^(RSD)	08/04/2011
126	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
127	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
128	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
129	Lusher Elementary School Refurbishment ^(OPSB)	10/31/2016
130	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
131	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
132	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
133	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
134	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
135	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012

136	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
137	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
138	Mary M. Bethune Elementary School Refurbishment ^(OPSB)	10/26/2017
139	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
140	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
141	McDonogh #7 High School Repairs ^(OPSB)	
142	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
143	McDonogh #28 School Refurbishment ^(RSD)	03/15/2016
144	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
145	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
146	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
147	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
148	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
149	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
150	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
151	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
152	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
153	Modular Campuses Close Outs ^(RSD)	
154	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
155	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010
156	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
157	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
158	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
159	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
160	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
161	New Carter G. Woodson School ^(RSD)	09/14/2012
162	New Fannie C. Williams School ^(RSD)	08/24/2012
163	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
164	New L.B. Landry High School ^(RSD)	06/30/2010
165	New Lake Area High School ^(RSD)	12/28/2009
166	New Lawrence D. Crocker School ^(RSD)	04/29/2013
167	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
168	New Parkview School ^(RSD)	10/12/2012
169	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
170	New William Frantz Elementary School ^(RSD)	
171	New Orleans High School Signature Center Study ^(RSD)	
172	Oretha C. Haley Demo ^(RSD)	05/07/2012
173	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
174	Parkview Elementary School Demolition ^(RSD)	08/06/2009
175	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
176	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
177	Paul B. Habans Elementary School ^(RSD)	06/30/2016
178	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
179	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
180	Phillis Wheatley Elementary School ^(RSD)	07/10/2014

181	Ray Abrams Elementary School ^(RSD)	03/17/2017
182	Rosenwald Elementary School Refurbishment ^(RSD)	04/07/2016
183	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
184	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
185	Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD)	02/15/2016
186	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
187	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
188	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
189	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
190	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
191	Schaumburg Chillers ^(RSD)	11/14/2008
192	Schwarz Alternative Repairs ^(RSD)	07/14/2009
193	Schwarz Alternative Modularity Demolition ^(RSD)	04/02/2015
194	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
195	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
196	Sherwood Forest Elementary School ^(RSD)	06/30/2016
197	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
198	Sophie B. Wright School Renovation ^(RSD)	06/08/2016
199	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
200	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
201	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
202	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
203	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
204	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
205	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
206	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
207	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
208	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
209	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
210	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
211	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
212	Thurgood Marshall Elementary School Refurbishment ^(RSD)	08/10/2018
213	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
214	Timbers HVAC ^(OPSB)	09/11/2013
215	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
216	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
217	Village de L'est Elementary School Refurbishment ^(RSD)	10/12/2016
218	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
219	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
220	Valena C. Jones Elementary School ^(RSD)	01/10/2013
221	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
222	Warren Easton High School Renovation ^(OPSB)	12/15/2015
223	Warren Easton School Courtyard Waterproofing ^(OPSB)	11/24/2017
224	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
225	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
226	New William J. Guste Elementary School ^(RSD)	10/06/2008

227	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
228	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
229	William Frantz Elementary School Roof ^(RSD)	08/12/2010
