


# Superintendent's Report August, 2016



**Dr. Henderson Lewis Jr.**  
Orleans Parish School Board



**Mr. John White**  
Louisiana Department of Education  
**Mr. Patrick Dobard**  
Recovery School District

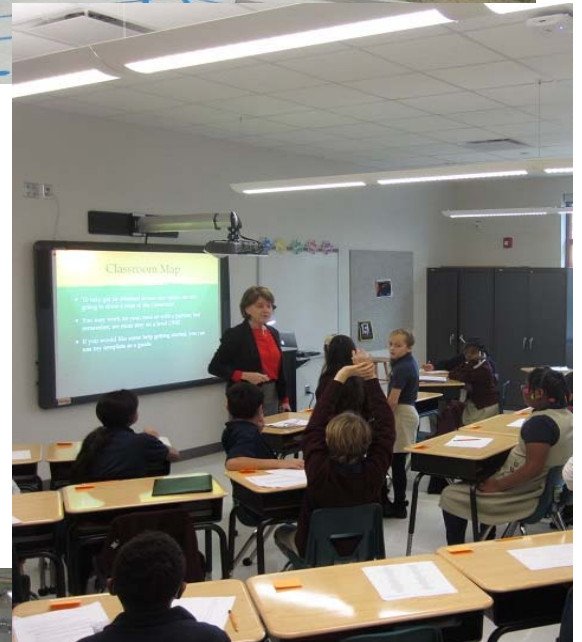

Prepared By





# Table of Contents

Right-Click on the school name to proceed to that page

<b>TABLE OF CONTENTS</b>	<b>1</b>
<b>FINANCIAL OVERVIEW</b>	<b>3</b>
<b>COMMUNITY MEETINGS</b>	<b>4</b>
<b>BID OPENINGS</b>	<b>5</b>
<b>DBE OVERVIEW MONTHLY SUMMARY</b>	<b>6</b>
<b>NEW &amp; MAJOR RENOVATION</b>	<b>11</b>
Ray Abrams Elementary School <sup>(RSD)</sup>	11
Avery Alexander Elementary School <sup>(RSD)</sup>	11
Benjamin Franklin Elementary School Renovation <sup>(OPSB)</sup>	11
JoEllen Smith Medical Center Demolition <sup>(OPSB)</sup>	12
New Karr High School, CMAR <sup>(OPSB)</sup>	12
John McDonogh High School Renovation CMAR <sup>(RSD)</sup>	12
Ernest "Dutch" Morial Elementary School <sup>(RSD)</sup>	13
Harriet R. Tubman Elementary School Renovation <sup>(RSD)</sup>	13
Booker T. Washington School CMAR <sup>(RSD)</sup>	13
Sophie B. Wright School Cornice Replacement <sup>(RSD)</sup>	14
<b>REFURBISHMENTS</b>	<b>15</b>
Benjamin Banneker Elementary Kitchen School Refurbishment <sup>(RSD)</sup>	15
Agnes L. Bauduit Elementary School Refurbishment <sup>(RSD)</sup>	15
A. D. Crossman School Kitchen Refurbishment <sup>(RSD)</sup>	15
William J. Fischer Elementary Refurbishment <sup>(RSD)</sup>	16
Gaudet Elementary School Refurbishment <sup>(RSD)</sup>	16
Samuel J. Green Elementary School Refurbishment <sup>(RSD)</sup>	16
Andrew Jackson School Refurbishment <sup>(RSD)</sup>	17
Lafayette Elementary School Refurbishment <sup>(RSD)</sup>	17
Laurel Elementary School Refurbishment <sup>(RSD)</sup>	17
Live Oak Elementary School Refurbishment <sup>(RSD)</sup>	18
Lusher Elementary School Refurbishment <sup>(OPSB)</sup>	18
Thurgood Marshall Elementary School Refurbishment <sup>(RSD)</sup>	18
McDonogh #32 School Refurbishment <sup>(RSD)</sup>	19
Village de l'Est Elementary School Refurbishment <sup>(RSD)</sup>	19
Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing <sup>(RSD)</sup>	19

<b>OTHER PROJECTS</b>	20
Eleanor L. McMain School Maintenance Upgrades <sup>(OPSB)</sup>	20
<b>DEMOLITIONS</b>	21
Demolition of Modulares at Abramson and Carver <sup>(RSD)</sup>	21
Demolition of Modulares at Livingston <sup>(RSD)</sup>	21
<b>COMPLETED PROJECTS</b>	22

# Overview

## FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$551 million in open contracts for the capital program after issuing \$6.7 million in new contracts, change orders and amendments in August. In addition, the total change orders to date, \$6.6 million, account for one percent (1.10%) of the total open construction contracts. RSD anticipates issuing approximately \$1.6 million in construction contracts/change orders, and \$ -71 thousand in professional service contracts/amendments in September.



The OPSB has \$233 million in open contracts for the capital program after issuing \$334 thousand in new contracts, change orders and amendments in August. In addition, the total change orders to date, \$8.5 million, account for approximately four percent (4.28%) of the total open construction contracts. OPSB anticipates issuing approximately \$15 thousand in construction contracts/change orders and –\$200 thousand in professional service contracts and amendments in September.

# Community Meetings



## Future Community Meetings

### **September 30, 2016**

Sherwood Forest Elementary School Ribbon Cutting  
4801 Maid Marion Drive New Orleans, LA 70128

### **October 4, 2016**

Sophie B. Wright High School Ribbon Cutting  
1426 Napoleon Avenue New Orleans, LA 70115

### **October 18, 2016**

Paul B. Habans Elementary School Ribbon Cutting  
3501 Seine Drive New Orleans, LA 70114

### **November 2, 2016**

Alfred Lawless High School Ribbon Cutting  
5301 North Rocheblave Street New Orleans, LA 70117

## **Bid Openings**

**No projects are scheduled to bid in the next 60 days**

## Disadvantaged Business Enterprises (DBE) Monthly Summary

### Recovery School District



#### New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of August 31, 2016. The DBE subcontracts value is \$79,948,197 of the \$362,548,187 total of awarded contracts.

#### Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 47 projects as of August 31, 2016. The DBE subcontracts value is \$19,483,289 of the \$64,799,535 total of awarded contracts.

#### Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of August 31, 2016. The DBE subcontracts value is \$33,454,327 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$ 536,485,279

### Orleans Parish School Board

#### New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of August 31, 2016. The DBE subcontracts value is \$54,086,557 of the \$199,371,360 total of awarded contracts.

#### Stabilization/Demolition/Mothballing:


DBE Contractors secured subcontracts on 2 projects as of August 31, 2016. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$200,274,359

\* DBE provisions were included in projects bid after June 30, 2012



## Current RSD Program DBE Participation

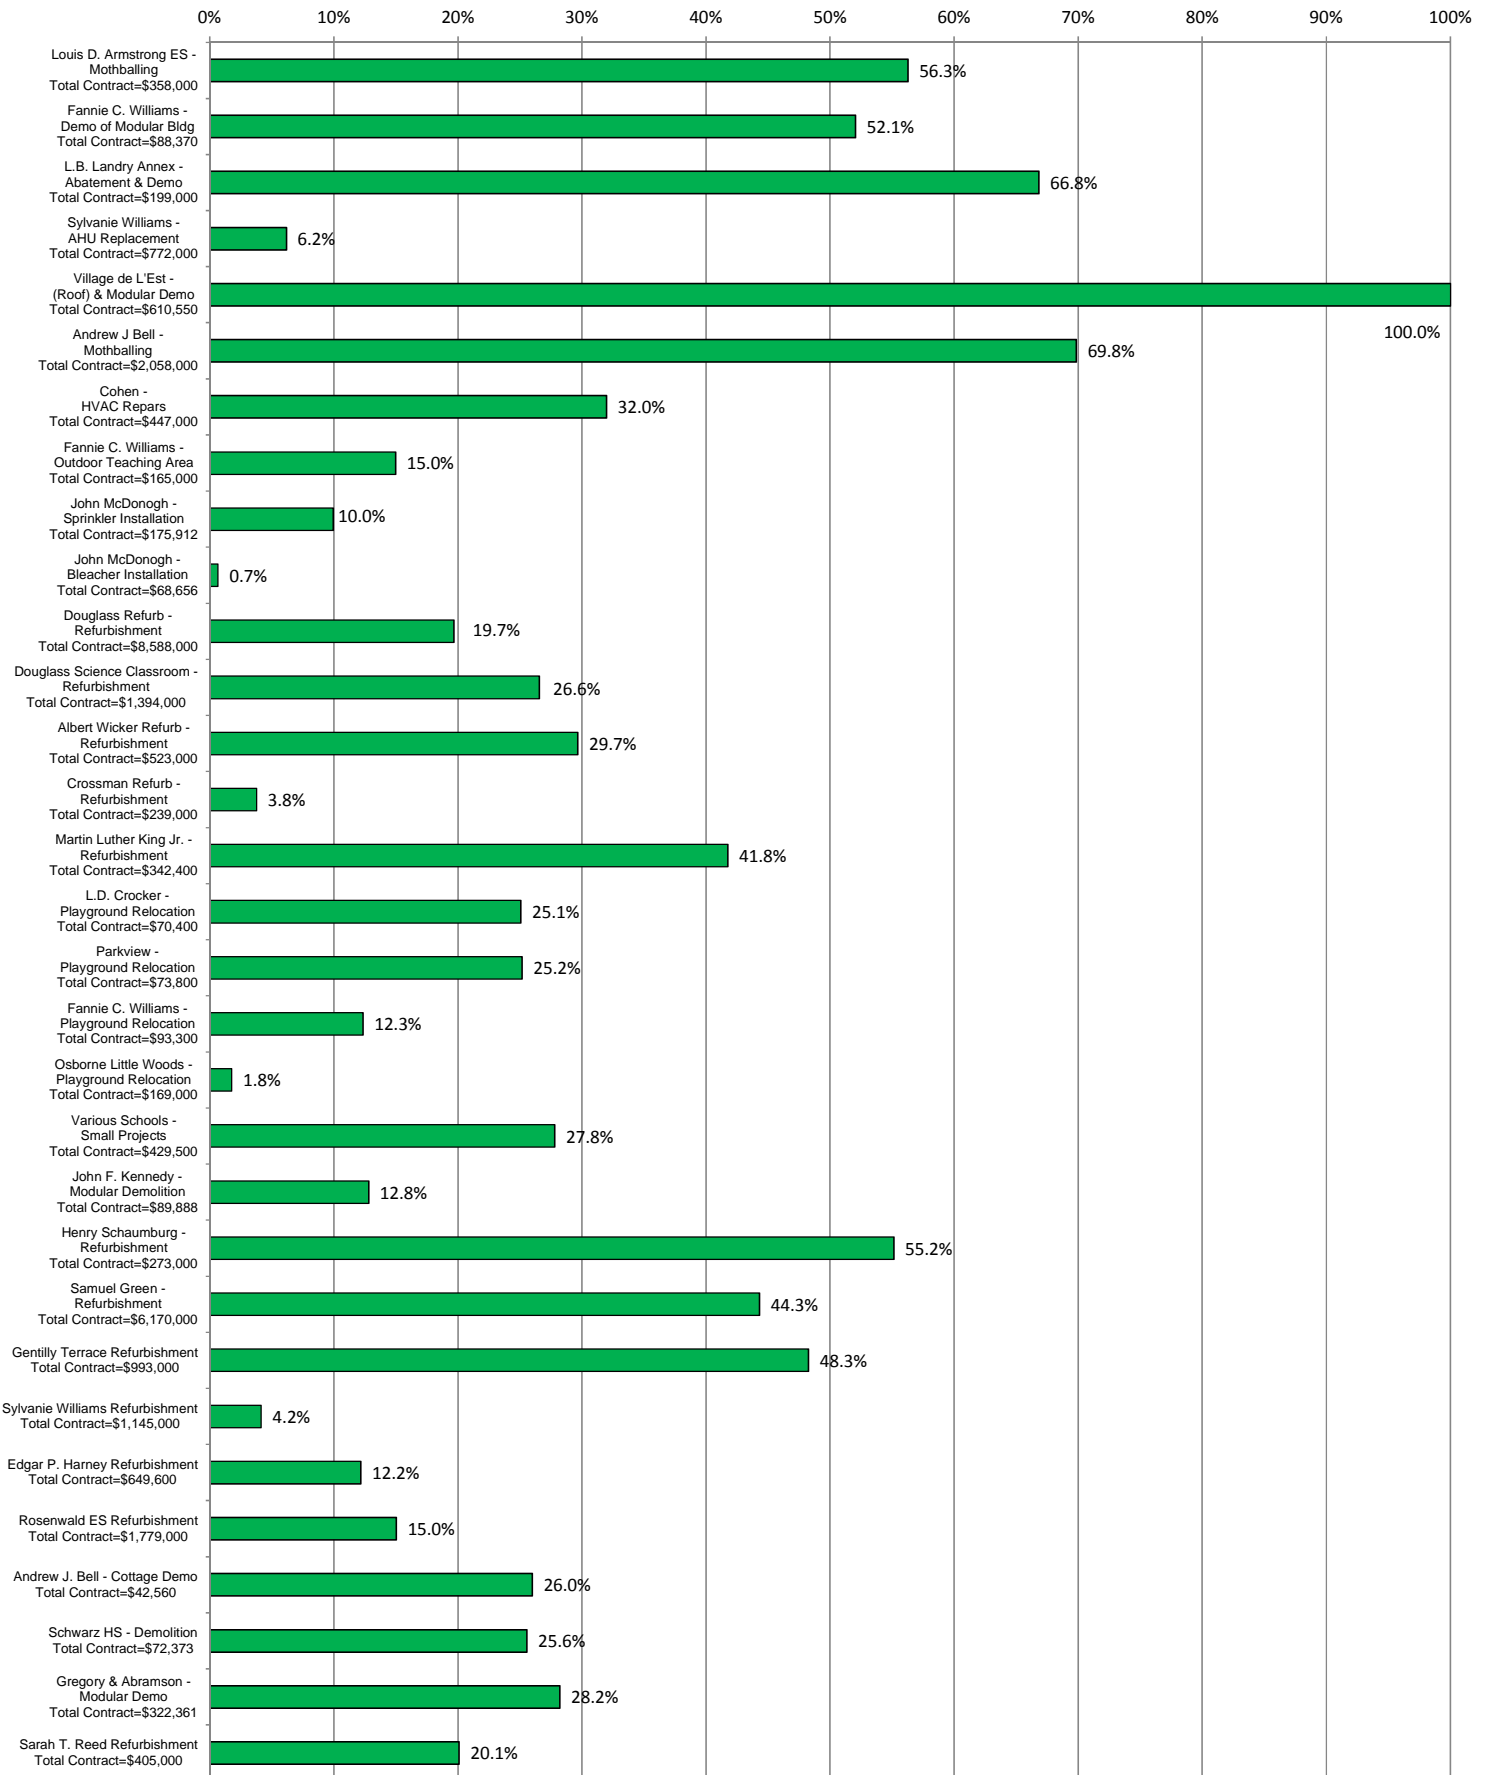


Notes: Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

Status Date: 31 August 2016

## Current RSD Program DBE Participation


(Continued)

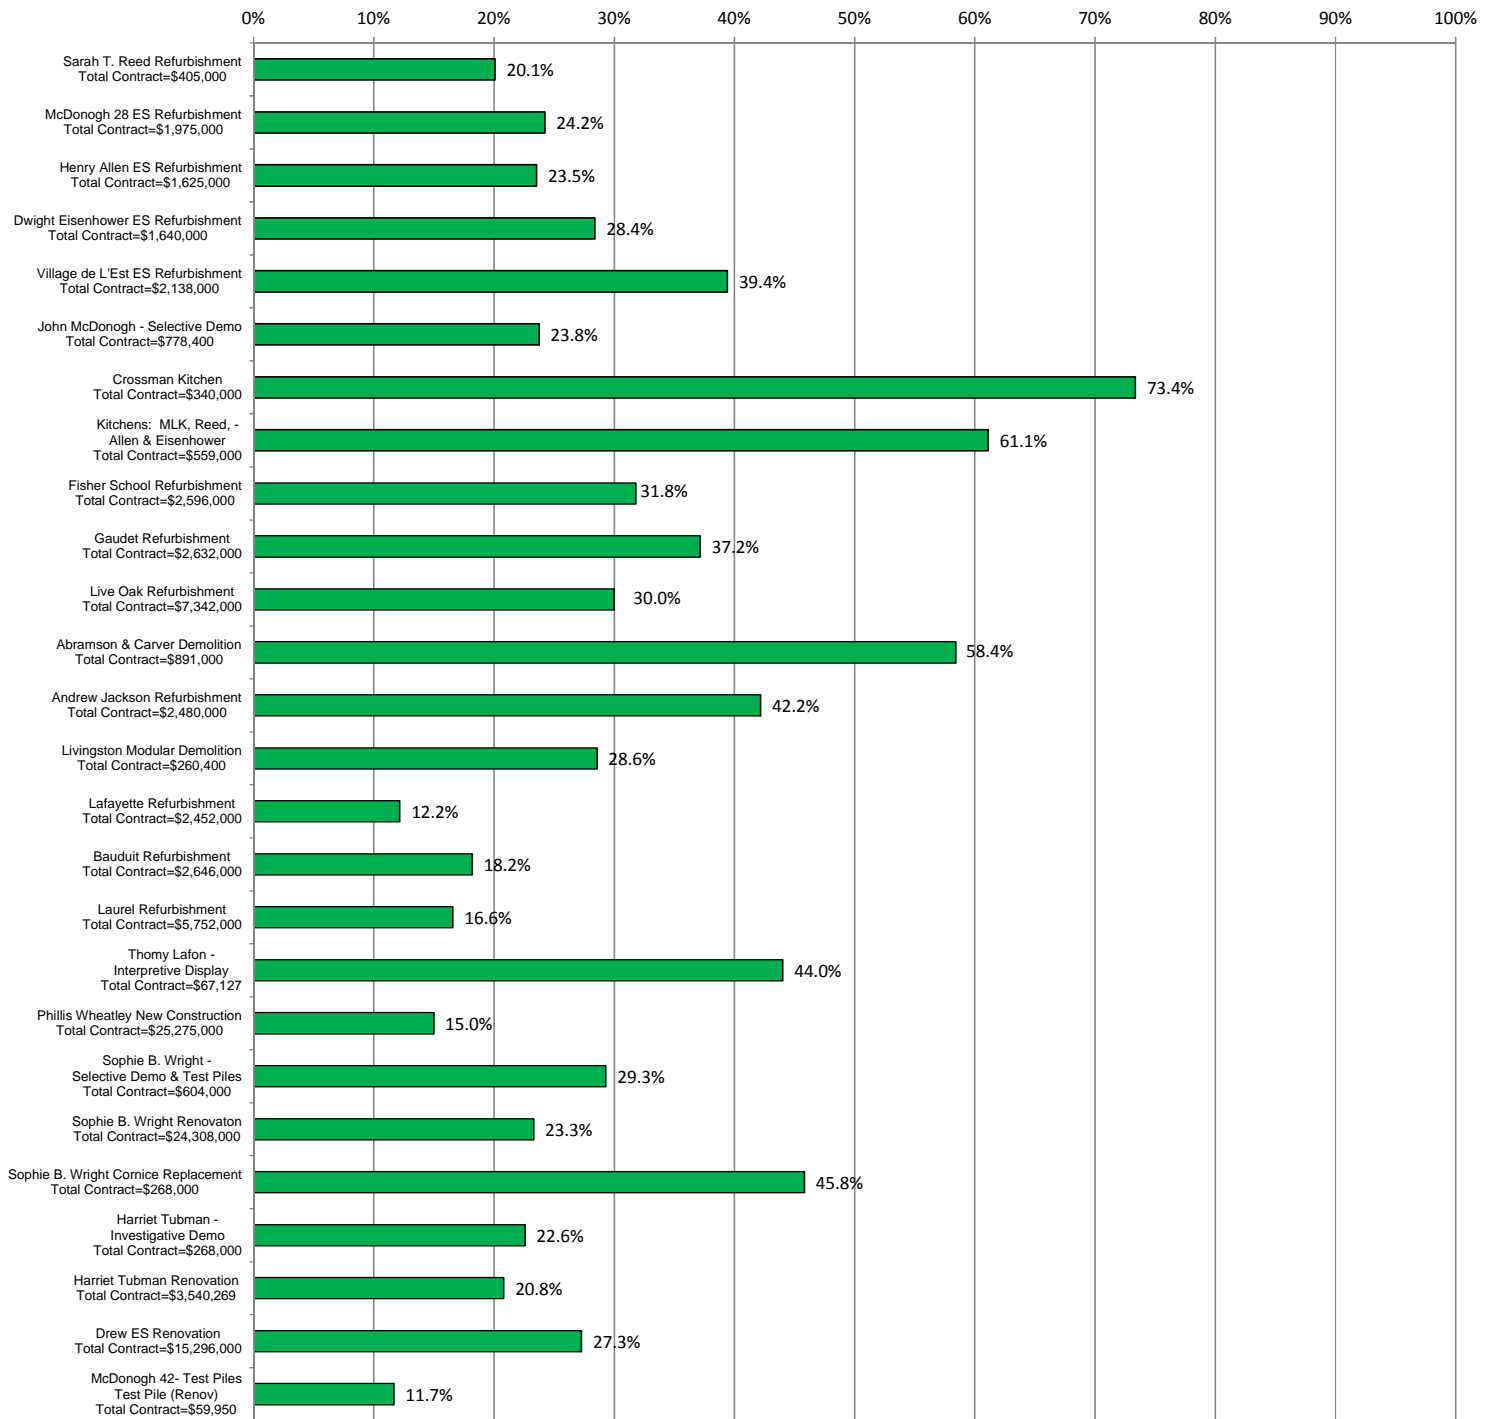

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount


## Current RSD Program DBE Participation

(Continued)

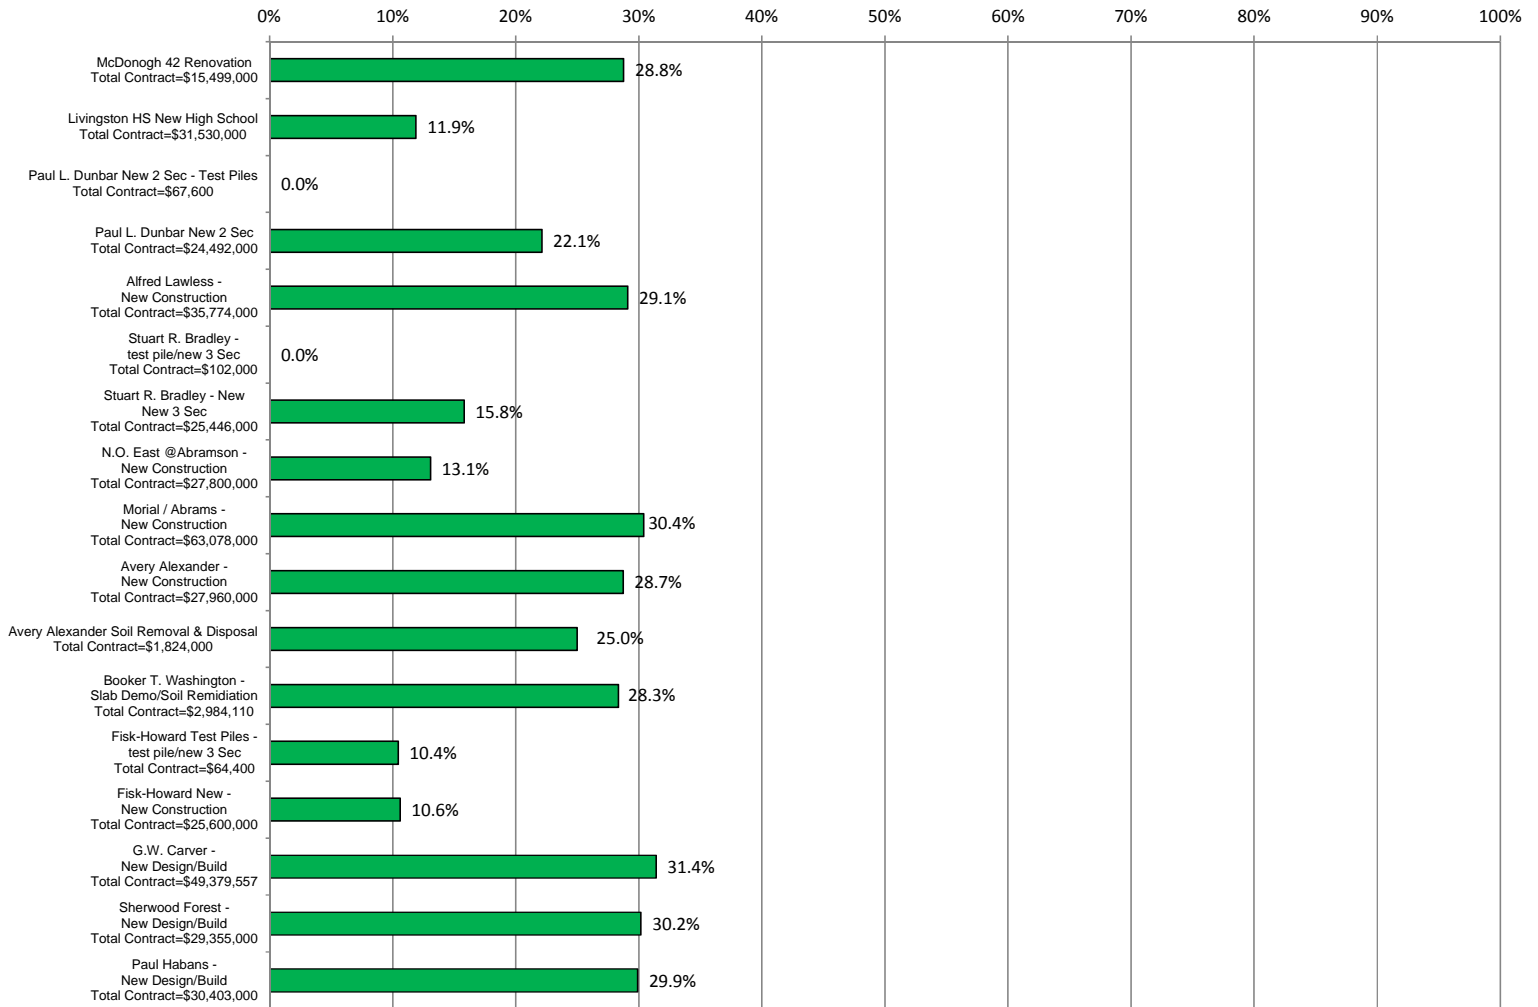

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
RSD DBE Participation Target = 25% of Total Contract Amount

### Current OPSB Program DBE Participation

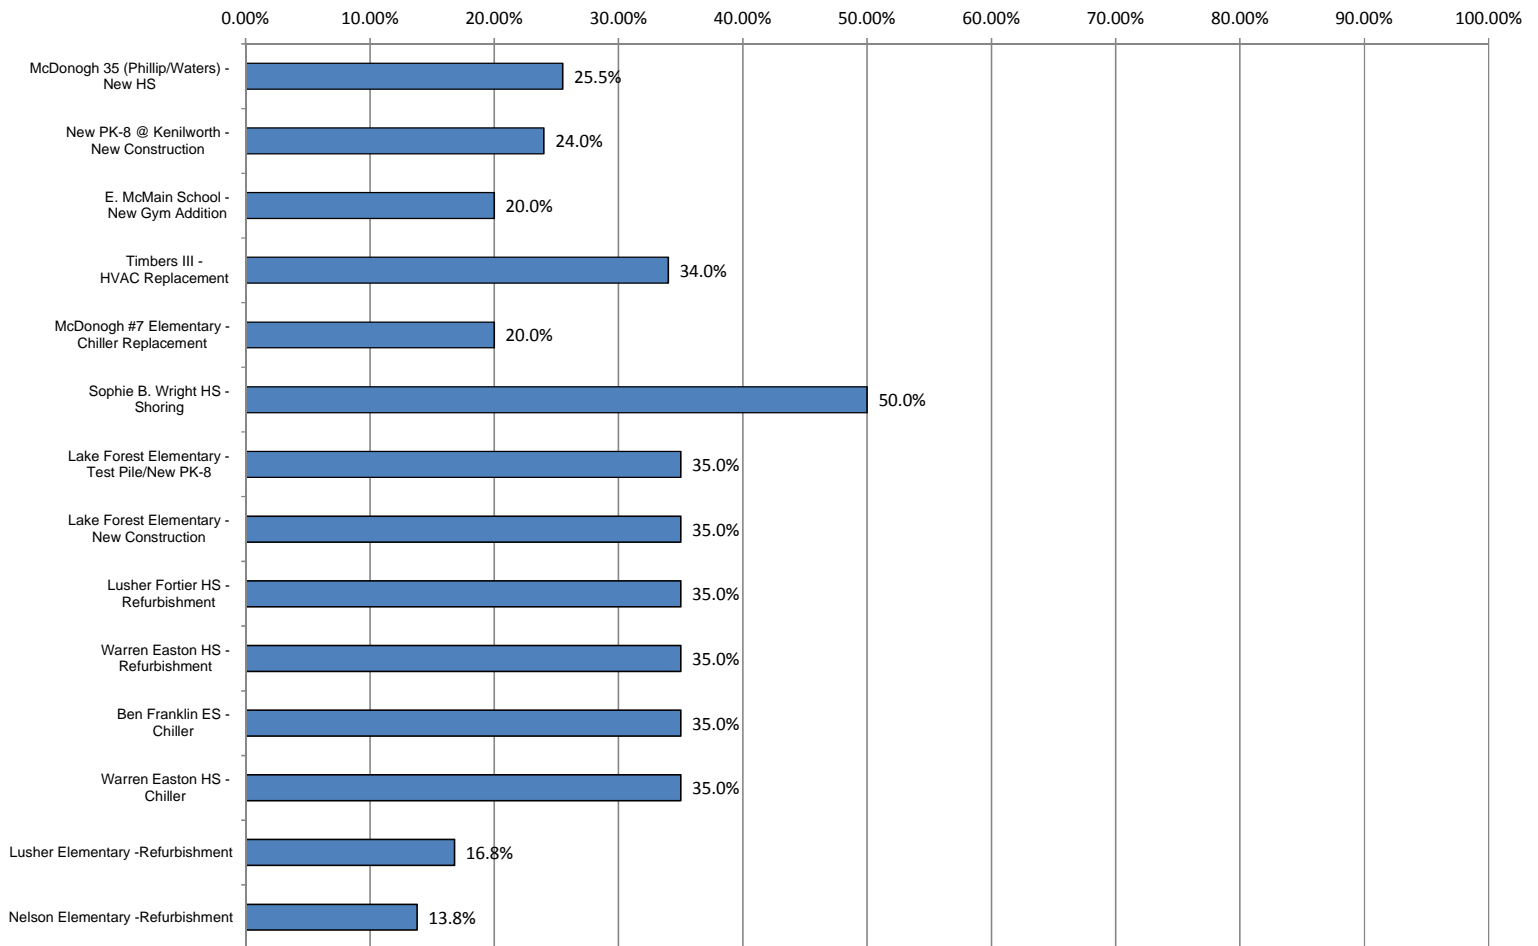

**Notes:** Data Based On Pre-Construction and/or monthly DBE Reports.  
 OPSB DBE Participation Target = 35% of Total Contract Amount

## New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

### Ray Abrams Elementary School <sup>(RSD)</sup>

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – McDonnell Group, LLC

#### Construction Phase

- Window installation is ongoing
- Elevator trim out continues
- Installation of ceiling grid continues
- Interior gypsum board finishes are underway
- Site paving and grading continues

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



### Avery Alexander Elementary School <sup>(RSD)</sup>

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

#### Construction Phase

- Installation of brick is ongoing
- Stud wall framing and interior gypsum board is ongoing
- MEP installation is 90% complete
- Window installation continues
- Permanent power is anticipated in September

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



### Benjamin Franklin Elementary School Renovation <sup>(OPSB)</sup>

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

#### Procurement Phase

- Owner is review scope with A&E



### **JoEllen Smith Medical Center Demolition (OPSB)**

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – Core Construction

#### Demolition Phase

- Additional abatement will be required in the main building
- Remediation work is moving forward at the medical office building

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – November 2016



### **New Karr High School CMAR (OPSB)**

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – TBD

Contractor - TBD

#### Procurement Phase

- Attorney General to determine if OPSB is Eligible for CMAR Procurement

Contractual Substantial Completion – November 2018

Forecasted Substantial Completion – November 2018



### **John McDonogh High School Renovation CMAR (RSD)**

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

#### Design Phase

- Work on Construction Documents continues
- Test pile program to start in September
- Bids for the Gymnasium Demolition were received and are being reviewed





### **Ernest "Dutch" Morial Elementary School <sup>(RSD)</sup>**

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – McDonnell Group, LLC

#### Construction Phase

- Window installation is nearly complete
- Interior painting has started
- Terrazzo installation is ongoing
- Elevator trim out is ongoing

Contractual Substantial Completion – January 2017

Forecasted Substantial Completion – February 2017



### **Harriet R. Tubman Elementary School Renovation <sup>(RSD)</sup>**

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

#### Construction Phase

- Repairs to existing framing continues
- Cafetorium foundation work continues
- Window refurbishment is ongoing

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



### **Booker T. Washington School CMAR <sup>(RSD)</sup>**

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

#### Construction Phase

- Test pile installation is complete, pile load test & report due in September
- Submittal package sent to FEMA/Historical Preservation



## Sophie B. Wright High School Cornice Replacement <sup>(RSD)</sup>

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Replace existing cornice

Funding Source – FEMA

Architect – Waggonner & Ball Architects, APC

Contractor – Battco Construction

### Construction Phase

- Waterproofing is complete
- Installation of replacement cornice to follow mock up acceptance in September

Contractual Substantial Completion – December 2016

Forecasted Substantial Completion – December 2016





## REFURBISHMENTS

### Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad <sup>(RSD)</sup>

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

2300 Dumaine Street, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

#### Procurement Phase

- 1st Advertisement - March 15th
- 2nd Advertisement - March 22nd
- 3rd Advertisement - March 29th
- Pre-Bid Conference - March 30th
- Bid Opening - April 19th



### Agnes L. Bauduit Elementary School Refurbishment <sup>(RSD)</sup>

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor – One Construction

#### Construction Phase

- Structural framing for HVAC units has begun
- Ceiling framing is ongoing
- Abatement of 3rd floor to take place October 19th
- Roof top units to be delivered end of October

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



### A. D. Crossman School Kitchen Refurbishment <sup>(RSD)</sup>

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - CDW Services

#### Construction Phase

- New grease trap and piping has been installed
- A&E to review installation of grease trap

Contractual Substantial Completion – July 2016

Forecasted Substantial Completion – October 2016



### **William J. Fischer Elementary School Refurbishment <sup>(RSD)</sup>**

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects


Contractor - Perez

#### Construction Phase

- Tuck pointing is ongoing
- Site parking is complete
- Restroom repairs are nearly complete
- Window delivery is anticipated mid September

Contractual Substantial Completion – February 2017

Forecasted Substantial Completion – February 2017

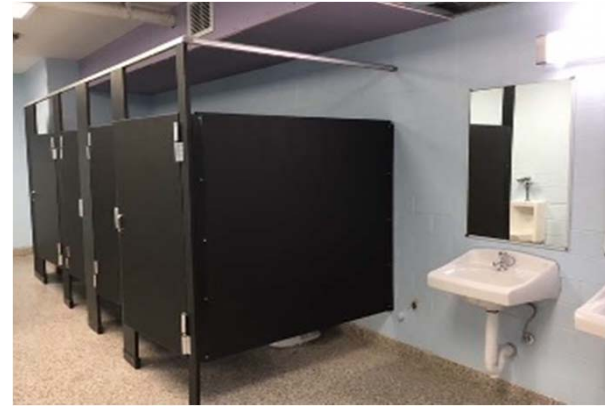

### **Gaudet Elementary School Refurbishment <sup>(RSD)</sup>**

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - One Construction

#### Construction Phase

- Roofing work is ongoing
- Electrical and lighting work is ongoing
- Chiller are set, piping connection is underway
- Restroom repairs are ongoing
- Kitchen work is nearing completion

Contractual Substantial Completion – November 2016

Forecasted Substantial Completion – November 2016



### **Samuel J. Green Elementary School Refurbishment Phase 2 <sup>(RSD)</sup>**

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school HVAC

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - TBD

#### Procurement Phase

- Bids are under advisement



### **Andrew Jackson School Refurbishment (RSD)**

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

#### Construction Phase

- Windows were stripped, repaired and reset on 3rd floor
- Stucco repairs continues on the rear of the building
- Work continues after school hours and on weekends

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



### **Lafayette Elementary School Refurbishment (RSD)**

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Tuna Construction

#### Construction Phase

- Windows restoration is underway
- Painting continues in stairwell #2
- Work continues on dumpster pad

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



### **Laurel Elementary School Refurbishment (RSD)**

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

#### Construction Phase

- Notice to Proceed August 31

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017





### **Live Oak Elementary School Refurbishment<sup>(RSD)</sup>**

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

#### Construction Phase

- Existing chiller #2 partial replacement is underway
- Mini split systems are installed and working
- Painting continues in the interior of the building
- Work continues after school hours and on weekends

Contractual Substantial Completion – July 2017

Forecasted Substantial Completion – July 2017



### **Lusher Elementary School Refurbishment<sup>(OPSB)</sup>**

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source – FEMA

Architect – Meyer Engineers, LTD.

Contractor - Dynamic

#### Construction Phase

- Punch List items for Annex and Main building are complete
- Elevator work will extent into August 2016

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – October 2016



### **Thurgood Marshall Elementary School Refurbishment<sup>(RSD)</sup>**

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

#### Design Phase - CD

- Securing FEMA approval on elevator location
- A&E is incorporating additional scope

#### Procurement Phase

- Anticipated 1st Advertisement – October 2016
- Anticipated Bid Opening – December 2016



### **McDonogh #32 School Refurbishment <sup>(RSD)</sup>**

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- A&E to revise drawings

Procurement Phase

- Anticipated 1st Advertisement – October 2016
- Anticipated Bid Opening – December 2016



### **Village de l'Est Elementary School Refurbishment <sup>(RSD)</sup>**

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

Construction Phase

- Punch list work continues
- Substantial Completion is anticipated in September

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – October 2016



### **Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing <sup>(RSD)</sup>**

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - TBD

Design Phase - CD

- 100 % Construction Documents are being reviewed

Procurement Phase

- Anticipated 1st Advertisement – December 2016
- Anticipated Bid Opening – January 2017



## OTHER PROJECTS

### **Eleanor L. McMain School Maintenance Upgrades** <sup>(OPSB)</sup>

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work.

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – Tuna Construction

#### Construction Phase

- Testing and Balance work to be completed
- Fire alarm working is ongoing on 2nd floor
- Punch list work has started

Contractual Substantial Completion – June 2016

Forecasted Substantial Completion – October 2016



## DEMOLITIONS

### Demolition of Modular Buildings at Abramson and Carver <sup>(RSD)</sup>

5552 Read Boulevard and 3059 Higgins Boulevard, New Orleans, LA

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairone Martinez JV

Contractor - Construction Masters, Inc.

#### Construction Phase

- Carver - Final grading is in progress
- Carver - Chain link fence is complete, Ornamental gate to be installed
- Abramson - Demolition of modulares is complete
- Abramson - Contractor establishing erosion control protection

Contractual Substantial Completion – October 2016

Forecasted Substantial Completion – October 2016



### Demolition of Modular Buildings at Livingston <sup>(RSD)</sup>

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – Concrete Busters of Louisiana

#### Construction Phase

- removal of modulares continues
- Fence removal is ongoing

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – September 2016





## Comprehensive List - Completed Projects

1	Abrams   Morial   Abramson   Coghill Demolition <sup>(RSD)</sup>	11/17/2008
2	A. D. Cross Elementary School Energy Conservation <sup>(RSD)</sup>	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School <sup>(RSD)</sup>	06/12/2012
4	A. D. Crossman Elementary School Refurbishment <sup>(RSD)</sup>	06/04/2014
5	A. P. Tureaud Elementary School Roof Repairs <sup>(RSD)</sup>	06/13/2013
6	Agnes Bauduit Elementary School Boiler <sup>(RSD)</sup>	12/07/2009
7	Albert Wicker Elementary School Refurbishment <sup>(RSD)</sup>	03/27/2014
8	Albert Wicker Elementary School Roof Repairs <sup>(RSD)</sup>	06/13/2013
9	Alfred Lawless Senior <sup>(RSD)</sup>	12/18/2015
10	Alfred Lawless Senior High Security Fencing <sup>(RSD)</sup>	06/15/2011
11	Alice M. Harte Elementary School <sup>(OPSB)</sup>	11/19/2014
12	Alice M. Harte Elementary School Demolition <sup>(OPSB)</sup>	12/14/2011
13	Andrew J. Bell Junior High School Roof Replacement <sup>(RSD)</sup>	02/08/2014
14	Andrew J. Bell Junior High School Mothball <sup>(RSD)</sup>	06/28/2011
15	Andrew Jackson Elementary School Roof Repairs <sup>(RSD)</sup>	07/27/2012
16	Andrew Jackson Elementary School Solar Panels <sup>(RSD)</sup>	01/14/2013
17	Andrew H. Wilson Elementary School Cottage <sup>(RSD)</sup>	10/11/2010
18	Arthur Ashe Elementary School Kitchen Renovation <sup>(OPSB)</sup>	
19	Augustine Elementary School Roof <sup>(RSD)</sup>	04/13/2012
20	Avery-Alexander Elementary School Demolition <sup>(RSD)</sup>	06/15/2012
21	Barbara C. Jordan Elementary School Demolition <sup>(RSD)</sup>	05/30/2011
22	Bell JH Shoring <sup>(RSD)</sup>	06/28/2011
23	Benjamin Banneker Elementary School Energy Conservation <sup>(RSD)</sup>	
24	Benjamin Franklin Senior High School <sup>(OPSB)</sup>	08/23/2013
25	Bienville Elementary School Demolition <sup>(RSD)</sup>	05/04/2009
26	Booker T. Washington High School Environmental Remediation <sup>(RSD)</sup>	12/13/2015
27	Booker T. Washington High School Partial Demolition <sup>(RSD)</sup>	04/07/2013
28	Carter G. Woodson Middle School Demolition <sup>(RSD)</sup>	02/09/2010
29	Central Services Warehouse Demolition <sup>(OPSB)</sup>	01/05/2012
30	Charles J. Colton Elementary Selective Demolition <sup>(RSD)</sup>	07/26/2010
31	Charles J. Colton Elementary School <sup>(RSD)</sup>	05/23/2013
32	Charles R. Drew Elementary School <sup>(RSD)</sup>	04/17/2015
33	Charles R. Drew Elementary Roof & Installation of Kitchen Hood <sup>(RSD)</sup>	06/08/2011
34	Cohen High School Health Clinic <sup>(RSD)</sup>	12/24/2008
35	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School <sup>(RSD)</sup>	
36	Demolition of Modular Buildings at Gregory and Abramson <sup>(RSD)</sup>	06/23/2015
37	Douglass High School Under Floor Utilities <sup>(RSD)</sup>	
38	Dr. Martin Luther King School Roof Repairs <sup>(RSD)</sup>	06/13/2012
39	Dr. Martin Luther King Jr. School Renovation <sup>(RSD)</sup>	12/15/2014
40	Dwight D. Eisenhower Elementary School Kitchen Refurbishment <sup>(RSD)</sup>	02/18/2016
41	Dwight D. Eisenhower Elementary School Roof Repairs <sup>(RSD)</sup>	07/27/2012
42	Dwight D. Eisenhower Elementary School Refurbishment <sup>(RSD)</sup>	12/23/2015



43	East Bank Swing Space for Audubon Charter School <sup>(OPSB)</sup>	12/30/2011
44	Edgar P. Harney Elementary School Refurbishment <sup>(RSD)</sup>	
45	Edgar P. Harney Elementary School Roof Repairs <sup>(RSD)</sup>	06/13/2012
46	Edna Karr High School - Gymnasium Repair <sup>(OPSB)</sup>	12/23/2013
47	Edna Karr High School - Assessment <sup>(OPSB)</sup>	
48	Edward Livingston Middle School Demolition <sup>(RSD)</sup>	09/28/2010
49	Edward Henry Phillips Junior High School Demolition <sup>(OPSB)</sup>	11/19/2010
50	New Edward Hynes School <sup>(OPSB)</sup>	02/06/2012
51	Edwards   Hardin   Lockett   Lawless Demolition <sup>(RSD)</sup>	11/03/2008
52	Edward Livingston High School <sup>(RSD)</sup>	01/05/2015
53	Eleanor L. McMain School Replacement of Existing Chillers <sup>(OPSB)</sup>	08/30/2011
54	Eleanor L. McMain School Clinic <sup>(OPSB)</sup>	07/24/2013
55	Eleanor L. McMain School Roof Replacement <sup>(OPSB)</sup>	05/13/2016
56	Ernest N. Morial Elementary Security Fencing <sup>(RSD)</sup>	05/10/2011
57	Fannie C. Williams Elementary School Demolition <sup>(RSD)</sup>	03/10/2009
58	Fisk-Howard Elementary School Demolition <sup>(RSD)</sup>	10/04/2011
59	Florence J. Chester Elementary School Demolition <sup>(RSD)</sup>	06/05/2011
60	Fortier (Lusher) High School Refurbishment <sup>(OPSB)</sup>	02/05/2016
61	Francis W. Gregory Demolition <sup>(RSD)</sup>	12/21/2011
62	Frederick A. Douglass High Refurbishment <sup>(RSD)</sup>	10/28/2014
63	Frederick A. Douglass High School Science Lab <sup>(RSD)</sup>	07/05/2016
64	Frederick A. Douglass High Switchgear <sup>(RSD)</sup>	08/04/2009
65	Frederick A. Douglass High Emergency Boiler Roof Repairs <sup>(RSD)</sup>	
66	Gentilly Terrace Elementary School Refurbishment <sup>(RSD)</sup>	09/22/2015
67	George Mondy Elementary School Mothball <sup>(RSD)</sup>	
68	George Washington Carver School <sup>(RSD)</sup>	03/07/2016
69	George Washington Carver High School Demolition <sup>(RSD)</sup>	08/24/2011
70	Greater St. Stephens School <sup>(OPSB)</sup>	03/18/2013
71	Harriet R. Tubman Elementary School Selective Demolition <sup>(RSD)</sup>	12/14/2014
72	Henry Allen Elementary School Refurbishment <sup>(RSD)</sup>	03/08/2016
73	Henry Allen Elementary School Kitchen Refurbishment <sup>(RSD)</sup>	02/18/2016
74	Henry Allen Elementary School Roof <sup>(RSD)</sup>	05/24/2010
75	Henry C. Schaumburg School Refurbishment <sup>(RSD)</sup>	06/26/2015
76	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation <sup>(RSD)</sup>	12/16/2011
77	Holy Cross Modular Relocation <sup>(RSD)</sup>	12/14/2010
78	Israel M. Augustine Middle School Roof Replacement <sup>(RSD)</sup>	04/13/2012
79	Israel M. Augustine Middle School Mothball <sup>(RSD)</sup>	01/18/2013
80	James Derham Demolition <sup>(RSD)</sup>	02/23/2012
81	James W. Johnson Elementary School Roof <sup>(RSD)</sup>	07/31/2010
82	New Jean Batiste de Bienville School <sup>(RSD)</sup>	06/15/2012
83	Jean Gordon Elementary School Demolition <sup>(RSD)</sup>	08/16/2010
84	John Dibert Elementary School Roof <sup>(RSD)</sup>	08/20/2010
85	John W. Hoffman Elementary School Demolition <sup>(RSD)</sup>	05/25/2010
86	John F. Kennedy Modular Relocation (Schwarz Campus) <sup>(RSD)</sup>	11/05/2010
87	John F. Kennedy Modular Relocation (Coghill Modular Campus) <sup>(RSD)</sup>	08/05/2011
88	John F. Kennedy Modular Demolition <sup>(RSD)</sup>	09/16/2014

89	John F. Kennedy High School Demolition <sup>(RSD)</sup>	01/12/2012
90	John McDonogh Senior High School Bleachers and Sprinklers <sup>(RSD)</sup>	03/27/2014
91	John McDonogh Senior High School Roof <sup>(RSD)</sup>	05/04/2010
92	John A. Shaw Elementary School Mothball <sup>(RSD)</sup>	12/12/2012
93	Joseph S. Clark Senior High School Roof Repairs <sup>(RSD)</sup>	07/27/2012
94	Joseph A. Craig Elementary Canopies <sup>(RSD)</sup>	06/06/2011
95	Joseph A. Craig Elementary Elevator Installation <sup>(RSD)</sup>	01/20/2012
96	Joseph A. Hardin Elementary Security Fencing <sup>(RSD)</sup>	05/10/2011
97	Lafayette Elementary School Roof and Masonry <sup>(RSD)</sup>	06/22/2012
98	Lake Area   Landry Demolition <sup>(RSD)</sup>	05/01/2008
99	Lake Forest PK-8 at the Greater St. Stephens Site <sup>(OPSB)</sup>	11/13/2015
100	Langston Hughes Elementary School (Phase I) <sup>(RSD)</sup>	08/11/2009
101	Langston Hughes Elementary School - New Gymnasium (Phase II) <sup>(RSD)</sup>	11/10/2010
102	Langston Hughes Elementary School - Dumpster Pad <sup>(RSD)</sup>	10/12/2012
103	Lawrence D. Crocker Elementary School Demolition <sup>(RSD)</sup>	04/02/2010
104	L.B. Landry Annex Demolition <sup>(RSD)</sup>	05/02/2013
105	Little Woods Elementary School Demolition <sup>(RSD)</sup>	08/09/2010
106	Little Woods School (Dolores T. Aaron Elementary School) <sup>(RSD)</sup>	08/01/2013
107	Live Oak Elementary School Roof <sup>(RSD)</sup>	08/04/2011
108	Live Oak Elementary School Exterior Door Replacement <sup>(RSD)</sup>	08/26/2011
109	Lorraine Hansberry Elementary School Mothball <sup>(RSD)</sup>	12/27/2012
110	Louis D. Armstrong Elementary School <sup>(RSD)</sup>	02/18/2013
111	Mahalia Jackson Elementary School <sup>(OPSB)</sup>	05/11/2010
112	Mahalia Jackson Elementary School Dumpster / Other Improvements <sup>(OPSB)</sup>	03/06/2012
113	Mahalia Jackson Elementary School Office Renovation <sup>(OPSB)</sup>	04/30/2013
114	Martin Behrman Elementary School Roof <sup>(RSD)</sup>	02/23/2010
115	Martin Luther King Jr. Elementary Canopy System <sup>(RSD)</sup>	11/05/2011
116	Martin Luther King Jr. School Modular Building, Deck, Canopy <sup>(RSD)</sup>	07/31/2012
117	Martin Luther King Jr. School Kitchen Refurbishment <sup>(RSD)</sup>	02/18/2016
118	Mary Church Terrell Elementary School Demolition <sup>(RSD)</sup>	04/17/2013
119	Mary M. Bethune Elementary 1st Floor Replacement <sup>(OPSB)</sup>	01/24/2011
120	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing <sup>(OPSB)</sup>	01/21/2011
121	McDonogh #7 High School Repairs <sup>(OPSB)</sup>	
122	McDonogh #15 Elementary Exterior Masonry to SOI Standards <sup>(RSD)</sup>	06/11/2012
123	McDonogh #28 School Refurbishment <sup>(RSD)</sup>	03/15/2016
124	McDonogh #28 Elementary School Roof <sup>(RSD)</sup>	11/19/2011
125	McDonogh #32 Roof Replacement <sup>(RSD)</sup>	02/24/2012
126	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium <sup>(OPSB)</sup>	01/17/2014
127	McDonogh #35 School at the Phillip/ Waters Site <sup>(OPSB)</sup>	09/23/2015
128	McDonogh #42 Elementary School Renovation <sup>(RSD)</sup>	05/28/2015
129	McDonogh #42 Elementary School Roof <sup>(RSD)</sup>	12/21/2011
130	McDonogh #42 Elementary School HVAC Replacement <sup>(RSD)</sup>	08/09/2010
131	Mildred C. Osborne Elementary School Demolition <sup>(RSD)</sup>	02/18/2010
132	Mildred C. Osborne Elementary School <sup>(RSD)</sup>	12/03/2012
133	Modular Campuses Close Outs <sup>(RSD)</sup>	

134	Modular Classroom Demolition at Fannie C. Williams Elementary School <sup>(RSD)</sup>	05/22/2013
135	Modular Structures at Langston Hughes Elementary School <sup>(RSD)</sup>	04/05/2010
136	Morris F.X. Jeff Elementary School Demolition <sup>(RSD)</sup>	
137	Morris F.X. Jeff Elementary School Mothball <sup>(RSD)</sup>	01/15/2013
138	Murray G. Henderson Elementary School Roof <sup>(RSD)</sup>	06/23/2012
139	Nelson Elementary School Refurbishment <sup>(OPSB)</sup>	04/18/2016
140	New Andrew H. Wilson Elementary School <sup>(RSD)</sup>	10/11/2009
141	New Carter G. Woodson School <sup>(RSD)</sup>	09/14/2012
142	New Fannie C. Williams School <sup>(RSD)</sup>	08/24/2012
143	New Joseph A. Craig Elementary School <sup>(RSD)</sup>	12/09/2009
144	New L.B. Landry High School <sup>(RSD)</sup>	06/30/2010
145	New Lake Area High School <sup>(RSD)</sup>	12/28/2009
146	New Lawrence D. Crocker School <sup>(RSD)</sup>	04/29/2013
147	New PK-8 School at North Kenilworth Park at Curran Site <sup>(OPSB)</sup>	01/29/2016
148	New Parkview School <sup>(RSD)</sup>	10/12/2012
149	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens <sup>(RSD)</sup>	
150	New William Frantz Elementary School <sup>(RSD)</sup>	
151	New Orleans High School Signature Center Study <sup>(RSD)</sup>	
152	Oretha C. Haley Demo <sup>(RSD)</sup>	05/07/2012
153	Oretha C. Haley Elementary School Mothball <sup>(RSD)</sup>	09/17/2012
154	Parkview Elementary School Demolition <sup>(RSD)</sup>	08/06/2009
155	Paul L. Dunbar Elementary School Demolition <sup>(RSD)</sup>	06/16/2010
156	Paul L. Dunbar Elementary School <sup>(RSD)</sup>	06/02/2015
157	Paul B. Habans Elementary School <sup>(RSD)</sup>	06/30/2016
158	Paul B. Habans Elementary School Roof Repairs <sup>(RSD)</sup>	07/27/2012
159	Phillis Wheatley Elementary School Demolition <sup>(RSD)</sup>	09/26/2011
160	Phillis Wheatley Elementary School <sup>(RSD)</sup>	07/10/2014
161	Rosenwald Elementary School Refurbishment <sup>(RSD)</sup>	04/07/2016
162	Robert M. Lusher Elementary Roof Removal & Replacement <sup>(OPSB)</sup>	07/14/2011
163	Samuel J. Green Elementary School Refurbishment <sup>(RSD)</sup>	02/15/2016
164	Sarah T. Reed High School Bleachers <sup>(RSD)</sup>	01/11/2012
165	Sarah T. Reed High School Auditorium Wall <sup>(RSD)</sup>	03/29/2010
166	Sarah T. Reed High School Kitchen Refurbishment <sup>(RSD)</sup>	02/18/2016
167	Sarah T. Reed High School Refurbishment <sup>(RSD)</sup>	12/01/2015
168	Seabrook Computer Training Center Demolition <sup>(OPSB)</sup>	06/25/2010
169	Schaumburg Chillers <sup>(RSD)</sup>	11/14/2008
170	Schwarz Alternative Repairs <sup>(RSD)</sup>	07/14/2009
171	Schwarz Alternative Modulares Demolition <sup>(RSD)</sup>	04/02/2015
172	Schwarz Modular Building Demolition <sup>(RSD)</sup>	04/02/2015
173	Sherwood Forest Elementary School Demolition <sup>(RSD)</sup>	10/28/2010
174	Sherwood Forest Elementary School <sup>(RSD)</sup>	06/30/2016
175	Small New Orleans East High School at Abramson <sup>(RSD)</sup>	09/24/2015
176	Sophie B. Wright School Renovation <sup>(RSD)</sup>	06/08/2016
177	Sophie B. Wright School Selective Demolition <sup>(RSD)</sup>	01/31/2014
178	Sophie B. Wright Various Repairs/Restroom Renovations <sup>(OPSB)</sup>	07/26/2011
179	Stuart R. Bradley Elementary School Demolition <sup>(RSD)</sup>	01/27/2010

180	Stuart R. Bradley Elementary School <sup>(RSD)</sup>	06/26/2015
181	Sylvanie Williams Elementary School AHU Replacement <sup>(RSD)</sup>	07/30/2013
182	Sylvanie Williams Elementary School Play Yard <sup>(RSD)</sup>	09/23/2010
183	Sylvanie Williams Elementary School Roof Repairs <sup>(RSD)</sup>	07/27/2012
184	Sylvanie Williams Elementary School HVAC/Chiller Replacement <sup>(RSD)</sup>	04/13/2012
185	Sylvanie Williams Elementary School Refurbishment <sup>(RSD)</sup>	02/18/2016
186	Temporary Campus for McDonogh #11 Expropriation <sup>(OPSB)</sup>	
187	Thomas A. Edison Elementary School Demolition <sup>(RSD)</sup>	03/25/2010
188	Thomy Lafon Elementary School Demolition <sup>(RSD)</sup>	11/27/2011
189	Thomy Lafon School Interpretative Display <sup>(RSD)</sup>	10/15/2013
190	Timbers Park Office Building #1 & #2 Demolition <sup>(OPSB)</sup>	09/18/2011
191	Timbers HVAC <sup>(OPSB)</sup>	09/11/2013
192	Timbers III - IT Room Relocation <sup>(OPSB)</sup>	02/11/2015
193	Village de L'est Elementary School Subsidence <sup>(RSD)</sup>	06/18/2012
194	Village de L'est Elementary School Roof and Modular Demolition <sup>(RSD)</sup>	06/16/2013
195	Vorice J. Waters Elementary School Demolition <sup>(RSD)</sup>	01/14/2010
196	Valena C. Jones Elementary School <sup>(RSD)</sup>	01/10/2013
197	Walter L. Cohen High School HVAC <sup>(RSD)</sup>	04/04/2014
198	Warren Easton High School Renovation <sup>(OPSB)</sup>	12/15/2015
199	Warren Easton High School Window Replacement <sup>(OPSB)</sup>	09/07/2012
200	West Bank Swing Space for Alice Harte Elementary School <sup>(OPSB)</sup>	07/11/1931
201	New William J. Guste Elementary School <sup>(RSD)</sup>	10/06/2008
202	William J. Guste Elementary School Science Lab <sup>(RSD)</sup>	08/04/2009
203	William Frantz Elementary School Environmental Remediation & Selective Demolition <sup>(RSD)</sup>	04/15/2010
204	William Frantz Elementary School Roof <sup>(RSD)</sup>	08/12/2010
