


Superintendent's Report December 2017



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Ms. Kunjan Narechania
Recovery School District

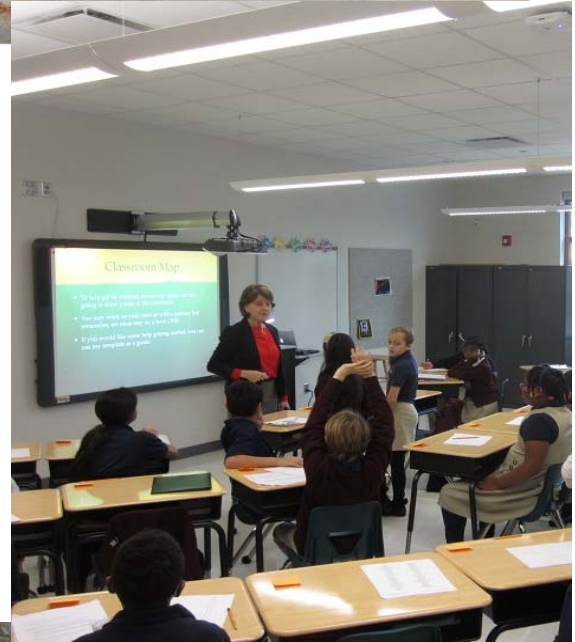

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	2
COMMUNITY MEETINGS	3
BID OPENINGS	4
DBE OVERVIEW MONTHLY SUMMARY	5
NEW & MAJOR RENOVATION	10
Benjamin Franklin Elementary School Renovation ^(OPSB)	10
New Karr High School, CMAR ^(RSD)	10
New Orleans Charter Science and Mathematics High School ^(OPSB)	10
John McDonogh High School Renovation CMAR ^(RSD)	11
Harriet R. Tubman Elementary School Renovation ^(RSD)	11
Booker T. Washington School CMAR ^(RSD)	11
REFURBISHMENTS	12
Harney Elementary School Downspout and Gutter Repairs ^(RSD)	12
Lafayette Elementary School Refurbishment ^(RSD)	12
Laurel Elementary School Refurbishment ^(RSD)	12
Thurgood Marshall Elementary School Refurbishment ^(RSD)	13
McDonogh #28 School Flooring Refurbishment ^(RSD)	13
McDonogh #32 School Refurbishment ^(RSD)	13
Eleanor McMain School Envelope Repairs ^(OPSB)	14
Harriet R. Tubman Elementary School Cottage Renovation ^(RSD)	14
Schaumburg Elementary School Roof Repairs ^(RSD)	14
Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing ^(RSD)	15
DEMOLITIONS	16
Demolition of Modulares at Abramson 3 ^(RSD)	16
Demolition of Modulares at Coghill ^(RSD)	16
COMPLETED PROJECTS	17

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$327 million in open contracts for the capital program after issuing \$322 thousand in new contracts, change orders and amendments in December. In addition, the total change orders to date, \$4.8 million, account for one percent (1.79%) of the total open construction contracts. RSD anticipates issuing \$46.8 million in construction contracts/change orders, and \$1.6 million in professional service contracts/amendments in January.



The OPSB has \$232 million in open contracts for the capital program after issuing \$15 The OPSB has \$175 million in open contracts for the capital program after issuing \$0 thousand in new contracts, change orders and amendments in December. In addition, the total change orders to date, \$7.23 million, account for approximately five percent (5.15%) of the total open construction contracts. OPSB anticipates issuing approximately \$1.9 million in construction contracts/change orders and \$113 thousand in professional service contracts and amendments in January.

Community Meetings



Future Community Meetings

February 6, 2018

New Edna Karr Community Meeting
1110 Kabel Drive, New Orleans, LA 70131

Bid Openings

Projects which are scheduled to bid in the next 60 days

February 7, 2018

McDonogh 28 Flooring Renovation Phase 2 bid Opening

March 7, 2018

Lafayette School Refurbishment Renovation Phase 2 bid Opening

Disadvantaged Business Enterprises (DBE) Monthly Summary



Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of December 31, 2017. The DBE subcontracts value is \$82,136,234 of the \$362,866,202 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 54 projects as of December 31, 2017. The DBE subcontracts value is \$23,111,655 of the \$73,075,270 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of December 31, 2017. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 2 projects as of December 31, 2017. The DBE subcontracts value is \$29,764,319 of the \$86,699,352 total of awarded contracts.

Total Amount of Contracts: \$ 631,778,381

Orleans Parish School Board



New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of December 31, 2017. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of December 31, 2017. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$231,354,830

* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

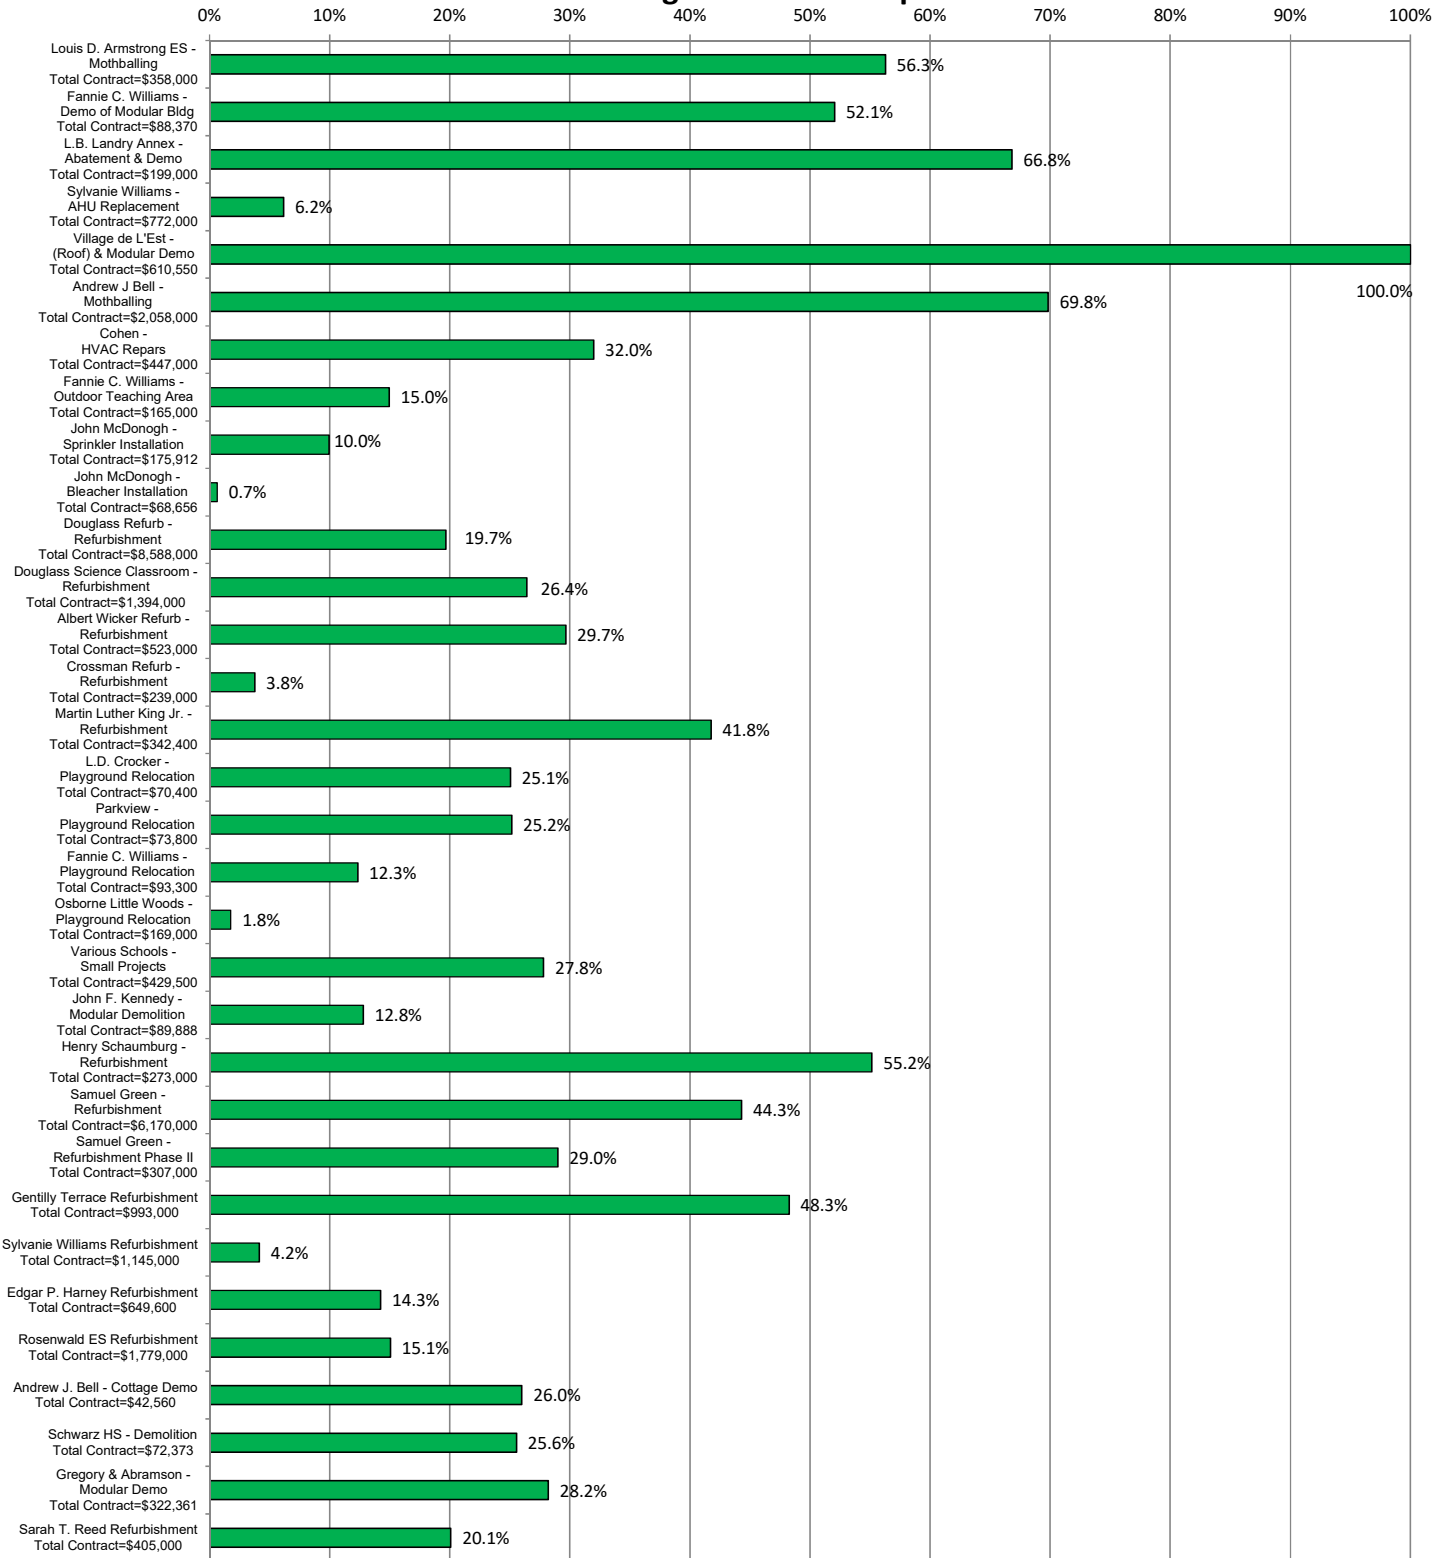


Notes: Data Based On Pre-Construction and/or 6 Monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Status Date: 31 December 2017

Current RSD Program DBE Participation


(Continued)

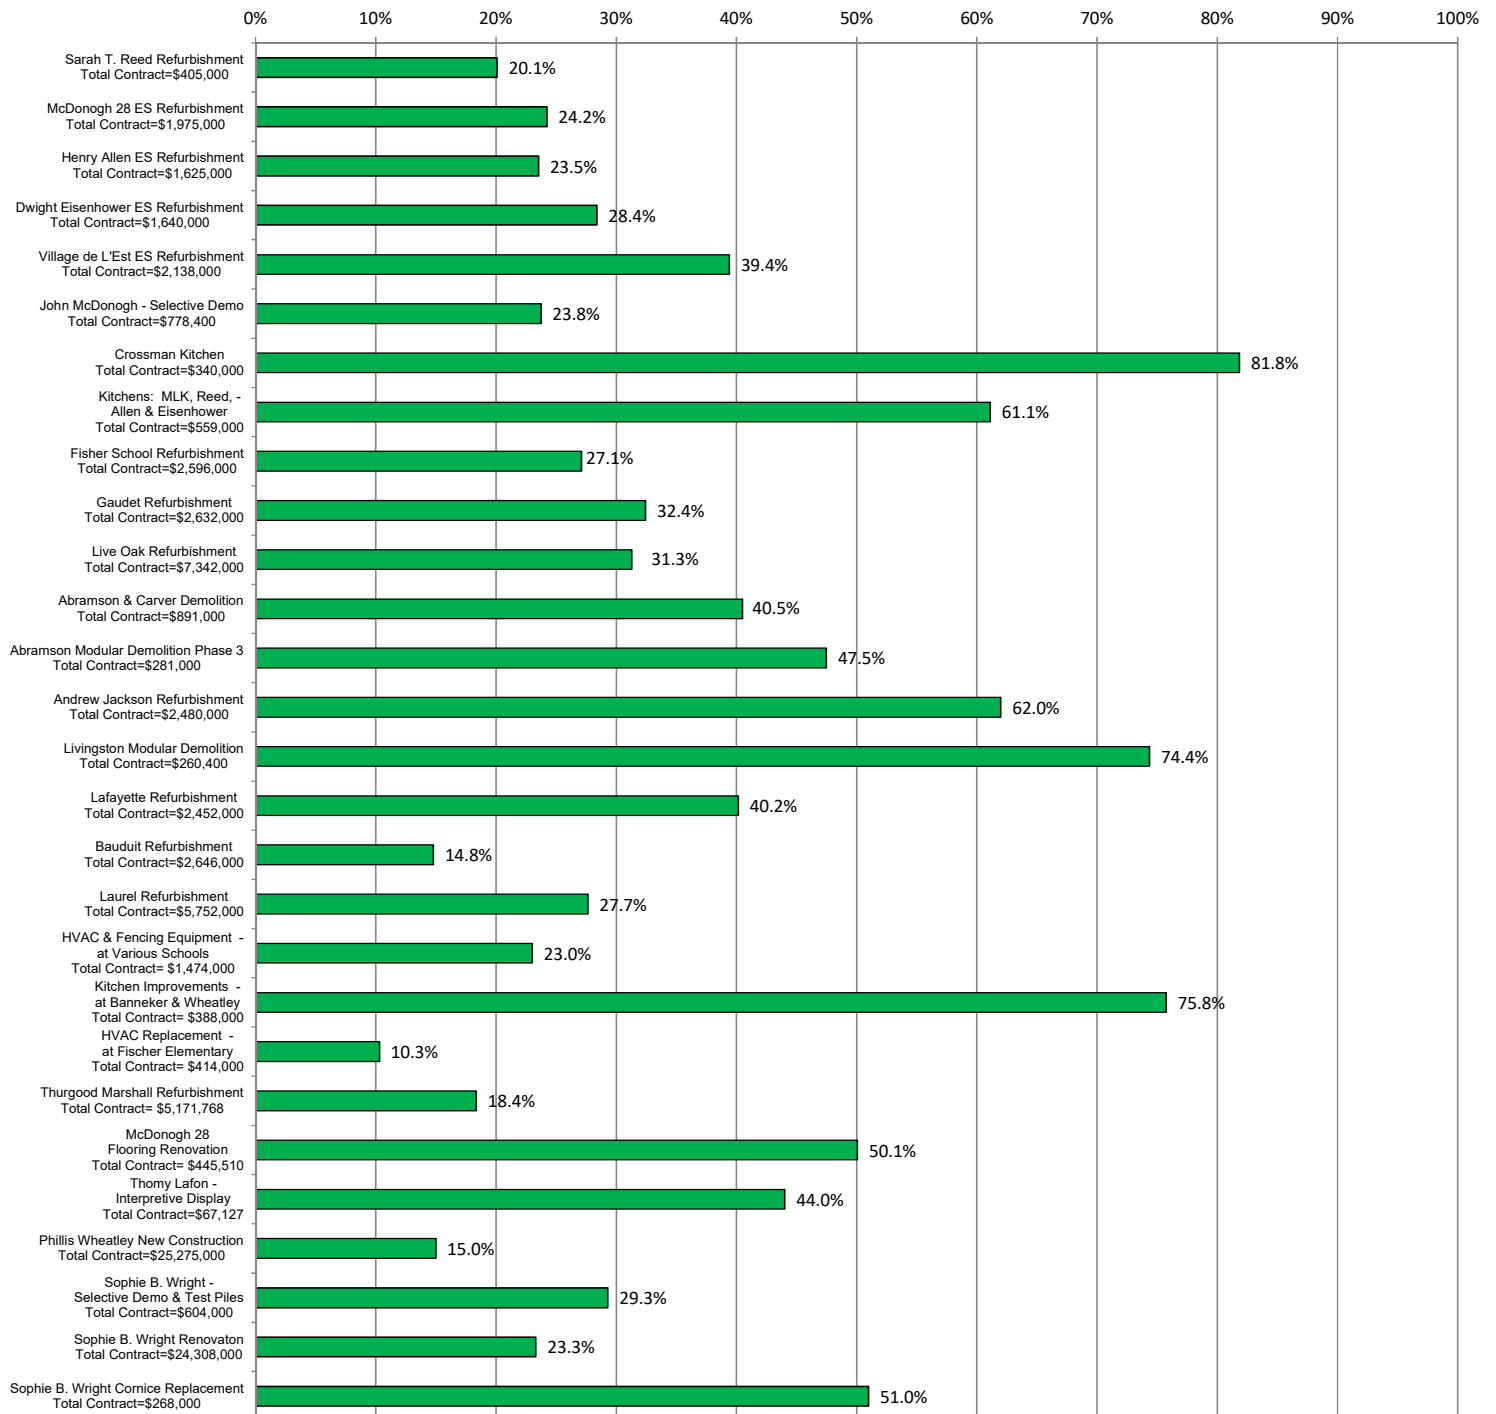

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

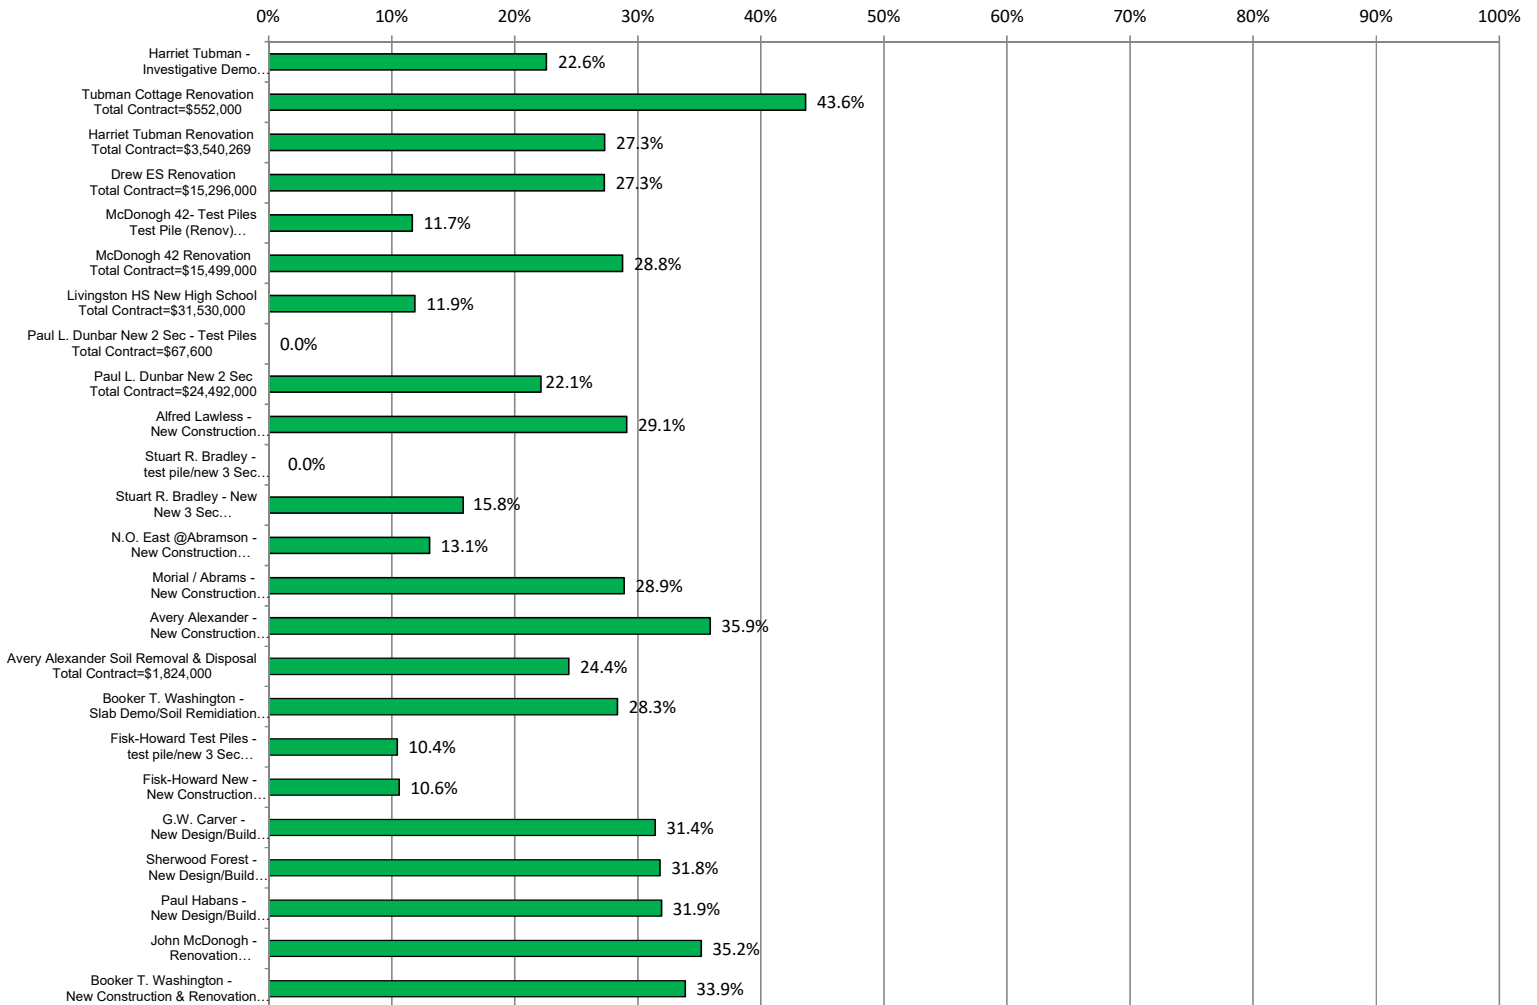

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

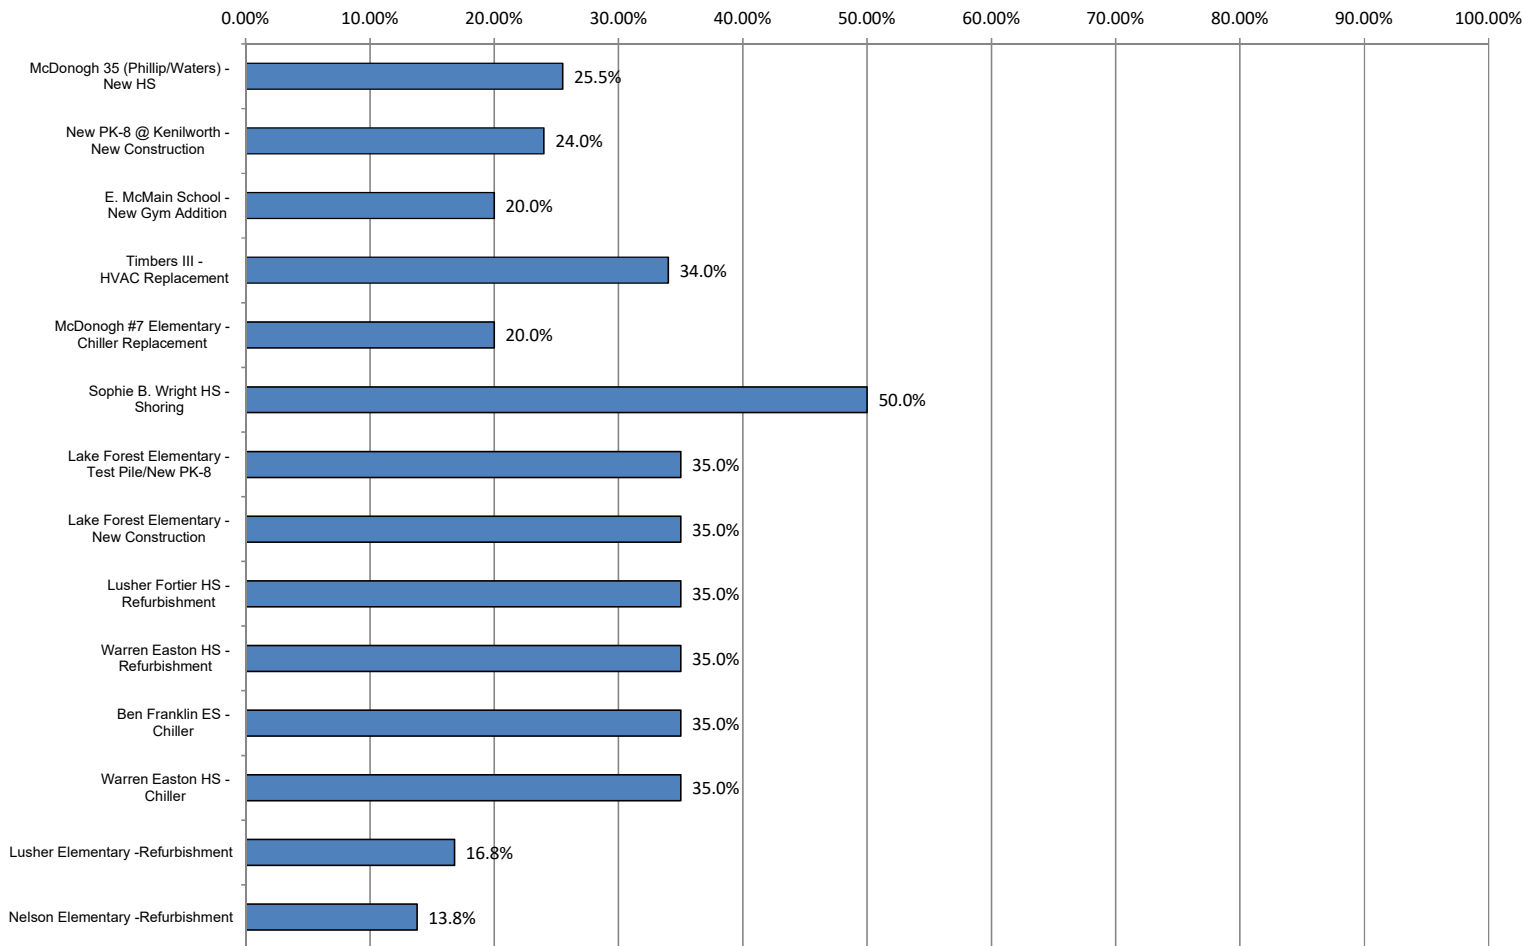

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Construction Masters

Construction Phase

- Contractor mobilized
- Demolition has started

Contractual Substantial Completion – August 2018

Forecasted Substantial Completion – August 2018



New Karr High School CMAR ^(RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - TBD

Design Phase

- GMP was sign by Owner

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



New Orleans Charter Science and Mathematics High School ^(OPSB)

2011 Bienville Street, New Orleans, LA 70112 District D Ward 4

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – VergesRome Architects

Contractor - TBD

Design Phase

- 90% Construction documents are being developed

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



John McDonogh High School Renovation CMAR ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- Installation of interior finishes continues
- Connections to exterior mechanical units is ongoing
- Exterior repairs are nearing completion
- Gymnasium roof decking is ongoing

Contractual Substantial Completion – October 2018

Forecasted Substantial Completion – October 2018



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairone Martinez JV

Contractor - Construction Masters Inc

Construction Phase

- Floor replacement continues on second floor
- MEP system installation ongoing
- Exterior plaster repair and painting continues
- New fence installation is ongoing

Contractual Substantial Completion – July 2018

Forecasted Substantial Completion – July 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates


Contractor – Core Construction

Construction Phase

- Erection of steel continues in Area E
- Roofing work is ongoing at the kitchen and performance wing
- CMU wall construction at the gymnasium continues
- Spray on fire proofing ongoing

Contractual Substantial Completion – January 2019

Forecasted Substantial Completion – January 2019

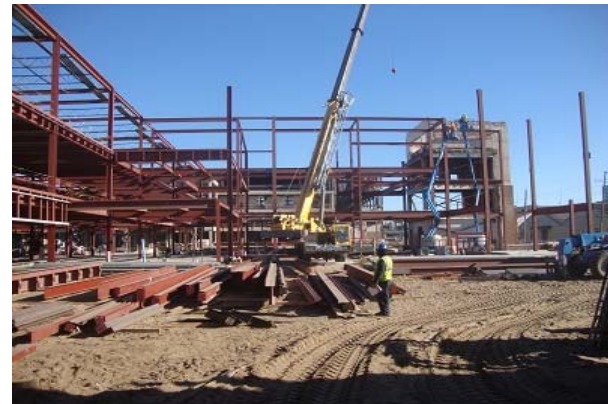

REFURBISHMENTS

Harney Elementary School Downspout and Gutter Repairs ^(RSD)

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of downspouts and gutters

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - TBD

Design Phase

- A&E has started separating the scope of work into two separate projects



Lafayette Elementary School Refurbishment Phase 2 ^(RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to floor replacement

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- 1st Advertisement - January 24th
- 2nd Advertisement - January 31st
- 3rd Advertisement - February 7th
- Pre-Bid Conference - February 8th
- Bid Opening - March 7th



Laurel Elementary School Refurbishment ^(RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Contractor is working on punch list
- Parking lot work is ongoing
- Weather is holding up concrete work

Contractual Substantial Completion – November 2017

Forecasted Substantial Completion – February 2018



Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Blanchard Mechanical Contractors

Construction Phase

- Window installation has started on 3rd floor
- Duct work rough-in continues
- Electrical rough in continues on all floors
- Exterior cleaning and tuck point continues

Contractual Substantial Completion – June 2018

Forecasted Substantial Completion – June 2018



McDonogh #28 School Flooring Refurbishment Phase 2 ^(RSD)

2733 Esplanade Boulevard, New Orleans, LA 70114 District A Ward 7

Scope of work: Refurbishment of existing elementary school flooring

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement - January 3rd
- 2nd Advertisement - January 10th
- 3rd Advertisement - January 17th
- Pre-Bid Conference - January 18th
- Bid Opening - February 7th



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – HMS Architects

Contractor - TBD

Design Phase

- Owner is reviewing 90% Construction Documents



Eleanor McMain School Envelope Repairs ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Exterior stucco and window repairs

Funding Source – General Fund & Harrah's

Architect – Concordia, LLC

Contractor – TBD

Design Phase

- A&E is working on Schematic Design drawings



Harriet R. Tubman Elementary School Cottage Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing cottage to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Framing repairs continue
- Interior hazardous material removal continues
- Repairs to roof structure is ongoing

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Schaumburg Elementary School Roof Repairs ^(RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

Scope of work: Replacement of roof

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - TBD

Procurement Phase

- Bids are under advisement



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

6501 Berkley Drive, New Orleans, LA 70131 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - Industrial and Mechanical Contractors, Inc

Construction Phase

- Village - Control work ongoing
- Village - Ductwork installation continues
- Reed - Gate work is ongoing
- Reed - Windows to be reordered due to wrong size
- Rosenwald - Contractor is nearing completion

Contractual Substantial Completion – December 2017

Forecasted Substantial Completion – January 2018



DEMOLITIONS

Demolition of Modular Buildings at Abramson 3 ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – Ashley Savarino Unlimited Construction

Construction Phase

- Excavation of limestone continues
- Delivery of fill material has started

Contractual Substantial Completion – February 2018

Forecasted Substantial Completion – February 2018



Demolition of Modular Buildings at Coghill ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – TBD

Procurement Phase

- Contractor sending final contract documents for Owner review



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. D. Crossman School Kitchen Refurbishment ^(RSD)	01/15/2017
6	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
7	Agnes Bauduit Elementary School Refurbishment ^(RSD)	10/31/2017
8	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
9	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
10	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
11	Alfred Lawless Senior ^(RSD)	12/18/2015
12	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
13	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
14	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
15	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
16	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
17	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
18	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
19	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
20	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
21	Augustine Elementary School Roof ^(RSD)	04/13/2012
22	Avery-Alexander Elementary School ^(RSD)	06/19/2017
23	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
24	Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)	10/30/2017
25	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
26	Bell JH Shoring ^(RSD)	06/28/2011
27	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
28	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
29	Bienville Elementary School Demolition ^(RSD)	05/04/2009
30	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
31	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
32	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
33	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
34	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
35	Charles J. Colton Elementary School ^(RSD)	05/23/2013
36	Charles R. Drew Elementary School ^(RSD)	04/17/2015
37	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
38	Cohen High School Health Clinic ^(RSD)	12/24/2008
39	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
40	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
41	Demolition of Modular Buildings at Abramson and Carver ^(RSD)	01/18/2017
42	Demolition of Modular Buildings at Livingston ^(RSD)	01/18/2017
43	Douglass High School Under Floor Utilities ^(RSD)	

44	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
45	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
46	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
47	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
48	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
49	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011
50	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
51	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
52	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
53	Edna Karr High School - Assessment ^(OPSB)	
54	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
55	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
56	New Edward Hynes School ^(OPSB)	02/06/2012
57	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
58	Edward Livingston High School ^(RSD)	01/05/2015
59	Eleanor L. McMains School Replacement of Existing Chillers ^(OPSB)	08/30/2011
60	Eleanor L. McMains School Clinic ^(OPSB)	07/24/2013
61	Eleanor L. McMains School Maintenance Upgrades ^(OPSB)	12/12/2016
62	Eleanor L. McMains School Roof Replacement ^(OPSB)	05/13/2016
63	Ernest "Dutch" Morial Elementary ^(RSD)	03/17/2017
64	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
65	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
66	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
67	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
68	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
69	Francis W. Gregory Demolition ^(RSD)	12/21/2011
70	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
71	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
72	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
73	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
74	Gaudet Elementary School Refurbishment ^(RSD)	12/20/2016
75	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
76	George Mondy Elementary School Mothball ^(RSD)	
77	George Washington Carver School ^(RSD)	03/07/2016
78	George Washington Carver High School Demolition ^(RSD)	08/24/2011
79	Greater St. Stephens School ^(OPSB)	03/18/2013
80	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
81	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
82	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
83	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
84	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
85	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
86	Holy Cross Modular Relocation ^(RSD)	12/14/2010
87	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
88	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
89	James Derham Demolition ^(RSD)	02/23/2012

90	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
91	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
92	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
93	JoEllen Smith Medical Center Demolition ^(OPSB)	
94	John Dibert Elementary School Roof ^(RSD)	08/20/2010
95	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
96	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
97	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
98	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
99	John F. Kennedy High School Demolition ^(RSD)	01/12/2012
100	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
101	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
102	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
103	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
104	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
105	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
106	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
107	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
108	Lake Area Landry Demolition ^(RSD)	05/01/2008
109	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
110	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
111	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
112	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
113	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
114	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
115	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
116	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
117	Live Oak Elementary School Refurbishment ^(RSD)	01/06/2017
118	Live Oak Elementary School Roof ^(RSD)	08/04/2011
119	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
120	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
121	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
122	Lusher Elementary School Refurbishment ^(OPSB)	10/31/2016
123	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
124	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
125	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
126	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
127	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
128	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
129	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
130	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
131	Mary M. Bethune Elementary School Refurbishment ^(OPSB)	10/26/2017
132	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
133	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
134	McDonogh #7 High School Repairs ^(OPSB)	
135	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012

136	McDonogh #28 School Refurbishment ^(RSD)	03/15/2016
137	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
138	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
139	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
140	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
141	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
142	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
143	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
144	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
145	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
146	Modular Campuses Close Outs ^(RSD)	
147	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013
148	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010
149	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
150	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
151	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
152	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
153	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
154	New Carter G. Woodson School ^(RSD)	09/14/2012
155	New Fannie C. Williams School ^(RSD)	08/24/2012
156	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
157	New L.B. Landry High School ^(RSD)	06/30/2010
158	New Lake Area High School ^(RSD)	12/28/2009
159	New Lawrence D. Crocker School ^(RSD)	04/29/2013
160	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
161	New Parkview School ^(RSD)	10/12/2012
162	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
163	New William Frantz Elementary School ^(RSD)	
164	New Orleans High School Signature Center Study ^(RSD)	
165	Oretha C. Haley Demo ^(RSD)	05/07/2012
166	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
167	Parkview Elementary School Demolition ^(RSD)	08/06/2009
168	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
169	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
170	Paul B. Habans Elementary School ^(RSD)	06/30/2016
171	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
172	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
173	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
174	Ray Abrams Elementary School ^(RSD)	03/17/2017
175	Rosenwald Elementary School Refurbishment ^(RSD)	04/07/2016
176	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
177	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
178	Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD)	02/15/2016
179	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
180	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010

181	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
182	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
183	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
184	Schaumburg Chillers ^(RSD)	11/14/2008
185	Schwarz Alternative Repairs ^(RSD)	07/14/2009
186	Schwarz Alternative Modulares Demolition ^(RSD)	04/02/2015
187	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
188	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
189	Sherwood Forest Elementary School ^(RSD)	06/30/2016
190	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
191	Sophie B. Wright School Renovation ^(RSD)	06/08/2016
192	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
193	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
194	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
195	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015
196	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
197	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
198	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
199	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
200	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
201	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
202	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
203	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
204	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
205	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
206	Timbers HVAC ^(OPSB)	09/11/2013
207	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
208	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
209	Village de L'est Elementary School Refurbishment ^(RSD)	10/12/2016
210	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
211	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
212	Valena C. Jones Elementary School ^(RSD)	01/10/2013
213	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
214	Warren Easton High School Renovation ^(OPSB)	12/15/2015
215	Warren Easton School Courtyard Waterproofing ^(OPSB)	11/24/2017
216	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
217	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
218	New William J. Guste Elementary School ^(RSD)	10/06/2008
219	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
220	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
221	William Frantz Elementary School Roof ^(RSD)	08/12/2010
