


Superintendent's Report November, 2016



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Mr. Patrick Dobard
Recovery School District

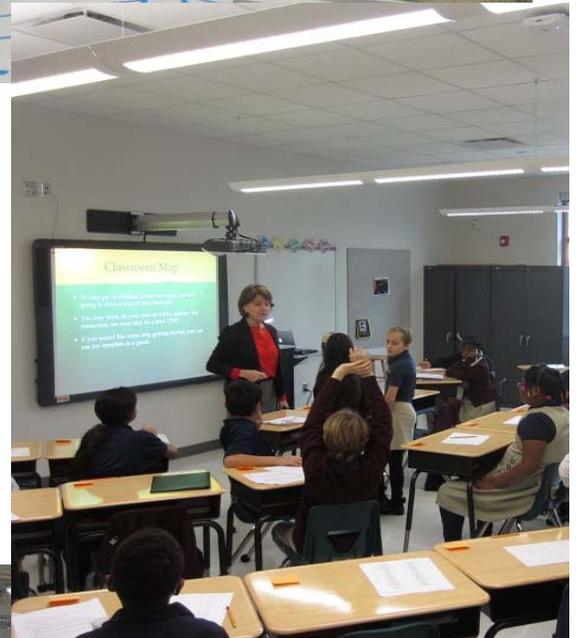

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

TABLE OF CONTENTS	1
FINANCIAL OVERVIEW	3
COMMUNITY MEETINGS	4
BID OPENINGS	5
DBE OVERVIEW MONTHLY SUMMARY	6
NEW & MAJOR RENOVATION	11
Ray Abrams Elementary School ^(RSD)	11
Avery Alexander Elementary School ^(RSD)	11
Benjamin Franklin Elementary School Renovation ^(OPSB)	11
JoEllen Smith Medical Center Demolition ^(OPSB)	12
New Karr High School, CMAR ^(RSD)	12
John McDonogh High School Renovation CMAR ^(RSD)	12
Ernest "Dutch" Morial Elementary School ^(RSD)	13
Harriet R. Tubman Elementary School Renovation ^(RSD)	13
Booker T. Washington School CMAR ^(RSD)	13
Sophie B. Wright School Cornice Replacement ^(RSD)	14
REFURBISHMENTS	15
Benjamin Banneker Elementary Kitchen School Refurbishment ^(RSD)	15
Agnes L. Bauduit Elementary School Refurbishment ^(RSD)	15
A. D. Crossman School Kitchen Refurbishment ^(RSD)	15
William J. Fischer Elementary Refurbishment ^(RSD)	16
Gaudet Elementary School Refurbishment ^(RSD)	16
Samuel J. Green Elementary School Refurbishment ^(RSD)	16
Andrew Jackson School Refurbishment ^(RSD)	17
Lafayette Elementary School Refurbishment ^(RSD)	17
Laurel Elementary School Refurbishment ^(RSD)	17
Live Oak Elementary School Refurbishment ^(RSD)	18
Lusher Elementary School Refurbishment ^(OPSB)	18
Thurgood Marshall Elementary School Refurbishment ^(RSD)	18
McDonogh #32 School Refurbishment ^(RSD)	19
Village de l'Est Elementary School Refurbishment ^(RSD)	19
Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing ^(RSD)	19

OTHER PROJECTS	20
Eleanor L. McMain School Maintenance Upgrades ^(OPSB)	20
DEMOLITIONS	21
Demolition of Modulares at Abramson and Carver ^(RSD)	21
Demolition of Modulares at Livingston ^(RSD)	21
COMPLETED PROJECTS	22

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$561 million in open contracts for the capital program after issuing \$8 million in new contracts, change orders and amendments in November. In addition, the total change orders to date, \$8 million, account for one percent (1.51%) of the total open construction contracts. RSD anticipates issuing approximately \$620 thousand in construction contracts/change orders, and \$23 million in professional service contracts/amendments in December.



The OPSB has \$231 million in open contracts for the capital program after issuing -\$26 thousand in new contracts, change orders and amendments in November. In addition, the total change orders to date, \$8.4 million, account for approximately four percent (4.31%) of the total open construction contracts. OPSB anticipates issuing approximately -\$27 thousand in construction contracts/change orders and -\$225 thousand in professional service contracts and amendments in December.

Community Meetings



Future Community Meetings

November 2, 2016

Alfred Lawless High School Ribbon Cutting
5301 North Rocheblave Street New Orleans, LA 70117

December 13, 2016

Ground Breaking for New Booker T Washington High School
1201 South Roman Street New Orleans, LA 70125

December 14, 2016

Robert Russa Moton School Ribbon Cutting
8550 Curran Boulevard New Orleans, LA 70127

Bid Openings

Projects which are scheduled to bid in the next 60 days

January 25, 2017

Bethune School Refurbishment Bid Opening

February 1, 2017

Kitchen Improvements at Benjamin Banneker / Wheatley Grease Trap Bid Opening

March 1, 2017

HVAC Equipment Repairs at Village de l'Est, Sarah T. Reed, and Rosenwald Bid Opening

Disadvantaged Business Enterprises (DBE) Monthly Summary

Recovery School District



New & Renovations:

DBE Contractors secured subcontracts on 24 projects as of November 30, 2016. The DBE subcontracts value is \$89,745,976 of the \$394,544,776 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 48 projects as of November 30, 2016. The DBE subcontracts value is \$19,547,610 of the \$65,106,535 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of November 30, 2016. The DBE subcontracts value is \$34,525,219 of the \$109,137,557 total of awarded contracts.



Total Amount of Contracts: \$ 568,788,868

Orleans Parish School Board

New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of November 30, 2016. The DBE subcontracts value is \$54,086,557 of the \$199,371,360 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of November 30, 2016. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$200,274,359

* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

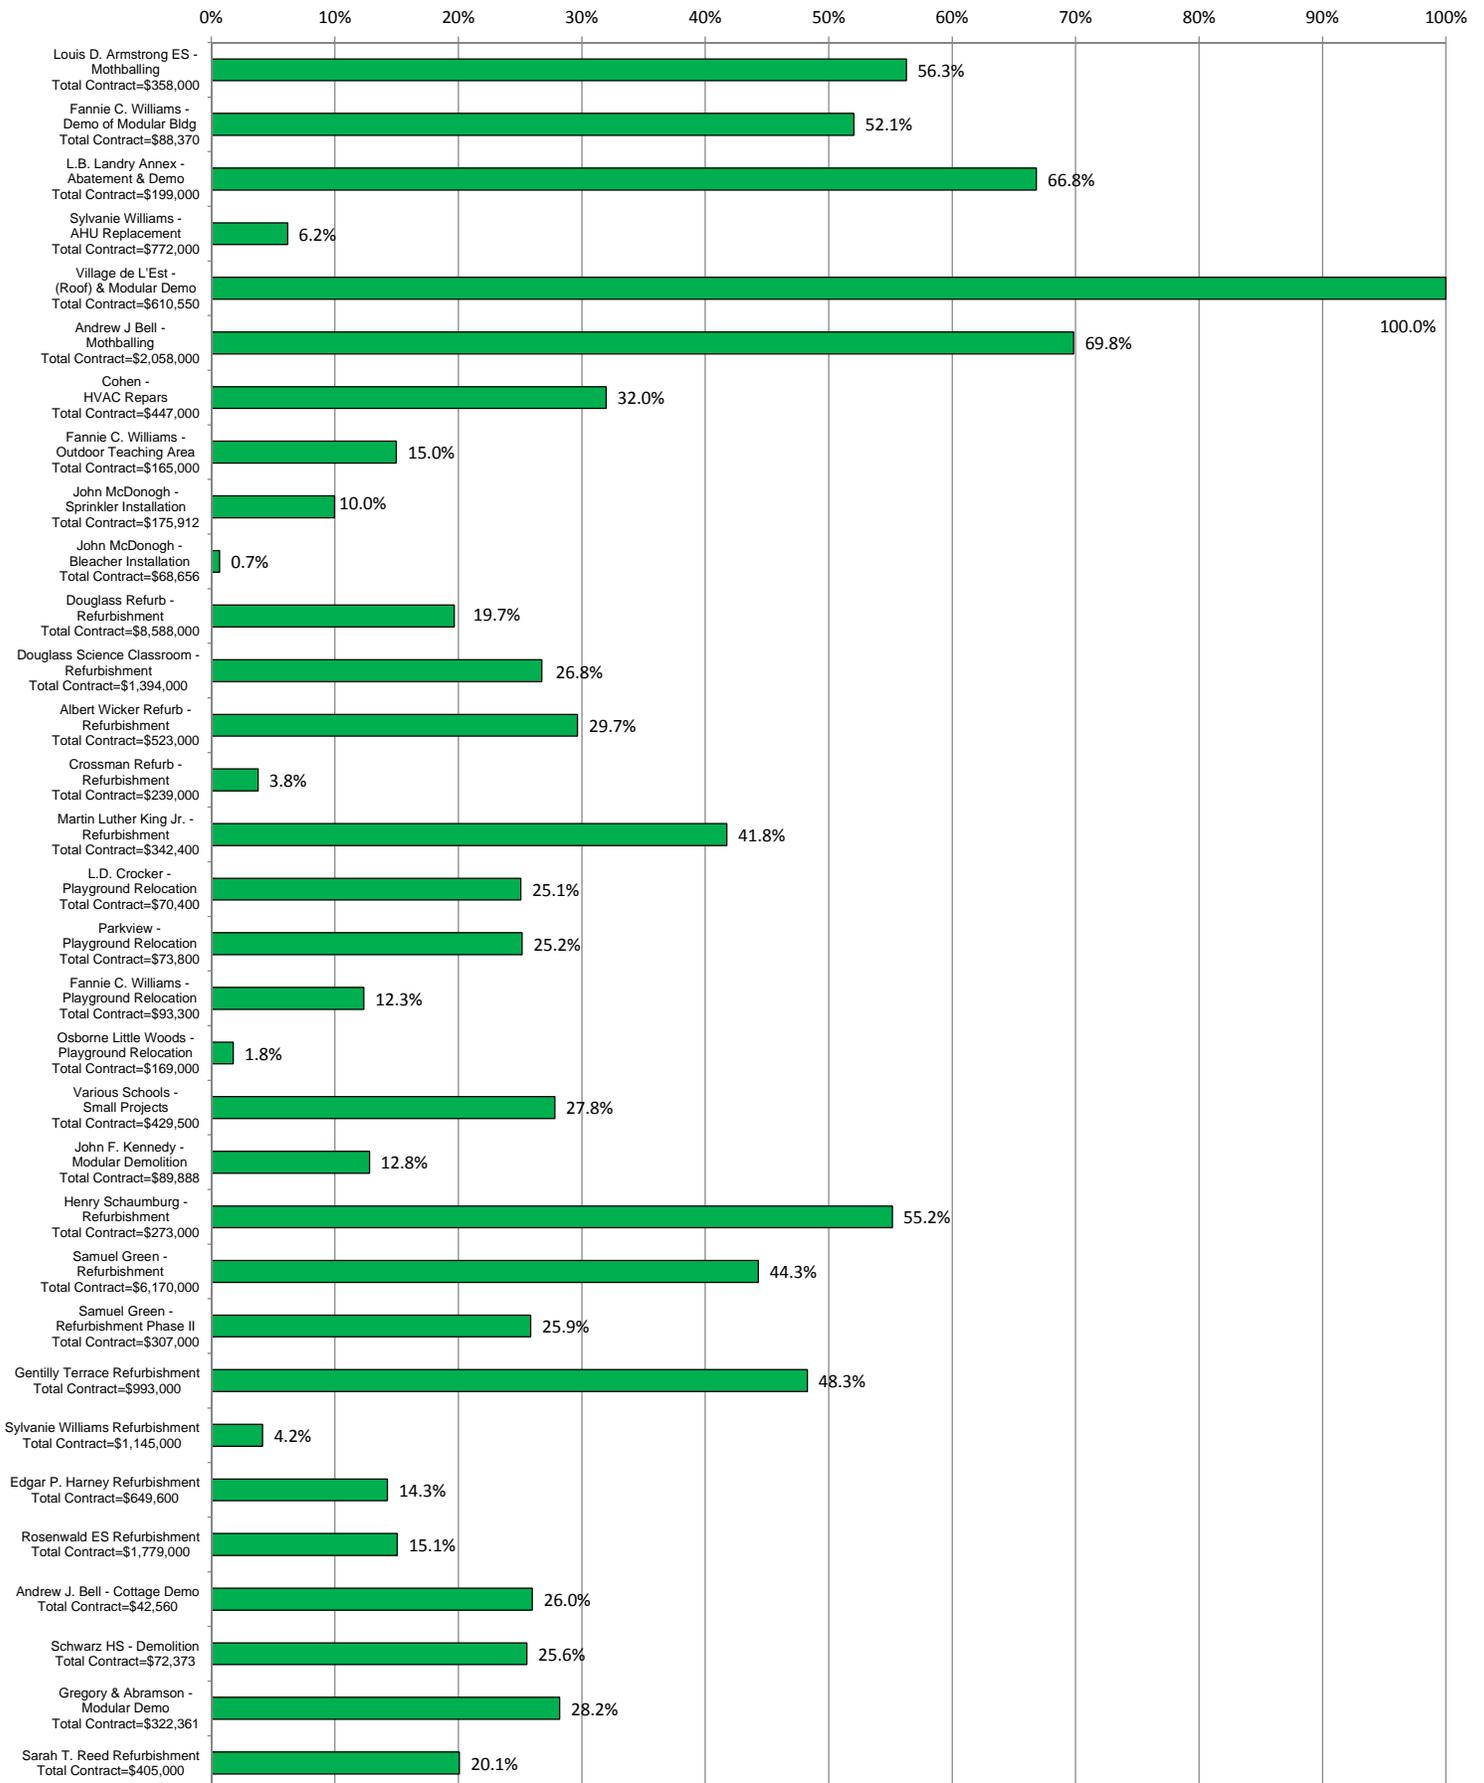


Notes: Data Based On Pre-Construction and/or 7 monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Status Date: 30 November 2016

Current RSD Program DBE Participation


(Continued)

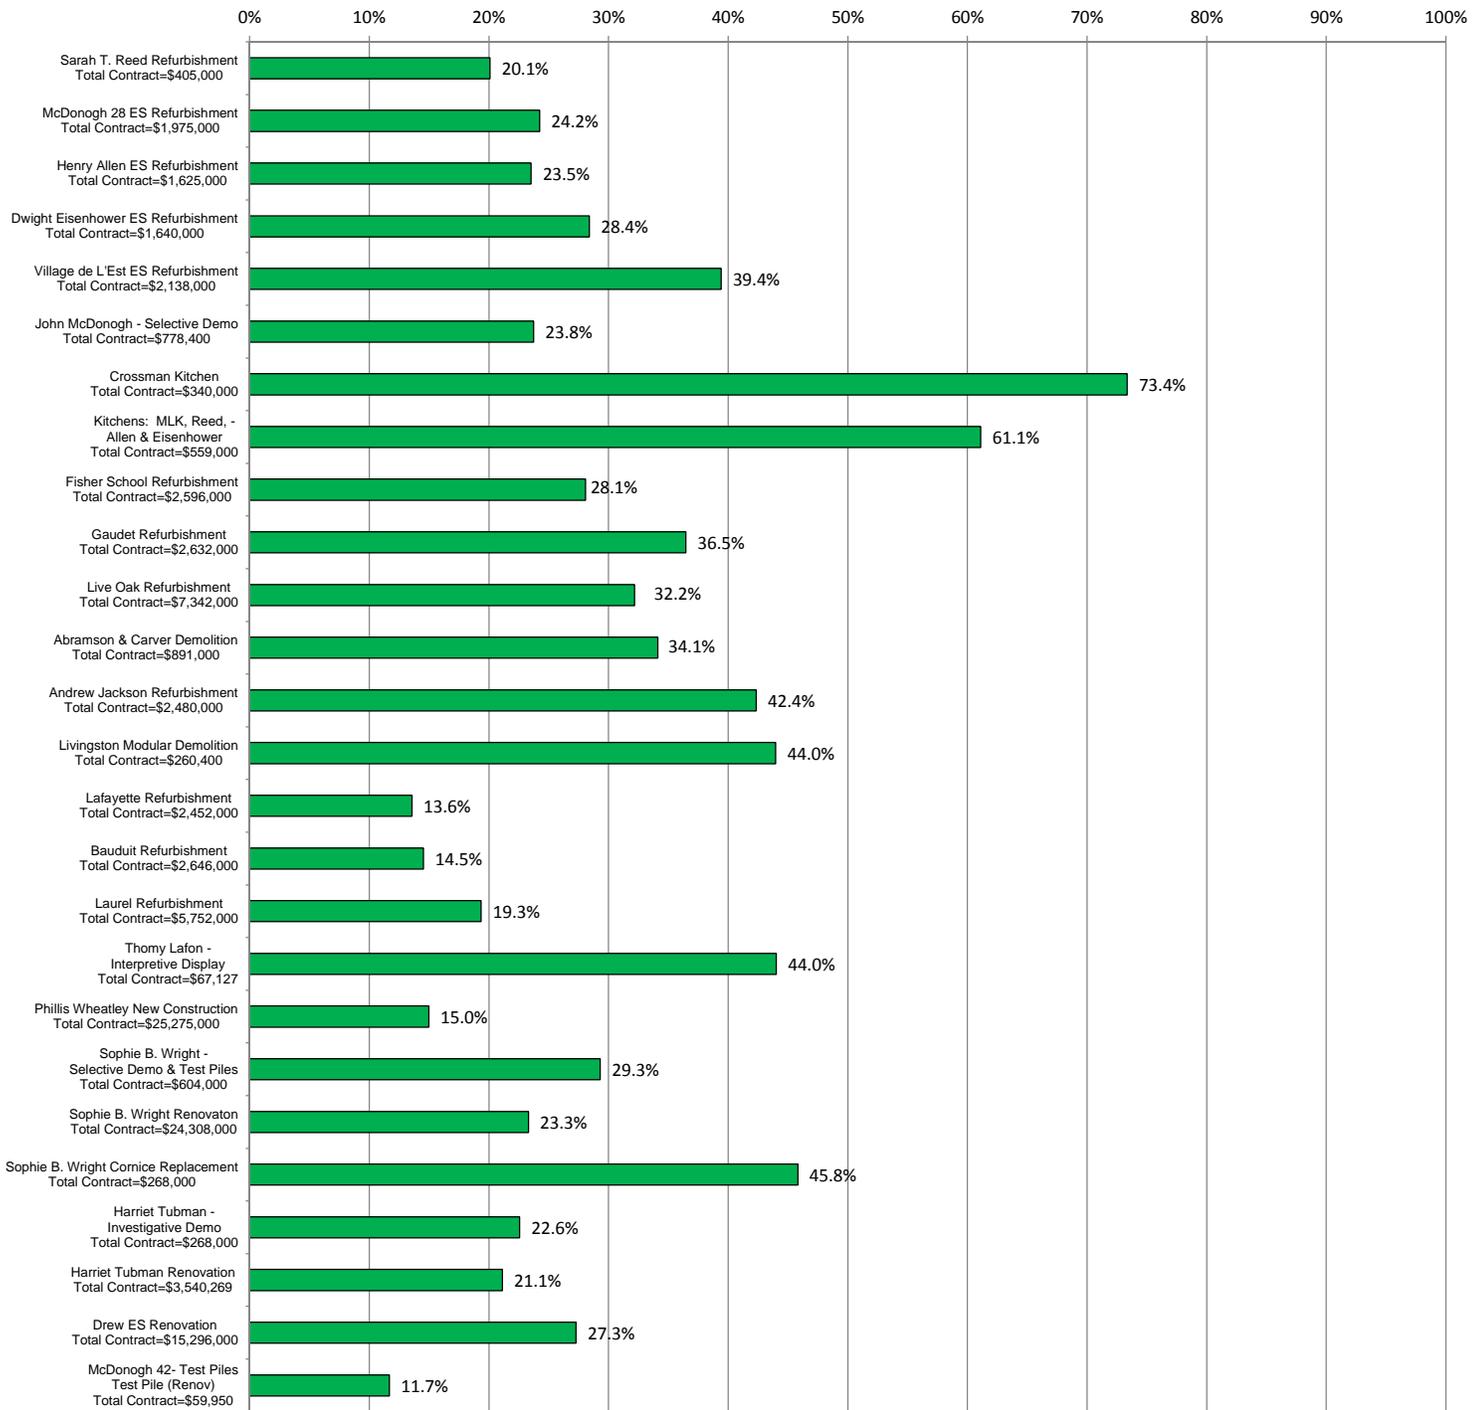

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

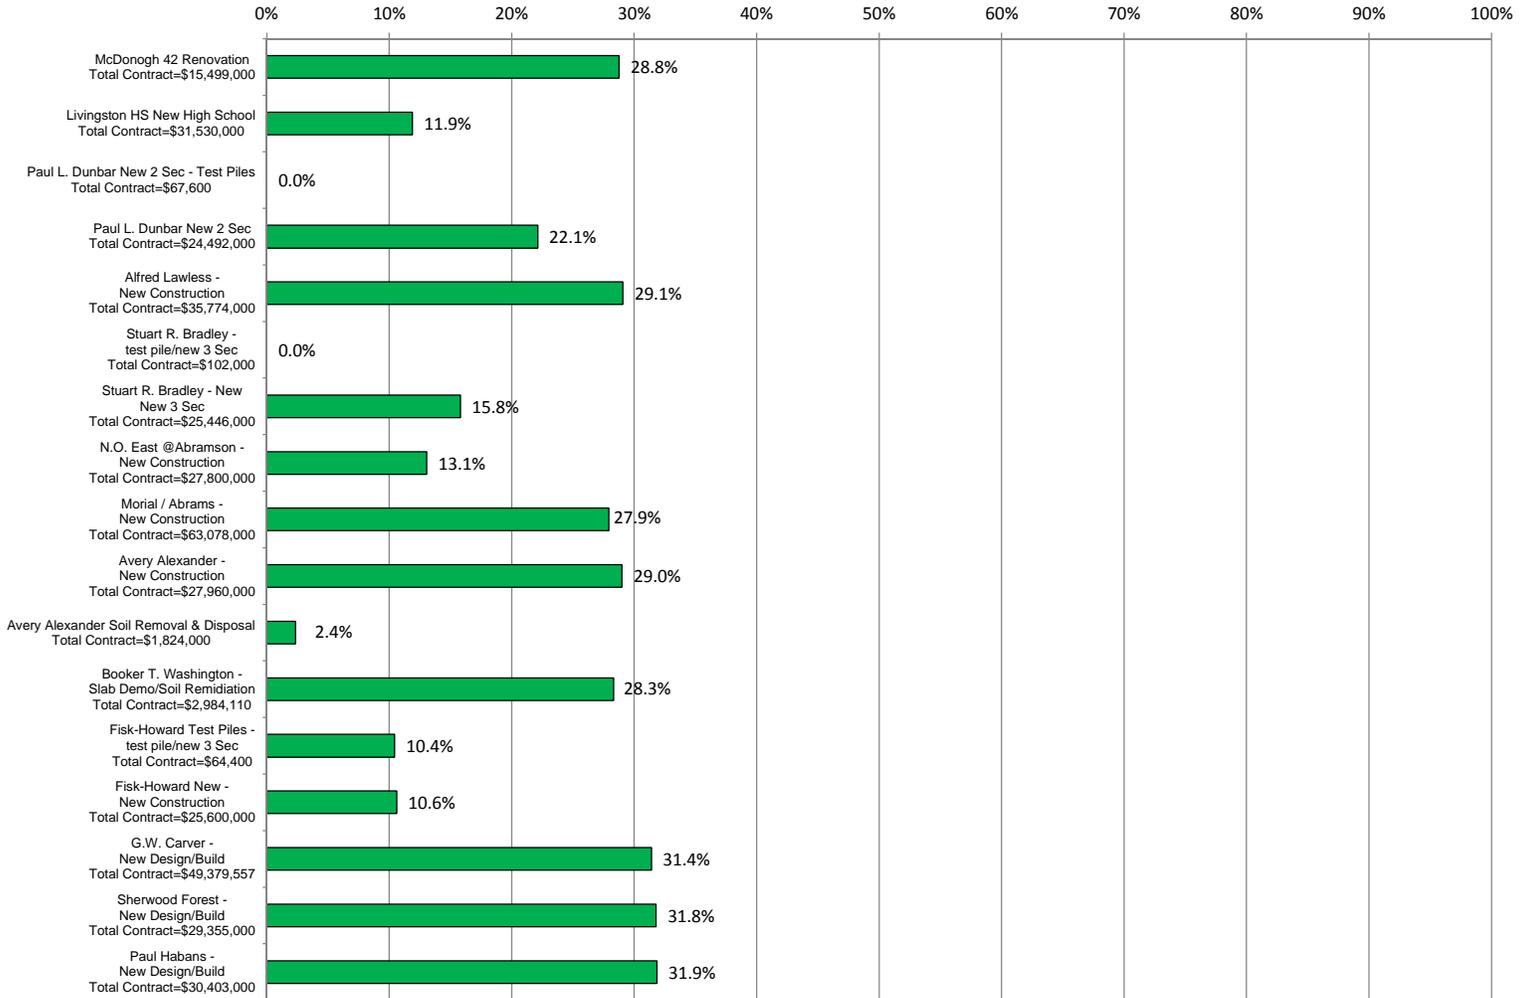

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

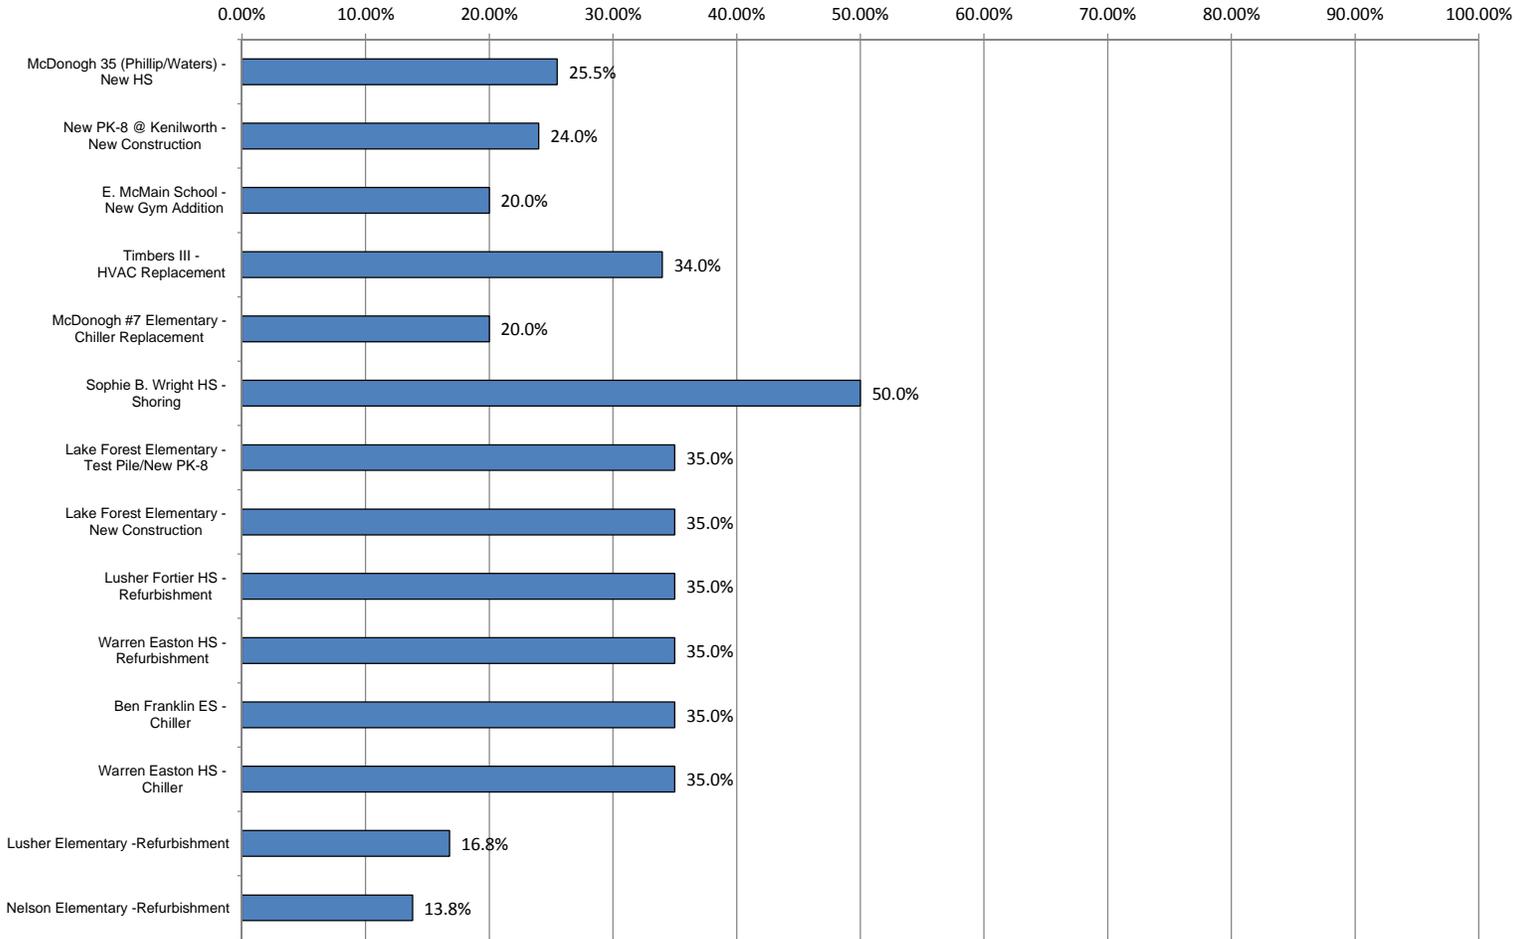

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Ray Abrams Elementary School ^(RSD)

6519 Virgilian Street, New Orleans, LA 70126 District D Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Ceiling tile installation has started
- HVAC start up is underway
- Installation of site fencing continues
- Quarry tile installation continues
- Cast stone stair tread installation is ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – March 2017



Avery Alexander Elementary School ^(RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Construction Phase

- Interior finishes are underway
- Kitchen hood is being installed
- Site grading continues
- Parking lots and drive are being poured
- Lighting installation is ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Design Phase - CD

- A&E continues work on construction documents for the repairs of the exterior and the windows



JoEllen Smith Medical Center Demolition (OPSB)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Demolition of existing medical center

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor – Core Construction

Demolition Phase

- Foundation removal continues
- Pile survey due in January 2017

Contractual Substantial Completion – January 2017

Forecasted Substantial Completion – January 2017



New Karr High School CMAR (RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - TBD

Procurement Phase

- 50% Construction Documents due December 20th

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



John McDonogh High School Renovation CMAR (RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Design Phase

- Work on Construction Documents continues
- Archaeological exploration work continues
- With remediation complete on the gymnasium, demolition has commenced

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



Ernest "Dutch" Morial Elementary School ^(RSD)

7701 Grant Street, New Orleans, LA 70126 District E Ward 9

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – McDonnell Group, LLC

Construction Phase

- Installation of interior finishes continue
- Preparing HVAC installation for start up
- Plumbing fixture installation continues
- Roofing cap sheet installation continues
- Site fencing is ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – February 2017



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters Inc

Construction Phase

- Electrical rough-in is underway
- Steel Joist and deck are being installed on the cafetorium
- Exterior sidewalk work continues
- Installation of refurbished windows is ongoing
- Wood floor replacement has started

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: The auditorium and entry will be renovated and the remainder of the facility will be demolished and constructed anew

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Ground Breaking Ceremony December 13th
- Pile driving is 75% complete
- Excavation and forming of pile caps has started

Contractual Substantial Completion – 2018

Forecasted Substantial Completion – 2018



Sophie B. Wright High School Cornice Replacement ^(RSD)

1426 Napoleon Avenue, New Orleans, LA 70115 District B Ward 13

Scope of work: Replace existing cornice

Funding Source – FEMA

Architect – Waggoner & Ball Architects, APC

Contractor – Baitco Construction

Construction Phase

- Installation of replacement cornice is 90% complete
- Priming and painting to begin over the holiday break

Contractual Substantial Completion – December 2016

Forecasted Substantial Completion – December 2016



REFURBISHMENTS

Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

2300 Dumaine Street, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - TBD

Procurement Phase

- 1st Advertisement - December 28th
- 2nd Advertisement - January 4th
- 3rd Advertisement - January 11th
- Pre-Bid Conference - January 12th
- Bid Opening - February 1st



Agnes L. Bauduit Elementary School Refurbishment ^(RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor – One Construction

Construction Phase

- Window installation continues
- Installation of ducts is ongoing
- Installation of ceiling tiles has started

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – May 2017



A. D. Crossman School Kitchen Refurbishment ^(RSD)

4407 South Carrollton Avenue, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - CDW Services

Construction Phase

- Contractor to perform corrective work on grease trap installation
- Anticipated Substantial December 2016

Contractual Substantial Completion – July 2016

Forecasted Substantial Completion – December 2016



William J. Fischer Elementary School Refurbishment ^(RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Perez

Construction Phase

- Installation of window frames continue on second floor
- Exterior canopy work continues
- Roof submittals are being reviewed
- Electrical work in the classrooms is ongoing

Contractual Substantial Completion – February 2017

Forecasted Substantial Completion – February 2017



Gaudet Elementary School Refurbishment ^(RSD)

12000 Hayne Boulevard, New Orleans, LA 70128 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - One Construction

Construction Phase

- Anticipated Substantial Completion is December 15th
- Contractor is working fire alarm system
- Security alarm work to be preformed

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – December 2016



Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD)

2319 Valence Street, New Orleans, LA 70115 District B Ward 13

Scope of work: Refurbishment of existing elementary school

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Crescent Commercial

Construction Phase

- Installation of pipe insulation is underway
- Installation of drinking fountains has started

Contractual Substantial Completion – February 2017

Forecasted Substantial Completion – February 2017



Andrew Jackson School Refurbishment (RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Construction Phase

- School will move into third floor classrooms over Christmas Break
- Exterior stucco repairs continue
- Roof work continues on parapet and curbs
- Back flow preventer being installed

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Tuna Construction

Construction Phase

- Window sashes are being installed in classrooms
- Work continues in stairwell #3
- Installation of masonry at the dumpster pad is complete
- Sidewalk replacement has started

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – June 2017



Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Roof work to be performed over Christmas Break
- Window repairs are underway on 1st and 3rd floors
- Kitchen abatement is scheduled during Christmas Break

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017



Live Oak Elementary School Refurbishment ^(RSD)

3128 Constance Street, New Orleans, LA 70115 District B Ward 11

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- Finish coat being applied to the wood floors
- Replacement of balancing valves is ongoing
- Contractor to repair asphalt at utility tie-in
- Work continues after school hours and on weekends

Contractual Substantial Completion – July 2017

Forecasted Substantial Completion – January 2017



Lusher Elementary School Refurbishment ^(OPSB)

7315 Willow Street, New Orleans, LA 70118 District A Ward 14

Scope of work: Renovation and repairs to the existing bridge, roof, windows, exterior doors, and restroom accessibility

Funding Source – FEMA

Architect – Meyer Engineers, LTD.

Contractor - Dynamic

Construction Phase

- Substantial Complete October 31st

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – October 2016



Thurgood Marshall Elementary School Refurbishment ^(RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Design Phase - CD

- A&E is finalizing Bid Documents
- Anticipated Bid Opening – March 15th

Procurement Phase

- Anticipated 1st Advertisement – February 2017
- Anticipated Bid Opening – March 2017



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Byron J. Stewart & Associates, APC Architects & Planners

Contractor - TBD

Design Phase – CD

- A&E to revise drawings

Procurement Phase

- Anticipated 1st Advertisement – February 2017
- Anticipated Bid Opening – March 2017



Village de l'Est Elementary School Refurbishment ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor - Dynamic Constructors LLC

Construction Phase

- Substantial Completion is anticipated in December

Contractual Substantial Completion – April 2016

Forecasted Substantial Completion – December 2016



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing ^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - TBD

Procurement Phase

- 1st Advertisement - January 25th
- 2nd Advertisement - February 1st
- 3rd Advertisement - February 8th
- Pre-Bid Conference - February 9th
- Bid Opening - March 1st



OTHER PROJECTS

Eleanor L. McMain School Maintenance Upgrades ^(OPSB)

5721 S. Claiborne Avenue, New Orleans, LA 70125 District A Ward 14

Scope of work: Various maintenance work.

Funding Source – General Fund & Harrah's

Architect – Duplantis Design Group

Contractor – Tuna Construction

Construction Phase

- Punch list work is almost complete

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – December 2016



DEMOLITIONS

Demolition of Modular Buildings at Abramson and Carver ^(RSD)

5552 Read Boulevard and 3059 Higgins Boulevard, New Orleans, LA

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - Construction Masters, Inc.

Construction Phase

- Carver - Punch list walk December 8th
- Carver - Contractor to install water main shut off valve
- Abramson - Contractor to adjust ornamental fence

Contractual Substantial Completion – October 2016

Forecasted Substantial Completion – November 2016



Demolition of Modular Buildings at Livingston ^(RSD)

7301 Dwyer Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – GAEA Consultants, LLC

Contractor – Concrete Busters of Louisiana

Construction Phase

- Removal of limestone continues
- Concrete sidewalks and canopy to be removed

Contractual Substantial Completion – September 2016

Forecasted Substantial Completion – October 2016



Comprehensive List - Completed Projects

1	Abrams Morial Abramson Coghill Demolition ^(RSD)	11/17/2008
2	A. D. Cross Elementary School Energy Conservation ^(RSD)	
3	A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD)	06/12/2012
4	A. D. Crossman Elementary School Refurbishment ^(RSD)	06/04/2014
5	A. P. Tureaud Elementary School Roof Repairs ^(RSD)	06/13/2013
6	Agnes Bauduit Elementary School Boiler ^(RSD)	12/07/2009
7	Albert Wicker Elementary School Refurbishment ^(RSD)	03/27/2014
8	Albert Wicker Elementary School Roof Repairs ^(RSD)	06/13/2013
9	Alfred Lawless Senior ^(RSD)	12/18/2015
10	Alfred Lawless Senior High Security Fencing ^(RSD)	06/15/2011
11	Alice M. Harte Elementary School ^(OPSB)	11/19/2014
12	Alice M. Harte Elementary School Demolition ^(OPSB)	12/14/2011
13	Andrew J. Bell Junior High School Roof Replacement ^(RSD)	02/08/2014
14	Andrew J. Bell Junior High School Mothball ^(RSD)	06/28/2011
15	Andrew Jackson Elementary School Roof Repairs ^(RSD)	07/27/2012
16	Andrew Jackson Elementary School Solar Panels ^(RSD)	01/14/2013
17	Andrew H. Wilson Elementary School Cottage ^(RSD)	10/11/2010
18	Arthur Ashe Elementary School Kitchen Renovation ^(OPSB)	
19	Augustine Elementary School Roof ^(RSD)	04/13/2012
20	Avery-Alexander Elementary School Demolition ^(RSD)	06/15/2012
21	Barbara C. Jordan Elementary School Demolition ^(RSD)	05/30/2011
22	Bell JH Shoring ^(RSD)	06/28/2011
23	Benjamin Banneker Elementary School Energy Conservation ^(RSD)	
24	Benjamin Franklin Senior High School ^(OPSB)	08/23/2013
25	Bienville Elementary School Demolition ^(RSD)	05/04/2009
26	Booker T. Washington High School Environmental Remediation ^(RSD)	12/13/2015
27	Booker T. Washington High School Partial Demolition ^(RSD)	04/07/2013
28	Carter G. Woodson Middle School Demolition ^(RSD)	02/09/2010
29	Central Services Warehouse Demolition ^(OPSB)	01/05/2012
30	Charles J. Colton Elementary Selective Demolition ^(RSD)	07/26/2010
31	Charles J. Colton Elementary School ^(RSD)	05/23/2013
32	Charles R. Drew Elementary School ^(RSD)	04/17/2015
33	Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD)	06/08/2011
34	Cohen High School Health Clinic ^(RSD)	12/24/2008
35	Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD)	
36	Demolition of Modular Buildings at Gregory and Abramson ^(RSD)	06/23/2015
37	Douglass High School Under Floor Utilities ^(RSD)	
38	Dr. Martin Luther King School Roof Repairs ^(RSD)	06/13/2012
39	Dr. Martin Luther King Jr. School Renovation ^(RSD)	12/15/2014
40	Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
41	Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD)	07/27/2012
42	Dwight D. Eisenhower Elementary School Refurbishment ^(RSD)	12/23/2015
43	East Bank Swing Space for Audubon Charter School ^(OPSB)	12/30/2011

44	Edgar P. Harney Elementary School Refurbishment ^(RSD)	
45	Edgar P. Harney Elementary School Roof Repairs ^(RSD)	06/13/2012
46	Edna Karr High School - Gymnasium Repair ^(OPSB)	12/23/2013
47	Edna Karr High School - Assessment ^(OPSB)	
48	Edward Livingston Middle School Demolition ^(RSD)	09/28/2010
49	Edward Henry Phillips Junior High School Demolition ^(OPSB)	11/19/2010
50	New Edward Hynes School ^(OPSB)	02/06/2012
51	Edwards Hardin Lockett Lawless Demolition ^(RSD)	11/03/2008
52	Edward Livingston High School ^(RSD)	01/05/2015
53	Eleanor L. McMMain School Replacement of Existing Chillers ^(OPSB)	08/30/2011
54	Eleanor L. McMMain School Clinic ^(OPSB)	07/24/2013
55	Eleanor L. McMMain School Roof Replacement ^(OPSB)	05/13/2016
56	Ernest N. Morial Elementary Security Fencing ^(RSD)	05/10/2011
57	Fannie C. Williams Elementary School Demolition ^(RSD)	03/10/2009
58	Fisk-Howard Elementary School Demolition ^(RSD)	10/04/2011
59	Florence J. Chester Elementary School Demolition ^(RSD)	06/05/2011
60	Fortier (Lusher) High School Refurbishment ^(OPSB)	02/05/2016
61	Francis W. Gregory Demolition ^(RSD)	12/21/2011
62	Frederick A. Douglass High Refurbishment ^(RSD)	10/28/2014
63	Frederick A. Douglass High School Science Lab ^(RSD)	07/05/2016
64	Frederick A. Douglass High Switchgear ^(RSD)	08/04/2009
65	Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD)	
66	Gentilly Terrace Elementary School Refurbishment ^(RSD)	09/22/2015
67	George Mondy Elementary School Mothball ^(RSD)	
68	George Washington Carver School ^(RSD)	03/07/2016
69	George Washington Carver High School Demolition ^(RSD)	08/24/2011
70	Greater St. Stephens School ^(OPSB)	03/18/2013
71	Harriet R. Tubman Elementary School Selective Demolition ^(RSD)	12/14/2014
72	Henry Allen Elementary School Refurbishment ^(RSD)	03/08/2016
73	Henry Allen Elementary School Kitchen Refurbishment ^(RSD)	02/18/2016
74	Henry Allen Elementary School Roof ^(RSD)	05/24/2010
75	Henry C. Schaumburg School Refurbishment ^(RSD)	06/26/2015
76	Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD)	12/16/2011
77	Holy Cross Modular Relocation ^(RSD)	12/14/2010
78	Israel M. Augustine Middle School Roof Replacement ^(RSD)	04/13/2012
79	Israel M. Augustine Middle School Mothball ^(RSD)	01/18/2013
80	James Derham Demolition ^(RSD)	02/23/2012
81	James W. Johnson Elementary School Roof ^(RSD)	07/31/2010
82	New Jean Batiste de Bienville School ^(RSD)	06/15/2012
83	Jean Gordon Elementary School Demolition ^(RSD)	08/16/2010
84	John Dibert Elementary School Roof ^(RSD)	08/20/2010
85	John W. Hoffman Elementary School Demolition ^(RSD)	05/25/2010
86	John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD)	11/05/2010
87	John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD)	08/05/2011
88	John F. Kennedy Modular Demolition ^(RSD)	09/16/2014
89	John F. Kennedy High School Demolition ^(RSD)	01/12/2012

90	John McDonogh Senior High School Bleachers and Sprinklers ^(RSD)	03/27/2014
91	John McDonogh Senior High School Roof ^(RSD)	05/04/2010
92	John A. Shaw Elementary School Mothball ^(RSD)	12/12/2012
93	Joseph S. Clark Senior High School Roof Repairs ^(RSD)	07/27/2012
94	Joseph A. Craig Elementary Canopies ^(RSD)	06/06/2011
95	Joseph A. Craig Elementary Elevator Installation ^(RSD)	01/20/2012
96	Joseph A. Hardin Elementary Security Fencing ^(RSD)	05/10/2011
97	Lafayette Elementary School Roof and Masonry ^(RSD)	06/22/2012
98	Lake Area Landry Demolition ^(RSD)	05/01/2008
99	Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB)	11/13/2015
100	Langston Hughes Elementary School (Phase I) ^(RSD)	08/11/2009
101	Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD)	11/10/2010
102	Langston Hughes Elementary School - Dumpster Pad ^(RSD)	10/12/2012
103	Lawrence D. Crocker Elementary School Demolition ^(RSD)	04/02/2010
104	L.B. Landry Annex Demolition ^(RSD)	05/02/2013
105	Little Woods Elementary School Demolition ^(RSD)	08/09/2010
106	Little Woods School (Dolores T. Aaron Elementary School) ^(RSD)	08/01/2013
107	Live Oak Elementary School Roof ^(RSD)	08/04/2011
108	Live Oak Elementary School Exterior Door Replacement ^(RSD)	08/26/2011
109	Lorraine Hansberry Elementary School Mothball ^(RSD)	12/27/2012
110	Louis D. Armstrong Elementary School ^(RSD)	02/18/2013
111	Mahalia Jackson Elementary School ^(OPSB)	05/11/2010
112	Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB)	03/06/2012
113	Mahalia Jackson Elementary School Office Renovation ^(OPSB)	04/30/2013
114	Martin Behrman Elementary School Roof ^(RSD)	02/23/2010
115	Martin Luther King Jr. Elementary Canopy System ^(RSD)	11/05/2011
116	Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD)	07/31/2012
117	Martin Luther King Jr. School Kitchen Refurbishment ^(RSD)	02/18/2016
118	Mary Church Terrell Elementary School Demolition ^(RSD)	04/17/2013
119	Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB)	01/24/2011
120	Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB)	01/21/2011
121	McDonogh #7 High School Repairs ^(OPSB)	
122	McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD)	06/11/2012
123	McDonogh #28 School Refurbishment ^(RSD)	03/15/2016
124	McDonogh #28 Elementary School Roof ^(RSD)	11/19/2011
125	McDonogh #32 Roof Replacement ^(RSD)	02/24/2012
126	McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB)	01/17/2014
127	McDonogh #35 School at the Phillip/ Waters Site ^(OPSB)	09/23/2015
128	McDonogh #42 Elementary School Renovation ^(RSD)	05/28/2015
129	McDonogh #42 Elementary School Roof ^(RSD)	12/21/2011
130	McDonogh #42 Elementary School HVAC Replacement ^(RSD)	08/09/2010
131	Mildred C. Osborne Elementary School Demolition ^(RSD)	02/18/2010
132	Mildred C. Osborne Elementary School ^(RSD)	12/03/2012
133	Modular Campuses Close Outs ^(RSD)	
134	Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD)	05/22/2013

135	Modular Structures at Langston Hughes Elementary School ^(RSD)	04/05/2010
136	Morris F.X. Jeff Elementary School Demolition ^(RSD)	
137	Morris F.X. Jeff Elementary School Mothball ^(RSD)	01/15/2013
138	Murray G. Henderson Elementary School Roof ^(RSD)	06/23/2012
139	Nelson Elementary School Refurbishment ^(OPSB)	04/18/2016
140	New Andrew H. Wilson Elementary School ^(RSD)	10/11/2009
141	New Carter G. Woodson School ^(RSD)	09/14/2012
142	New Fannie C. Williams School ^(RSD)	08/24/2012
143	New Joseph A. Craig Elementary School ^(RSD)	12/09/2009
144	New L.B. Landry High School ^(RSD)	06/30/2010
145	New Lake Area High School ^(RSD)	12/28/2009
146	New Lawrence D. Crocker School ^(RSD)	04/29/2013
147	New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB)	01/29/2016
148	New Parkview School ^(RSD)	10/12/2012
149	New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD)	
150	New William Frantz Elementary School ^(RSD)	
151	New Orleans High School Signature Center Study ^(RSD)	
152	Oretha C. Haley Demo ^(RSD)	05/07/2012
153	Oretha C. Haley Elementary School Mothball ^(RSD)	09/17/2012
154	Parkview Elementary School Demolition ^(RSD)	08/06/2009
155	Paul L. Dunbar Elementary School Demolition ^(RSD)	06/16/2010
156	Paul L. Dunbar Elementary School ^(RSD)	06/02/2015
157	Paul B. Habans Elementary School ^(RSD)	06/30/2016
158	Paul B. Habans Elementary School Roof Repairs ^(RSD)	07/27/2012
159	Phillis Wheatley Elementary School Demolition ^(RSD)	09/26/2011
160	Phillis Wheatley Elementary School ^(RSD)	07/10/2014
161	Rosenwald Elementary School Refurbishment ^(RSD)	04/07/2016
162	Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB)	07/14/2011
163	Samuel J. Green Elementary School Refurbishment ^(RSD)	02/15/2016
164	Sarah T. Reed High School Bleachers ^(RSD)	01/11/2012
165	Sarah T. Reed High School Auditorium Wall ^(RSD)	03/29/2010
166	Sarah T. Reed High School Kitchen Refurbishment ^(RSD)	02/18/2016
167	Sarah T. Reed High School Refurbishment ^(RSD)	12/01/2015
168	Seabrook Computer Training Center Demolition ^(OPSB)	06/25/2010
169	Schaumburg Chillers ^(RSD)	11/14/2008
170	Schwarz Alternative Repairs ^(RSD)	07/14/2009
171	Schwarz Alternative Modulars Demolition ^(RSD)	04/02/2015
172	Schwarz Modular Building Demolition ^(RSD)	04/02/2015
173	Sherwood Forest Elementary School Demolition ^(RSD)	10/28/2010
174	Sherwood Forest Elementary School ^(RSD)	06/30/2016
175	Small New Orleans East High School at Abramson ^(RSD)	09/24/2015
176	Sophie B. Wright School Renovation ^(RSD)	06/08/2016
177	Sophie B. Wright School Selective Demolition ^(RSD)	01/31/2014
178	Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB)	07/26/2011
179	Stuart R. Bradley Elementary School Demolition ^(RSD)	01/27/2010
180	Stuart R. Bradley Elementary School ^(RSD)	06/26/2015

181	Sylvanie Williams Elementary School AHU Replacement ^(RSD)	07/30/2013
182	Sylvanie Williams Elementary School Play Yard ^(RSD)	09/23/2010
183	Sylvanie Williams Elementary School Roof Repairs ^(RSD)	07/27/2012
184	Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD)	04/13/2012
185	Sylvanie Williams Elementary School Refurbishment ^(RSD)	02/18/2016
186	Temporary Campus for McDonogh #11 Expropriation ^(OPSB)	
187	Thomas A. Edison Elementary School Demolition ^(RSD)	03/25/2010
188	Thomy Lafon Elementary School Demolition ^(RSD)	11/27/2011
189	Thomy Lafon School Interpretative Display ^(RSD)	10/15/2013
190	Timbers Park Office Building #1 & #2 Demolition ^(OPSB)	09/18/2011
191	Timbers HVAC ^(OPSB)	09/11/2013
192	Timbers III - IT Room Relocation ^(OPSB)	02/11/2015
193	Village de L'est Elementary School Subsidence ^(RSD)	06/18/2012
194	Village de L'est Elementary School Roof and Modular Demolition ^(RSD)	06/16/2013
195	Vorice J. Waters Elementary School Demolition ^(RSD)	01/14/2010
196	Valena C. Jones Elementary School ^(RSD)	01/10/2013
197	Walter L. Cohen High School HVAC ^(RSD)	04/04/2014
198	Warren Easton High School Renovation ^(OPSB)	12/15/2015
199	Warren Easton High School Window Replacement ^(OPSB)	09/07/2012
200	West Bank Swing Space for Alice Harte Elementary School ^(OPSB)	07/11/1931
201	New William J. Guste Elementary School ^(RSD)	10/06/2008
202	William J. Guste Elementary School Science Lab ^(RSD)	08/04/2009
203	William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD)	04/15/2010
204	William Frantz Elementary School Roof ^(RSD)	08/12/2010
