


Superintendent's Report July, 2017



Dr. Henderson Lewis Jr.
Orleans Parish School Board



Mr. John White
Louisiana Department of Education
Ms. Kunjan Narehania
Recovery School District

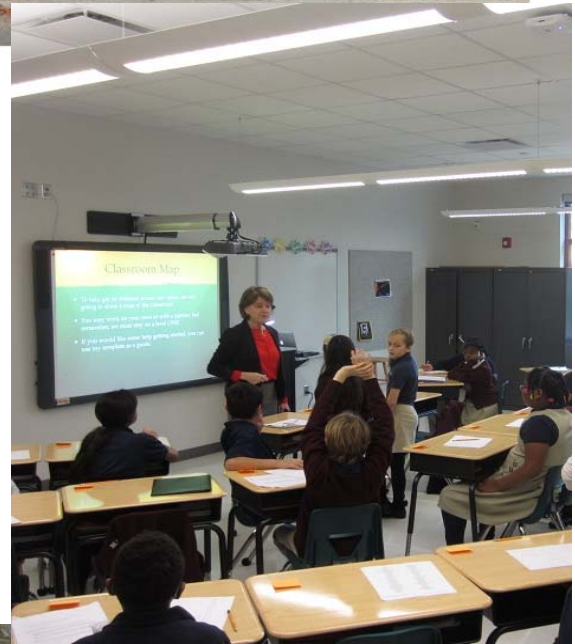

Prepared By



Table of Contents

Right-Click on the school name to proceed to that page

| | |
|---|----|
| TABLE OF CONTENTS | 1 |
| FINANCIAL OVERVIEW | 2 |
| COMMUNITY MEETINGS | 3 |
| BID OPENINGS | 4 |
| DBE OVERVIEW MONTHLY SUMMARY | 5 |
| NEW & MAJOR RENOVATION | 10 |
| Avery Alexander Elementary School ^(RSD) | 10 |
| Benjamin Franklin Elementary School Renovation ^(OPSB) | 10 |
| New Karr High School, CMAR ^(RSD) | 10 |
| John McDonogh High School Renovation CMAR ^(RSD) | 11 |
| Harriet R. Tubman Elementary School Renovation ^(RSD) | 11 |
| Booker T. Washington School CMAR ^(RSD) | 11 |
| REFURBISHMENTS | 12 |
| Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD) | 12 |
| Agnes L. Bauduit Elementary School Refurbishment ^(RSD) | 12 |
| Mary M. Bethune Elementary School Refurbishment ^(OPSB) | 12 |
| Warren Easton Courtyard Waterproofing ^(OPSB) | 13 |
| William J. Fischer Elementary School HVAC Replacement ^(RSD) | 13 |
| Andrew Jackson School Refurbishment ^(RSD) | 13 |
| Lafayette Elementary School Refurbishment ^(RSD) | 14 |
| Laurel Elementary School Refurbishment ^(RSD) | 14 |
| Thurgood Marshall Elementary School Refurbishment ^(RSD) | 14 |
| McDonogh #28 School Flooring Refurbishment ^(RSD) | 15 |
| McDonogh #32 School Refurbishment ^(RSD) | 15 |
| Harriet R. Tubman Elementary School Cottage Renovation ^(RSD) | 15 |
| Schaumburg Roof & Harney Gutters & Downspouts ^(RSD) | 16 |
| Village de l'Est Elementary & Sarah T. Reed HVAC Equipment and Fencing ^(RSD) | 16 |
| DEMOLITIONS | 17 |
| Demolition of Modulares at Abramson 3 ^(RSD) | 17 |
| Demolition of Modulares at Coghill ^(RSD) | 17 |
| COMPLETED PROJECTS | 18 |

Overview

FINANCIAL OVERVIEW - ALL PROJECTS



The RSD has \$465 million in open contracts for the capital program after issuing \$0 million in new contracts, change orders and amendments in July. In addition, the total change orders to date, \$8.1 million, account for two percent (2.08%) of the total open construction contracts. RSD anticipates issuing \$4.9 million in construction contracts/change orders, and \$887 thousand in professional service contracts/amendments in August.



The OPSB has \$232 million in open contracts for the capital program after issuing \$114 thousand in new contracts, change orders and amendments in July. In addition, the total change orders to date, \$9.2 million, account for approximately four percent (4.70%) of the total open construction contracts. OPSB anticipates issuing approximately \$0 thousand in construction contracts/change orders and \$386 thousand in professional service contracts and amendments in August.

Community Meetings



Future Community Meetings

August 8, 2017

NPP Community Meeting for
New Orleans Charter Science and Mathematics High School
2200 Lafitte Avenue, New Orleans LA 70119

August 24, 2017

Ribbon Cutting for Ernest "Dutch" Morial School
7701 Grant Street, New Orleans LA 70126

August 30, 2017

Ribbon Cutting for Avery Alexander School
5800 St. Roch Avenue, New Orleans LA 70112

August 31, 2017

Ribbon Cutting for Ray Abrams School
6519 Virgilian Street, New Orleans LA 70126

Bid Openings

Projects which are scheduled to bid in the next 60 days

August 2, 2017

Harriet Tubman School Cottage Renovation Bid Opening

August 30, 2017

Ben Franklin Elementary School Renovation Bid Opening

September 13, 2017

Schaumburg Roof and Repairs Bid Opening

Disadvantaged Business Enterprises (DBE) Monthly Summary



Recovery School District

New & Renovations:

DBE Contractors secured subcontracts on 23 projects as of July 31, 2017. The DBE subcontracts value is \$81,863,976 of the \$362,314,202 total of awarded contracts.

Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 53 projects as of July 31, 2017. The DBE subcontracts value is \$21,760,188 of the \$68,109,085 total of awarded contracts.

Design-Build New:

DBE Contractors secured subcontracts on 3 projects as of July 31, 2017. The DBE subcontracts value is \$34,542,724 of the \$109,137,557 total of awarded contracts.

CMAR New:

DBE Contractors secured subcontracts on 2 projects as of July 31, 2017. The DBE subcontracts value is \$32,624,001 of the \$86,699,352 total of awarded contracts.

Total Amount of Contracts: \$ 626,260,196

Orleans Parish School Board



New & Renovations:

DBE Contractors secured subcontracts on 14 projects as of July 31, 2017. The DBE subcontracts value is \$54,086,557 of the \$230,451,831 total of awarded contracts.


Stabilization/Demolition/Mothballing:

DBE Contractors secured subcontracts on 2 projects as of July 31, 2017. The DBE subcontracts value is \$296,520 of the \$902,999 total of awarded contracts.

Total Amount of Contracts: \$231,354,830


* DBE provisions were included in projects bid after June 30, 2012

Current RSD Program DBE Participation

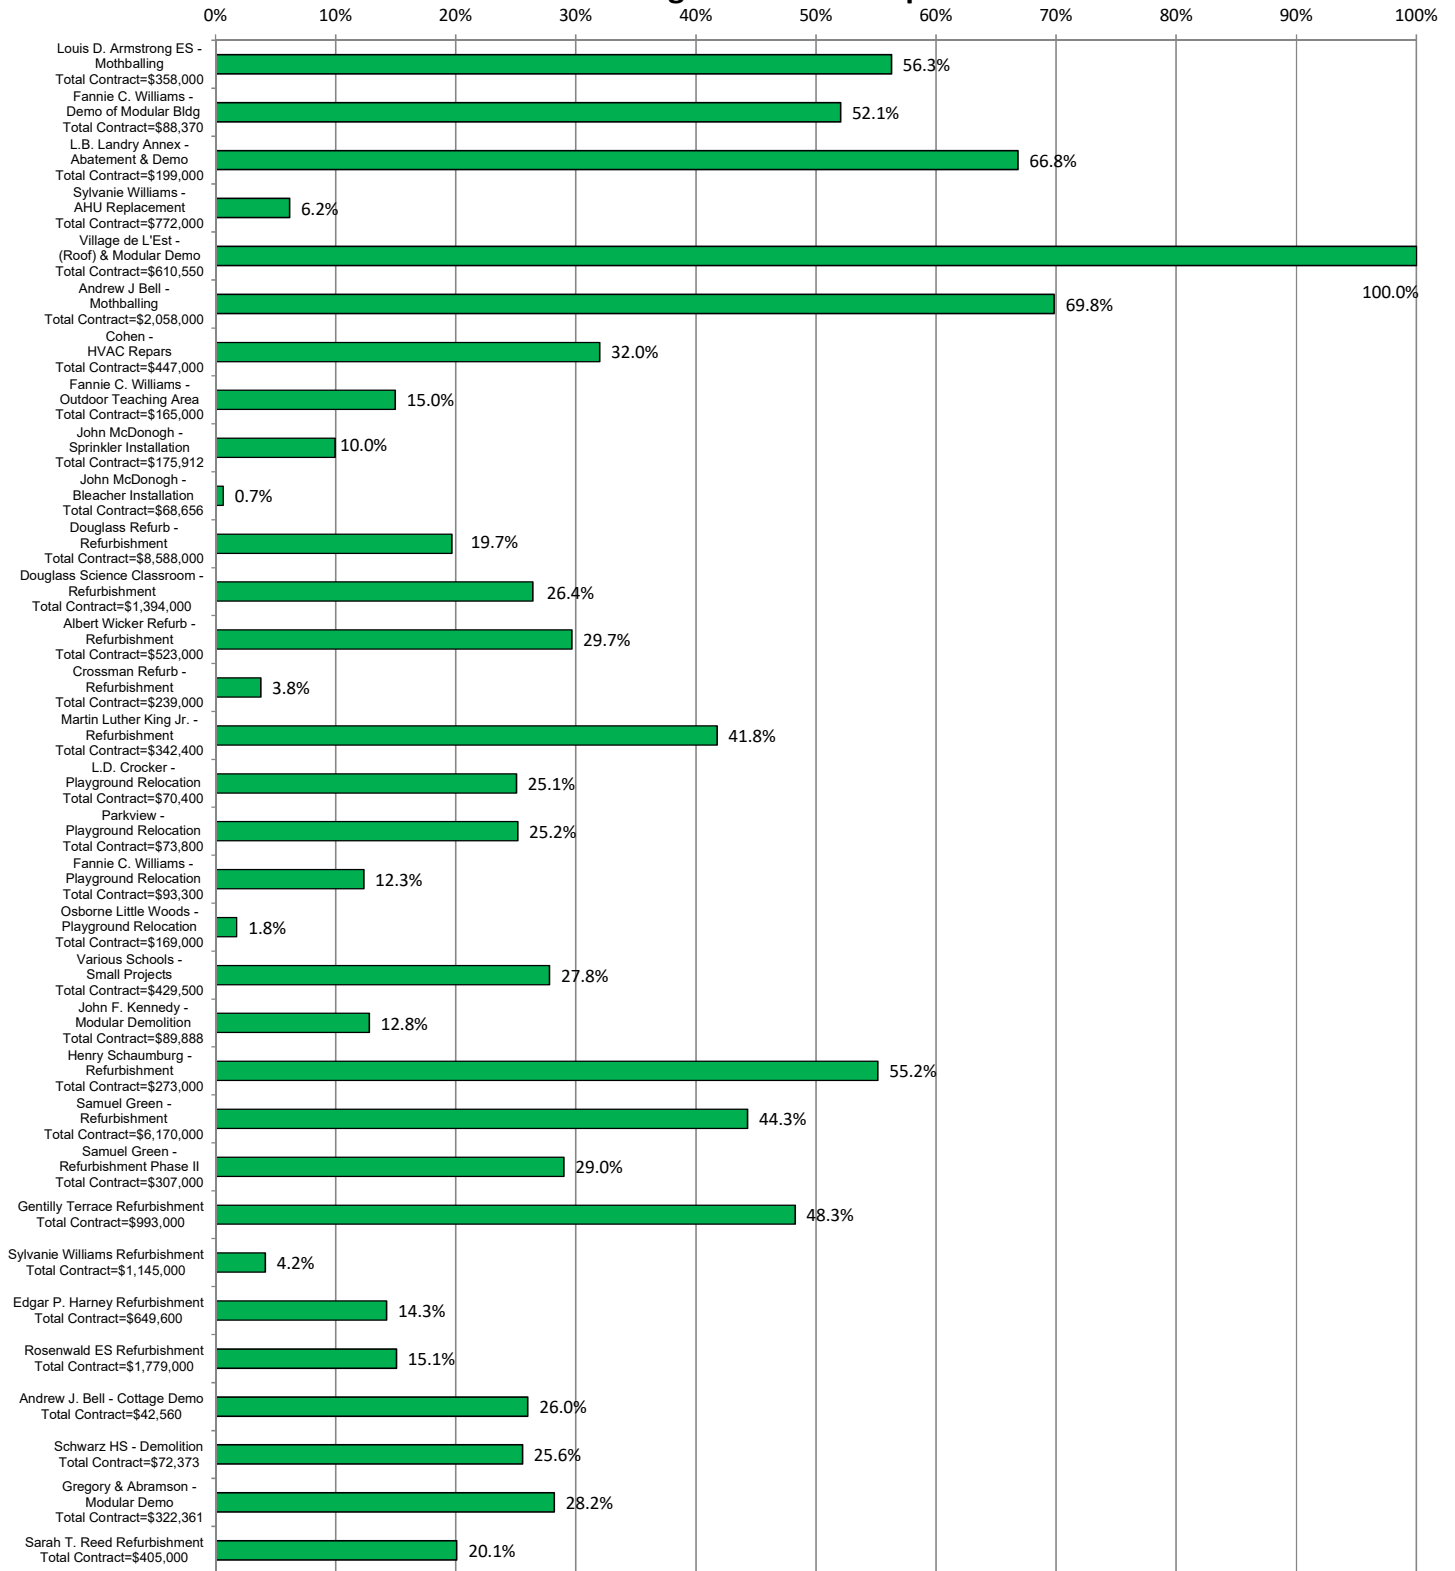

Current RSD Program DBE Participation


(Continued)

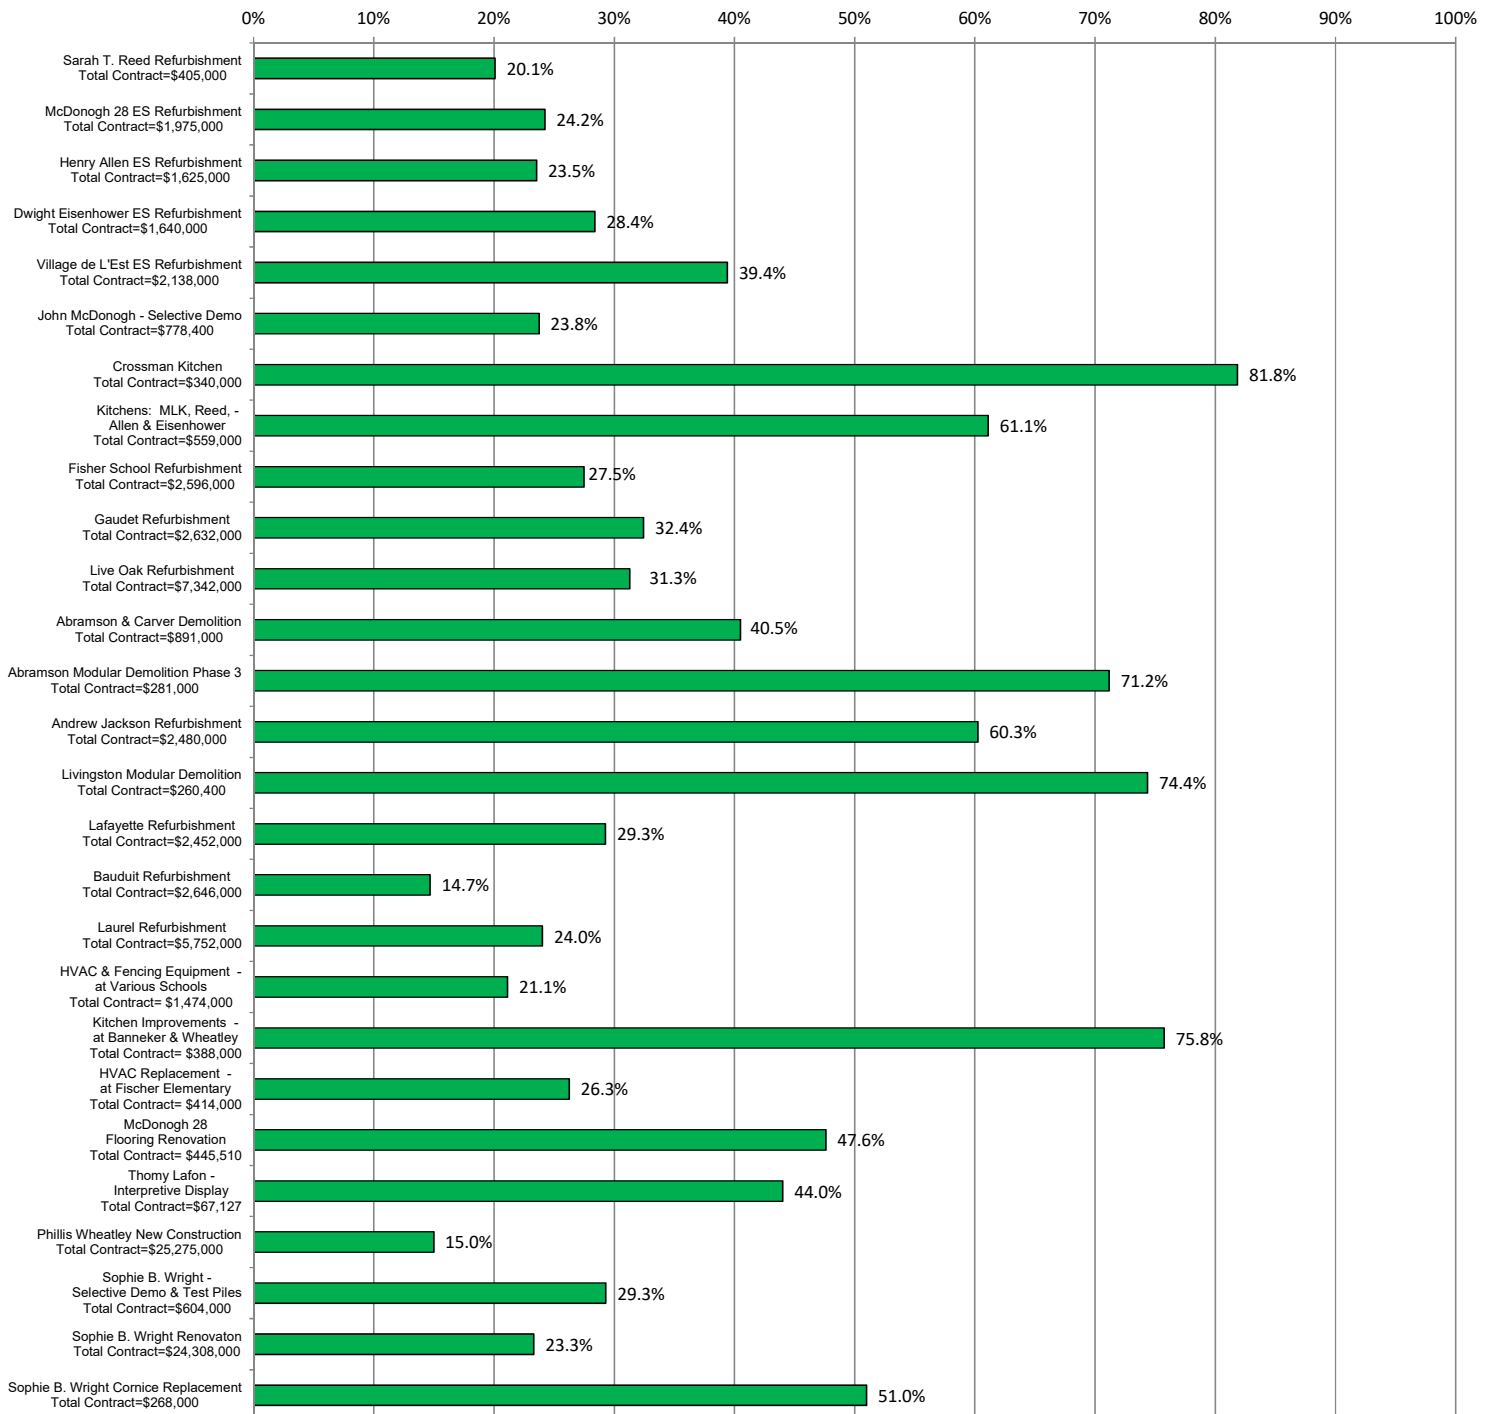

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount


Current RSD Program DBE Participation

(Continued)

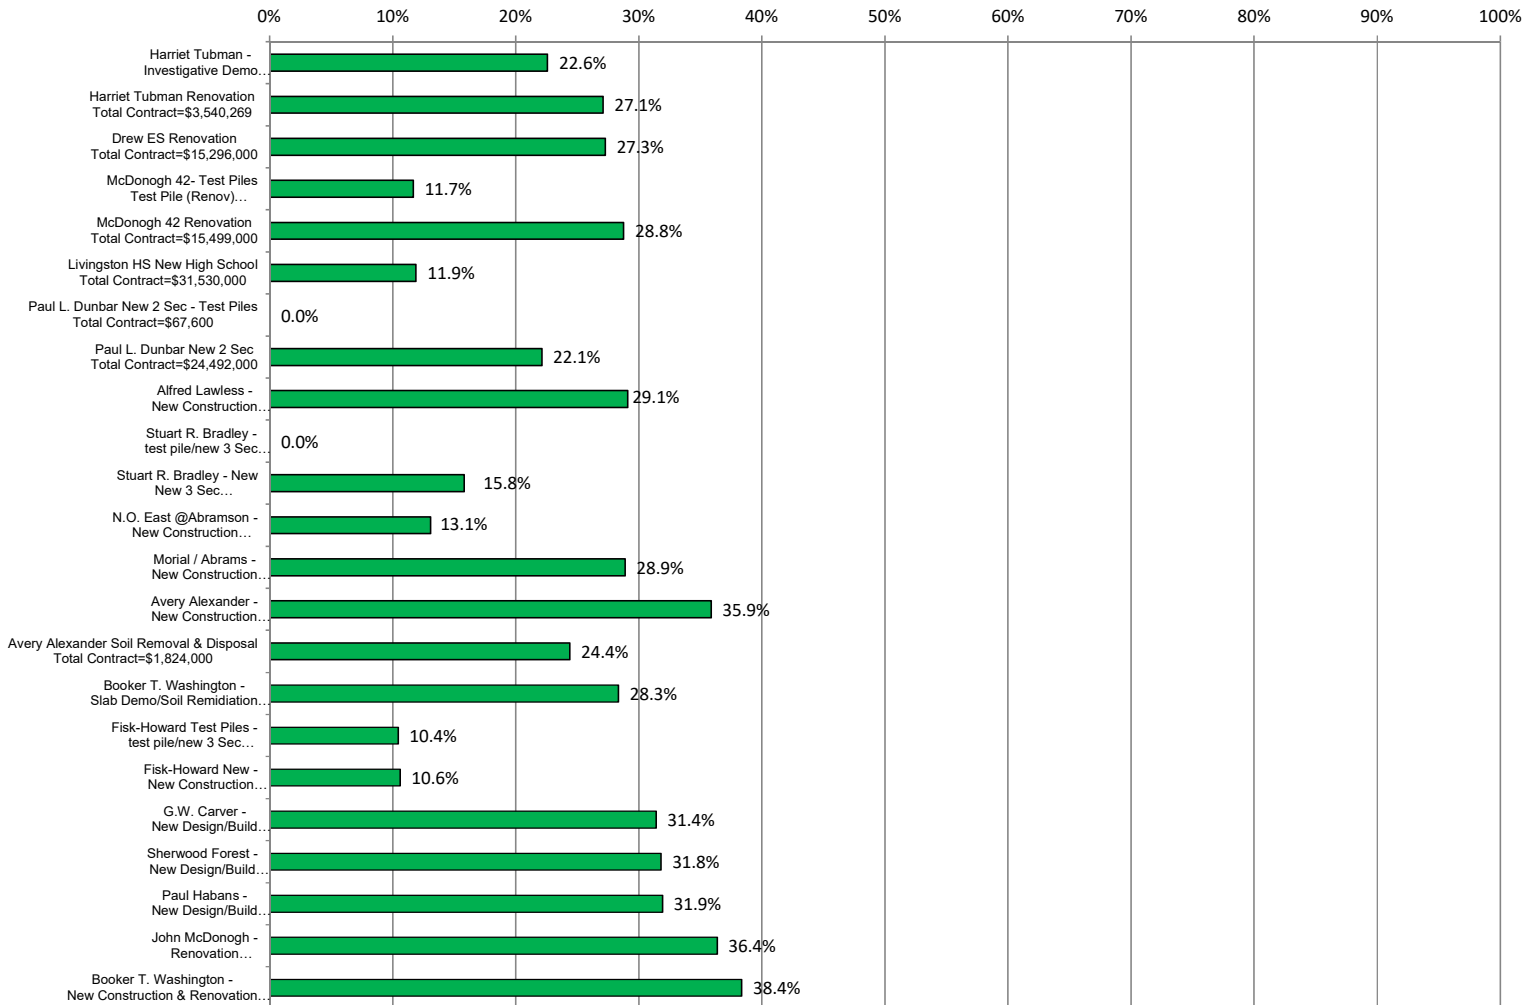

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
RSD DBE Participation Target = 25% of Total Contract Amount

Current OPSB Program DBE Participation

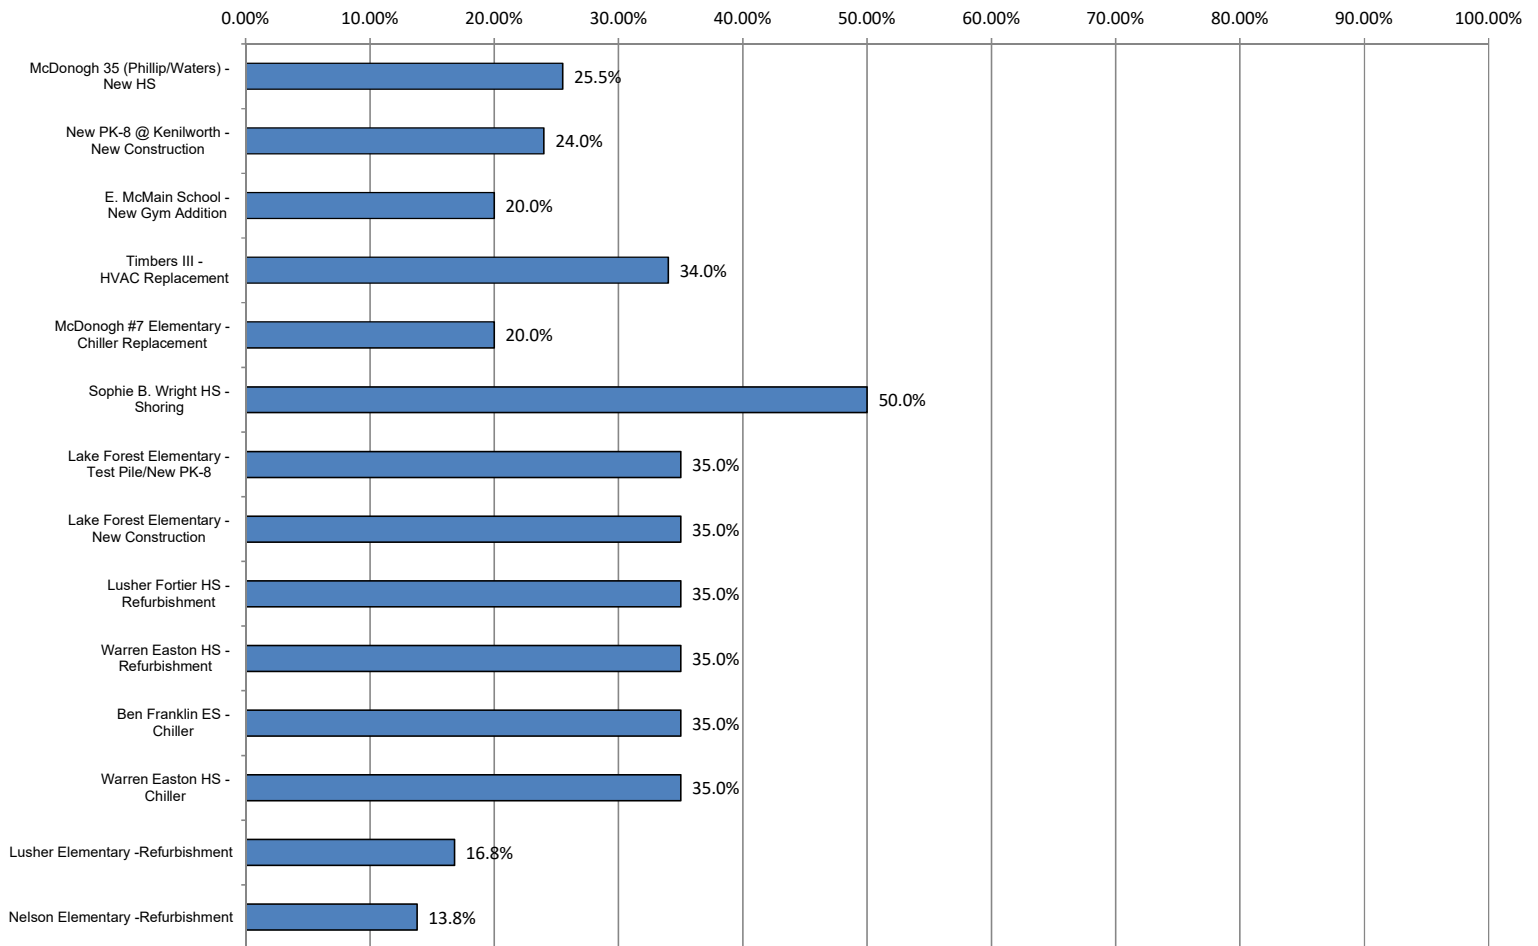

Notes: Data Based On Pre-Construction and/or monthly DBE Reports.
 OPSB DBE Participation Target = 35% of Total Contract Amount

New & Major Renovation – Project Status

(Forecasted dates only include the next project phase)

Avery Alexander Elementary School ^(RSD)

5800 St. Roch Avenue, New Orleans, LA 70122 District D Ward 8

Scope of work: New Pre-K – 8 School

Funding Source – FEMA

Architect – Sizeler Thompson Brown Architects

Contractor – Core Construction

Close-Out Phase

- Ribbon Cutting August 30th

Contractual Substantial Completion – June 2017

Actual Substantial Completion – June 2017



Benjamin Franklin Elementary School Renovation ^(OPSB)

1116 Jefferson Avenue, New Orleans, LA 70115 District CA Ward 14

Scope of work: Renovation of existing elementary school

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - TBD

Procurement Phase

- 1st Advertisement - July 26th
- 2nd Advertisement - August 2nd
- 3rd Advertisement - August 9th
- Pre-Bid Conference - August 10th
- Bid Opening - August 30th



New Karr High School CMAR ^(RSD)

4400 General Meyer Avenue, New Orleans, LA 70131 District C Ward 15

Scope of work: Construction of new high school

Funding Source – FEMA

Architect – Trapolin Peer Architects

Contractor - TBD

Design Phase

- A&E working on Value Engineering
- Test pile program to start August 29th

Contractual Substantial Completion – TBD

Forecasted Substantial Completion – TBD



John McDonogh High School Renovation CMAR ^(RSD)

2426 Esplanade Avenue, New Orleans, LA 70119 District D Ward 6

Scope of work: Renovation of existing school to meet code requirements

Funding Source – FEMA

Architect – VergesRome Architects, APAC

Contractor - Core Construction

Construction Phase

- Activities ongoing at the Main Building include, interior partitions, window refurbishment and MEP rough in
- Masonry tuckpointing is ongoing
- Gymnasium underground rough in work continues

Contractual Substantial Completion – October 2018

Forecasted Substantial Completion – October 2018



Harriet R. Tubman Elementary School Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing elementary school and new addition to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairone Martinez JV

Contractor - Construction Masters Inc

Construction Phase

- Refurbishment of windows is nearing completion
- Floor replacement is ongoing on second floor
- MEP system repairs are ongoing
- Exterior plaster repairs continue
- Cottage Refurbishment Bid Date is August 2nd

Contractual Substantial Completion – May 2018

Forecasted Substantial Completion – May 2018



Booker T. Washington School CMAR ^(RSD)

1201 South Roman Street, New Orleans, LA 70125 District B Ward 2

Scope of work: Renovation of existing auditorium and construction of new high school

Funding Source – FEMA

Architect – Hewitt-Washington & Associates

Contractor – Core Construction

Construction Phase

- Erection of steel at the gymnasium continues
- Pouring of concrete columns and deck continues
- Exterior masonry removal is ongoing

Contractual Substantial Completion – January 2019

Forecasted Substantial Completion – January 2019



REFURBISHMENTS

Banneker School Kitchen Refurbishment and Wheatley Dumpster Pad ^(RSD)

421 Burdette Street, New Orleans, LA 70118 District A Ward 16

2300 Dumaine Street, New Orleans, LA 70119 District A Ward 3

Scope of work: Refurbishment of existing elementary school kitchen at Banneker and addition of grease trap at Wheatley

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Commander Corp

Construction Phase

- Dumpster pads are to be poured in August
- Banneker kitchen plumbing rough in continues
- Banneker kitchen hood installation is ongoing

Contractual Substantial Completion – September 2017

Forecasted Substantial Completion – September 2017



Agnes L. Bauduit Elementary School Refurbishment ^(RSD)

3649 Laurel Street, New Orleans, LA 70115 District B Ward 12

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Duplantis Design Group, PC

Contractor – One Construction

Construction Phase

- Third floor is substantially complete
- Second floor finishes are being installed
- First floor ductwork and lighting installation is underway
- Exterior chiller work is ongoing

Contractual Substantial Completion – May 2017

Forecasted Substantial Completion – August 2017



Mary M. Bethune Elementary School Refurbishment ^(OPSB)

4040 Eagle Street, New Orleans, LA 70118 District A Ward 17

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Chenevert Architects

Contractor – Construction Masters Inc.

Construction Phase

- Interior work is nearing completion
- Exterior tuck pointing is ongoing
- Roof work is 60 % complete

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017



Warren Easton School Courtyard Waterproofing ^(OPSB)

3019 Canal Street, New Orleans, LA 70119 District B Ward 4

Scope of work: Repairs to courtyard waterproofing

Funding Source – FEMA

Architect – Chenevert Architects LLC

Contractor - Thigpen Construction Company

Construction Phase

- Brick and mortar repairs continue

Contractual Substantial Completion – November 2017

Forecasted Substantial Completion – November 2017



William J. Fischer Elementary School HVAC Replacement ^(RSD)

1801 L.B. Landry Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Replacement of existing HVAC

Funding Source – FEMA

Architect – SCNZ Architects

Contractor - Blanchard Mechanical

Construction Phase

- New HVAC units have been installed
- Testing to start in August

Contractual Substantial Completion – August 2017

Forecasted Substantial Completion – August 2017



Andrew Jackson School Refurbishment ^(RSD)

1400 Camp Street, New Orleans, LA 70130 District B Ward 1

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls, roof and kitchen

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - CDW Services

Construction Phase

- Exterior stucco work continues
- Work at the dumpster pad continues

Contractual Substantial Completion – June 2017

Forecasted Substantial Completion – August 2017



Lafayette Elementary School Refurbishment (RSD)

2727 South Carrollton Avenue, New Orleans, LA 70118 District A Ward 16

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – N-Y Associates, Inc.

Contractor - Tuna Construction

Construction Phase

- Window sash refurbishment is nearing completion
- Window hardware installation is ongoing
- 3rd floor VCT installation is nearing completion

Contractual Substantial Completion – July 2017

Forecasted Substantial Completion – August 2017



Laurel Elementary School Refurbishment (RSD)

820 Jackson Avenue, New Orleans, LA 70130 District B Ward 10

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – Mahlum Scairono Martinez JV

Contractor - Tuna Construction

Construction Phase

- Fencing work at Pre-K is ongoing
- HVAC at the main building is running
- Work has started on parking lot
- Repointing of masonry is complete

Contractual Substantial Completion – October 2017

Forecasted Substantial Completion – October 2017



Thurgood Marshall Elementary School Refurbishment (RSD)

4621 Canal Street, New Orleans, LA 70119 District A Ward 4

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Procurement Phase

- Notice to Proceed August 23rd
- Pre-Construction meeting August 24th



McDonogh #28 School Flooring Refurbishment ^(RSD)

2733 Esplanade Boulevard, New Orleans, LA 70114 District A Ward 7

Scope of work: Refurbishment of existing elementary school flooring

Funding Source – FEMA, CDBG

Architect – SCNZ Architects

Contractor - Insultech

Construction Phase

- Flooring repairs are substantially complete

Contractual Substantial Completion – August 2017

Actual Substantial Completion – August 2017



McDonogh #32 School Refurbishment ^(RSD)

800 DeArmas Street, New Orleans, LA 70114 District C Ward 15

Scope of work: Refurbishment of existing elementary school, including but not limited to structure, windows, doors, masonry walls and roof

Funding Source – FEMA, CDBG

Architect – HMS Architects

Contractor - TBD

Design Phase - CD

- Project place "On Hold", awaiting contract execution with A&E



Harriet R. Tubman Elementary School Cottage Renovation ^(RSD)

2013 General Meyer Avenue, New Orleans, LA 70114 District C Ward 15

Scope of work: Renovation of existing cottage to meet code requirements

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor - TBD

Procurement Phase

- 1st Advertisement - June 28th
- 2nd Advertisement - July 5th
- 3rd Advertisement - July 12th
- Pre-Bid Conference - June 13th
- Bid Opening - August 2nd



Schaumburg Roof & Harney Gutters & Downspouts^(RSD)

9501 Grant Street, New Orleans, LA 70127 District E Ward 9

2503 Willow Street New Orleans, LA 70113 District B Ward 11

Scope of work: Replacement of roof at Schaumburg and gutters at Harney

Funding Source – FEMA

Architect – Scairono Martinez

Contractor - TBD

Harney Design Phase

- 50% Construction Documents were received June 30th
- 100% Construction Documents are due August 28th

Schaumburg Procurement Phase

- 1st Advertisement - August 9th
- 2nd Advertisement - August 16th
- 3rd Advertisement - August 23rd
- Pre-Bid Conference - August 24th
- Bid Opening - September 13th



Village de l'Est, Rosenwald, Sarah T. Reed HVAC Equip. & Fencing^(RSD)

5100 Cannes Street, New Orleans, LA 70129 District E Ward 9

5316 Michoud Boulevard, New Orleans, LA 70129 District E Ward 9

Scope of work: Replacement of HVAC equipment and fencing

Funding Source – FEMA

Architect – Marrero Couvillion & Associates

Contractor - Industrial and Mechanical Contractors, Inc

Construction Phase

- HVAC Submittals are being processed
- Demolition of HVAC at Reed has started

Contractual Substantial Completion – November 2017

Forecasted Substantial Completion – November 2017



DEMOLITIONS

Demolition of Modular Buildings at Abramson 3 ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – Ashley Savarino Unlimited Construction

Procurement Phase

- Contracts are being signed
- Pre-Construction meeting is scheduled for August 8th



Demolition of Modular Buildings at Coghill ^(RSD)

5552 Reed Road, New Orleans, LA District C Ward 15

Scope of work: Demolition of existing modular buildings

Funding Source – FEMA

Architect – Mahlum Scairono Martinez JV

Contractor – TBD

Design Phase

- 50% Construction Documents were received July 31st
- 100% Construction Documents are due August 14th



Comprehensive List - Completed Projects

| | | |
|----|---|------------|
| 1 | Abrams Morial Abramson Coghill Demolition ^(RSD) | 11/17/2008 |
| 2 | A. D. Cross Elementary School Energy Conservation ^(RSD) | |
| 3 | A. D. Crossman Elementary School and Benjamin Banneker Elementary School ^(RSD) | 06/12/2012 |
| 4 | A. D. Crossman Elementary School Refurbishment ^(RSD) | 06/04/2014 |
| 5 | A. D. Crossman School Kitchen Refurbishment ^(RSD) | 01/15/2017 |
| 6 | A. P. Tureaud Elementary School Roof Repairs ^(RSD) | 06/13/2013 |
| 7 | Agnes Bauduit Elementary School Boiler ^(RSD) | 12/07/2009 |
| 8 | Albert Wicker Elementary School Refurbishment ^(RSD) | 03/27/2014 |
| 9 | Albert Wicker Elementary School Roof Repairs ^(RSD) | 06/13/2013 |
| 10 | Alfred Lawless Senior ^(RSD) | 12/18/2015 |
| 11 | Alfred Lawless Senior High Security Fencing ^(RSD) | 06/15/2011 |
| 12 | Alice M. Harte Elementary School ^(OPSB) | 11/19/2014 |
| 13 | Alice M. Harte Elementary School Demolition ^(OPSB) | 12/14/2011 |
| 14 | Andrew J. Bell Junior High School Roof Replacement ^(RSD) | 02/08/2014 |
| 15 | Andrew J. Bell Junior High School Mothball ^(RSD) | 06/28/2011 |
| 16 | Andrew Jackson Elementary School Roof Repairs ^(RSD) | 07/27/2012 |
| 17 | Andrew Jackson Elementary School Solar Panels ^(RSD) | 01/14/2013 |
| 18 | Andrew H. Wilson Elementary School Cottage ^(RSD) | 10/11/2010 |
| 19 | Arthur Ashe Elementary School Kitchen Renovation ^(OPSB) | |
| 20 | Augustine Elementary School Roof ^(RSD) | 04/13/2012 |
| 21 | Avery-Alexander Elementary School Demolition ^(RSD) | 06/15/2012 |
| 22 | Barbara C. Jordan Elementary School Demolition ^(RSD) | 05/30/2011 |
| 23 | Bell JH Shoring ^(RSD) | 06/28/2011 |
| 24 | Benjamin Banneker Elementary School Energy Conservation ^(RSD) | |
| 25 | Benjamin Franklin Senior High School ^(OPSB) | 08/23/2013 |
| 26 | Bienville Elementary School Demolition ^(RSD) | 05/04/2009 |
| 27 | Booker T. Washington High School Environmental Remediation ^(RSD) | 12/13/2015 |
| 28 | Booker T. Washington High School Partial Demolition ^(RSD) | 04/07/2013 |
| 29 | Carter G. Woodson Middle School Demolition ^(RSD) | 02/09/2010 |
| 30 | Central Services Warehouse Demolition ^(OPSB) | 01/05/2012 |
| 31 | Charles J. Colton Elementary Selective Demolition ^(RSD) | 07/26/2010 |
| 32 | Charles J. Colton Elementary School ^(RSD) | 05/23/2013 |
| 33 | Charles R. Drew Elementary School ^(RSD) | 04/17/2015 |
| 34 | Charles R. Drew Elementary Roof & Installation of Kitchen Hood ^(RSD) | 06/08/2011 |
| 35 | Cohen High School Health Clinic ^(RSD) | 12/24/2008 |
| 36 | Demolition of Caretakers Cottage at George Mondy Scholl and Andrew Bell School ^(RSD) | |
| 37 | Demolition of Modular Buildings at Gregory and Abramson ^(RSD) | 06/23/2015 |
| 38 | Demolition of Modular Buildings at Abramson and Carver ^(RSD) | 01/18/2017 |
| 39 | Demolition of Modular Buildings at Livingston ^(RSD) | 01/18/2017 |
| 40 | Douglass High School Under Floor Utilities ^(RSD) | |
| 41 | Dr. Martin Luther King School Roof Repairs ^(RSD) | 06/13/2012 |
| 42 | Dr. Martin Luther King Jr. School Renovation ^(RSD) | 12/15/2014 |
| 43 | Dwight D. Eisenhower Elementary School Kitchen Refurbishment ^(RSD) | 02/18/2016 |

| | | |
|----|---|------------|
| 44 | Dwight D. Eisenhower Elementary School Roof Repairs ^(RSD) | 07/27/2012 |
| 45 | Dwight D. Eisenhower Elementary School Refurbishment ^(RSD) | 12/23/2015 |
| 46 | East Bank Swing Space for Audubon Charter School ^(OPSB) | 12/30/2011 |
| 47 | Edgar P. Harney Elementary School Refurbishment ^(RSD) | |
| 48 | Edgar P. Harney Elementary School Roof Repairs ^(RSD) | 06/13/2012 |
| 49 | Edna Karr High School - Gymnasium Repair ^(OPSB) | 12/23/2013 |
| 50 | Edna Karr High School - Assessment ^(OPSB) | |
| 51 | Edward Livingston Middle School Demolition ^(RSD) | 09/28/2010 |
| 52 | Edward Henry Phillips Junior High School Demolition ^(OPSB) | 11/19/2010 |
| 53 | New Edward Hynes School ^(OPSB) | 02/06/2012 |
| 54 | Edwards Hardin Lockett Lawless Demolition ^(RSD) | 11/03/2008 |
| 55 | Edward Livingston High School ^(RSD) | 01/05/2015 |
| 56 | Eleanor L. McMain School Replacement of Existing Chillers ^(OPSB) | 08/30/2011 |
| 57 | Eleanor L. McMain School Clinic ^(OPSB) | 07/24/2013 |
| 58 | Eleanor L. McMain School Maintenance Upgrades ^(OPSB) | 12/12/2016 |
| 59 | Eleanor L. McMain School Roof Replacement ^(OPSB) | 05/13/2016 |
| 60 | Ernest "Dutch" Morial Elementary ^(RSD) | 03/17/2017 |
| 61 | Ernest N. Morial Elementary Security Fencing ^(RSD) | 05/10/2011 |
| 62 | Fannie C. Williams Elementary School Demolition ^(RSD) | 03/10/2009 |
| 63 | Fisk-Howard Elementary School Demolition ^(RSD) | 10/04/2011 |
| 64 | Florence J. Chester Elementary School Demolition ^(RSD) | 06/05/2011 |
| 65 | Fortier (Lusher) High School Refurbishment ^(OPSB) | 02/05/2016 |
| 66 | Francis W. Gregory Demolition ^(RSD) | 12/21/2011 |
| 67 | Frederick A. Douglass High Refurbishment ^(RSD) | 10/28/2014 |
| 68 | Frederick A. Douglass High School Science Lab ^(RSD) | 07/05/2016 |
| 69 | Frederick A. Douglass High Switchgear ^(RSD) | 08/04/2009 |
| 70 | Frederick A. Douglass High Emergency Boiler Roof Repairs ^(RSD) | |
| 71 | Gaudet Elementary School Refurbishment ^(RSD) | 12/20/2016 |
| 72 | Gentilly Terrace Elementary School Refurbishment ^(RSD) | 09/22/2015 |
| 73 | George Mondy Elementary School Mothball ^(RSD) | |
| 74 | George Washington Carver School ^(RSD) | 03/07/2016 |
| 75 | George Washington Carver High School Demolition ^(RSD) | 08/24/2011 |
| 76 | Greater St. Stephens School ^(OPSB) | 03/18/2013 |
| 77 | Harriet R. Tubman Elementary School Selective Demolition ^(RSD) | 12/14/2014 |
| 78 | Henry Allen Elementary School Refurbishment ^(RSD) | 03/08/2016 |
| 79 | Henry Allen Elementary School Kitchen Refurbishment ^(RSD) | 02/18/2016 |
| 80 | Henry Allen Elementary School Roof ^(RSD) | 05/24/2010 |
| 81 | Henry C. Schaumburg School Refurbishment ^(RSD) | 06/26/2015 |
| 82 | Henry C. Schaumburg - Window/Door, Air Condition, Water Fountain/Sink Installation ^(RSD) | 12/16/2011 |
| 83 | Holy Cross Modular Relocation ^(RSD) | 12/14/2010 |
| 84 | Israel M. Augustine Middle School Roof Replacement ^(RSD) | 04/13/2012 |
| 85 | Israel M. Augustine Middle School Mothball ^(RSD) | 01/18/2013 |
| 86 | James Derham Demolition ^(RSD) | 02/23/2012 |
| 87 | James W. Johnson Elementary School Roof ^(RSD) | 07/31/2010 |
| 88 | New Jean Batiste de Bienville School ^(RSD) | 06/15/2012 |
| 89 | Jean Gordon Elementary School Demolition ^(RSD) | 08/16/2010 |

| | | |
|-----|---|------------|
| 90 | JoEllen Smith Medical Center Demolition ^(OPSB) | |
| 91 | John Dibert Elementary School Roof ^(RSD) | 08/20/2010 |
| 92 | John W. Hoffman Elementary School Demolition ^(RSD) | 05/25/2010 |
| 93 | John F. Kennedy Modular Relocation (Schwarz Campus) ^(RSD) | 11/05/2010 |
| 94 | John F. Kennedy Modular Relocation (Coghill Modular Campus) ^(RSD) | 08/05/2011 |
| 95 | John F. Kennedy Modular Demolition ^(RSD) | 09/16/2014 |
| 96 | John F. Kennedy High School Demolition ^(RSD) | 01/12/2012 |
| 97 | John McDonogh Senior High School Bleachers and Sprinklers ^(RSD) | 03/27/2014 |
| 98 | John McDonogh Senior High School Roof ^(RSD) | 05/04/2010 |
| 99 | John A. Shaw Elementary School Mothball ^(RSD) | 12/12/2012 |
| 100 | Joseph S. Clark Senior High School Roof Repairs ^(RSD) | 07/27/2012 |
| 101 | Joseph A. Craig Elementary Canopies ^(RSD) | 06/06/2011 |
| 102 | Joseph A. Craig Elementary Elevator Installation ^(RSD) | 01/20/2012 |
| 103 | Joseph A. Hardin Elementary Security Fencing ^(RSD) | 05/10/2011 |
| 104 | Lafayette Elementary School Roof and Masonry ^(RSD) | 06/22/2012 |
| 105 | Lake Area Landry Demolition ^(RSD) | 05/01/2008 |
| 106 | Lake Forest PK-8 at the Greater St. Stephens Site ^(OPSB) | 11/13/2015 |
| 107 | Langston Hughes Elementary School (Phase I) ^(RSD) | 08/11/2009 |
| 108 | Langston Hughes Elementary School - New Gymnasium (Phase II) ^(RSD) | 11/10/2010 |
| 109 | Langston Hughes Elementary School - Dumpster Pad ^(RSD) | 10/12/2012 |
| 110 | Lawrence D. Crocker Elementary School Demolition ^(RSD) | 04/02/2010 |
| 111 | L.B. Landry Annex Demolition ^(RSD) | 05/02/2013 |
| 112 | Little Woods Elementary School Demolition ^(RSD) | 08/09/2010 |
| 113 | Little Woods School (Dolores T. Aaron Elementary School) ^(RSD) | 08/01/2013 |
| 114 | Live Oak Elementary School Refurbishment ^(RSD) | 01/06/2017 |
| 115 | Live Oak Elementary School Roof ^(RSD) | 08/04/2011 |
| 116 | Live Oak Elementary School Exterior Door Replacement ^(RSD) | 08/26/2011 |
| 117 | Lorraine Hansberry Elementary School Mothball ^(RSD) | 12/27/2012 |
| 118 | Louis D. Armstrong Elementary School ^(RSD) | 02/18/2013 |
| 119 | Lusher Elementary School Refurbishment ^(OPSB) | 10/31/2016 |
| 120 | Mahalia Jackson Elementary School ^(OPSB) | 05/11/2010 |
| 121 | Mahalia Jackson Elementary School Dumpster / Other Improvements ^(OPSB) | 03/06/2012 |
| 122 | Mahalia Jackson Elementary School Office Renovation ^(OPSB) | 04/30/2013 |
| 123 | Martin Behrman Elementary School Roof ^(RSD) | 02/23/2010 |
| 124 | Martin Luther King Jr. Elementary Canopy System ^(RSD) | 11/05/2011 |
| 125 | Martin Luther King Jr. School Modular Building, Deck, Canopy ^(RSD) | 07/31/2012 |
| 126 | Martin Luther King Jr. School Kitchen Refurbishment ^(RSD) | 02/18/2016 |
| 127 | Mary Church Terrell Elementary School Demolition ^(RSD) | 04/17/2013 |
| 128 | Mary M. Bethune Elementary 1st Floor Replacement ^(OPSB) | 01/24/2011 |
| 129 | Mary M. Bethune Elementary Rear Yard Repair/Resurfacing ^(OPSB) | 01/21/2011 |
| 130 | McDonogh #7 High School Repairs ^(OPSB) | |
| 131 | McDonogh #15 Elementary Exterior Masonry to SOI Standards ^(RSD) | 06/11/2012 |
| 132 | McDonogh #28 School Refurbishment ^(RSD) | 03/15/2016 |
| 133 | McDonogh #28 Elementary School Roof ^(RSD) | 11/19/2011 |
| 134 | McDonogh #32 Roof Replacement ^(RSD) | 02/24/2012 |

| | | |
|-----|---|------------|
| 135 | McDonogh #35 ADA Upgrades to Public Restrooms, Exterior Ramp & Handicap Seating in the Auditorium ^(OPSB) | 01/17/2014 |
| 136 | McDonogh #35 School at the Phillip/ Waters Site ^(OPSB) | 09/23/2015 |
| 137 | McDonogh #42 Elementary School Renovation ^(RSD) | 05/28/2015 |
| 138 | McDonogh #42 Elementary School Roof ^(RSD) | 12/21/2011 |
| 139 | McDonogh #42 Elementary School HVAC Replacement ^(RSD) | 08/09/2010 |
| 140 | Mildred C. Osborne Elementary School Demolition ^(RSD) | 02/18/2010 |
| 141 | Mildred C. Osborne Elementary School ^(RSD) | 12/03/2012 |
| 142 | Modular Campuses Close Outs ^(RSD) | |
| 143 | Modular Classroom Demolition at Fannie C. Williams Elementary School ^(RSD) | 05/22/2013 |
| 144 | Modular Structures at Langston Hughes Elementary School ^(RSD) | 04/05/2010 |
| 145 | Morris F.X. Jeff Elementary School Demolition ^(RSD) | |
| 146 | Morris F.X. Jeff Elementary School Mothball ^(RSD) | 01/15/2013 |
| 147 | Murray G. Henderson Elementary School Roof ^(RSD) | 06/23/2012 |
| 148 | Nelson Elementary School Refurbishment ^(OPSB) | 04/18/2016 |
| 149 | New Andrew H. Wilson Elementary School ^(RSD) | 10/11/2009 |
| 150 | New Carter G. Woodson School ^(RSD) | 09/14/2012 |
| 151 | New Fannie C. Williams School ^(RSD) | 08/24/2012 |
| 152 | New Joseph A. Craig Elementary School ^(RSD) | 12/09/2009 |
| 153 | New L.B. Landry High School ^(RSD) | 06/30/2010 |
| 154 | New Lake Area High School ^(RSD) | 12/28/2009 |
| 155 | New Lawrence D. Crocker School ^(RSD) | 04/29/2013 |
| 156 | New PK-8 School at North Kenilworth Park at Curran Site ^(OPSB) | 01/29/2016 |
| 157 | New Parkview School ^(RSD) | 10/12/2012 |
| 158 | New Equipment & Upgrades at 8 Central & 25 Satellite Kitchens ^(RSD) | |
| 159 | New William Frantz Elementary School ^(RSD) | |
| 160 | New Orleans High School Signature Center Study ^(RSD) | |
| 161 | Oretha C. Haley Demo ^(RSD) | 05/07/2012 |
| 162 | Oretha C. Haley Elementary School Mothball ^(RSD) | 09/17/2012 |
| 163 | Parkview Elementary School Demolition ^(RSD) | 08/06/2009 |
| 164 | Paul L. Dunbar Elementary School Demolition ^(RSD) | 06/16/2010 |
| 165 | Paul L. Dunbar Elementary School ^(RSD) | 06/02/2015 |
| 166 | Paul B. Habans Elementary School ^(RSD) | 06/30/2016 |
| 167 | Paul B. Habans Elementary School Roof Repairs ^(RSD) | 07/27/2012 |
| 168 | Phillis Wheatley Elementary School Demolition ^(RSD) | 09/26/2011 |
| 169 | Phillis Wheatley Elementary School ^(RSD) | 07/10/2014 |
| 170 | Ray Abrams Elementary School ^(RSD) | 03/17/2017 |
| 171 | Rosenwald Elementary School Refurbishment ^(RSD) | 04/07/2016 |
| 172 | Robert M. Lusher Elementary Roof Removal & Replacement ^(OPSB) | 07/14/2011 |
| 173 | Samuel J. Green Elementary School Refurbishment ^(RSD) | 02/15/2016 |
| 174 | Samuel J. Green Elementary School Refurbishment Phase 2 ^(RSD) | 02/15/2016 |
| 175 | Sarah T. Reed High School Bleachers ^(RSD) | 01/11/2012 |
| 176 | Sarah T. Reed High School Auditorium Wall ^(RSD) | 03/29/2010 |
| 177 | Sarah T. Reed High School Kitchen Refurbishment ^(RSD) | 02/18/2016 |
| 178 | Sarah T. Reed High School Refurbishment ^(RSD) | 12/01/2015 |
| 179 | Seabrook Computer Training Center Demolition ^(OPSB) | 06/25/2010 |

| | | |
|-----|--|------------|
| 180 | Schaumburg Chillers ^(RSD) | 11/14/2008 |
| 181 | Schwarz Alternative Repairs ^(RSD) | 07/14/2009 |
| 182 | Schwarz Alternative Modularity Demolition ^(RSD) | 04/02/2015 |
| 183 | Schwarz Modular Building Demolition ^(RSD) | 04/02/2015 |
| 184 | Sherwood Forest Elementary School Demolition ^(RSD) | 10/28/2010 |
| 185 | Sherwood Forest Elementary School ^(RSD) | 06/30/2016 |
| 186 | Small New Orleans East High School at Abramson ^(RSD) | 09/24/2015 |
| 187 | Sophie B. Wright School Renovation ^(RSD) | 06/08/2016 |
| 188 | Sophie B. Wright School Selective Demolition ^(RSD) | 01/31/2014 |
| 189 | Sophie B. Wright Various Repairs/Restroom Renovations ^(OPSB) | 07/26/2011 |
| 190 | Stuart R. Bradley Elementary School Demolition ^(RSD) | 01/27/2010 |
| 191 | Stuart R. Bradley Elementary School ^(RSD) | 06/26/2015 |
| 192 | Sylvanie Williams Elementary School AHU Replacement ^(RSD) | 07/30/2013 |
| 193 | Sylvanie Williams Elementary School Play Yard ^(RSD) | 09/23/2010 |
| 194 | Sylvanie Williams Elementary School Roof Repairs ^(RSD) | 07/27/2012 |
| 195 | Sylvanie Williams Elementary School HVAC/Chiller Replacement ^(RSD) | 04/13/2012 |
| 196 | Sylvanie Williams Elementary School Refurbishment ^(RSD) | 02/18/2016 |
| 197 | Temporary Campus for McDonogh #11 Expropriation ^(OPSB) | |
| 198 | Thomas A. Edison Elementary School Demolition ^(RSD) | 03/25/2010 |
| 199 | Thomy Lafon Elementary School Demolition ^(RSD) | 11/27/2011 |
| 200 | Thomy Lafon School Interpretative Display ^(RSD) | 10/15/2013 |
| 201 | Timbers Park Office Building #1 & #2 Demolition ^(OPSB) | 09/18/2011 |
| 202 | Timbers HVAC ^(OPSB) | 09/11/2013 |
| 203 | Timbers III - IT Room Relocation ^(OPSB) | 02/11/2015 |
| 204 | Village de L'est Elementary School Subsidence ^(RSD) | 06/18/2012 |
| 205 | Village de L'est Elementary School Refurbishment ^(RSD) | 10/12/2016 |
| 206 | Village de L'est Elementary School Roof and Modular Demolition ^(RSD) | 06/16/2013 |
| 207 | Vorice J. Waters Elementary School Demolition ^(RSD) | 01/14/2010 |
| 208 | Valena C. Jones Elementary School ^(RSD) | 01/10/2013 |
| 209 | Walter L. Cohen High School HVAC ^(RSD) | 04/04/2014 |
| 210 | Warren Easton High School Renovation ^(OPSB) | 12/15/2015 |
| 211 | Warren Easton High School Window Replacement ^(OPSB) | 09/07/2012 |
| 212 | West Bank Swing Space for Alice Harte Elementary School ^(OPSB) | 07/11/1931 |
| 213 | New William J. Guste Elementary School ^(RSD) | 10/06/2008 |
| 214 | William J. Guste Elementary School Science Lab ^(RSD) | 08/04/2009 |
| 215 | William Frantz Elementary School Environmental Remediation & Selective Demolition ^(RSD) | 04/15/2010 |
| 216 | William Frantz Elementary School Roof ^(RSD) | 08/12/2010 |
